

ASTHETIC TOWNSHIP DEVELOPERS PRIVATE LIMITED

Reg. Office- 262, DDA OFFICE COMPLEX, JHANDEWALA EXT., NEW DELHI - 110055

Ref. No. APL/P/22/047

Date: 28 Apr 2022

To,
The Director
Northern Regional Office (MoEF&CC)
Bays No. 24-25, Sector- 31-A
Dakshin Marg,
Chandigarh-160030

Subject: Submission of six-monthly Compliance Report for June 2022 of the Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana by M/s. Asthetic Township Developers Pvt. Ltd.

Reference: F.No.21-137 /2018-IA-III, dated : 07/02/2019

Respected Sir,

This is with reference to above-mentioned subject, we are herewith submitting six monthly compliance report of **June 2022** for the period of **October 2021 – March 2022** for the Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana by M/s. Asthetic Township Developers Pvt. Ltd. along with the necessary annexure for your kind perusal.

We understand that the above is in line with requirement of Ministry of Environment & Forest and Climate Change, GOI.

Thanking you,
Yours Sincerely,



For M/s Asthetic Township Developers Pvt. Ltd.
Mukesh Gour
(Authorized Signatory)

Enclosure: Compliance Report; Soft copy of Report in C.D.

Copy to: 1. Member Secretary, Haryana State Pollution Control Board, C-11 Sec-6, Panchkula, Haryana
2. The Chairman, State Environmental Impact Assessment Authority, Bays No. 55 - 58, 1st Floor, Paryatan Bhawan, Sector 2, Panchkula, Haryana

CIN NO. U45201DL2006PTC147126

Email: asthetic64@gmail.com

Commercial Complex

‘Six Monthly Compliance Report’

**Expansion of Commercial Complex Project at
Sushant Lok, Sector-27, Gurugram Haryana by
M/s. Asthetic Township Developers Pvt. Ltd.**

SUBMITTED BY

**M/s Asthetic Township Developers
Pvt. Ltd.**

JUNE 2022

TABLE OF CONTENT

S. No	Description
Compliance of Specific and General Conditions	

LIST OF ANNEXURES

Annexure	Description
Annexure-I	Environment Clearance Letter
Annexure-II	HSPCB/Consent/: 329962320GUNOCTE7324277dated 03/02/2020
Annexure-III	Aravali NOC
Annexure IV	Renewal of Licence from Directorate of Town & Country Planning, Haryana
Annexure-V	Intekaal Letter
Annexure-VI	Water Balance
Annexure-VII	RWH Details
Annexure-VIII	Waste management plan during Construction & Operation Phase
Annexure IX	Photographs of construction of Wind Breaking wall of 10 mtrs. height for dust control
Annexure-X	Environment Monitoring Reports i.e. AAQ, Noise, Water & soil and its
Annexure-XI	Landscape plan
Annexure-XII	Photographs showing Excavated top soil is preserved
Annexure-XIII	PUC Certificate
Annexure-XIV	Environment Management and Monitoring Plan
Annexure-XV	Receiving of Previous Compliance Report of June, 2021
Annexure-XVI	RMC Purchase Bill
Annexure-XVII	Electricity Approval for construction
Annexure-XVIII	Current photographs of site
Annexure-XIX	Photographs of Basic Infrastructure provided at Project Site
Annexure-XX	AAI NOC

Annexure-XXI	Copy of receipt from MCG
--------------	--------------------------

Annexure-XXII	Copy of Purchase AACs block.
---------------	------------------------------

Annexure-XXIII	Photographs of Antismog gun and Logbook
----------------	---

Annexure-XXIV	Copy of HSD bills
---------------	-------------------

Annexure-XXV	Copies of Newspaper Advertisement
--------------	-----------------------------------

Annexure-XXVI	Copy of Office Memorandum (OM)
---------------	--------------------------------

Annexure-XXVII	Request Letter to GMDA
----------------	------------------------

LIST OF TABLES

Tables	Description	Page No
Table-1	Schedule of Ambient Air Quality Monitoring	01
Table-1(a)	Monitoring Result of SO ₂	01
Table-1(b)	Monitoring Result of NO ₂	02
Table-1(c)	Monitoring Result of PM ₁₀	02
Table- 1(d)	Monitoring Result of PM _{2.5}	03
Table-1(e)	Monitoring Result of CO	04
Table-2	Schedule of Noise Monitoring	05
Table-2(a)	Day time Monitoring result for Ambient Noise	06
Table-2(b)	Night time Monitoring result for Ambient Noise	06
Table-3	Schedule for Drinking Water sample collection	07
Table-3(a)	Drinking Water Monitoring Results	07
Table-4	Schedule for Soil sample collection	09
Table-4(a)	Soil Monitoring Results	09

LIST OF FIGURES

Figure Nos.	Description	Page No
Figure-1(a)	SO ₂ Concentration	01
Figure-1(b)	NO ₂ Concentration	02
Figure-1(c)	PM ₁₀ Concentration	03
Figure-1(d)	PM _{2.5} Concentration	04
Figure-1(e)	CO Concentration	05
Figure-2(a)	Graph showing day time noise monitoring result	06
Figure-2(b)	Graph showing night time noise monitoring result	07

COMPLIANCE REPORT

Specific and General Conditions as per the Environmental Clearance issued for Expansion vide F. No. 21-137/2018-IA.III Dated: 07/02/2019 (Annexure-I) for Construction and Operation phases of the Project.

S No	Conditions	Compliance
Part A : Specific conditions		
	I. Construction phase	
i.	The project proponent shall obtain all necessary clearance/ permission from all relevant agencies including town planning authority before commencement of work. All the construction shall be done in accordance with the local building byelaws.	We would obtain all the necessary clearances/ permission from all the concerned departments in due course of time. As we are in initial stage of construction phase. Following permission we have already obtained: i. Environmental Clearance, ii. Consent to Establish, iii. Aravali NOC, iv. Renewal of License from Directorate of Town & Country Planning, Haryana v. Intekaal Letter vi. AAI NOC Copies of these permissions/clearances are attached as Annexure I, II, III, IV & V respectively.
ii.	“Consent for Establishment /Operate” for the project shall be obtained from the State Pollution Control Board as required under Air (Prevention and Control of Pollution) Act, 1981 and the Water (Prevention and Control of Pollution) Act, 1974.	We have received Consent to Establish for the project. The Copy of the CTE issued by HSPCB vide CTE order no. HSPCB/Consent/: 329962320GUNOCTE7324277 dated 03/02/2020 is attached for your reference as Annexure-II .
iii.	The approval of the Competent Authority shall be obtained for structural safety of buildings due to earthquakes, adequacy of firefighting equipment etc as per National Building Code including protection measures from lightening etc.	We will submit the Structure Stability certificate in due course of time.
Topography and natural Drainage		
iv.	The natural drain system should be maintained for ensuring unrestricted flow of water. No construction shall be allowed to obstruct the natural drainage through the site, on wetland and water bodies. Check dams, bio-swales, landscape, and other	This condition will be complied. Topographical survey has already been done to maintain the natural unrestricted flow of water, when required.

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana
by M/s. Asthetic Township Developers Pvt. Ltd.**

	sustainable urban drainage systems (SUDS) are allowed for maintaining the drainage pattern and to harvest rain water. Buildings shall be designed to follow the natural topography as much as possible. Minimum cutting and filling should be done.	
Water requirement, Conservation, rain water Harvesting, and Ground Water Recharge		
v.	Fresh water requirement from HUDA supply shall not exceed 42 KLD with prior permission.	Request Letter has been given to GMDA for fresh water requirement. Copy of Letter is attached as Annexure-XXVII .
vi.	A certificate shall be obtained from the local body supplying water, specifying the total annual water availability with the local authority, the quantity of water already committed the quantity of water allotted to the project under consideration and the balance water available. This should be specified separately for ground water and surface water sources, ensuring that there is no impact on other users.	Request Letter has been given to GMDA for fresh water requirement regarding supply of water for operation of the project. Copy of Letter is attached as Annexure-XXVII .
vii.	The quantity of fresh water usage, water recycling and rainwater harvesting shall be measured and recorded to monitor the water balance as projected by the project proponent. The record shall be submitted to the Regional Office, MoEF&CC along with six monthly Monitoring reports.	For measurement of water consumption, we will install water meter at all the required points of water consumption and record of the same will be maintained and submitted.
viii.	At least 20% of the open spaces as required by the local building bye laws shall be pervious. Use of Grass pavers, paver blocks with at least 50% opening, landscape etc. would be considered as pervious surface.	This condition will be complied.
ix.	Installation of dual pipe plumbing for supplying fresh water for drinking, cooking and bathing etc and other for supply of recycled water for flushing, landscape irrigation, car washing, thermal cooling, conditioning etc. shall be done.	Dual plumbing system has already been taken into consideration. Water Balance showing use of treated water is attached as Annexure-VI for your reference.
x.	Use of water saving devices fixtures (viz. low flow flushing systems; use of low flow faucets tap aerators etc.) for water conservation shall be	This condition will be complied during Operation Phase. Use of water saving devices fixtures (viz. low flow flushing systems; use of low flow faucets

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana
by M/s. Asthetic Township Developers Pvt. Ltd.**

	incorporated in the building plan.	tap aerators etc.) for water conservation has been already taken in consideration for the project.
xi.	Separation of grey and black water should be done by the use of dual plumbing system. In case of single stack system separate recirculation lines for flushing by giving dual plumbing system be done.	Dual plumbing system has already been taken into consideration. Water Balance showing use of treated water is attached as Annexure-VI for your reference.
xii.	Water demand during construction should be reduced by use of pre-mixed concrete, curing agents and other best practices referred.	Ready Mix Concrete used for Construction work and Purchase bill for the period (October, 2021 to March, 2022) of RMC is attached as Annexure XVI .
xiii.	The local bye-law provisions on rain water harvesting should be followed. If local bye-law provision is not available, adequate provision for storage and recharge should be followed as per the Ministry of Urban Development Model Building Byelaws, 2016. As proposed 03 nos. of rain water harvesting recharge pits shall be provided for rain water harvesting after filtration as per CGWB guidelines.	We have proposed 03 nos. of rain water harvesting recharge pits for rain water harvesting. We have considered all the design criteria of local authority and CGWB. Detail of RWH is attached as Annexure-VII .
xiv.	No ground water shall be used during construction/ operation phase of the project.	STP treated water is being used for construction purpose and HUDA supply water will be used in operational phase of project.
xv.	Any ground water dewatering should be properly managed and shall conform to the approvals and the guidelines of the CGWA in the matter. Formal approval shall be taken from the CGWA for any ground water abstraction or dewatering.	Noted. No ground water will be used during construction/ operation phase of the project without prior permission.
Solid Waste Management		
xvi.	The provision of the Solid waste (Management) Rules, 2016, e-waste (Management) Rules, 2016, and the Plastics waste (Management) Rules, 2016 shall be followed.	Waste management plan for construction and operation phase of the project has been prepared and submitted during Environmental Clearance. Detailed waste management plan solid waste, e-waste, and Plastic waste is attached as Annexure-VIII .
xvii.	Disposal of muck during construction phase shall not create any adverse effect on the neighbouring communities and be disposed taking the necessary precautions for general safety and health aspects of people, only in approved sites with the approval of	All Construction and demolition (C&D) waste is being disposed by Municipal Corporation Gurgaon (MCG). Copy of receipt from MCG is attached as Annexure-XXI .

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana
by M/s. Asthetic Township Developers Pvt. Ltd.**

	competent authority.	
xviii.	Separate wet and dry bins must be provided in each unit and at the ground level for facilitating segregation of waste. Solid waste shall be segregated into wet garbage and inert materials. Wet garbage shall be composted in Organic Waste Converter. Adequate area shall be provided for solid waste management within the premises which will include area for segregation composting. The inert waste from project will be sent to dumping site.	Detailed waste management plan is prepared. Waste management plan is attached as Annexure-VIII .
xix.	Any hazardous waste generated during construction phase, shall be disposed off as per applicable rules and norms with necessary approvals of the State Pollution Control Board.	Hazardous waste generated during Construction and Operation phase of the project will be disposed off as per Hazardous and Other Wastes (Management and Transboundary Movement) Rules, 2016.
xx.	A certificate from the competent authority handling municipal solid wastes, indicating the existing civic capacities of handling and their adequacy to cater to the M.S.W. generated from project shall be obtained.	Municipal Solid Wastes is being managed by Municipal corporation Gurgaon (MCG).
Sewage Treatment Plant		
xxi.	Sewage shall be treated in the STP based on SBR technology with tertiary treatment i.e. Ultra Filtration. The treated effluent from STP shall be recycled/re-used for flushing and horticulture. Excess water shall be discharged to Municipal Sewer with prior permission.	This condition will be complied. We are in a stage of finalization of contractor for STP installation. We will submit the document in due course of time. This will be submitted after installation & commissioning of STP for Operational Phase.
xxii.	A certificate from the competent authority for discharging treated effluent/ untreated effluents into the Public sewer/ disposal/ drainage systems along with the final disposal point shall be obtained.	Our project is based on zero liquid discharge. So, there will not be any discharge treated effluent/ untreated effluents in to public sewer.
xxiii.	No sewage or untreated effluent water would be discharged through storm water drains.	This condition will be complied.
xxiv.	The project proponents would devise a monitoring plan to the satisfaction of the State Pollution Control Board so as to continuously monitor the treated waste water being used for flushing in terms of faecal	This Condition will be complied and we will re-used treated waste water for flushing and other use as per the guideline of HSPCB.

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana
by M/s. Asthetic Township Developers Pvt. Ltd.**

	coliforms and other pathogenic bacteria.	
xxv.	The project proponents would commission a third party study on the implementation of conditions related to quality and quantity of recycle and reuse of treated water, efficiency of treatment systems, quality of treated water being supplied for flushing (specially the bacterial counts), comparative bacteriological studies from toilet seats using recycled treated waters and fresh waters for flushing, and quality of water being supplied through spray faucets attached to toilet seats.	This condition will be complied as project is in construction phase. Detailed plan for Operational phase will be submitted in due course of time.
xxvi.	The installation of the Sewage Treatment Plant (STP) shall be certified by an independent expert and a report in this regard shall be submitted to the Ministry before the project is commissioned for operation. Periodical monitoring of water quality of treated sewage shall be conducted. Necessary measures should be made to mitigate the odour problem from STP.	We will obtain the adequacy report for designed STP and submit the same in due course of time. We will ensure that there should not be any odour problem. This will be submitted after installation & commissioning of STP for Operational Phase.
xxvii.	Sludge from the onsite sewage treatment, including septic tanks, shall be collected, conveyed and disposed as per Ministry of Urban Development, Central Public Health and Environmental Engineering Organization (CPHEEO) Manual on Sewerage and Sewage Treatment Systems, 2013.	This condition will be complied and we will give agreement to the competent agency for disposal of sludge.
Energy		
xxviii.	Compliance with the Energy Conservation Building Code (ECBC) of Bureau of Energy Efficiency shall be ensured. Buildings in the States which have notified their own ECBC, shall comply with the State ECBC. Outdoor and common area lighting shall be LED. Concept of passive solar design that minimize energy consumption in buildings by using design elements, such as	This condition will be complied. As we are in construction stage of the project. We will submit the detailed ECBC plan in due course of time.

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana
by M/s. Asthetic Township Developers Pvt. Ltd.**

	building orientation, landscaping, efficient building envelope, appropriate fenestration, increased day lighting design and thermal mass etc. shall be incorporated in the building design. Wall, window, and roof u- values shall be as per ECBC specifications.	
xxix.	Energy conservation measures like installation of CFLs/ LED for the lighting the area outside the building should be integral part of the project design and should be in place before project commissioning. Used CFLs, TFL and LED shall be properly collected and disposed off / sent for recycling as per the prevailing guidelines / rules of the regulatory authority to avoid mercury contamination.	This condition will be complied. As we are in construction stage of the project. We will submit the detailed ECBC plan in due course of time. The E-Waste (Management) Rules, 2016 will be followed for disposal of Used CFLs, TFL and LED during Construction and Operation Phase. An agreement will be made with authorized vendor for safe handling and disposal of E-waste.
xxx.	Solar, wind or other Renewable Energy shall be installed to meet electricity generation equivalent to 1% of the demand load or as per the state level/ Local building bye-laws requirement, whichever is higher. Follow super ECBC requirement of ECBC 2017 and provide compliance report.	This condition will be complied. We are doing feasibility detailing for the same. Detailed plan for Energy Conservation Plan as per ECBC 2017 will be submitted during operation phase of the project.
xxxi.	Solar power shall be used for lighting in the apartment to reduce the power load on grid. Separate electric meter-shall be installed for solar power. Solar water heating shall be provided to meet 20% of the hot water demand of the commercial and institutional building or as per the requirement of the local building bye-laws, whichever is higher. Residential buildings are also recommended to meet its hot water demand from solar water heaters, as far as possible.	This condition will be complied and detailed will be submitted in due course of time.
xxxii.	Use of environment friendly materials in bricks, blocks and other construction materials, shall be required for at least 20% of the construction material quantity. These include Fly Ash bricks, hollow bricks, AACs, Fly Ash Lime Gypsum blocks, Compressed earth blocks, and other environment	Environment friendly AACs block are being used as construction material. Copy of Purchase bills is attached as Annexure-XXII. Ready mixed concrete is being used in building construction. Copy of RMC bills is attached as Annexure-XVI.

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana
by M/s. Asthetic Township Developers Pvt. Ltd.**

	friendly materials- Fly ash should be used as building material in the construction as per the provision of Fly Ash Notification of September, 1999 and amended as on 27 August, 2003 and 25 th January, 2016. Ready mixed concrete must be used in building construction.	
xxxiii.	A certificate of adequacy of available power from the agency supplying power to the project along with the load allowed for the project shall be submitted.	Permission for Electricity Connection from Dakshin Haryana Bijli Vitran Nigam for Construction work has been obtained and copy of permission is attached as Annexure XVII .
Air Quality and Noise		
xxxiv.	Construction site shall be adequately barricaded before the construction begins. Dust, smoke & other air pollution prevention measures shall be provided for the building as well as the site. These measures shall include screens for the building under construction, continuous dust wind breaking walls all around the site (at least 3 meter height). Plastic/tarpaulin sheet covers shall be provided for vehicles bringing in sand, cement, murram and other construction materials prone to causing dust pollution at the site as well as taking Out debris from the site. Sand, murram, loose soil, cement stored on site shall be covered adequately so as to prevent dust pollution. Wet jet shall be provided for grinding and stone cutting. Unpaved surfaces and loose soil shall be adequately sprinkled with water to suppress dust.	Construction site has been adequately barricaded by Wind Breaking wall of 10m height for dust control. Photograph of the same is attached for your reference as Annexure-IX . Unpaved surfaces are being adequately sprinkled with water to suppress dust. Anti-smog gun is being used to reduce air pollution by spraying atomized water into the atmosphere to settle dust and other suspended particles. Photographs of antismog gun and Logbook for use of Antismog gun is attached as Annexure-XXIII .
xxxv.	Notification GSR 94(E) dated 25.01.2018 of MoEF&CC regarding Mandatory implementation of Dust Mitigation Measures for Construction and Demolition Activities for projects requiring Environmental Clearance shall be complied with.	Construction site has been adequately barricaded by Wind Breaking wall of 10m height for dust control. Photograph of the same is attached for your reference as Annexure-IX . Unpaved surfaces are being adequately sprinkled with water to suppress dust. Anti-smog gun is being used to reduce air pollution by spraying atomized water into the atmosphere to settle dust and other suspended particles. Photographs of antismog gun and Logbook for use of Antismog gun is attached as Annexure-

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana
by M/s. Asthetic Township Developers Pvt. Ltd.**

		XXIII.
xxxvi.	All construction and demolition debris shall be stored at the site (and not dumped on the roads or open spaces outside) before they are properly disposed. All demolition and construction waste shall be managed as per the provisions of the Construction and Demolition Waste Rules, 2016. All workers working at the construction site and involved in loading, unloading, carriage of construction material and construction debris or working in any area with dust pollution shall be provided with dust mask.	C&D Waste generated at project site during construction work have been given to Municipal Corporation Gurugram. Bill for lifting of Construction waste at site is attached as Annexure XXI. Mask has been provided to all construction workers for protection from the dust.
xxvii.	The diesel generator sets to be used during construction phase shall be low sulphur diesel type and shall conform to Environmental (Protection) prescribed for air and noise emission standards.	High speed Diesel are being used for DG Sets. Copy of HSD bills are attached as Annexure-XXVI. DG Noise and stack emission monitoring report is attached as Annexure-X.
xxviii.	The gaseous emissions from DG set shall be dispersed through adequate stack height as per CPCB standards. Acoustic enclosure shall be provided to the generator sets to mitigate the noise pollution. The location of the DG set and exhaust pipe height shall be as per the provisions of the Central Pollution Control Board (CPCB) norms.	Adequate stack height as per CPCB standards will be provided for the DG sets during Operation Phase. DG Set will be acoustically enclosed for noise control.
xxxix.	For indoor air quality the ventilation provisions as per National Building Code of India.	Noted and Agreed. For indoor air quality the ventilation provisions will be provided as per National Building Code of India.
xl.	Ambient noise levels shall conform to residential standard both during day and night as per Noise Pollution (Control and Regulation) Rules, 2000. Incremental pollution loads on the ambient air and noise quality shall be closely monitored during construction phase Adequate measures shall be made to reduce ambient air and noise level during construction phase, so as to conform	Regular Monitoring, as per the statutory requirements of Ambient Noise and Ambient Air Quality will be conducted. AAQ and Ambient Noise Monitoring report is attached as Annexure-X.

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana
by M/s. Asthetic Township Developers Pvt. Ltd.**

	to the stipulated standards by CPCB / SPCB.	
Green Cover		
xli.	No tree cutting/transplantation of existing trees has been proposed in the project. A minimum of 1 tree for every 80 sqm of land should be planted and maintained. The existing trees will be counted for this purpose. The landscape planning should include plantation of native species. The species with heavy foliage, broad leaves and wide canopy cover are desirable. Water intensive and/or invasive species should not be used for landscaping As proposed 2423.82 sqm area shall be provided for green area development.	This condition will be complied. Landscape Plan attached for your reference as Annexure-XI .
Top Soil preservation and Reuse		
xlii.	Topsoil should be stripped to a depth of 20 c m from the areas proposed for buildings, roads, paved areas, and external services. It should be stockpiled appropriately in designated areas and reapplied during plantation of the proposed vegetation on site.	Excavated top soil is preserved for use during Landscape development activities. Photograph of the same is attached as Annexure-XII .
xliii.	As proposed, adequate provision will be made for car/vehicle parking at the proposed project site. There shall also be adequate parking provisions for visitors so as not to disturb the traffic and allow smooth movement at the site.	This condition will be complied. Approved parking plan will be submitted in due course of time.
xliv.	A comprehensive mobility plan, as per MoUD best practices guidelines (URDPFI), shall be prepared to include motorized, non-motorized, public, and private networks. Road should be designed with due consideration for environment, and safety of users. The road system can be designed with these basic criteria. • Hierarchy of roads with proper segregation of vehicular and pedestrian traffic. • Traffic calming measures • Proper design of entry and exit	This condition will be complied.

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana
by M/s. Asthetic Township Developers Pvt. Ltd.**

	points. • Parking norms as per local regulation	
xlvi.	A detailed traffic management and traffic decongestion plan shall be drawn up to ensure that the current level of service of the roads within a 05 kms radius of the project is maintained and improved upon after the implementation of the project. This plan should be based on cumulative impact of all development and increased habitation being carried out or proposed to be carried out by the project or other agencies in this 05 Kms radius of the site in different scenarios of space and time and the traffic management plan shall be duly validated and certified by the State Urban Development department and the P.W.D./ competent authority for road augmentation and shall also have their consent to the implementation of components of the plan which involve the participation of these departments.	This condition will be complied and the same will be submitted in due course of time.
	Vehicles hired for bringing construction material to the site should be in good condition and should have a pollution check certificate and should conform to applicable air and noise emission standards be operated only during non-peak hours.	We are ensuring that all vehicles which are coming to the site are in good condition & monitoring record of PUC certificate of Vehicle is enclosed as Annexure-XIII.
Environment management Plan		
	An environmental management plan (EMP) as prepared and submitted shall be implemented to ensure compliance with the environmental conditions specified above. A dedicated Environment Monitoring Cell with defined functions and responsibility shall be put in place to implement the EMP. The environmental cell shall ensure that the environment infrastructure like Sewage Treatment Plant, Landscaping, Rain Water Harvesting, Energy efficiency and	Environment Management and Monitoring Plan is submitted for EC. Copy the same is attached as Annexure-XIV for your reference

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana
by M/s. Asthetic Township Developers Pvt. Ltd.**

	conservation, water efficiency and conservation, solid waste management, renewable energy etc. are kept operational and meet the required standards. The environmental cell shall also keep the record of environment monitoring and those related to the environment infrastructure.	
Others		
xlvi.	Provisions shall be made for the housing of construction labour within the site with all necessary infrastructure and facilities such as fuel for cooking, mobile toilets, mobile STP, safe drinking water, medical health care, creche etc. The housing may be in the form of temporary structures to be removed after the completion of the project.	Noted & Agreed. Photographs of Basic infrastructure provided at project site are attached as Annexure XIX .
xli.	A First Aid Room shall be provided in the project both during construction and operations of the project.	Photographs showing first Aid room at the project is attached as Annexure XIX .
i.	The company shall draw up and implement corporate social Responsibility plan as per the Company's Act of 2013.	This condition will be complied as per the amended requirements.
ii.	As per the Ministry's Office Memorandum F. No. 22-6512017-1A. III dated 1 st May 2018, and proposed by the project proponent, an amount of Rs. 2.4 Crore @1.5% of project Cost shall be earmarked under Corporate Environment Responsibility (CER) for the activities such as drinking water supply, health and education. The activities proposed under CER shall be restricted to the affected area around the project. The entire activities proposed under the CER shall be treated as project and shall be monitored. The monitoring report shall be submitted to the regional office as a part of half yearly compliance report, and to the District Collector. It should be posted on the website of the project proponent	As per OM dated 30th September 2020, it was clarified that no separate allocation of fund for compliance of CER will be required. The proponent has already allocated separate budget for implementation of Environment Management Plan. Copy of OM is attached as Annexure-XXVI .

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana
by M/s. Asthetic Township Developers Pvt. Ltd.**

PART B – GENERAL CONDITIONS		
i.	A copy of the environmental clearance letter shall also be displayed on the website of the concerned State Pollution Control Board. The EC letter shall also be displayed at the Regional Office. District industries Centre and Collector's Office/ Tehsildars office for 30 days.	This condition will be complied.
ii.	The funds earmarked for environmental protection measures shall be kept in separate account and shall not be diverted for other purpose. Year-wise expenditure shall be reported to this Ministry and its concerned Regional Office.	This condition will be complied.
iii.	Officials from the concerned Regional Office of MoEF&CC who would be monitoring the implementation of environmental safeguards should be given full cooperation, facilities and documents/data by the project proponents during their inspection. A complete set of all the documents submitted to MoEF&CC shall be forwarded to the concerned APCCF, Regional Office of MoEF&CC.	This condition will be complied. A complete set of all the documents we have submitted for Environmental Clearance will be submitted to APCCF, Regional Office of MoEF&CC in due course of time.
iv.	In the case of any change(s) in the scope of the project, the project would require a fresh appraisal by this Ministry.	Noted the Condition.
v.	The Ministry reserves the right to add additional safeguard measures subsequently if found necessary and to take action including revoking of the environment clearance under the provisions of the Environmental (Protection) Act, 1986 to ensure effective implementation of the suggested safeguard measures in a time bound and satisfactory manner.	If any additional condition will be imposed on project we will comply with all the conditions.
vi.	All other statutory clearances such as the approvals for storage of diesel from Chief Controller of Explosives, Fire Department, Civil Aviation Department, the Forest Conservation Act, 1980 and the Wildlife (Protection) Act, 1972 etc.	We are in process for getting all statutory clearance from concerned department, which will be obtained and submitted in due course of time. Currently, we obtained AAI NOC which is attached as Annexure XX .

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana
by M/s. Asthetic Township Developers Pvt. Ltd.**

	shall be obtained, as applicable by project proponents from the respective competent authorities.	
vii.	These stipulations would be enforced among others under the provisions of the Water (Prevention and Control of Pollution) Act, 1974, the Air (Prevention and Control of Pollution) Act 1981, the Environment (Protection) Act, 1986, the Public Liability (Insurance) Act, 1991 and the EIA Notification, 2006.	Noted the condition.
viii.	The project proponent shall advertise in at least two local Newspapers widely circulated in the region, one of which shall be in the vernacular language informing that the project has been accorded Environmental Clearance and copies of clearance letters are available with the State Pollution Control Board and may also be seen on the website of the Ministry of Environment, Forest and Climate Change at http://www.envfor.nic.in . The advertisement shall be made within Seven days from the date of receipt of the Clearance letter and a copy of the same shall be forwarded to the concerned Regional Office of this Ministry.	Copies of the newspaper advertisement is attached in Annexure-XXV .
ix.	Any appeal against this clearance shall lie with the National Green Tribunal, if preferred, within a period of 30 days as prescribed under Section 16 of the National Green Tribunal Act, 2010.	Noted the condition.
x.	A copy of the clearance letter shall be sent by the proponent to concerned Panchayat, Zilla Parishad/Municipal Corporation, Urban Local Body and the Local NGO, if any, from whom suggestions/ representations, if any, were received while processing the proposal. The clearance letter shall also be put on the website of the company by the proponent.	This condition will be complied.
xi.	The proponent shall upload the	We will regularly upload the status of

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana
by M/s. Asthetic Township Developers Pvt. Ltd.**

	status of compliance of the stipulated EC conditions, including results of monitored data on their website and shall update the same periodically. It shall simultaneously be sent to the Regional Office of MoEF&CC, the respective Zonal Office of CPCB and the SPCB. The criteria pollutant levels namely; PM _{2.5} , PM ₁₀ , SO ₂ NO _x (ambient levels as well as stack emissions) or critical sectoral parameters indicated for the project shall be monitored and displayed at a convenient location near the main gate of the company in the public domain.	compliance of all the stipulated EC conditions. We will also submit Environmental Monitored data and shall update the same periodically. We will regularly submit compliance reports to the Regional Office of MoEF&CC, the respective Zonal Office of CPCB and the SPCB, which is due for submission on 1 st June and 1 st December of every year. We have monitored all the criteria pollutant levels namely; PM _{2.5} , PM ₁₀ , SO ₂ NO _x (ambient levels as well as stack emissions). All Monitoring report is attached as Annexure-X .
xii.	The environmental statement for each financial year ending 31 st March in Form-V as is mandated to be submitted by the project proponent to the concerned State Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall also be put on the website of the company along with the status of compliance of EC conditions and shall also be sent to the respective Regional Offices of MoEF&CC by email.	This condition will be complied during Operation phase of the project.

Annexure-I
Environmental Clearance Letter

F.No.21-137/2018-IA-III
Government of India
Ministry of Environment, Forest and Climate Change
(IA.III Section)

Indira Paryavaran Bhawan,
Jor Bagh Road, New Delhi - 3

Date: 7th February, 2019

To,

**Shri Vijay Kumar Yadav, Managing Director,
M/s Asthetic Township Developers Pvt. Ltd.,
Apt. no. E - 301, Uniworld City,
Sector 30, Gurgaon - 122002.**

Phone: 9811929655

E-mail: atwnship@gmail.com

Subject: Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana by M/s Asthetic Township Developers Pvt. Ltd. - Environmental Clearance - reg.

Sir,

This has reference to your online proposal No. IA/HR/MIS/84906/2018 dated 15th November, 2018 submitted to this Ministry for grant of Environmental Clearance (EC) in terms of the provisions of the Environment Impact Assessment (EIA) Notification, 2006 under the Environment (Protection) Act, 1986.

2. The proposal for grant of environmental clearance to the project 'Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana by M/s Asthetic Township Developers Pvt. Ltd.', was considered by the EAC in its 36th meeting held on 26-28 November, 2018. The details of the project, as per the documents submitted by the project proponent, and also as informed during the above meeting are as under:-

- (i) The project is located at Sushant Lok, Sector-27, District Gurugram, Haryana. Latitude: 28°27.996" N and Longitude: 77°4.495" E.
- (ii) This is an Expansion project. The total plot area is 11,537.57 sqm, FSI area is 42,088.21 sqm and total construction (built-up) area of 71,057.12 sqm. Maximum height of the building is 95.95 m.
- (iii) The project was earlier granted Environment Clearance by SEIAA, Haryana vide letter no. SEIAA/HR/2013/1507 dated 24th December, 2013 for plot area 11,537.57 sqm and Built-up area 41,841.21 sqm
- (iv) The total water requirement for the construction of Expansion of Commercial Complex Project is estimated to be approx. 355 KLD. The water supply during Construction phase will be met through HUDA. During the construction phase, soak pits and septic tanks are provided for disposal of waste water. Temporary toilets will be provided for labourers.

- (v) During operational phase, total water demand of the project is estimated to be 337 KLD and the same will be met by 42 KLD fresh water from HUDA and 295 KLD treated water. Wastewater generated (131 KLD) will be treated in STP of total 160 KLD capacity. About 118 KLD of treated wastewater will be generated from which 97 KLD will be used for flushing, 3 KLD for gardening and remaining 18 KLD for DG cooling. Additional 177 KLD treated water will be sourced from HUDA supply for use for DG cooling (12 KLD) and HVAC cooling (165 KLD).
- (vi) About 1226 kg/day solid waste will be generated from the project. The biodegradable waste (490.4 kg/day) will be processed in OWC, Inert wastes (122.6 kg/day) will be sent to land fill and the non-biodegradable waste generated (613 kg/day) will be handed over to vendors.
- (vii) The total power requirement during operation phase is 4004 KW and will be met from Dakshin Haryana Bijli Vitran Nigam (DHBVN).
- (viii) Parking facility for 677 No. of four wheelers are proposed to be provided against the requirement of 672 No. (according to local norms).
- (ix) Proposed energy saving measures: Energy will be saved using energy efficient lighting fixtures, Electronic Ballast, Timer based lighting and APFC Panel.
- (x) It is not located within 10 km of any Eco Sensitive areas.
- (xi) Estimated Cost of the project is Rs. 160.3 Crores.
- (xii) Employment potential: It will generate direct and indirect employment opportunities for both skilled and unskilled labor during construction & operation phase.
- (xiii) Benefits of the project: Direct & Indirect employment opportunities and Infrastructural Development of the Area.

3. The project/activity is covered under category 'B' of item 8(a) 'Building and Construction projects' of the Schedule to the EIA Notification, 2006 and its subsequent amendments, and requires appraisal at State level. However due to absence of SEIAA/SEAC in Haryana, the proposal is appraised at Central Level.

4. Based on the information submitted by the Project Proponent and detailed discussions held on all the issues, the EAC recommended the project for grant of environmental clearance and stipulated specific conditions along with other environmental conditions. As per recommendations of the EAC, the Ministry of Environment, Forest and Climate Change hereby accords Environmental Clearance to the project Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana by M/s Asthetic Township Developers Pvt. Ltd., under the provisions of the EIA Notification, 2006 and amendments/circulars issued thereon, and subject to the specific and general conditions as under:-

PART A - SPECIFIC CONDITIONS:

- (i) The project proponent shall obtain all necessary clearance/ permission from all relevant agencies including town planning authority before commencement of work. All the construction shall be done in accordance with the local building byelaws.
- (ii) Consent to Establish/Operate for the project shall be obtained from the State Pollution Control Board as required under the Air (Prevention and Control of Pollution) Act, 1981 and the Water (Prevention and Control of Pollution) Act, 1974.
- (iii) The approval of the Competent Authority shall be obtained for structural safety of buildings due to earthquakes, adequacy of firefighting equipment etc as per National Building Code including protection measures from lightening etc.

Topography and natural Drainage

- (iv) The natural drain system should be maintained for ensuring unrestricted flow of water. No construction shall be allowed to obstruct the natural drainage through the site, on wetland and water bodies. Check dams, bio-swales, landscape, and other sustainable urban drainage systems (SUDS) are allowed for maintaining the drainage pattern and to harvest rain water. Buildings shall be designed to follow the natural topography as much as possible. Minimum cutting and filling should be done.

Water requirement, Conservation, rain water Harvesting, and Ground Water Recharge

- (v) Fresh water requirement from HUDA supply shall not exceed 42 KLD with prior permission.
- (vi) A certificate shall be obtained from the local body supplying water, specifying the total annual water availability with the local authority, the quantity of water already committed the quantity of water allotted to the project under consideration and the balance water available. This should be specified separately for ground water and surface water sources, ensuring that there is no impact on other users.
- (vii) The quantity of fresh water usage, water recycling and rainwater harvesting shall be measured and recorded to monitor the water balance as projected by the project proponent. The record shall be submitted to the Regional Office, MoEF&CC along with six monthly Monitoring reports.
- (viii) At least 20% of the open spaces as required by the local building bye-laws shall be pervious. Use of Grass pavers, paver blocks with at least 50% opening, landscape etc. would be considered as pervious surface.
- (ix) Installation of dual pipe plumbing for supplying fresh water for drinking, cooking and bathing etc and other for supply of recycled water for flushing,

landscape irrigation, car washing, thermal cooling, conditioning etc. shall be done.

- (x) Use of water saving devices/ fixtures (viz. low flow flushing systems; use of low flow faucets tap aerators etc) for water conservation shall be incorporated in the building plan.
- (xi) Separation of grey and black water should be done by the use of dual plumbing system. In case of single stack system separate recirculation lines for flushing by giving dual plumbing system be done.
- (xii) Water demand during construction should be reduced by use of pre-mixed concrete, curing agents and other best practices referred.
- (xiii) The local bye-law provisions on rain water harvesting should be followed. If local bye-law provision is not available, adequate provision for storage and recharge should be followed as per the Ministry of Urban Development Model Building Byelaws, 2016. As proposed 03 nos. of rain water harvesting recharge pits shall be provided for rain water harvesting after filtration as per CGWB guidelines.
- (xiv) No ground water shall be used during construction/ operation phase of the project.
- (xv) Any ground water dewatering should be properly managed and shall conform to the approvals and the guidelines of the CGWA in the matter. Formal approval shall be taken from the CGWA for any ground water abstraction or dewatering.

Solid Waste Management

- (xvi) The provisions of the Solid Waste (Management) Rules, 2016, e-Waste (Management) Rules, 2016, and the Plastics Waste (Management) Rules, 2016 shall be followed.
- (xvii) Disposal of muck during construction phase shall not create any adverse effect on the neighboring communities and be disposed taking the necessary precautions for general safety and health aspects of people, only in approved sites with the approval of competent authority.
- (xviii) Separate wet and dry bins must be provided in each unit and at the ground level for facilitating segregation of waste. Solid waste shall be segregated into wet garbage and inert materials. Wet garbage shall be composted in Organic Waste Converter. As proposed, 80 sqm area shall be provided for solid waste management within the premises which will include area for segregation, composting. The inert waste from project will be sent to dumping site.
- (xix) Any hazardous waste generated during construction phase, shall be disposed off as per applicable rules and norms with necessary approvals of the State Pollution Control Board.

- (xx) A certificate from the competent authority handling municipal solid wastes, indicating the existing civic capacities of handling and their adequacy to cater to the M.S.W. generated from project shall be obtained.

Sewage Treatment Plant

- (xxi) Sewage shall be treated in the STP based on SBR technology with tertiary treatment i.e. Ultra Filtration. The treated effluent from STP shall be recycled/re-used for flushing and horticulture. Excess water shall be discharged to Municipal Sewer with prior permission.
- (xxii) A certificate from the competent authority for discharging treated effluent/ untreated effluents into the Public sewer/ disposal/drainage systems along with the final disposal point shall be obtained.
- (xxiii) No sewage or untreated effluent water would be discharged through storm water drains.
- (xxiv) The project proponents would devise a monitoring plan to the satisfaction of the State Pollution Control Board so as to continuously monitor the treated waste water being used for flushing in terms of faecal coliforms and other pathogenic bacteria.
- (xxv) The project proponents would commission a third party study on the implementation of conditions related to quality and quantity of recycle and reuse of treated water, efficiency of treatment systems, quality of treated water being supplied for flushing (specially the bacterial counts), comparative bacteriological studies from toilet seats using recycled treated waters and fresh waters for flushing, and quality of water being supplied through spray faucets attached to toilet seats.
- (xxvi) The installation of the Sewage Treatment Plant (STP) shall be certified by an independent expert and a report in this regard shall be submitted to the Ministry before the project is commissioned for operation. Periodical monitoring of water quality of treated sewage shall be conducted. Necessary measures should be made to mitigate the odour problem from STP.
- (xxvii) Sludge from the onsite sewage treatment, including septic tanks, shall be collected, conveyed and disposed as per the Ministry of Urban Development, Central Public Health and Environmental Engineering Organization (CPHEEO) Manual on Sewerage and Sewage Treatment Systems, 2013.

Energy

- (xxviii) Compliance with the Energy Conservation Building Code (ECBC) of Bureau of Energy Efficiency shall be ensured. Buildings in the States which have notified their own ECBC, shall comply with the State ECBC. Outdoor and common area lighting shall be LED. Concept of passive solar design that minimize energy consumption in buildings by using design elements, such as building orientation, landscaping, efficient building envelope, appropriate fenestration,

increased day lighting design and thermal mass etc. shall be incorporated in the building design. Wall, window, and roof u-values shall be as per ECBC specifications.

- (xxix) Energy conservation measures like installation of CFLs/ LED for the lighting the area outside the building should be integral part of the project design and should be in place before project commissioning. Used CFLs, TFL and LED shall be properly collected and disposed off/sent for recycling as per the prevailing guidelines/rules of the regulatory authority to avoid mercury contamination.
- (xxx) Solar, wind or other Renewable Energy shall be installed to meet electricity generation equivalent to 1% of the demand load or as per the state level/ local building bye-laws requirement, whichever is higher. Follow super ECBC requirement of ECBC 2017 and provide compliance report.
- (xxxi) Solar power shall be used for lighting in the apartment to reduce the power load on grid. Separate electric meter shall be installed for solar power. Solar water heating shall be provided to meet 20% of the hot water demand of the commercial and institutional building or as per the requirement of the local building bye-laws, whichever is higher. Residential buildings are also recommended to meet its hot water demand from solar water heaters, as far as possible.
- (xxxii) Use of environment friendly materials in bricks, blocks and other construction materials, shall be required for at least 20% of the construction material quantity. These include Fly Ash bricks, hollow bricks, AACs, Fly Ash Lime Gypsum blocks, Compressed earth blocks, and other environment friendly materials. Fly ash should be used as building material in the construction as per the provision of Fly Ash Notification of September, 1999 and amended as on 27th August, 2003 and 25th January, 2016. Ready mixed concrete must be used in building construction.
- (xxxiii) A certificate of adequacy of available power from the agency supplying power to the project along with the load allowed for the project shall be submitted.

Air Quality and Noise

- (xxxiv) Construction site shall be adequately barricaded before the construction begins. Dust, smoke & other air pollution prevention measures shall be provided for the building as well as the site. These measures shall include screens for the building under construction, continuous dust/ wind breaking walls all around the site (at least 3 meter height). Plastic/tarpaulin sheet covers shall be provided for vehicles bringing in sand, cement, murrum and other construction materials prone to causing dust pollution at the site as well as taking out debris from the site. Sand, murrum, loose soil, cement, stored on site shall be covered adequately so as to prevent dust pollution. Wet jet shall be provided for grinding and stone cutting. Unpaved surfaces and loose soil shall be adequately sprinkled with water to suppress dust.

- (xxxv) Notification GSR 94(E) dated 25.01.2018 of MoEF&CC regarding Mandatory Implementation of Dust Mitigation Measures for Construction and Demolition Activities for projects requiring Environmental Clearance shall be complied with.
- (xxxvi) All construction and demolition debris shall be stored at the site (and not dumped on the roads or open spaces outside) before they are properly disposed. All demolition and construction waste shall be managed as per the provisions of the Construction and Demolition Waste Rules, 2016. All workers working at the construction site and involved in loading, unloading, carriage of construction material and construction debris or working in any area with dust pollution shall be provided with dust mask.
- (xxxvii) The diesel generator sets to be used during construction phase shall be low sulphur diesel type and shall conform to Environmental (Protection) prescribed for air and noise emission standards.
- (xxxviii) The gaseous emissions from DG set shall be dispersed through adequate stack height as per CPCB standards. Acoustic enclosure shall be provided to the DG sets to mitigate the noise pollution. Low sulphur diesel shall be used. The location of the DG set and exhaust pipe height shall be as per the provisions of the Central Pollution Control Board (CPCB) norms.
- (xxxix) For indoor air quality the ventilation provisions as per National Building Code of India.
- (xl) Ambient noise levels shall conform to residential standard both during day and night as per Noise Pollution (Control and Regulation) Rules, 2000. Incremental pollution loads on the ambient air and noise quality shall be closely monitored during construction phase. Adequate measures shall be made to reduce ambient air and noise level during construction phase, so as to conform to the stipulated standards by CPCB / SPCB.

Green Cover

- (xli) No tree cutting/transplantation of existing trees has been proposed in the project. A minimum of 1 tree for every 80 sqm of land should be planted and maintained. The existing trees will be counted for this purpose. The landscape planning should include plantation of native species. The species with heavy foliage, broad leaves and wide canopy cover are desirable. Water intensive and/or invasive species should not be used for landscaping. As proposed 2423.82 sqm area shall be provided for green area development.

Top Soil preservation and Reuse

- (xlii) Topsoil should be stripped to a depth of 20 cm from the areas proposed for buildings, roads, paved areas, and external services. It should be stockpiled appropriately in designated areas and reapplied during plantation of the proposed vegetation on site.

Transport

- (xliii) As proposed, adequate provision will be made for car/vehicle parking at the proposed project site. There shall also be adequate parking provisions for visitors so as not to disturb the traffic and allow smooth movement at the site.
- (xliv) A comprehensive mobility plan, as per MoUD best practices guidelines (URDPFI), shall be prepared to include motorized, non-motorized, public, and private networks. Road should be designed with due consideration for environment, and safety of users. The road system can be designed with these basic criteria.
 - Hierarchy of roads with proper segregation of vehicular and pedestrian traffic.
 - Traffic calming measures
 - Proper design of entry and exit points.
 - Parking norms as per local regulation
- (xlv) A detailed traffic management and traffic decongestion plan shall be drawn up to ensure that the current level of service of the roads within a 05 kms radius of the project is maintained and improved upon after the implementation of the project. This plan should be based on cumulative impact of all development and increased habitation being carried out or proposed to be carried out by the project or other agencies in this 05 Kms radius of the site in different scenarios of space and time and the traffic management plan shall be duly validated and certified by the State Urban Development department and the P.W.D./ competent authority for road augmentation and shall also have their consent to the implementation of components of the plan which involve the participation of these departments.
- (xlvi) Vehicles hired for bringing construction material to the site should be in good condition and should have a pollution check certificate and should conform to applicable air and noise emission standards be operated only during non-peak hours.

Environment management Plan

- (xlvii) An environmental management plan (EMP) as prepared and submitted shall be implemented to ensure compliance with the environmental conditions specified above. A dedicated Environment Monitoring Cell with defined functions and responsibility shall be put in place to implement the EMP. The environmental cell shall ensure that the environment infrastructure like Sewage Treatment Plant, Landscaping, Rain Water Harvesting, Energy efficiency and conservation, water efficiency and conservation, solid waste management, renewable energy etc. are kept operational and meet the required standards. The environmental cell shall also keep the record of environment monitoring and those related to the environment infrastructure.

Others

- (xlviii) Provisions shall be made for the housing of construction labour within the site with all necessary infrastructure and facilities such as fuel for cooking, mobile toilets, mobile STP, safe drinking water, medical health care, creche etc. The housing may be in the form of temporary structures to be removed after the completion of the project.
- (xlix) A First Aid Room shall be provided in the project both during construction and operations of the project.
- (l) The company shall draw up and implement corporate social Responsibility plan as per the Company's Act of 2013.
- (li) As per the Ministry's Office Memorandum F.No. 22-65/2017-IA.III dated 1st May 2018, and proposed by the project proponent, an amount of Rs. 2.4 Crore @1.5% of project Cost shall be earmarked under Corporate Environment Responsibility (CER) for the activities such as Education facilities in nearby communities, solar power, rain water harvesting and plantation in community areas. The activities proposed under CER shall be restricted to the affected area around the project. The entire activities proposed under the CER shall be treated as project and shall be monitored. The monitoring report shall be submitted to the regional office as a part of half yearly compliance report, and to the District Collector. It should be posted on the website of the project proponent.

PART B - GENERAL CONDITIONS

- (i) A copy of the environmental clearance letter shall also be displayed on the website of the concerned State Pollution Control Board. The EC letter shall also be displayed at the Regional Office, District Industries centre and Collector's Office/ Tehsildar's office for 30 days.
- (ii) The funds earmarked for environmental protection measures shall be kept in separate account and shall not be diverted for other purpose. Year-wise expenditure shall be reported to this Ministry and its concerned Regional Office.
- (iii) Officials from the concerned Regional Office of MoEF&CC who would be monitoring the implementation of environmental safeguards should be given full cooperation, facilities and documents/data by the project proponents during their inspection. A complete set of all the documents submitted to MoEF&CC shall be forwarded to the concerned APCCF, Regional Office of MoEF&CC.
- (iv) In the case of any change(s) in the scope of the project, the project would require a fresh appraisal by this Ministry.
- (v) The Ministry reserves the right to add additional safeguard measures subsequently, if found necessary, and to take action including revoking of the

environment clearance under the provisions of the Environmental (Protection) Act, 1986, to ensure effective implementation of the suggested safeguard measures in a time bound and satisfactory manner.

- (vi) All other statutory clearances such as the approvals for storage of diesel from Chief Controller of Explosives, Fire Department, Civil Aviation Department, the Forest Conservation Act, 1980 and the Wildlife (Protection) Act, 1972 etc. shall be obtained, as applicable by project proponents from the respective competent authorities.
- (vii) These stipulations would be enforced among others under the provisions of the Water (Prevention and Control of Pollution) Act, 1974, the Air (Prevention and Control of Pollution) Act 1981, the Environment (Protection) Act, 1986, the Public Liability (Insurance) Act, 1991 and the EIA Notification, 2006.
- (viii) The project proponent shall advertise in at least two local Newspapers widely circulated in the region, one of which shall be in the vernacular language informing that the project has been accorded Environmental Clearance and copies of clearance letters are available with the State Pollution Control Board and may also be seen on the website of the Ministry of Environment, Forest and Climate Change at <http://www.envfor.nic.in>. The advertisement shall be made within Seven days from the date of receipt of the Clearance letter and a copy of the same shall be forwarded to the concerned Regional Office of this Ministry.
- (ix) Any appeal against this clearance shall lie with the National Green Tribunal, if preferred, within a period of 30 days as prescribed under Section 16 of the National Green Tribunal Act, 2010.
- (x) A copy of the clearance letter shall be sent by the proponent to concerned Panchayat, Zilla Parishad/Municipal Corporation, Urban Local Body and the Local NGO, if any, from whom suggestions/ representations, if any, were received while processing the proposal. The clearance letter shall also be put on the website of the company by the proponent.
- (xi) The proponent shall upload the status of compliance of the stipulated EC conditions, including results of monitored data on their website and shall update the same periodically. It shall simultaneously be sent to the Regional Office of MoEF&CC, the respective Zonal Office of CPCB and the SPCB. The criteria pollutant levels namely; PM_{2.5}, PM₁₀, SO₂, NO_x (ambient levels as well as stack emissions) or critical sectoral parameters, indicated for the project shall be monitored and displayed at a convenient location near the main gate of the company in the public domain.
- (xii) The environmental statement for each financial year ending 31st March in Form-V as is mandated to be submitted by the project proponent to the concerned State Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall also be put on the website of the company along with the status of compliance of EC conditions

and shall also be sent to the respective Regional Offices of MoEF&CC by e-mail.

5. This issues with the approval of the Competent Authority.


(Kushal Vashist)
Director

Copy to:

- 1) The Secretary, Directorate of Environment, Government of Haryana, SCO 1-2-3, Sector 17 D (Second Floor), Chandigarh.
- 2) Addl. Principal Chief Conservator of Forests (Central), Ministry of Environment, Forests and Climate Change, Regional Office (NZ), Bay No.24-25, Sector 31-A, Dakshin Marg, Chandigarh -160030.
- 3) The Chairman, Central Pollution Control Board Parivesh Bhavan, CBD-cum-Office Complex, East Arjun Nagar, New Delhi - 110 032.
- 4) Member Secretary, Haryana Pollution Control Board, C-11, Sector-6, Panchkula, Haryana 134109
- 5) Monitoring Cell, MoEF&CC, Indira Paryavaran Bhavan, New Delhi.
- 6) Guard File/ Record File/ Notice Board.


(Kushal Vashist)
Director

Annexure-II

HSPCB/Consent/:

329962320GUNOCTE7324277 dated

03/02/2020



HARYANA STATE POLLUTION CONTROL BOARD

Gurgaon North Vikas Sadan, 1st Floor, Near DC Court, Gurgaon Ph.0124-2332775 Email:-
hspcbrogrn@gmail.com

Website: www.hrocmms.nic.in E-Mail - hspcbho@gmail.com

Telephone No.: 0172-2577870-73



No. HSPCB/Consent/ : 329962320GUNOCTE7324277

Dated:03/02/2020

To.

M/s : Asthetic Township Developers Pvt Ltd
Commercial Complex at Sector 27 Gurugram
GURGAON
122009

Sub. : Grant of consent to Establish to M/s Asthetic Township Developers Pvt Ltd

Please refer to your application no. 7324277 received on dated 2020-01-27 in regional office Gurgaon North.

With reference to your above application for consent to establish, M/s Asthetic Township Developers Pvt Ltd is hereby granted consent as per following specification/Terms and conditions.

Consent Under	AIR/WATER
Period of consent	03/02/2020 - 06/02/2026
Industry Type	Building and construction project having waste water generation more than 100 KLD
Category	RED
Investment(In Lakh)	30544.0
Total Land Area (Sq. meter)	11537.57
Total Builtup Area (Sq. meter)	71057.12
Quantity of effluent	
1. Trade	0.0 KL/Day
2. Domestic	131.0 KL/Day
Number of outlets	1.0
Mode of discharge	
1. Domestic	Reuse/Recycle
2. Trade	0
Permissible Domestic Effluent Parameters	
1. BOD	30 mg/l
2. COD	250 mg/l
3. TSS	100 mg/l

Permissible Trade Effluent Parameters	
1. NA	mg/l
Number of stacks	4
Height of stack	
1. DG Set (1500 KVA)	8 METER
2. DG Set (1500 KVA)	8 METER
3. DG Set (1500 KVA)	8 METER
4. DG Set (1000 KVA)	6 METER
Permissible Emission parameters	
1. NA	
Capacity of boiler	
1. NA	Ton/hr
Type of Furnace	
1. NA	
Type of Fuel	
1. Diesel	1.1 KL/day

HARYANA STATE

Terms and conditions

Regional Officer, Gurgaon North

Haryana State Pollution Control Board.

1. The industry has declared that the quantity of effluent shall be 131 KL/Day i.e 0KL/Day for Trade Effluent, 0 KL/Day for Cooling, 131 KL/Day for Domestic and the same should not exceed .
2. The above 'Consent to Establish' is valid for 60 months from the date of its issue to be extended for another one year at the discretion of the Board or till the time the unit starts its trial production whichever is earlier. The unit will have to set up the plant and obtain consent during this period.
3. The officer/official of the Board shall have the right to access and inspection of the industry in connection with the various processes and the treatment facilities being provided simultaneously with the construction of building/machinery. The effluent should conform the effluent standards as applicable
4. That necessary arrangement shall be made by the industry for the control of Air Pollution before commissioning the plant. The emitted pollutants will meet the emission and other standards as laid/will be prescribed by the Board from time to time.
5. The applicant will obtain consent under section 25/26 of the Water (Prevention & Control of Pollution) Act, 1974 and under section 21/22 of the Air (Prevention & Control of Pollution) Act, 1981 as amended to-date-even before starting trial production
6. The above Consent to Establish is further subject to the conditions that the unit complies with all the laws/rules/decisions and competent directions of the Board/Government and its functionaries in all respects before commissioning of the operation and during its actual working strictly.
7. No in-process or post-process objectionable emission or the effluent will be allowed, if the scheme furnished by the unit turns out to be defective in any actual experience
8. The Electricity Department will give only temporary connection and permanent connection to the unit will be given after verifying the consent granted by the Board, both under Water Act and Air Act.

9. Unit will raise the stack height of DG Set/Boiler as per Board's norms.
10. Unit will maintain proper logbook of Water meter/sub meter before/after commissioning.
11. That in the case of an industry or any other process the activity is located in an area approved and that in case the activity is sited in an residential or institutional or commercial or agricultural area, the necessary permission for siting such industry and process in an residential or institutional or commercial or agricultural area or controlled area under Town and Country Planning laws CLU or Municipal laws has to be obtained from the competent Authority in law permitting this deviation and be submitted in original with the request for consent to operate.
12. That there is no discharge directly or indirectly from the unit or the process into any interstate river or Yamuna River or River Ghaggar.
13. That the industry or the unit concerned is not sited within any prohibited distances according to the Environmental Laws and Rules, Notification, Orders and Policies of Central Pollution control Board and Haryana State Pollution Control Board.
14. That of the unit is discharging its sewage or trade effluent into the public sewer meant to receive trade effluent from industries etc. then the permission of the Competent Authority owing and operating such public sewer giving permission letter to his unit shall be submitted at time of consent to operate.
15. That if at any time, there is adverse report from any adjoining neighbor or any other aggrieved party or Municipal Committee or Zila Parishad or any other public body against the unit's pollution; the Consent to Establish so granted shall be revoked.
16. That all the financial dues required under the rules and policies of the Board have been deposited in full by the unit for this Consent to Establish.
17. In case of change of name from previous Consent to Establish granted, fresh Consent to Establish fee shall be levied.
18. Industry should adopt water conservation measures to ensure minimum consumption of water in their Process. Ground water based proposals of new industries should get clearance from Central Ground Water Authority for scientific development of previous resource.
19. That the unit will take all other clearances from concerned agencies, whenever required.
20. That the unit will not change its process without the prior permission of the Board.
21. That the Consent to Establish so granted will be invalid, if the unit falls in Aravali Area or non conforming area.
22. That the unit will comply with the Hazardous Waste Management Rules and will also make the non-leachate pit for storage of Hazardous waste and will undertake not to dispose off the same except for pit in their own premises or with the authorized disposal authority.
23. That the unit will submit an undertaking that it will comply with all the specific and general conditions as imposed in the above Consent to Establish within 30 days failing which Consent to Establish will be revoked.
24. That unit will obtain EIA from MoEF, if required at any stage.
25. In case of unit does not comply with the above conditions within the stipulated period, Consent to Establish will be revoked.
26. That unit will obtain consent to operate from the board before the start of product activity.

Specific Conditions

Other Conditions :

1. The project proponent will obtain all necessary clearances from all concerned departments. 2. Project proponent will not change the quantity of domestic effluent/trade effluent/air emission without prior permission of the Board. Project Proponent will obtain prior CTO before starting of production and apply for CTO/ CTE Extension at least 90 days before expiry date of this CTE. 3. Project Proponent will install STP/ETP/ACPM along with the main project. 4. Project Proponent will install adequate acoustic enclosures/chambers on their DG SETS with proper stack height as per prescribed norms to meet the prescribed standards under EP Rules. 5. Project Proponent will comply with the provisions of Water Act, 1974, Air Act, 1981, Solid Waste Management Rules, 2016, Hazardous & Other Waste Management Rules, 2016, Plastic Waste Management Rules, 2016, E-Waste Management Rules, 2016, Battery Managements Rules, C&D Waste Management Rules, 2016& amendments and other applicable environmental legislation. 6. Project Proponent will use only treated effluent supplied from Sewage treatment plant during construction phase of the project 7. That this CTE will not provide any relaxation /benefit from any other Act/Rules/Regulations applicable to the project/land in question. 8. Project Proponent will not discharge any type Treated or untreated effluent outside the premises of the project. 9. Project Proponent will not use in their DG set as a fuel i.e. pet coke, furnace oil and LSHS etc. 10. Stack emission level should be stringent than the existing standards in terms of the identified critical pollutants. 11. Effective fugitive emission control measures should be imposed in the process, transportation, parking etc. 12. Encourage use of cleaner fuels (pet coke / furnace oil /LSHS may be avoided). 13. Best available technology may be used. For example usage of EAF/SAF/IF in place of Cupola Furnace, Usage of Supercritical technology in place of sub – critical technology. 14. Increase of green belt cover by 40% of the total land area beyond the permissible requirement of 33%, wherever feasible. 15. Stipulation of greenbelt outside the project premises such as avenue plantation, plantation in vacant areas, social forestry etc. 16. Assessment of carrying capacity of transportation load on the roads inside the industrial premises. If the roads required to be widened, shall be prescribed as a condition. 17. Project Proponent will not discharge any type of effluent inside & outside of the premises of the project and reuse/recycle of treated waste water be ensured. 18. Continuous monitoring of emission and effluent quality / quantity to be installed & will connect the same with server of CPCB and HSPCB. 19. A detailed water harvesting plan may be submitted by the project proponent. 20. Project Proponent will achieve zero discharge and install latest technology of STP/ETP and reuse/recycle of treated effluent. 21. In case, domestic waste water generation is more than 10 KLD, the industry may install STP. 22. Dumping of waste (fly ash, slag, red mud etc.) may be permitted only at designated locations approved by SPCBs/PCCs. 23. More stringent norms for management of hazardous waste. The waste generated should be preferably utilized in co-processing. 24. Monitoring of compliance of EC conditions may be submitted with third party audit every year. 25. Project Proponent will dispose off their waste/spent oil of DG sets only to authorize recyclers by the HSPCB. 26. The % of the CER may be least 1.5 times the slabs given in the OM dated 01.05.2018 for SPA and 2 times for CPA in case of Environmental Clearance. 27. Project proponent will comply all the directions of CPCB in this regard and will comply all the orders issued by any court in this regard. 28. Project Proponent will submit an affidavit regarding compliances of above said conditions within 30 days. 29. The above Consent to Establish is further subject to the conditions that the unit complies with all the laws/rules/decisions and competent directions of the Board/Government and its functionaries in all respects before commissioning of the operation and during its actual working strictly. 30. Unit will deploy anti –smog gun at site to comply with the above said directions & keep proper record of operation of the same and submit action taken report to this office within 03 days positively, failing which action shall be initiated as per applicable Acts/ Rules /Notifications. 31. CTE so granted is on the basis of detail submitted by the unit in online application, CTE granted will be without prejudice to any violation made by unit in past & will be deemed revoked & further action will be taken as per law if any violation is observed at any stage. 32. At any stage, if any violation observed of any above conditions at any time, this CTE stands cancelled /revoked & further action will be taken as per law if any violation is observed at any stage.

Regional Officer, Gurgaon North
Haryana State Pollution Control Board.

Annexure-III
Aravali NOC

प्रेषक

उपायुक्त, गुडगांव।

सेवा में

M/s Asthetic Township Developers Pvt. Ltd.

क्रमांक 3373 /एस0के02 दिनांक 17-10-13

विषय: Request for issuing Aravali Notification 1992 & PLPA 1900 from DFO and Tehsildar through Deputy Commissioner of M/s Asthetic Township Developers Pvt. Ltd. project at village Sukhrali, Sector-27, Gurgaon.

यादि

उपरोक्त विषय पर आपके प्रार्थना पत्र के सन्दर्भ में।

विषयाधीन मामले में इस कार्यालय द्वारा तहसीलदार गुडगांव व उप-वन संरक्षक गुडगांव से रिपोर्ट प्राप्त की गई जो निम्न प्रकार है :-

तहसीलदार गुडगांव :- तहसीलदार गुडगांव के कार्यालय के पत्र क्रमांक 2327/ओ0के0 दिनांक 07.10.2013 द्वारा इस कार्यालय में प्राप्त रिपोर्ट अनुसार नीजा सुखराली की अराजी किला नं० 59//6, 15, 8/1/1, 13/2, कित्ता 4 रकबा 14-16-3 सालम के मालिक मै० अस्थैटिक टाउनशिप डवलपर्स प्रा०लि० बरूवे इन्तकाल नं० 1438-1534 से मालिक है व किला नं० 59//7 रकबा 8-0 सालम के सुधीर पुत्र साहिबराम पुत्र शिवधन्व बरूवे इन्तकाल नं० 1437 से मालिक है। बिन्दुवार रिपोर्ट निम्नप्रकार है :-


1. उपरोक्त अराजी अरावली क्षेत्र से बाहर है।
2. 07.05.1992 के नोटिफिकेशन से पूर्व अराजी मूमि की किस्म कमी भी गैर मुमकिन पहाड़, गैर मु० राडा, गैर मु० बीहड़, बंजड़ बीहड़ व रून्ड नहीं रही है।
3. गिरदावरी 1992 से पूर्व किस्म चाही है जो ताहाल है।

उप-वन संरक्षक, गुडगांव के कार्यालय के पत्र क्रमांक 2259-20जी दिनांक 03.10.2013 द्वारा इस कार्यालय में प्राप्त रिपोर्ट अनुसार M/s Asthetic Township Developers Pvt. Ltd. vide letter No. Nil dated 14-08-2013 made a request in connection with land measuring 2.851 acres having Killa No 6, 7, 8/1/1, 13/2, 15/1 land located at village Sukhrali, District Gurgaon, Applicant made a proposal to use this land for Commercial Colony Purpose In Continuation of report submitted by RFO, Gurgaon vide letter no. 703-G dated 24-08-2013 it is made clear that:

- A As per record available above said land is not part of notified Reserved Forest, Protected Forest under Indian Forest Act, 1927 or any area closed under section 4 & 5 of Punjab Land Preservation Act 1900.
- B It is clarified that by the notification no. S.O.8/P.A2/1900/S.4/2013 dated 4th January 2013 all Revenue Estate of Gurgaon Tehsil is notified u/s 4 of PLPA 1900 and S.O. 81/PA.2/1900/S.3/12 dated 19th December 2012 u/s 3 of PLPA 1900. The area is however not recorded as forest in the Government record but felling of any tree is strictly prohibited without the permission of Divisional Forest Officer, Gurgaon.
- C If approach is required from Protected Forest by the user agency, the clearance/regularization under Forest Conservation Act, 1980 will be required without prior clearance from Forest Department, the user of Forest land for approach road is strictly prohibited M/s Asthetic Township Developers Pvt. Ltd. whose land is located at village Sukhrali, District Gurgaon must obtain clearance as applicable under Forest Conservation Act 1980.

- D As per records available with the forest Department Gurgaon, the area does not fall in areas where plantations were raised by the Forest Department under Aravalli project.
- E All other statutory clearance mandated under the Environment Protection Act, 1986 or any other Act/order shall be obtained as application by the project proponents from the concerned authorities.
- F The project proponents will not violate any judicial order/ Pronouncement issued by the Hon'ble Supreme Court/High Courts.
- G It is clarified that the Hon'ble supreme Court has issued various judgment dated 06.05.2002, 29.10.2002, 16.12.2002, 18.03.2004, etc. pertaining to Aravalli region in Haryana, which should be complied with.
- H It shall be the responsibility of user agency/applicant to get necessary clearances/permissions under various Acts and Rules applicable if any, from the respective authorities/Department..

रिपोर्ट सेवा में प्रेषित है।


कृते: उपायुक्त गुडगांव।

कमांक

/एस0के02 दिनांक

इसकी एक प्रति Director General, Town & Country Planning, Haryana, Chandigarh को सूचनार्थ एवं आवश्यक कार्यवाही हेतु प्रेषित है।


कृते: उपायुक्त गुडगांव।

Annexure-V

From: Dy. Conservator of Forests,
Gurgaon, Haryana.

To, **M/s Asthetic Township Developers Pvt. Ltd.**
262, DDA Office Complex,
Jhandewalan Extn., New Delhi-110055

No. 2259-20-9


Dated: 3/10/13

Sub.: Clarification regarding Applicability of forest laws on Non Forest land Applied by **M/s Asthetic Township Developers Pvt. Ltd.** land located at Village-Sukhrali, Sector-27, Sushant Lok District-Gurgaon.

Applicant **M/s Asthetic Township Developers Pvt. Ltd., 262, DDA Office Complex, Jhandewalan Extn., New Delhi-110055** vide letter no. Nil. dated 14.08.2013 made a request in connection with land measuring 2.851 Acres having Killa No. 6, 7, 8/1/1, 13/2, 16/1, land located at village Sukhrali, Sector-27, Sushant Lok District Gurgaon. Applicant made a proposal to use this land for **Commercial Colony Purpose**. In continuation of report submitted by RFO, Gurgaon vide Letter No. 703-G dated 24.08.2013 it is made clear that:

- a) As per records available above said land is not part of notified Reserved Forest, Protected Forest under Indian Forest Act, 1927 or any area closed under section 4 & 5 of Punjab Land Preservation Act, 1900.
- b) It is clarified that by the Notification No. S.O.8/P.A 2/1900/S.4/2013 dated 4th January, 2013, whole Revenue Estate of Gurgaon is notified u/s 4 of PLPA 1900 and S.O.81/PA.2/1900/S.3/2012 dated 19th December, 2012 u/s 3 of PLPA 1900. The area is however not recorded as forest in the Government record but felling of any tree is strictly prohibited without the permission of Divisional Forest Officer, Gurgaon.
- c) If approach is required from Protected Forest by the user agency, the clearance/regularization under Forest Conservation Act 1980 will be required. Without prior clearance from Forest Department, the use of Forest land for approach road is strictly prohibited. **M/s Asthetic Township Developers Pvt. Ltd.** whose land is located at village, Sukhrali, Sector-27, Sushant Lok District Gurgaon must obtain clearance as applicable under Forest Conservation Act 1980.
- d) As per the records available with the Forest Department, Gurgaon, the area does not fall in areas where plantations were raised by the Forest Department under Aravalli project.
- e) All the statutory clearances mandated under the Environment Protection Act, 1986, as per the notification of Ministry of Environment and Forests, Government of India, dated 07-05-1992 or any other Act/order shall be obtained as applicable by the project proponents from the concerned authorities.
- f) The projec proponent will not violate any Judicial Order/ direction issued by the Hon'ble Supreme Court/ High Courts.
- g) It is clarified that Hon'ble Supreme Court has issued various judgments dated 07.05.2002, 29.10.2002, 16.12.2002, 18.03.2004, 14.5.2004 etc. pertaining to Aravalli region in Haryana, which should be complied with, Since the proposed site falls within 5 Km. of Delhi boundary. The permission from the Mining Department, Haryana pollution Board, Deptt. of Town & Country Planning Haryana and other appropriate authorities must be obtained who is under obligation to follow the directions in the various Hon'ble Supreme Court Judgments while granting permission.
- h) It shall be the responsibility of user agency/applicant to get necessary clearances/permissions under various Acts and Rules applicable if any, from the respective authorities/Department.

Date:
Place: Gurgaon


Dy. Conservator of Forest,
Gurgaon.

Endst. No.

Dated:

A copy is forwarded to:-

- 1) Conservator of Forests, South Circle, Gurgaon for kind information.
- 2) D.G. T.C.P, Ayojana Bhawan, Sec-18, Madhya, Marg, Chandigarh for kind information
- 3) Dy.Commissioner, Gurgaon w.r.t. his letter no.3538 dated 17.07.2013 for kind information & necessary action.
- 4) Guard File.


Dy. Conservator of Forest,
Gurgaon.

प्रेषक

सेवा में,

उपायुक्त, गुडगांव।

तहसीलदार, गुडगांव

3413
25-7-13

OK

तहसीलदार

गुडगांव

24/7/13

क्रमांक 2532/एम.वी

दिनांक 12-7-13

विषय:-

Request for issuing Aravali notification 1992 & PLPA from DFO and Tehsildar through Deputy Commissioner of M/s Asthetic Township Developers Pvt. Ltd. project at Village Sukhrui Sec-27, Sushantlok, Gurgaon

उपरोक्त विषय पर अनुरोध है कि संलग्न प्रार्थना पत्र में प्रस्तावित भूमि का Report (not covered under Aravali Notification area) जारी की जानी है। अतः आपको मूल कार्यालय की प्रति संलग्न करके लिखा जाता है कि आप विस्तारपूर्वक रिपोर्ट/टिप्पणी सहित तैयार करके एक सप्ताह के अन्दर-अन्दर इस कार्यालय में निम्न बिन्दुओं पर गिजवाना सुनिश्चित करें ताकि आगामी कार्यवाही की जा सके।

1. प्रार्थना पत्र में वर्णित खसरा न0 अरावली क्षेत्र में है अथवा नहीं।
2. 1992 के नोटिफिकेशन से पूर्व व उसके पश्चात की गिरदावरी तथा किस्म जमीन भी स्पष्ट रिपोर्ट करने का कष्ट करें।
3. वर्णित प्रार्थना पत्र में दर्शाया गए खसरा न0 शामिल/ग्राम पंचायत/नगरपालिका/नगर निगम की भूमि/मलकियत तो नहीं है।
4. आराजी भूमि की ता हाल मलकियत बारे।
5. आराजी भूमि बारे किसी इंतकाल की नजरसानी रिपोर्ट तो नहीं की गई है या इंतकाल मुतनाजा तो नहीं।
6. आराजी भूमि का किसी माननीय न्यायालय में केस तो नहीं चल रहा है।
7. आराजी भूमि पर किसी प्रकार का कोई भार तो है अथवा नहीं।

क्र. 1732 / जी. को. दिनांक 25-7-13.
एक प्रति/मूलसम में गिरदावर हस्ता. गुडगांव को
आवश्यक कार्यवाही एवं रिपोर्ट/टिप्पणी हेतु प्रेषित है।

तहसीलदार
गुडगांव

कृते: उपायुक्त, गुडगांव।


क्रमांक 371 R.R. dt 30/13

पहचानी उम्मा खुशनाली निमगावसाह

विवाह कर

सीमाजी

विवाह विन्यासकी काम करण हैं।



TV-113

श्रीकांत जी, रिपोर्ट की जाती है मैजिस्ट्रेट अस्थायीक दफ्तर में
 उपर्युक्त प्रमाणित रजि. अग्रेसर रज. 19/4 बसंत विहार नदी डिल्ली
 नदी नदी 1438-1534 मन्दार मुद्रा दुस्तीन/ सीमा 8-8-87
 59/16 (7-12) 15/1 (5-11-12) 8/1 (6-6-4) 13/2 (1-6-3) सिता 4
 रज. 14-16-3 सलाम की मालिक व कोविज है व सुन्दर पुत्र
 साहेबराज पुत्र शिवचन्द है 1437 मन्दार मुद्रा दुस्तीन/ सीमा 8-8-87
 59/17 (6-6-4) सलाम की मालिक व कोविज है मौजा सुन्दराली
 तहसील की सीमा मुद्रा नदी उपरोक्त आराजी की अरावली क्षेत्र से
 बाहर है उपरोक्त सलाम नदी नदी शासकत है। ग्राम पंचायत व
 नगरपालिका व नगरपालिका प्रशासित नहीं है उपरोक्त आराजी
 की पर कोई इलाका नदी नदी व मुद्रा नदी नहीं है
 उपरोक्त आराजी की अनुसार किसी माल किसी न्यायालय
 के कोई केश नहीं चल रहा है उपरोक्त आराजी की अनुसार
 किसी माल के अनुसार कोई कार व मोटर - बाइक नहीं है
 रिपोर्ट अग्रिम कोविज डेटू सेवा के पेश है

7/10/13

प्रमाण 2327 / ok. दिनांक 7-10-13

12/10/13 सीमा 8-8-87 सीमा 8-8-87 सीमा 8-8-87
 प्रमाण 59/16 (7-12) 15/1 (5-11-12) 8/1 (6-6-4) 13/2 (1-6-3)
 सिता 4 रज. 14-16-3 सलाम की मालिक व कोविज है मौजा सुन्दराली
 तहसील की सीमा मुद्रा नदी उपरोक्त आराजी की अरावली क्षेत्र से
 बाहर है उपरोक्त सलाम नदी नदी शासकत है। ग्राम पंचायत व
 नगरपालिका व नगरपालिका प्रशासित नहीं है उपरोक्त आराजी
 की पर कोई इलाका नदी नदी व मुद्रा नदी नहीं है
 उपरोक्त आराजी की अनुसार किसी माल किसी न्यायालय
 के कोई केश नहीं चल रहा है उपरोक्त आराजी की अनुसार
 किसी माल के अनुसार कोई कार व मोटर - बाइक नहीं है
 रिपोर्ट अग्रिम कोविज डेटू सेवा के पेश है

ਮਾਧਰੀ ਨਿਗਮ ਦੀ ਮਾਮੂਲੀ ਗਈ 24 ਏ

ॐ नमो भगवते वासुदेवाय ॥ १ ॥
 ॐ नमो भगवते वासुदेवाय ॥ २ ॥
 ॐ नमो भगवते वासुदेवाय ॥ ३ ॥
 ॐ नमो भगवते वासुदेवाय ॥ ४ ॥
 ॐ नमो भगवते वासुदेवाय ॥ ५ ॥
 ॐ नमो भगवते वासुदेवाय ॥ ६ ॥
 ॐ नमो भगवते वासुदेवाय ॥ ७ ॥
 ॐ नमो भगवते वासुदेवाय ॥ ८ ॥
 ॐ नमो भगवते वासुदेवाय ॥ ९ ॥
 ॐ नमो भगवते वासुदेवाय ॥ १० ॥

लक्ष्मीलक्षार

सुप्रभात

Annexure-IV

Renewal of Licence from Directorate of Town & Country Planning, Haryana

Directorate of Town & Country Planning, Haryana

Plot no. 3, Nagar Yojana Bhawan, Sector-18A, Madhya Marg, Chandigarh
Phone: 0172-2549349, e-mail:tcpharyana7@gmail.com
website:-http://tcpharyana.gov.in

Regd. To

Asthetic Township Developers Pvt. Ltd.
APT No. E-602, Uniworld City,
Sector 30, Gurugram.

Memo No. LC-2400-Asstt(RK)/2019/


31572

Dated: 20-12-2019

Subject: Renewal of licence No. 97 of 2011 dated 09.11.2011.

Please refer to your application dated 04.10.2019 on the matter cited as subject above.

2. Licence No. 97 of 2011 dated 09.11.2011 granted for setting up of commercial colony on the land measuring 2.851 acres in Sector 27, Gurugram Manesar Urban Complex is hereby renewed upto 08.11.2024 on the same terms & conditions laid down therein.
3. This renewal will not tantamount to certification of satisfactory performance of the applicant entitling him for further renewal of license.
4. The BG on account of IDW shall be got revalidated well before its expiry.
5. Service plan estimates of the colony shall be submitted for approval in the office of competent authority after approval of revised building plans.
6. That the licensee company shall submit the ultimate power load requirement within current validity period of license.
7. That the amendment in Rule 13 in respect of charging of renewal fees is under consideration, for which the draft notification was notified on 20.08.2019. Therefore, increased renewal fees shall be deposited by you in accordance with the final notification or as decided by the Department.



(K. Makrand Pandurang, IAS)
Director,
Town & Country Planning
Haryana, Chandigarh

Endst. No. LC-2400-Asstt(RK)/2019/

Dated:

A copy is forwarded to the following for information and necessary action:-

- i. Chief Administrator, HSVP, Panchkula.
- ii. Senior Town Planner, Gurugram.
- iii. Website Administrator with a request to update the status of renewal of license on the website of the Department.
- iv. District Town Planner, Gurugram.
- v. Chief Account Officer of this Directorate.



(Narender Kumar)
Distt. Town Planner (HQ)
For Director, Town & Country Planning
Haryana, Chandigarh

ORDERS

Whereas, License No. 97 of 2011 dated 09.11.2011 stands granted to Asthetic Township Developers Pvt. Ltd., APT No. E-602, Uniworld City, Sector 30, Gurugram for setting up of commercial colony over an area measuring 2.851 acres in Sector 27, Gurugram Manesar Urban Complex under the provisions of Haryana Development and Regulation of Urban Areas Act, 1975. As per terms and conditions of the licenses and of the agreement executed on LC-IV, the colonizer is required to comply with the provisions of the Haryana Development and Regulation of Urban Areas Act, 1975 and its Rules, 1976.

And, whereas, for delay in compliance of the provisions of Rule 24, 26(2), 27 & 28 of the Haryana Development and Regulation of Urban Areas Rules, 1976 upto 31.03.2019, the licensee has submitted a request for composition of said offence. As per the rates finalized by the Govt. the composition fee has worked out as Rs. 2,24,000/-. The company has deposited composition charges amounting Rs. 2,24,000/- through e-payment TCP3172519112750204 dated 27.11.2019.

Accordingly, in exercise of power conferred under Section-13(1) of the Haryana Development and Regulation of Urban Areas Act, 1975, I hereby order to compound the offence committed due to delay in compliance of above said Rules upto 31.03.2019.



(K. Makrand Pandurang, IAS)
Director,
Town and Country Planning,
Haryana, Chandigarh

Endst. No. LC-2400-Asstt(RK)/2019/ 31579

Dated: 20-12-2019

A copy is forwarded to the following for information and necessary action:-

1. Chief Accounts Officer, O/o Director, Town and Country Planning Haryana Chandigarh.
2. Asthetic Township Developers Pvt. Ltd., APT No. E-602, Uniworld City, Sector 30, Gurugram.


(Narender Kumar)
Distt. Town Planner (HQ)
For Director, Town and Country Planning,
Haryana, Chandigarh

Annexure-V
Intekaal Letter

Annexure-VI

Water Balance

Table 5: Calculations for Daily Water Demand

S. No.	Unit Type	Occupancy	Rate of demand (lpcd)	Total water requirement (KLD)
A	Domestic Water			
1	Ground Floor (Retail Shop)			
	• Staff	131	30	4
	• Visitors	1183	15	18
2	First to Nineteenth Floor (Office)			
	• Staff	3305	30	99
	• Visitors	367	15	6
3.	Sky Lounge (Terrace)			
	• Visitors	794	15	12
TOTAL DOMESTIC WATER DEMAND = 139 KLD				
B	HORTICULTURE (2423.82m ²)		1 l/sqm/day	3 KLD
C	HVAC (1650 TR)	10 hours	@10 Litre/TR	165 KLD
D.	DG Cooling (3 X 1500 KVA + 1 X 1000 KVA)	0.9 lt/kva/hr		30 KLD
GRAND TOTAL (A+B+C) = 337 KLD				

*DG Sets water demand are calculated for 6 Hours operation/day.

Table 6: Waste Water Calculations

Domestic Water Requirement	139 KLD
• Fresh water (@30% of domestic water)	42 KLD
• Flushing water (@ 70% of domestic water)	97 KLD
Waste Water Generated (@ 80% fresh water + 100% flushing water)	34 +97 = 131 KLD
STP Capacity	160 KL

The water balance diagrams for different seasons are shown below:

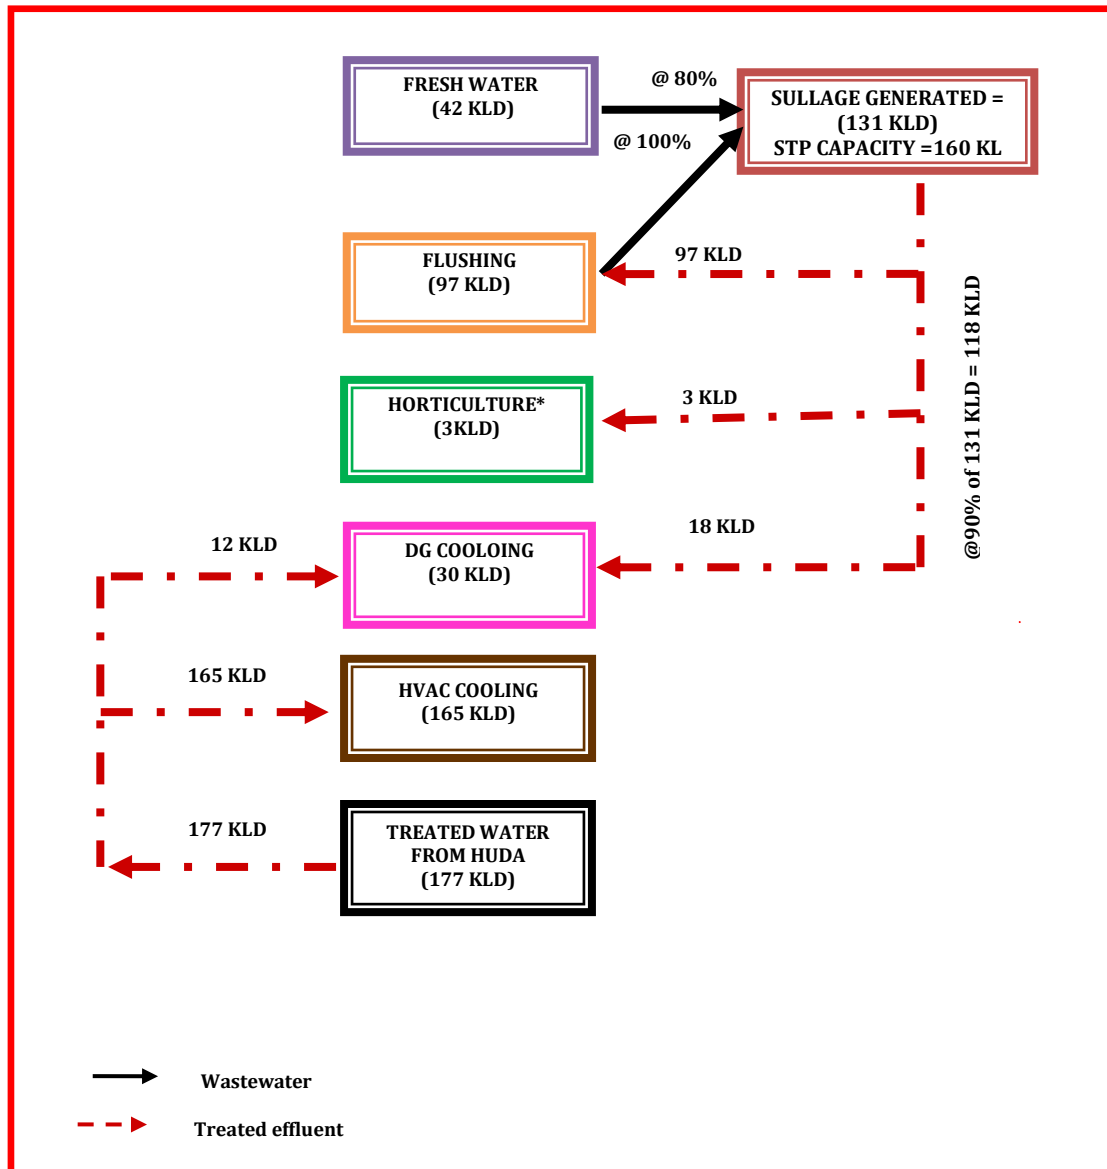


Figure 1: Water Balance Diagram (Non-Rainy Season)

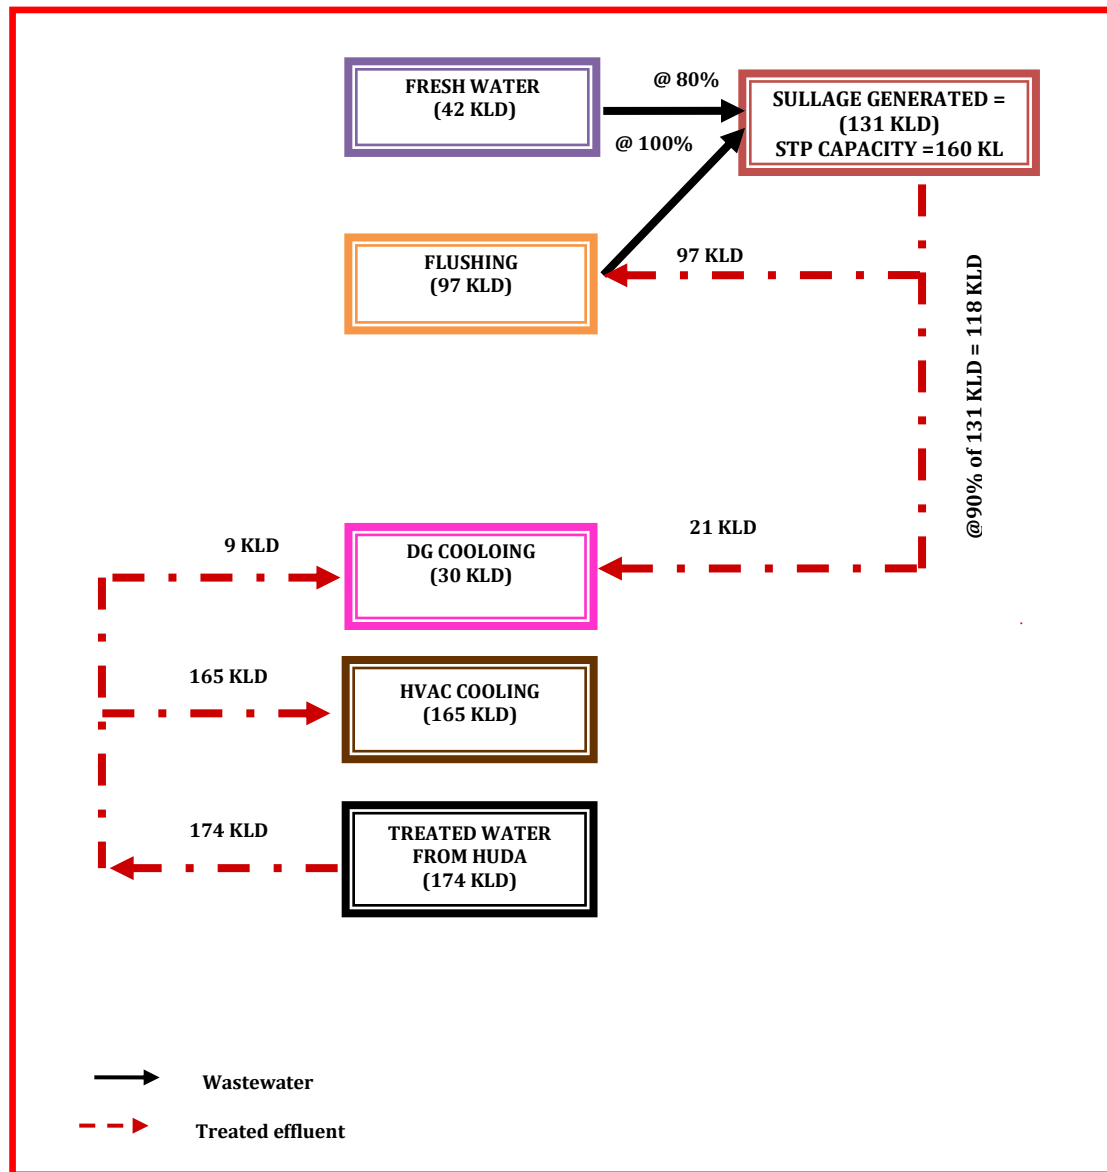


Figure 2: Water Balance Diagram (Rainy Season)

Wastewater Generation & Treatment

It is expected that the project will generate approx. 131KLD of wastewater. The wastewater will be treated in onsite STP of 160 KL capacity. The treated effluent 118 KLD will be reused for flushing, horticulture, DG Cooling & HVAC.

2.2 What is the quality of water required, in case, the supply is not from a municipal source? (Provide physical, chemical, Biological characteristics with class of water quality).

The required water will be met through the HUDA. The total water requirement is approx. 337 KLD.

SBR TECHNOLOGY

Sewerage System

An external sewage network shall collect the sewage from all units, and flow by gravity to the proposed sewage treatment plant.

Following are the benefits of providing the Sewage Treatment Plant in the present circumstances:

- Reduced net daily water requirements, source for Horticultural purposes by utilization of the treated waste water.
- Reduced dependence on the public utilities for water supply and sewerage systems.
- Sludge generated from the Sewage Treatment Plant shall be rich in organic content and an excellent fertilizer for horticultural purposes.

a. Wastewater Details

(a)	Daily load	:	131 KLD
(b)	Duration of flow to STP	:	24 hours
(c)	Temperature	:	Maximum 46°C
(d)	pH	:	6.5 to 8.5
(e)	Colour	:	Mild
(f)	T.S.S. (mg/l)	:	300-400
(g)	BOD ₅ (mg/l)	:	250-350
(h)	COD (mg/l)	:	400-600
(i)	Oil & Grease	:	10-50
(j)	Color	:	Mild

b. Final discharge characteristics

(a)	pH	:	6.5 to 7.5
(b)	Oil & Grease	:	<10 mg/l

(c)	B.O.D.	:	<20 mg/l
(d)	C.O.D.	:	<50 mg/l
(e)	Total Suspended Solids	:	<10 mg/l
(h)	Color	:	Clear

c. Treatment Technology

Sequence Batch Reactor is a most prominent technique for removing organic carbon and nutrient in a relatively short period. The fill and draw scheme constitute the basic principle of the SBR system. Raw sewage will be collected under gravity into the equalization tank after allowing to pass through the bar screen. The bar screen, by removing coarse solids from the sewage help in protecting the raw sewage pump. The raw sewage equalization tank, through temporarily holding the incoming sewage facilitates both pumping of sewage through the STP and dampening the flow variation in the received sewage. The sewage collected in equalization tank is pumped and passed through the SBR tank. Air will be introduced in this tank to prevent any potential foul smell problem & to provide the mixing of wastewater to avoid the sedimentation of solids in this tank.

The SBR is basically a single tank that serves both biological reactor and settler in a temporal sequence, whereas aeration and settling are simultaneous but in a spatial sequence.

From the reactors, The suspended solids will settle at the bottom of the tank & clear supernatant will overflow to Collection cum storage tank collected sludge at bottom shall be transferred through pumps to sludge holding tank. The clear supernatant after clarifier will be collected in to filter feed tank. This tank will act as housing tank for filter feed pumps. The clarified & dis-infected water will be then fed to filtration unit.

Filtration unit consisting of Dual Media sand filter and activated carbon filter will remove the residual impurities such as odor/color, suspended solids, BOD/COD. The treated water after the filtration unit will be collected in Irrigation cum Flushing water storage tank from where it is transferred to flushing water tank at terrace & Irrigation System.

Excess sludge from the bottom of the settling tank will be removed and transferred to sludge holding tank. Air grid shall be provided in this tank to avoid conversion into anaerobic

conditions, thickening of sludge and keep sludge in homogenous condition. The digested & thickened sludge shall be further thickened through Sludge Dewatering System and disposed off periodically through closed tanker or can be reused as manure.

Stages of Treatment: The treatment process consists of the following stages:

- Equalization
- Bio- Degradation
- Clarification & Settling
- Filtration

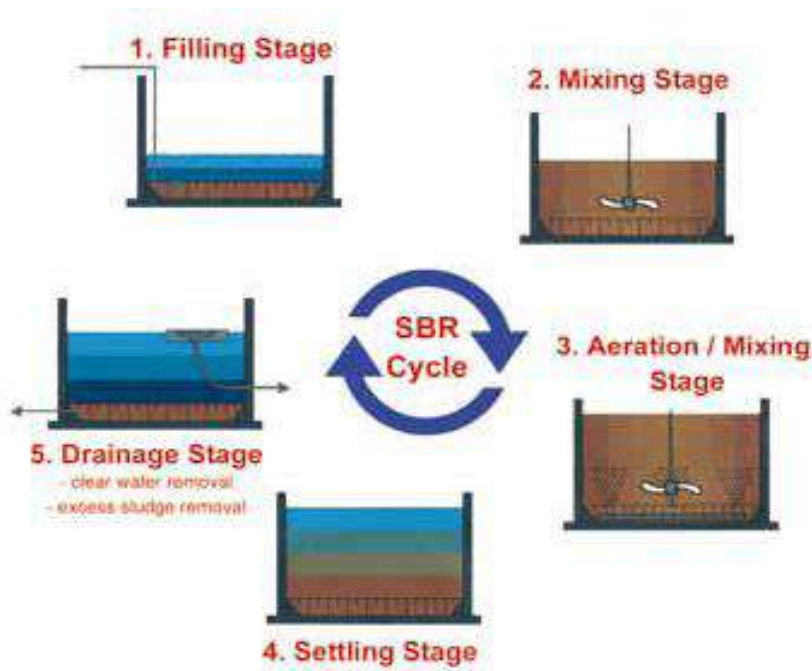


Figure 3: Flow Diagram of SBR

Sewer System

The alignment and slope of the sewer line will follow the road network, drains or natural ground surface and will be connected to the trunk sewers. The discharge point will be a treatment plant, a pumping station, a water course or an intercepting sewer. Pumping stations would be provided at places where the natural slope of the terrain is insufficient to permit gravity flow or the cost of excavation is uneconomical to do the same.

2.3 How much of water requirement can be met from the recycling of treated wastewater? (Give the details of quantities, sources and usage)

It is expected that the project will generate approx. 131 KLD of wastewater. The wastewater will be treated in onsite STP of 160 KL capacity. The treated effluent 118 KLD will be reused for flushing, horticulture, DG Cooling & HVAC.

2.4 Will there be diversion of water from other users? (Please assess the impacts of the project on other existing uses and quantities of consumption).

No. There will not be any diversion of water from other users. Rise in water demand is a local phenomenon but the project would only involve spatial shifting of water demand within a region.

2.5 What is the incremental pollution load from wastewater generated from the proposed activity? (Give details of the quantities and composition of wastewater generated from the proposed activity)

131 KLD of sullage generated which will be treated through onsite STP of 160 KL capacity.

2.6 Give details of the water requirements met from water harvesting? Furnish details of the facilities created.

The storm water collection system for the premises shall be self-sufficient to avoid any collection/stagnation and flooding of water. The amount of storm water run-off depends upon many factors such as intensity and duration of precipitation, characteristics of the tributary area and the time required for such flow to reach the drains. The drains shall be located near the carriage way along either side of the roads. Taking the advantage of road camber, the rainfall run off from roads shall flow towards the drains. Storm water from various plots/shall be connected to adjacent drain by a pipe through catch basins. Therefore, it has been calculated to provide 3 rainwater harvesting pits at selected locations, which will catch the maximum run-off from the site.

- 1) Since the existing topography is congenial to surface disposal, a network of storm water pipe drains is planned adjacent to roads. All building roof water will be brought down through rain water pipes.

Annexure-VII

RWH Details

2.3 How much of water requirement can be met from the recycling of treated wastewater? (Give the details of quantities, sources and usage)

It is expected that the project will generate approx. 131 KLD of wastewater. The wastewater will be treated in onsite STP of 160 KL capacity. The treated effluent 118 KLD will be reused for flushing, horticulture, DG Cooling & HVAC.

2.4 Will there be diversion of water from other users? (Please assess the impacts of the project on other existing uses and quantities of consumption).

No. There will not be any diversion of water from other users. Rise in water demand is a local phenomenon but the project would only involve spatial shifting of water demand within a region.

2.5 What is the incremental pollution load from wastewater generated from the proposed activity? (Give details of the quantities and composition of wastewater generated from the proposed activity)

131 KLD of sullage generated which will be treated through onsite STP of 160 KL capacity.

2.6 Give details of the water requirements met from water harvesting? Furnish details of the facilities created.

The storm water collection system for the premises shall be self-sufficient to avoid any collection/stagnation and flooding of water. The amount of storm water run-off depends upon many factors such as intensity and duration of precipitation, characteristics of the tributary area and the time required for such flow to reach the drains. The drains shall be located near the carriage way along either side of the roads. Taking the advantage of road camber, the rainfall run off from roads shall flow towards the drains. Storm water from various plots/shall be connected to adjacent drain by a pipe through catch basins. Therefore, it has been calculated to provide 3 rainwater harvesting pits at selected locations, which will catch the maximum run-off from the site.

- 1) Since the existing topography is congenial to surface disposal, a network of storm water pipe drains is planned adjacent to roads. All building roof water will be brought down through rain water pipes.

- 2) Proposed storm water system consists of pipe drain, catch basins and seepage pits at regular intervals for rain water harvesting and ground water recharging.
- 3) For basement parking, the rainwater from ramps will be collected in the basement storm water storage tank. This water will be pumped out to the nearest external storm water drain.
- 4) The peak hourly rainfall of 45 mm/hr shall be considered for designing the storm water drainage system.

Rain water harvesting has been catered to and designed as per the guideline of CGWA. Peak hourly rainfall has been considered as 45 mm/hr. The recharge pit of 4 m diameter and 3 m depth is constructed for recharging the water. Inside the recharge pit, a recharge bore is constructed having adequate diameter and depth. The bottom of the recharge structure will be kept 5m above this level. At the bottom of the recharge well, a filter media is provided to avoid choking of the recharge bore. Design specifications of the rain water harvesting plan are as follows:

- Catchments/roofs would be accessible for regular cleaning.
- The roof will have smooth, hard and dense surface which is less likely to be damaged allowing release of material into the water. Roof painting has been avoided since most paints contain toxic substances and may peel off.
- All gutter ends will be fitted with a wire mesh screen and a first flush device would be installed. Most of the debris carried by the water from the rooftop like leaves, plastic bags and paper pieces will get arrested by the mesh at the terrace outlet and to prevent contamination by ensuring that the runoff from the first 20 minutes of rainfall is flushed off.
- No sewage or wastewater would be admitted into the system.
- No wastewater from areas likely to have oil, grease, or other pollutants has been connected to the system.

Table 7: Comparative Details of Rain water Harvesting

S. No.	Particulars	EC accorded	Expansion	Total (EC accorded + Expansion)
1.	Rain water Harvesting Pits	3	---	3

Calculations for storm water load :

$$\text{Net Plot Area} = 11,537.57\text{m}^2$$

$$\text{Roof-top area} = \text{Ground Coverage} = 4,524.140 \text{ m}^2$$

$$\text{Green Area} = 2,423.82 \text{ m}^2$$

$$\begin{aligned}\text{Paved area} &= \text{Net Plot Area} - (\text{Roof-top Area} + \text{Green Area}) \\ &= 11537.57 - (4524.140 + 2423.82) \\ &= 4589.61 \text{ m}^2\end{aligned}$$

Run-off Load.

$$\begin{aligned}\text{Roof-top Area} &= 4524.140 \times 0.045 \times 0.9 \\ &= 183.227\text{m}^3/\text{hr}.\end{aligned}$$

$$\begin{aligned}\text{Green Area} &= 2423.82 \times 0.045 \times 0.2 \\ &= 21.81\text{m}^3/\text{hr}.\end{aligned}$$

$$\begin{aligned}\text{Paved Area} &= 4,589.61 \times 0.045 \times 0.7 \\ &= 144.57 \text{ m}^3/\text{hr}.\end{aligned}$$

$$\begin{aligned}\text{Total Runoff Load} &= 183.227 + 21.81 + 144.57 \text{ m}^3/\text{hr} \\ &= 349.607 \text{ m}^3/\text{hr}.\end{aligned}$$

$$\text{Taking 20 minutes retention time, volume of storm water} = 349.607 / 3 = 116.53 \text{ m}^3$$

$$\text{Capacity of Recharge pit} = \pi r^2 h = 3.14 \times 2 \times 2 \times 3 = 37.68 \text{ m}^3$$

$$\text{Hence No. of pits required} = 116.53 / 37.68 = \mathbf{3 \text{ pits}}$$

Total of 3 Rain Water Harvesting pits are proposed for artificial ground water recharge.

2.7 What would be the impact of the land use changes occurring due to the project on the runoff characteristics (quantitative as well as qualitative) of the area in the post construction phase on a long term basis? Would it aggravate the problems of flooding or water logging in any way?

Annexure-VIII

**Waste management plan during
Construction & Operation Phase**

- Provision of slit traps in storm water drains
- Good housekeeping in the above areas

10.2.4 EMP FOR LAND ENVIRONMENT

Construction Phase

The waste generated from construction activity includes construction debris, biomass from land clearing activities, waste from the temporary make shift tents for the labors and hazardous waste. Following section discuss the management of each type of waste. Besides waste generation, management of the topsoil is an important area for which management measures are required.

Construction Debris

Construction debris is bulky and heavy and re-utilization and recycling is an important strategy for management of such waste. As concrete and masonry constitute the majority of waste generated, recycling of this waste by conversion to aggregate can offer benefits of reduced landfill space and reduced extraction of raw material for new construction activity. This is particularly applicable to the project site as the construction is to be completed in a phased manner.

Mixed debris with high gypsum, plaster, shall not be used as fill, as they are highly susceptible to contamination, and will be send to designated solid waste landfill site.

Metal scrap from structural steel, piping, concrete reinforcement and sheet metal work shall be removed from the site by construction contractors. A significant portion of wood scrap will be reused on site. Recyclable wastes such as plastics, glass fiber insulation, roofing etc shall be sold to recyclers.

Hazardous waste

Construction sites are sources of many toxic substances such as paints, solvents wood preservatives, pesticides, adhesives and sealants. Hazardous waste generated during

construction phase shall be stored in sealed containers and disposed off as per The Hazardous Wastes (Management, Handling & Trans boundary Movement) Rules, 2016.

Some management practices to be developed are:

- Herbicides and pesticide will not be over applied (small-scale applications) and not applied prior to rain.
- Paintbrushes and equipment for water and oil based paints shall be cleaned within a contained area and will not be allowed to contaminate site soils, water courses or drainage systems.
- Provision of adequate hazardous waste storage facilities. Hazardous waste collection containers will be located as per safety norms and designated hazardous waste storage areas will be away from storm drains or watercourses.
- Segregation of potentially hazardous waste from non-hazardous construction site debris.
- Well labeled all hazardous waste containers with the waste being stored and the date of generation.
- Instruct employees and subcontractors in identification of hazardous and solid waste.

Even with careful management, some of these substances are released into air, soil and water and many are hazardous to workers. With these reasons, the best choice is to avoid their use as much as possible by using low-toxicity substitutes and low VOC (Volatile Organic Compound) materials.

Waste from Temporary Makes Shift Tents for Labors

Wastes generated from temporary make shift labor tents which will be managed by the contractor of the site. The wastewater generated will be channelized to the septic tank.

Top Soil Management

To minimize disruption of soil and for conservation of top soil, the contractor shall keep the top soil cover separately and stockpile it. After the construction activity is over, top soil will be utilized for landscaping activity. Other measures, which would be followed to prevent soil erosion and contamination include:

- Maximize use of organic fertilizer for landscaping and green belt development
- To prevent soil contamination by oil/grease, leak proof containers would be used for storage and transportation of oil/grease and wash off from the oil/grease handling area shall be drained through impervious drains and treated appropriately before disposal
- Removal of as little vegetation as possible during the development and re-vegetation of bare areas after the project.
- Working in a small area at a point of time (phase wise construction)
- Construction of erosion prevention troughs/berms.

Operational Phase

The philosophy of solid waste management at the proposed complex will be to encouraging the four R's of waste i.e. **Reduction, Reuse, Recycling and Recovery** (materials & energy). Regular public awareness meetings will be conducted to involve the public in the proper segregation and storage techniques. The Environmental Management Plan for the solid waste focuses on three major components during the life cycle of the waste management system i.e., collection and transportation, treatment or disposal and closure and post-closure care of treatment/disposal facility.

Collection and Transportation

- During the collection stage, the solid waste of the project will be segregated into biodegradable waste and non-biodegradable. Biodegradable waste and non biodegradable waste will be collected in

separate bins. Biodegradable waste will be treated in the project premises by Organic waste convertor. The recyclable wastes will be sent off to recyclabers. Proper guidelines for segregation, collection and storage will be prepared as per MSW Rules, 2016.

- To minimize littering and odour, waste will be stored in well-designed containers/ bins that will be located at strategic locations to minimize disturbance in traffic flow
- Care would be taken such that the collection vehicles are well maintained and generate minimum noise and emissions. During transportation of the waste, it will be covered to avoid littering.

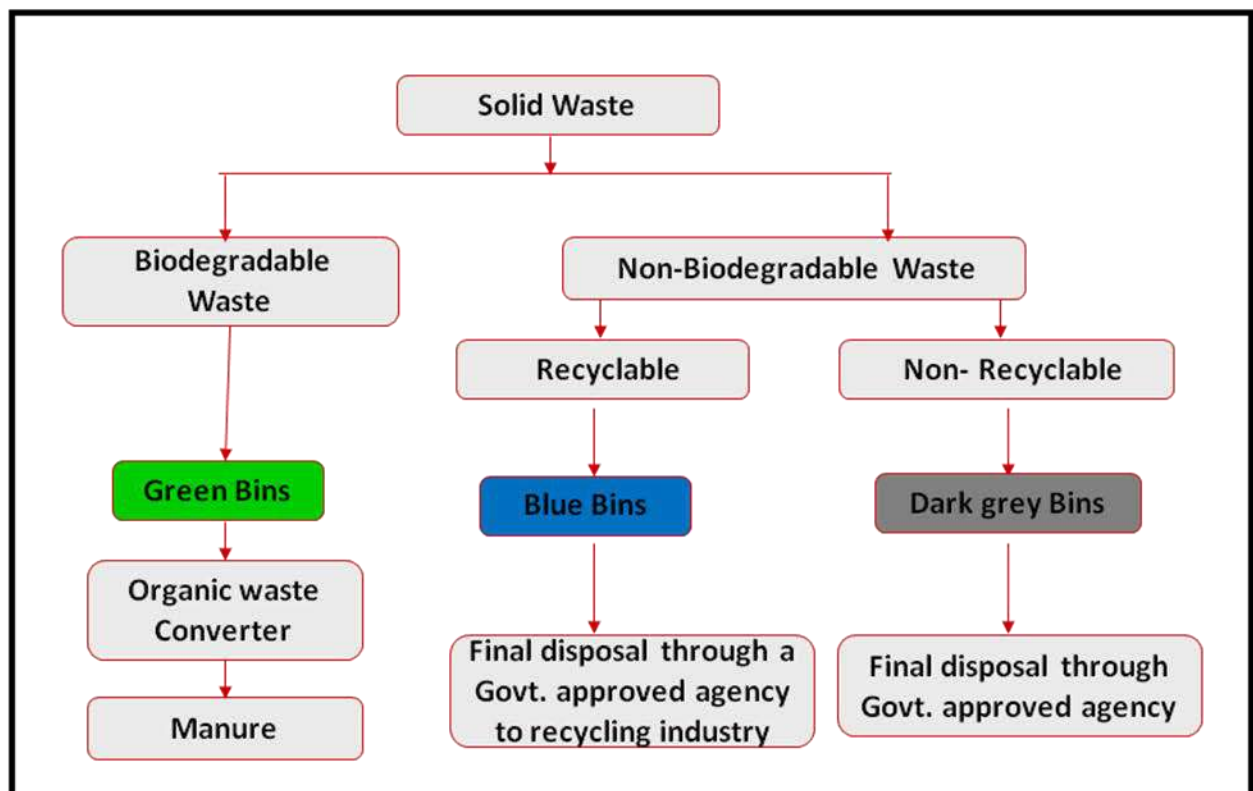


Figure 6: Waste Management Flow Diagram

Organic Waste Converter

A waste converter is a machine used for the treatment and recycling of solid and liquid refuse material. A converter is a self-contained system capable of performing the following functions: pasteurization of organic waste; sterilization of pathogenic or biohazard waste; grinding and pulverization of refuse into unrecognizable output; trash compaction; dehydration.

Benefits of organic waste converter:

1. Large quantity of solid waste is converted to manure in a very short period
2. Manure can be used as compost for gardening
3. Machine requires less space and the efficiency is high
4. Manpower and maintenance is very less
5. This is one of the latest techniques of managing biodegradable solid waste.

Operation cost of OWC:

Organic Waste Converter - 300 (Dim. 3m × 4m) is proposed to be used for composting waste 120kg/batch or 3000 kg/day & it requires electricity of about 13.5 HP.

No. of batches /day = $3000/120 = 25$ batches/day.

No. of batches to convert 490 kg/day = $490/120 = 4.08$ say 4 batches.

Operation Cost-monthly per capita:

The operating cost of OWC - 300 = 1, 80,000 INR/month

Cost/day = $1, 80,000/30$
= 6000/-

1 batch/day cost = $6000/25$
= 240 INR

Cost for 4 batch/day = $4 \times 240/-$
= 960/-

Monthly operating cost = 30×960
= Rs. 28,800/- per month

Disposal

With regards to the disposal/treatment of waste, the management will take the services of the authorized agency for waste management and disposal of the same on the project site during its operational phase.

10.2.5 EMP FOR ECOLOGICAL ENVIRONMENT

Construction activity changes the natural environment. The project requires the implementation of following choices exclusively or in combination.

Construction Stage

- Restriction of construction activities to defined project areas, which are ecologically sensitive
- Restrictions on location of temporary labor tents and offices for project staff near the project area to avoid human induced secondary additional impacts on the flora and fauna species
- Cutting, uprooting, coppicing of trees or small trees if present in and around the project site for cooking, burning or heating purposes by the labors will be prohibited and suitable alternatives for this purpose will be made
- Along with the construction work, the peripheral green belt would be developed with suggested native plant species, as they will grow to a full-fledged covered at the time of completion.

Operation Stage

Improvement of the current ecology of the project site will entail the following measures:

- Plantation and Landscaping
- Green Belt Development
- Park and Avenue Plantation

Annexure-IX

**Photographs of construction of Wind
Breaking wall of 10 mtrs. height for
dust control**


WIND BREAKING WALL



Front - Inside Barricading



Front side Barricading

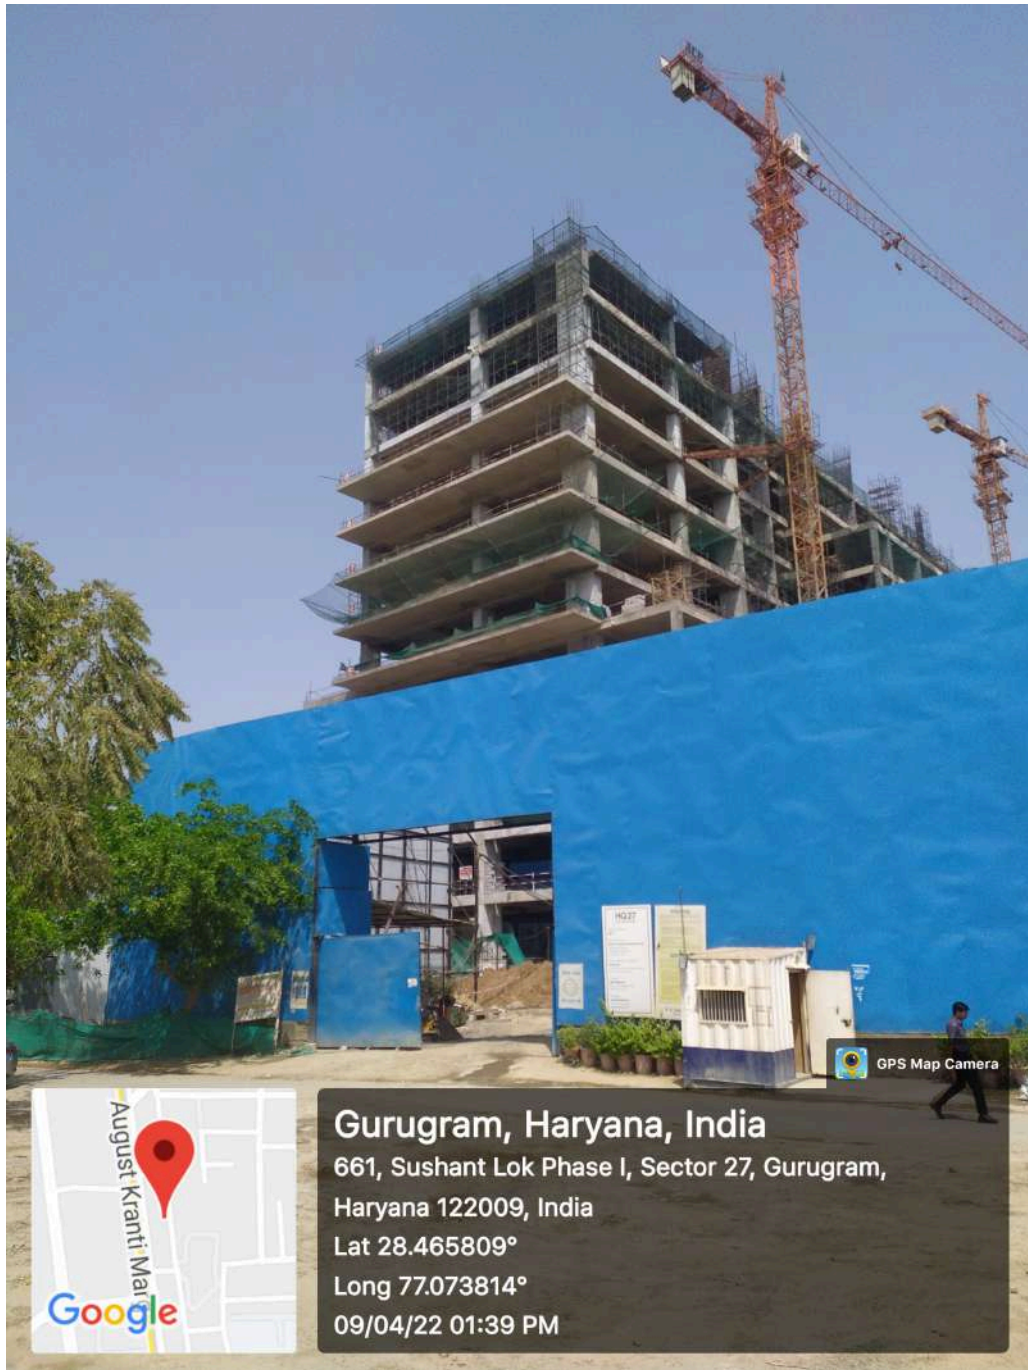

Gurugram, Haryana, India


661, Sushant Lok Phase I, Sector 27, Gurugram,
Haryana 122009, India

Lat 28.465809°

Long 77.073814°

09/04/22 01:39 PM

GPS Map Camera

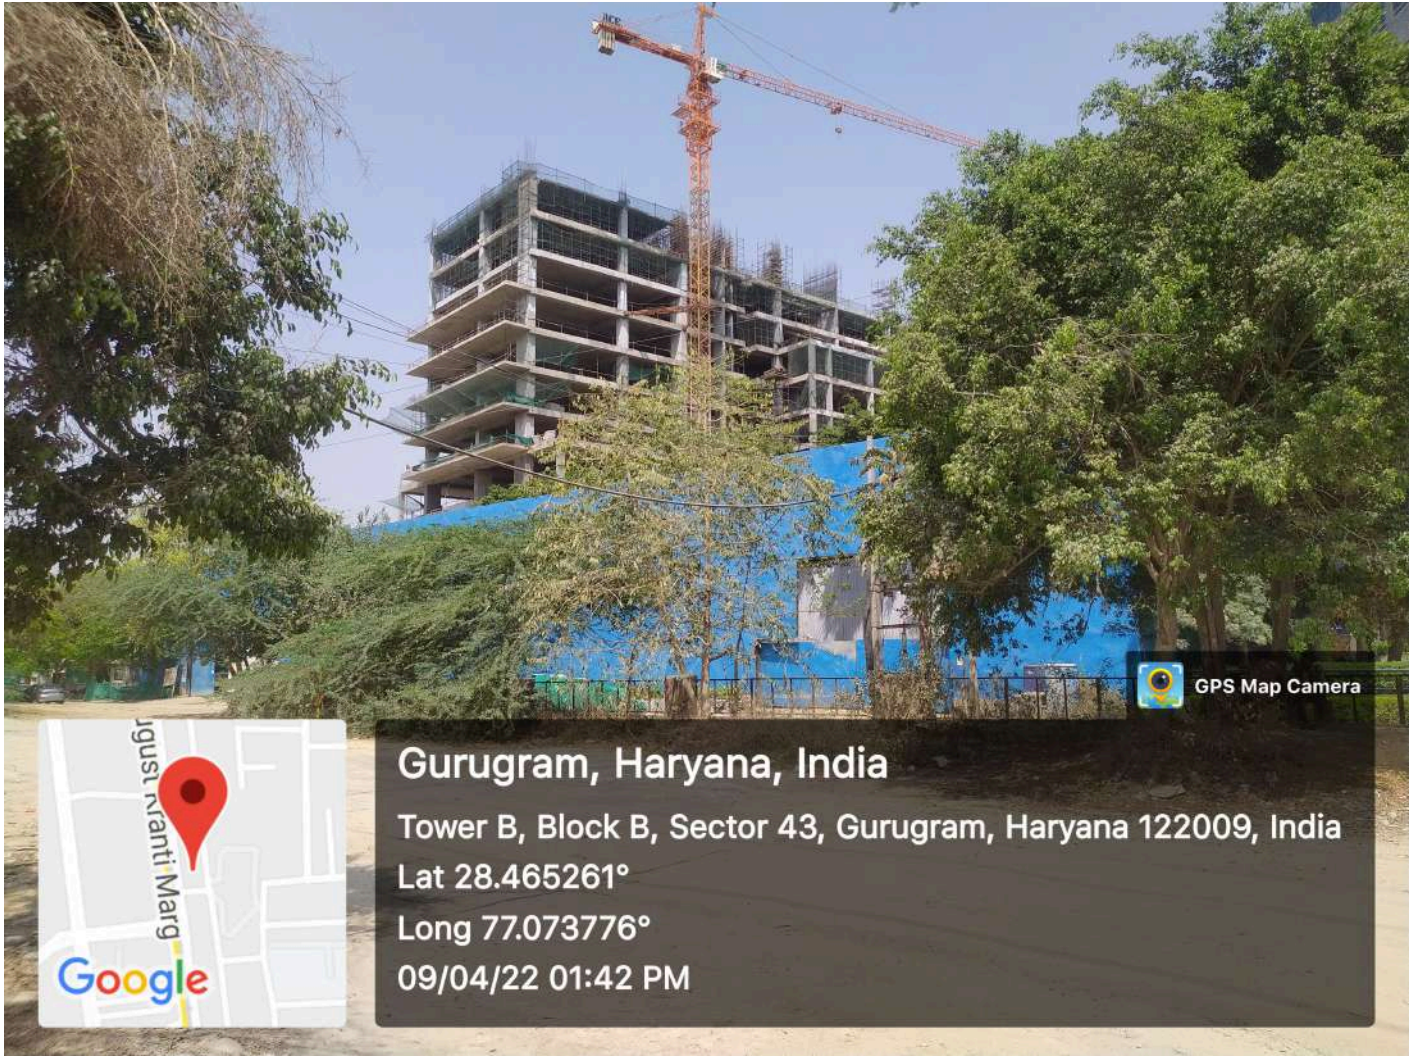

Gurugram, Haryana, India

Tower B, Block B, Sector 43, Gurugram, Haryana 122009, India

Lat 28.465261°

Long 77.073776°

09/04/22 01:42 PM

GPS Map Camera

Annexure-X

Environment Monitoring Reports i.e.
AAQ, Noise, Water & soil and its
interpretation

TEST REPORT

Issued to

M/s Asthetic Township Developers Pvt. Ltd.
Apt. No. E-301, Unworld City, Sec-30
Gurgaon- 122002



Doc No. : ELPL/IV/QF/20
Amend. No. & Amend. Date : 02 & 17.02.2018
Lab Reference No. : 220211001 W
Issue Date : 17/02/2022
Your Reference : Email

Sample Particulars: Water sample was collected from Tab at Commercial Complex project at Sushant Lok, Sec- 27, Gurugram Haryana on 10/02/2022.

Type of sample	: Drinking water	Sample Registration Date	: 11/02/2022
Sampling Date	: 10/02/2022	Analysis Starting Date	: 11/02/2022
Sampling Done by	: Lab representative	Analysis Completion Date	: 17/02/2022
Quantity received	: 2 Ltr approx.	Tests Required	: Mentioned below
Sample's Location	: Main Gate Office	Sampling Method	: ELPL/III/SOP/20

Page 1 of 2

S.No	Test Parameters	Units	Results	IS 10500 : 2012		Test Method
				Acceptable Limit, max.	Permissible Limit in the Absence of Alternate source, max.	
1	Color	Hazen	BDL (DL-5.0)	5	15	IS 3025 (Pt-04)
2	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Pt-05)
3	pH	-	7.32	6.5-8.5	No relaxation	IS 3025 (Pt-11)
4	Taste	-	Agreeable	Agreeable	Agreeable	IS 3025 (Pt-08)
5	Turbidity	NTU	BDL(DL-1.0)	1	5	IS 3025 (Pt-10)
6	Total Dissolved Solids	mg/l	372	500	2000	IS 3025 (Pt-16)
7	Ammonia (as total ammonia-N)	mg/l	BDL (DL 0.1)	0.5	No relaxation	IS 3025 (Pt-34)
8	Anionic Detergents (as MBAS)	mg/l	BDL (DL 0.1)	0.2	1.0	Annex K of IS 13428
9	Calcium as Ca	mg/l	84.2	75	200	IS 3025 (Pt-40)
10	Chloramines (as Cl ₂)	mg/l	BDL (DL0.1)	4.0	No relaxation	IS 3025 (Pt-26)
11	Chloride as Cl	mg/l	73.4	250	1000	IS 3025 (Pt-32)
12	Fluoride as F	mg/l	0.22	1.0	1.5	APHA 23 rd Ed 4500F
13	Free Residual Chlorine	mg/l	BDL (DL0.05)	0.2	1	IS 3025 (Pt-26)
14	Nitrate as NO ₃	mg/l	1.68	45	No relaxation	IS 3025 (Pt-34)
15	Phenolic Compounds (as C ₆ H ₅ OH)	mg/l	BDL (DL 0.001)	0.001	0.002	IS 3025 (Pt-43)
16	Sulphate as SO ₄	mg/l	39.7	200	400	IS 3025 (Pt-24)
17	Sulphide (as H ₂ S)	mg/l	BDL(DL 0.02)	0.05	No relaxation	IS 3025 (Pt-29)
18	Total Alkalinity as CaCO ₃	mg/l	89.1	200	600	IS 3025 (Pt-23)
19	Total Hardness as CaCO ₃	mg/l	355	200	600	IS 3025 (Pt-21)
20	Cyanide (as CN)	mg/l	BDL(DL 0.02)	0.05	No relaxation	IS 3025 (Pt-27)
21	Aluminum (as Al)	mg/l	BDL(DL 0.01)	0.03	0.2	APHA23 rd Ed.3120B
22	Barium (as Ba)	mg/l	BDL (DL 0.1)	0.7	No relaxation	APHA23 rd Ed.3120B

Analyzed By

Authorized Signatory



TEST REPORT

Issued to

M/s Asthetic Township Developers Pvt. Ltd.
Apt. No. E-301, Unworld City, Sec-30
Gurgaon- 122002



Doc No. : ELPL/IV/QF/20
Amend. No. & Amend. Date : 02 & 17.02.2018
Lab Reference No. : 220211001 W
Issue Date : 17/02/2022
Your Reference : Email

Sample Particulars: Water sample was collected from Tab at Commercial Complex project at Sushant Lok, Sec- 27, Gurugram Haryana on 10/02/2022.

Type of sample	: Drinking water	Sample Registration Date	: 11/02/2022
Sampling Date	: 10/02/2022	Analysis Starting Date	: 11/02/2022
Sampling Done by	: Lab representative	Analysis Completion Date	: 17/02/2022
Quantity received	: 2 Ltr approx.	Tests Required	: Mentioned below
Sample's Location	: Main Gate Office	Sampling Method	: ELPL/III/SOP/20

Page 2 of 2

S.No	Test Parameters	Units	Results	IS 10500 : 2012		Test Method
				Acceptable Limit, max.	Permissible Limit in the Absence of Alternate source, max.	
23	Boron (as B)	mg/l	BDL (DL 0.1)	0.5	1.0	APHA 23 rd Ed.3120B
24	Copper (as Cu)	mg/l	BDL (DL 0.02)	0.05	1.5	APHA 23 rd Ed. 3120B
25	Iron as Fe	mg/l	BDL (DL 0.05)	1.0	No relaxation	IS 3025 (Pt-02)
26	Magnesium as Mg	mg/l	35.2	30	100	APHA 23 rd Ed.3500 mg B
27	Manganese as Mn	mg/l	BDL (DL 0.05)	0.1	0.3	APHA 23 rd Ed.3120B
28	Selenium (as Se)	mg/l	BDL (DL 0.01)	0.01	No relaxation	APHA 23 rd Ed.3120B
29	Silver (as Ag)	mg/l	BDL (DL 0.05)	0.1	No relaxation	APHA 23 rd Ed.3120B
30	Zinc (as Zn)	mg/l	BDL (DL 0.05)	5	15	APHA 23 rd Ed.3120B
31	Cadmium (as Cd)	mg/l	BDL(DL 0.001)	0.003	No relaxation	APHA 23 rd Ed.3120B
32	Lead (as Pb)	mg/l	BDL (DL 0.005)	0.01	No relaxation	APHA 23 rd Ed.3120B
33	Mercury (as Hg)	mg/l	BDL(DL0.001)	0.001	No relaxation	APHA 23 rd Ed.3120B
34	Molybdenum (as MO)	mg/l	BDL (DL 0.05)	0.07	No relaxation	APHA 23 rd Ed.3120B
35	Nickel (as Ni)	mg/l	BDL (DL 0.01)	0.02	No relaxation	APHA 23 rd Ed.3120B
36	Total Arsenic (as As)	mg/l	BDL (DL 0.01)	0.01	No relaxation	APHA 23 rd Ed.3120B
37	Total Chromium (as Cr)	mg/l	BDL (DL 0.03)	0.05	No relaxation	APHA 23 rd Ed.3120B

*****END OF REPORT*****

Analyzed By
V. Kumar

Authorized Signatory
Sanjay Kumar
ECOSTEPS LABORATORY PRIVATE LIMITED

TEST REPORT

Issued to

M/s Asthetic Township Developers Pvt. Ltd.
Apt. No. E-301, Unworld City, Sec-30
Gurgaon- 122002



Doc No. : ELPL/IV/QF/20
Amend. No. & Amend. Date : 02 & 17.02.2018
Lab Reference No. : 220211002 S
Issue Date : 17/02/2022
Your Reference : Email
(Page 1 of 1)

Sample Particulars: Soil sample was collected from ground at Commercial Complex project at Sushant Lok, Sec- 27, Gurugram Haryana on 10/02/2022.

Type of sample	: Soil	Sample Registration Date	: 11/02/2022
Sampling Date	: 10/02/2022	Analysis Starting Date	: 11/02/2022
Sampling Done by	: Lab representative	Analysis Completion Date	: 17/02/2022
Quantity received	: 1 Kg approx.	Tests Required	: Mentioned below
Sample's Location	: Project Site	Sampling Method	: Grab Method

S.No.	Test Parameters	Unit	Result	Test Method
1	pH (1:5)	-	8.72	IS 2720(P-26)
2	Conductivity (1:5)	µmhos/cm	362	USDA Method
3	Color	-	Brown	USDA Method
4.	Texture		Sandy Clay Loam	
	Silt	%	11	
	Clay	%	39	USDA Method
	Sand	%	50	
5	Sodium Absorption Ratio	-	1.06	USDA Method
6	Cation Exchange Capacity	Meq/100gm	22.2	IS 2720(P-24)
7	Porosity	%	44.8	USDA Method
8	Water Holding Capacity	%	46.2	USDA Method
9	Bulk Density	gm/cc	1.11	USDA Method
10	Chloride as Cl	mg/kg	195.4	USDA Method
11	Calcium as Ca	mg/kg	3561.4	USDA Method
12	Sodium as Na	mg/kg	250	USDA Method
13	Potassium as K	mg/kg	100	USDA Method
14	Magnesium as Mg	mg/kg	388.2	USDA Method
15	Organic matter	%	0.69	IS 2720(P-22)
16	Available Nitrogen	mg/kg	122	USDA Method
17	Phosphorous	mg/kg	98	USDA Method

*****END OF REPORT*****

Analyzed By

Authorized Signatory



TEST REPORT

Issued to

M/s Asthetic Township Developers Pvt. Ltd.
Apt. No. E-301, Unworld City, Sec-30
Gurgaon- 122002



Doc No. : ELPL/IV/QF/20
Amend. No. & Amend. Date : 02 & 17.02.2018
Lab Reference No. : 220211015 A
Issue Date : 17/02/2022
Your Reference : Email
(Page 1 of 1)

Sample Particulars: Ambient Air Quality Monitoring was done at Commercial Complex project at Sushant Lok, Sec- 27, Gurugram Haryana, from 10/02/2022 to 11/02/2022

Type of sample	: Ambient Air	Sample Registration Date	: 11/02/2022
Sampling Date	: 10/02/2022-11/02/2022	Analysis Starting Date	: 11/02/2022
Sampling Done by	: Lab representative	Analysis Completion Date	: 16/02/2022
Quantity received	: 24 Hourly Sample	Tests Required	: Mentioned below
Sample's Location	: Near Retail Area	Sampling Method	: ELPL/III/SOP/21

S.No.	Test Parameters	Units	Results	NAAQS	Test Method
1	Particulate Matter as PM ₁₀	µg/m ³	252	100 (24 Hourly)	IS 5182 (Pt-23)
2	Particulate Matter as PM _{2.5}	µg/m ³	172.9	060 (24 Hourly)	ELPL/III/SOP/23
3	Sulphur Dioxide as SO ₂	µg/m ³	18.5	080 (24 Hourly)	IS 5182 (Pt-02)
4	Oxides of Nitrogen as NO _x	µg/m ³	38.15	080 (24 Hourly)	IS 5182 (Pt-06)
5	Carbon Monoxide as CO	mg/m ³	0.51	002 (08 Hourly)	IS 5182 (Pt-10)

*****END OF REPORT*****

Analyzed By



TEST REPORT

Issued to

M/s Asthetic Township Developers Pvt. Ltd.
Apt. No. E-301, Unworld City, Sec-30
Gurgaon- 122002



Doc No. : ELPL/IV/QF/20
Amend. No. & Amend. Date : 02 & 17.02.2018
Lab Reference No. : 220211016 N
Issue Date : 17/02/2022
Your Reference : Email
(Page 1 of 1)

Sample Particulars: Ambient Noise Level Monitoring was done at Commercial Complex project at Sushant Lok, Sec- 27, Gurugram Haryana, on 10/02/2022 to 11/02/2022.

Type of sample	: Ambient Noise	Sample Registration Date	: 11/02/2022
Sampling Date	: 10/02/2022-11/02/2022	Analysis Starting Date	: 11/02/2022
Sampling Done by	: Lab representative	Analysis Completion Date	: 12/02/2022
Quantity received	: 24 Hourly Sample	Tests Required	: Mentioned below
Sample's Location	: Near Retail Area	Sampling Method	: ELPL/III/SOP/37

Time	Unit	Leq	Method
Day Time(06:00 am to 10:00 pm)	dB (A)	62.8	ELPL/III/SOP/37
Night Time(10:00 pm to 06:00 am)	dB (A)	43.0	ELPL/III/SOP/37

Standards for Ambient Noise As per Noise Pollution (Regulation & Control Rule-2000)			
Area Code	Category of Area/Zone	Limits in dB (A) Leq*	
		Day time	Night time
(A)	Industrial area	75	70
(B)	Commercial area	65	55
(C)	Residential area	55	45
(D)	Silence Zone	50	40

*****END OF REPORT*****

*Leq : It is energy mean of the noise level over a specified period.

Analyzed By

Authorized Signatory



Environmental Monitoring Report

1. Ambient Air Quality Monitoring

Ambient air quality monitoring has been done quarterly basis at locations AAQ-1 (Near Retail Area) for 24 Hrs. The detail of monitoring schedule is given in **Table-1**.

Table 1: Schedule of Ambient Air Quality Monitoring

S. No.	Duration of sampling (hours)	Date		Sample collected on	Location
		From	To		
1	24	10/02/2022	11/02/2022	11/02/2022	AAQ-1 (Near Retail Area)

Sulphur Dioxide (SO₂)

Monitoring results of SO₂ are given in **Table-1 (a)** and graphical representation is given in **Figure-1 (a)**

Table- 1(a): Monitoring results for SO₂

S. No.	Sampling dates	Location Code	Sampling duration	Results (µg/m ³)	NAAQS (as per CPCB), µg/m ³
1	10/02/2022 to 11/02/2022	AAQ - 1	24 Hourly	18.5	80

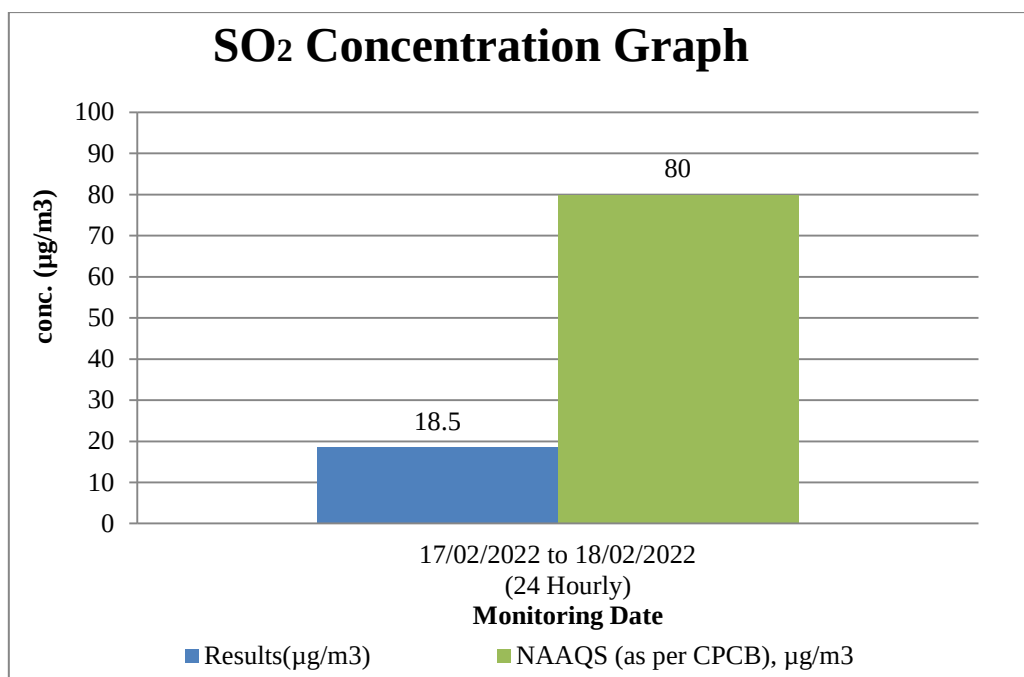


Figure-1(a): SO₂ concentrations at project site

The concentration of SO₂ was observed below permissible Limit as per NAAQS.

Nitrogen Dioxide (NO₂)

Monitoring results of NO₂ is given in **Table-1 (b)** and graphical representation is given in **Figure-1 (b)**

Table-1 (b) Monitoring results for NO₂

S. No.	Sampling dates	Location Code	Sampling duration	Results (µg/m ³)	NAAQS (as per CPCB), µg/m ³
1	10/02/2022 to 11/02/2022	AAQ - 1	24 Hourly	38.15	80

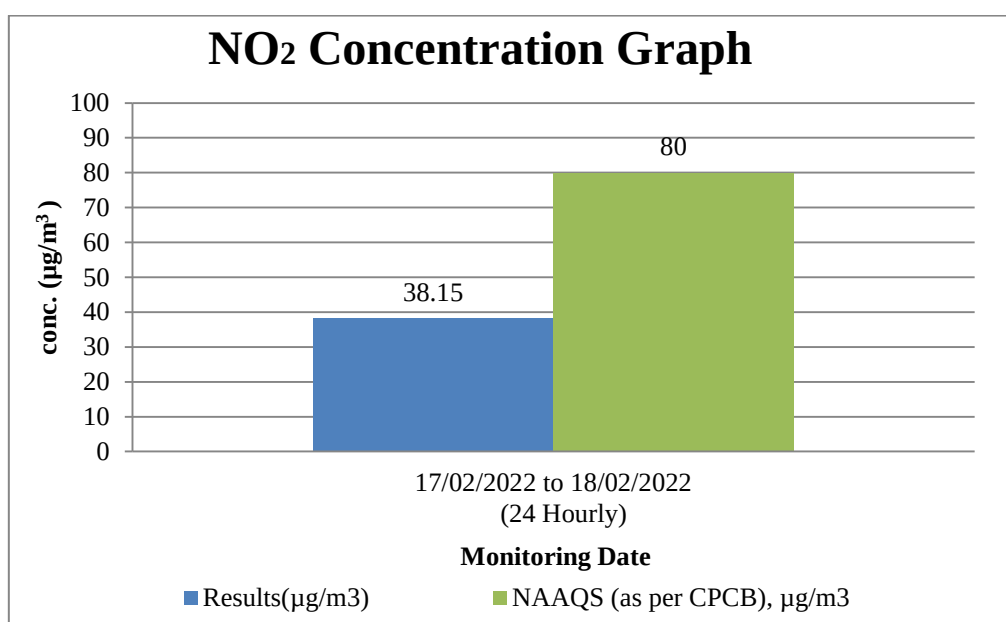


Figure 1 (b): NO₂ concentrations at project site

The concentration of NO₂ was below the limits as permissible limit as per NAAQS.

Particulate Matter

PM₁₀: Monitoring results of PM₁₀ is given in **Table- 1(c)** and graphical representation is given in **Figure- 1(c)**.

Table-1 (c) : Monitoring results for PM₁₀

S. No.	Sampling dates	Location Code	Sampling duration	Results (µg/m ³)	NAAQS (as per CPCB), µg/m ³
1	10/02/2022 to 11/02/2022	AAQ - 1	24 Hourly	252	100

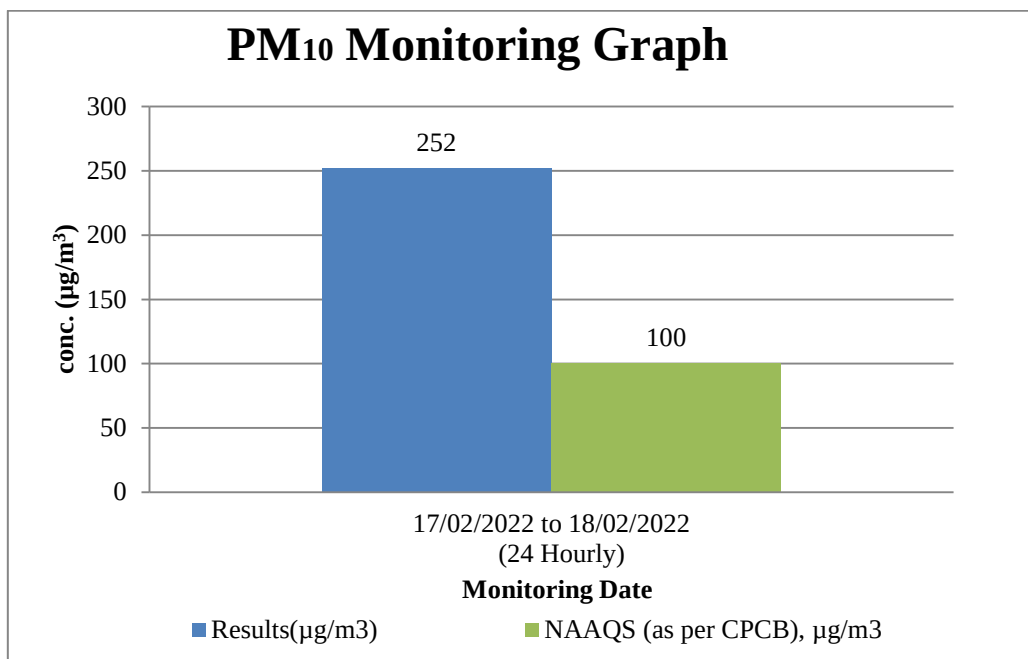


Figure 1 (c): PM₁₀ concentrations at project site

The concentration of PM₁₀ was found higher than permissible limit by NAAQS.

PM_{2.5}: Monitoring results of PM_{2.5} is given in **Table-1 (d)** and graphical representation is given in **Figure- 1 (d)**

Table 1 (d): Monitoring results for PM_{2.5}

S. No.	Sampling dates	Location Code	Sampling duration	Results (µg/m ³)	NAAQS (as per CPCB), µg/m ³
1	10/02/2022 to 11/02/2022	AAQ - 1	24 Hourly	172.9	60

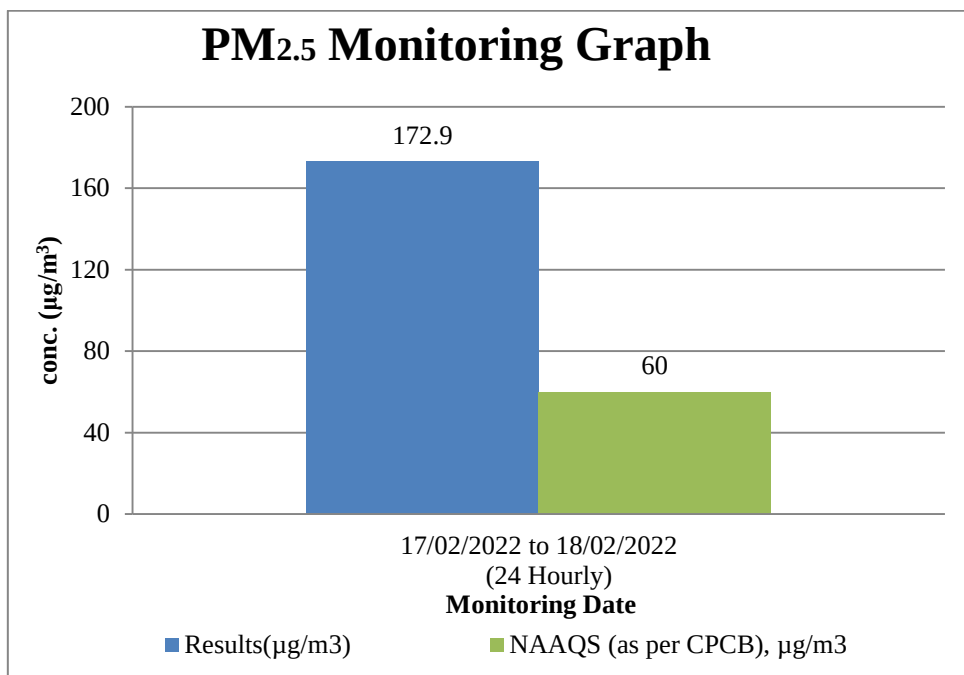


Figure 1 (d): PM_{2.5} concentrations at Project site

The concentration of PM_{2.5} was found to be higher than permissible limit by NAAQS.

Carbon MoNoxide (CO)

Monitoring results of CO is given in **Table-1(e)** and graphical representation is given in **Figure-1(e)**

Table -1 (e): Monitoring results for CO

S. No.	Sampling dates	Location Code	Sampling duration	Results (µg/m ³)	NAAQS (as per CPCB), µg/m ³
1	10/02/2022 to 11/02/2022	AAQ - 1	24 Hourly	0.51	002

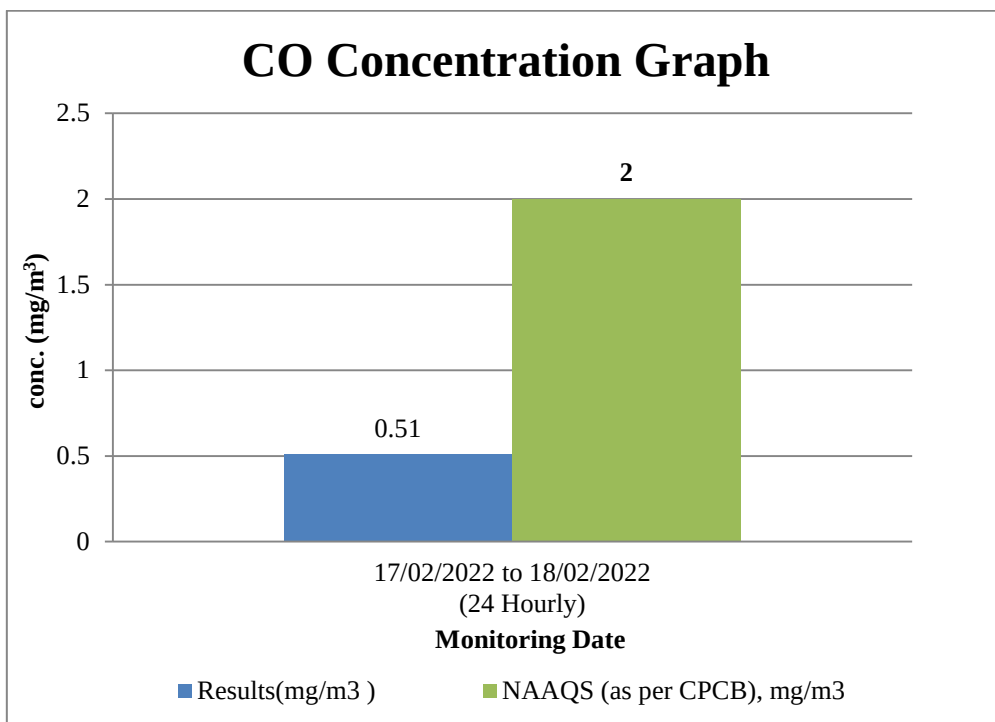


Figure 1 (e): CO concentrations at Project site

The concentration of CO was within the limit as prescribed by NAAQS.

2. Noise Monitoring

Noise monitoring was done quarterly basis at location ANQ-1 (Near Retail Area), for 24 Hrs. The details of monitoring are given in **Table-(2)**

Table (2): Schedule of Noise Monitoring

S. No.	Duration of sampling (hours)	Date		Sample collected on	Location
		From	To		
1	24	10/02/2022	11/02/2022	11/02/2022	ANQ-1 (Near Retail Area)

Monitoring has been done for 24 hours. The results for day time & night time observations are given below:

Day Time

Monitoring results of day time is given in **Table- 2 (a)** and graphical representation is given in **Figure- 2 (a)**

Table 2 (a): Day Time monitoring result

S. No.	Monitoring Locations	Duration of Monitoring	Results dB(A)	Permissible Limit dB(A) (as per CPCB)
1	ANQ - 1	Day time (6:00 AM to 10:00 PM)	62.8	65

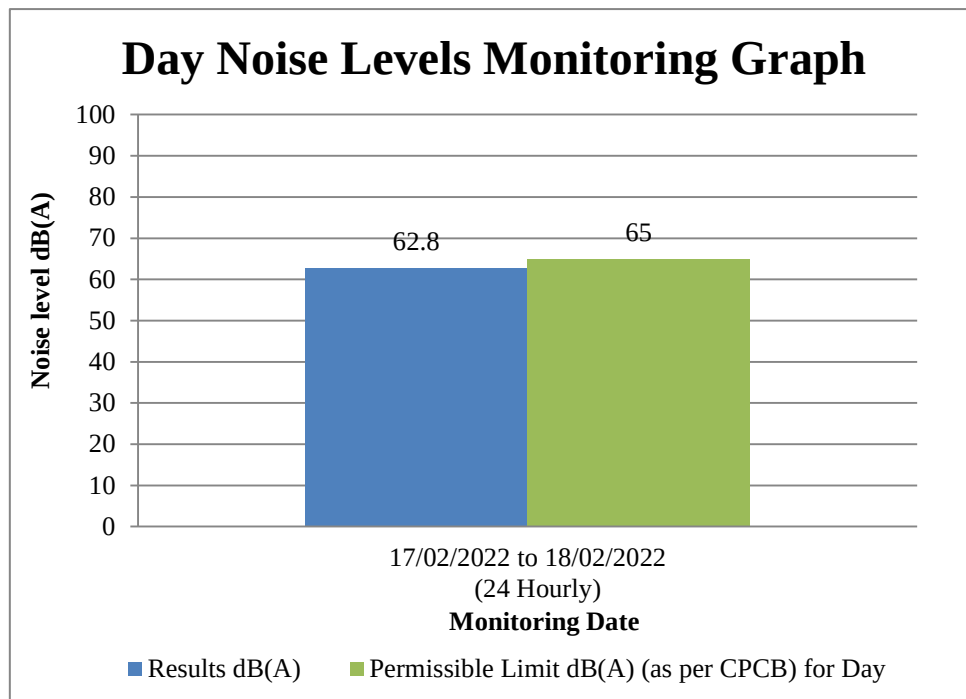


Figure 2 (a): Graph showing day time Noise monitoring result

The day Noise result was found to be within the limit as prescribed by NAAQS.

Night Time

Monitoring results of night time is given in **Table- 2 (b)** and graphical representation is given in **Figure-2 (b)**.

Table – 2 (b): Night Time monitoring result

S. No.	Monitoring Locations	Duration of Monitoring	Results dB(A)	Permissible Limit dB(A) (as per CPCB)
1	ANQ - 1	Night time (10:00 PM to 06:00AM)	43.0	55

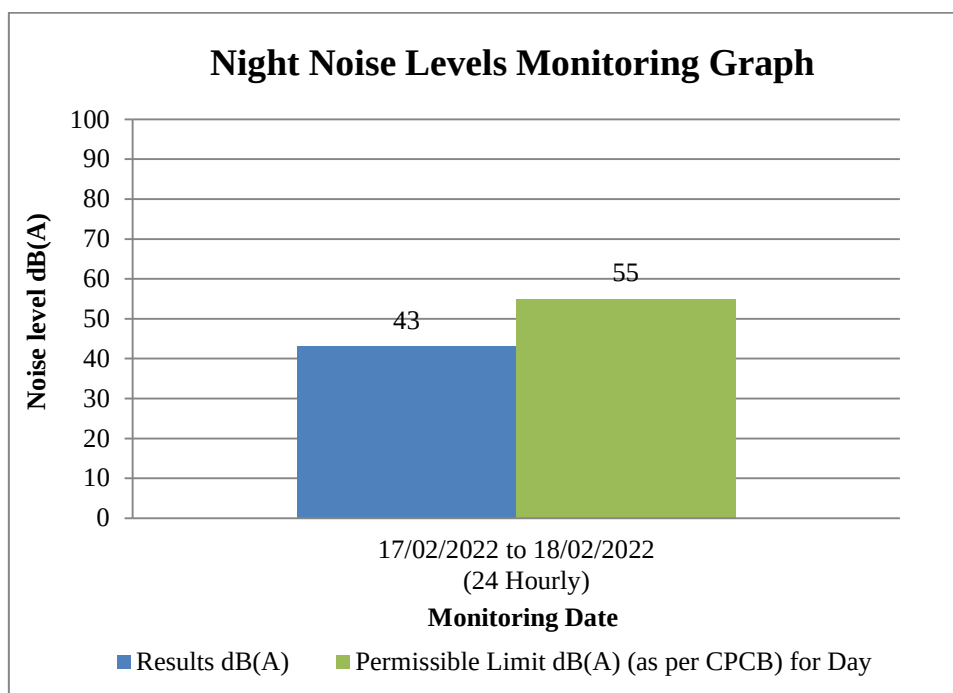


Figure 2 (b): Graph showing night time Noise monitoring result

The night Noise result was found to be within the limit as prescribed by NAAQS.

3. Drinking Water Monitoring

Schedule for Drinking water monitoring is given in **Table 3**.

Table 3: Schedule for Drinking water sample collection

Day of sampling	Sample collected on	Location
Day 1	10/02/2022	Main Gate Office

Drinking water for Day-1 monitoring results given in **Table 3(a)**.

Table 3(a): - Drinking Water Monitoring Results

S. No	Test Parameters	Units	Results	IS 10500 : 2012		Test Method
				Acceptable Limit, max.	Permissible Limit in the Absence of Alternate source, max.	
1	Color	Hazen	BDL (DL-5.0)	5	15	IS 3025 (Pt-04)
2	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Pt-05)
3	pH	-	7.32	6.5-8.5	No relaxation	IS 3025 (Pt-11)
4	Taste	-	Agreeable	Agreeable	Agreeable	IS 3025 (Pt-08)
5	Turbidity	NTU	BDL(DL-1.0)	1	5	IS 3025 (Pt-10)
6	Total Dissolved Solids	mg/l	372	500	2000	IS 3025 (Pt-16)
7	Ammonia (as total	mg/l	BDL (DL0.1)	0.5	No relaxation	IS 3025 (Pt-34)

**“Commercial Complex Project” located at Sushant Lok, Sec-27, Gurugram Haryana by
M/s Asthetic Township Developers Pvt. Ltd.**

	ammonia-N)					
8	Anionic Detergents (as MBAS)	mg/l	BDL (DL0.1)	0.2	1.0	Annex K of IS 13428
9	Calcium as Ca	mg/l	84.2	75	200	IS 3025 (Pt-40)
10	Chloramines (as Cl ₂)	mg/l	BDL(DL0.1)	4.0	No relaxation	IS 3025 (Pt-26)
11	Chloride as Cl	mg/l	73.4	250	1000	IS 3025 (Pt-32)
12	Fluoride as F	mg/l	0.22	1.0	1.5	APHA 23 rd Ed 4500F
13	Free Residual Chlorine	mg/l	BDL(DL0.05)	0.2	1	IS 3025 (Pt-26)
14	Nitrate as NO ₃	mg/l	1.68	45	No relaxation	IS 3025 (Pt-34)
15	Phenolic Compounds (as C ₆ H ₅ OH)	mg/l	BDL(DL 0.001)	0.001	0.002	IS 3025 (Pt-43)
16	Sulphate as SO ₄	mg/l	39.7	200	400	IS 3025 (Pt-24)
17	Sulphide (as H ₂ S)	mg/l	BDL(DL 0.02)	0.05	No relaxation	IS 3025 (Pt-29)
18	Total Alkalinity as CaCO ₃	mg/l	89.1	200	600	IS 3025 (Pt-23)
19	Total Hardness as CaCO ₃	mg/l	355	200	600	IS 3025 (Pt-21)
20	Cyanide (as CN)	mg/l	BDL(DL 0.02)	0.05	No relaxation	IS 3025 (Pt-27)
21	Aluminum (as Al)	mg/l	BDL(DL 0.01)	0.03	0.2	APHA 23 rd Ed.3120B
22	Barium (as Ba)	mg/l	BDL(DL 0.1)	0.7	No relaxation	APHA 23 rd Ed.3120B
23	Boron (as B)	mg/l	BDL (DL 0.1)	0.5	1.0	APHA 23 rd Ed.3120B
24	Copper (as Cu)	mg/l	BDL(DL 0.02)	0.05	1.5	APHA 23 rd Ed.3120B
25	Iron as Fe	mg/l	BDL(DL 0.05)	1.0	No relaxation	IS 3025 (Pt-02)
26	Magnesium as Mg	mg/l	35.2	30	100	APHA 23 rd Ed.3500B mg B
27	Manganese as Mn	mg/l	BDL(DL 0.05)	0.1	0.3	APHA 23 rd Ed.3120B
28	Selenium (as Se)	mg/l	BDL(DL 0.01)	0.01	No relaxation	APHA 23 rd Ed.3120B
29	Silver (as Ag)	mg/l	BDL(DL 0.05)	0.1	No relaxation	APHA 23 rd Ed.3120B
30	Zinc (as Zn)	mg/l	BDL(DL 0.05)	5	15	APHA 23 rd Ed.3120B
31	Cadmium (as Cd)	mg/l	BDL(DL 0.001)	0.003	No relaxation	APHA 23 rd Ed.3120B
32	Lead (as Pb)	mg/l	BDL(DL 0.005)	0.01	No relaxation	APHA 23 rd Ed.3120B
33	Mercury (as Hg)	mg/l	BDL(DL0.001)	0.001	No relaxation	APHA 23 rd Ed.3120B
34	Molybdenum (as MO)	mg/l	BDL(DL 0.05)	0.07	No relaxation	APHA 23 rd Ed.3120B
35	Nickel (as Ni)	mg/l	BDL(DL0.01)	0.02	No relaxation	APHA 23 rd Ed.3120B
36	Total Arsenic (as As)	mg/l	BDL(DL 0.01)	0.01	No relaxation	APHA

**“Commercial Complex Project” located at Sushant Lok, Sec-27, Gurugram Haryana by
M/s Asthetic Township Developers Pvt. Ltd.**

						23 rd Ed.3120B
37	Total Chromium (as Cr)	mg/l	BDL(DL 0.03)	0.05	No relaxation	APHA 23 rd Ed.3120B

4. Soil monitoring

Schedule for Soil monitoring are given in **Table 4**.

Table 4: Schedule for Soil sample collection

Day of sampling	Sample collected on	Locations
Day 1	10/02/2022	Project Site

Soil monitoring for Day-1 was monitored for Soil monitoring. The results are furnished in **Table-6(a)** below: -

Table 4(a): Results of Soil monitoring

S.No.	Test Parameters	Unit	Result	Test Method
1	pH (1:5)	-	8.72	IS 2720(P-26)
2	Conductivity (1:5)	µmhos/cm	362	USDA Method
3	Color	-	Brown	USDA Method
4.	Texture		Sandy Clay Loam	USDA Method
	Silt	%	11	
	Clay	%	39	
	Sand	%	50	
5	Sodium Absorption Ratio	-	1.06	USDA Method
6	Cation Exchange Capacity	Meq/100gm	22.2	IS 2720(P-24)
7	Porosity	%	44.8	USDA Method
8	Water Holding Capacity	%	46.2	USDA Method
9	Bulk Density	gm/cc	1.11	USDA Method
10	Chloride as Cl	mg/kg	195.4	USDA Method
11	Calcium as Ca	mg/kg	3561.4	USDA Method
12	Sodium as Na	mg/kg	250	USDA Method
13	Potassium as K	mg/kg	100	USDA Method
14	Magnesium as Mg	mg/kg	388.2	USDA Method
15	Organic matter	%	0.69	IS 2720(P-22)
16	Available Nitrogen	mg/kg	122	USDA Method
17	Phosphorous	mg/kg	98	USDA Method

Annexure-XI
Landscape plan

LEAV

ISO 9001:2008
Architecture
Management
Planning

T: +91 11 24622195
+91 11 24646709
F: +91 11 24634069




LEGEND			TREE LIST			
SPEC.	SYMBOL	DESCRIPTION	AREA (SQM)	SPEC. SYMBO.	DESCRIPTION	QUANTITY
1		3-R-100 H+CH	0,01	1	DOUGLAS RESIN	4
2		LAJUN H+CH	197,21	2	CASIA RETILLA	32
3		PLANTER COCO	5,68	3	CASIA JAMAICA	17
4		PROTECTOR COCO	660,79	4	PL. ALEREA	34
TOTAL GREEN AREA REPOSED			868,69	5	TERMINALIA	81
TOTAL GREEN AREA PLANT			10,01	6	ACACIA	18
4		GRASS PAPER	103,5	6	ACACIA	18
5		WATER BONES	70,00			
TOTAL AREA OF PLANT (100 M ² MIN)						
GROUPED FLOOR BUILDING AREA: 100 M ²						
TOTAL GREEN AREA: 878,70 M ²						
TOTAL GREEN AREA PLANT: 10,01 M ²						
TOTAL GREEN AREA (100 M ² MIN): 888,71 M ²						
TOTAL NO. OF TREES						189
• 1320 ALEREA (20% - 0204/4)						
• 2568 ACACIA						

Annexure-XII

**Photographs showing Excavated top
soil is preserved**

Photographs showing Excavated Top Soil

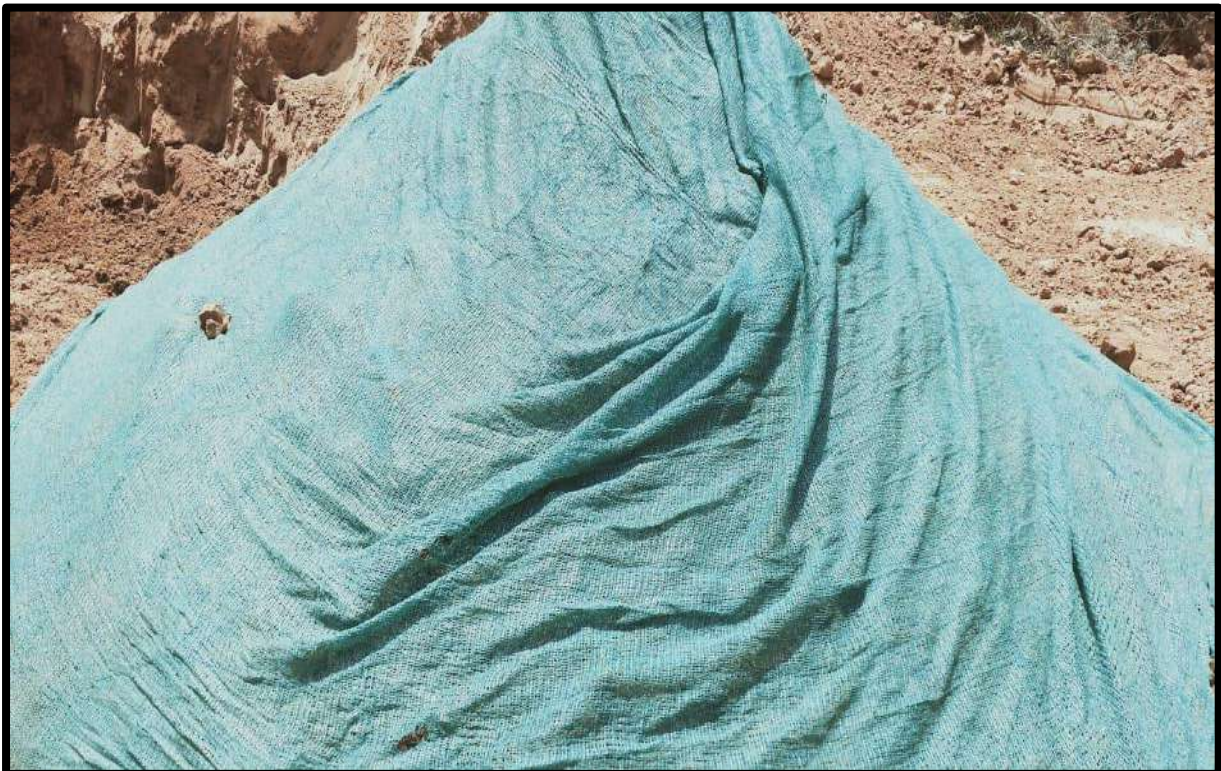

Annexure-XIII
PUC Certificate

Form 59

[See rules 115 (2)]

Pollution Under Control Certificate

Authorised By :
Government of HaryanaDate : 27/01/2022
Time : 11:39:38 AM
Valid upto : 26/07/2022

State SL. No. : HR05502520001117
Registration No. : HR87B4113
Date of Registration : 13/Jul/2018
Valid upto : June-2018
Pollutant : *****0226
Vehicle : Bharat (Trem) Stage III
Fuel : DIESEL
Engine No. : HR0550252
Cost : Rs.100.00(GST as applicable)
Remarks : No



Registration plate

HR87B
4113

Pollutant (as applicable)	Units (as applicable)	Emission limits	Measured Value (upto 2 decimal places)
2	3	4	5
Carbon Monoxide (CO)	percentage (%)		
Hydrocarbon, (THC/HC)	ppm		
CO	percentage (%)		
RPM	RPM	2500 ± 200	
		1 ± 0.03	
	1/metre	2.45	1.29

This PUC certificate is system generated through the national register of motor vehicles and does not require any signature.

Note : 1. Vehicle owners to link their mobile numbers to registered vehicle by logging to <https://vahan.parivahan.gov.in>

Authorised Signature with stamp of PUC operator
60mm x 20 mm



Annexure-XIV

**Environment Management and
Monitoring Plan**

ENVIRONMENT MANAGEMENT PLAN AND ENVIRONMENT MONITORING PLAN

ENVIRONMENT MANAGEMENT PLAN

The Environment Management Plan (EMP) would consist of all mitigation measures for each component of the environment due to the activities increased during the construction, operation and the entire life cycle to minimize adverse environmental impacts resulting from the activities of the project. It would also delineate the environmental monitoring plan for compliance of various environmental regulations. It will state the steps to be taken in case of emergency such as accidents at the sites including fire. The detailed EMP for the complex is given below.

Environmental Management Plan

The Environment Management Plan (EMP) is a site specific plan developed to ensure that the project is implemented in an environmental sustainable manner where all contractors and subcontractors, including consultants, understand the potential environmental risks arising from the project and take appropriate actions to properly manage that risk. EMP also ensures that the project implementation is carried out in accordance with the design by taking appropriate mitigation actions to reduce adverse environmental impacts during its life cycle. The plan outlines existing and potential problems that may adversely impact the environment and recommends corrective measures where required. Also, the plan outlines roles and responsibility of the key personnel and contractors who will be in-charge of the responsibilities to manage the project site.

The EMP is generally

- Prepared in accordance with rules and requirements of the MoEF and CPCB/ SPCB
- To ensure that the component of facility are operated in accordance with the design
- A process that confirms proper operation through supervision and monitoring
- A system that addresses public complaints during construction and operation of the facilities and
- A plan that ensures remedial measures is implemented immediately.

The key benefits of the EMP are that it offers means of managing its environmental performance thereby allowing it to contribute to improved environmental quality. The other benefits include cost control and improved relations with the stakeholders.

EMP includes four major elements :

- **Commitment & Policy:** The management will strive to provide and implement the Environmental Management Plan that incorporates all issues related to air, water, land and noise.
- **Planning:** This includes identification of environmental impacts, legal requirements and setting environmental objectives.
- **Implementation:** This comprises of resources available to the developers, accountability of contractors, training of operational staff associated with environmental control facilities and documentation of measures to be taken.
- **Measurement & Evaluation:** This includes monitoring, counteractive actions and record keeping.

It is suggested that as part of the EMP, a monitoring committee would be formed by M/s Aesthetic Township Developers Pvt. Ltd., comprising of the site in-charge/coordinator, environmental group representative and project implementation team representative. The committee's role would be to ensure proper operation and management of the EMP including the regulatory compliance.

The components of the environmental management plan, potential impacts arising, out of the project and remediation measures are summarized below in **Table 1** and EMP for dust suppression is mentioned in **Table 2**.

TABLE 1: SUMMARY OF POTENTIAL IMPACTS AND REMEDIAL MEASURES

S. No.	Environmental components	Potential Impacts	Potential Source of Impact	Controls Through EMP & Design	Impact Evaluation	Preventive Measures
1.	Ground Water Quality	Ground Water Contamination	<u>Construction Phase</u> Sewage generated from temporary labor tents.	Mobile STP and treated sewage will be used for construction purposes.	No significant impact as majority of labors would be locally deployed	--
			<u>Operation Phase</u> Sewage Discharge from the project	Proponent will provide the STP to treat the sewage of Project.	No negative impact on ground water quality envisaged. Not significant.	In an unlikely event of soil and ground water contamination. Remediation measures will be implemented.
2.	Ground Water Quantity	Ground Water Depletion	<u>Construction Phase</u> Ground water will be not be used during construction.	Not Applicable	No significant impact on ground water quantity envisaged.	
			<u>Operation Phase</u> Groundwater will not during operation phase. The required water will be met through the municipal supply	- Rain water harvesting scheme. - Black and Grey water treatment and reuse. - Storm water collection for water harvesting. - Percolation well to be introduced in landscape plan. - Awareness Campaign to	No significant impact on surface/ground water quantity envisaged.	In an unlikely event of non-availability of water supply, water will be brought using tankers.

S. No.	Environmental components	Potential Impacts	Potential Source of Impact	Controls Through EMP & Design	Impact Evaluation	Preventive Measures
				reduce the water consumption		
3.	Surface Water Quality	Surface water contamination	<u>Construction Phase</u> Surface runoff from site during construction activity.	Silt traps and other measures such as additional onsite diversion ditches will be constructed to control surface run-off during site development	No off-site impact envisaged as no surface water receiving body is present in the core zone.	--
			<u>Operation Phase</u> Discharge of domestic wastewater to STP.	Domestic water will be treated in STP	No off-site impact envisaged	Excess of water will be discharged as per CPCB standards.
4.	Air Quality	Dust Emissions	<u>Construction Phase</u> All heavy construction activities	Suitable control measures will be adopted for subsiding the PM level in the air as per air pollution control plan.	Not significant because dust generation will be temporary and will settle fast due to dust suppression techniques (wet scrubbers) used.	During construction phase the contractors are advised to facilitate masks for the labors. Water sprinklers will be used for suppression of dust during construction phase.
		Emissions of SPM, SO ₂ , NO ₂ and CO	<u>Construction Phase</u> Operation of construction	On-site construction and improved maintenance of equipment	Not significant.	Regular monitoring of emissions and control measures will be taken

S. No.	Environmental components	Potential Impacts	Potential Source of Impact	Controls Through EMP & Design	Impact Evaluation	Preventive Measures
			equipment and vehicles during site development. • Running D.G. sets (back up)			to reduce the emission levels.
			<u>Operation Phase</u> • Power generation by DG Sets during power failure • Emission from vehicular traffic in use <u>Construction Phase</u> • Operation of construction equipment and vehicle movements during site development. • Running DG sets (for power back up)	• Use of Low Sulphur diesel if available • Use of clean fuel if available • Green belt will be developed with specific species to help to reduce PM level • Use of equipment fitted with silencers • Proper maintenance of equipment • Provision of noise shields near the heavy construction operations and acoustic enclosures for DG sets Construction activity will be limited to day time hours only	Not significant	Regular monitoring of emissions and control measures will be taken to reduce the emission levels.

S. No.	Environmental components	Potential Impacts	Potential Source of Impact	Controls Through EMP & Design	Impact Evaluation	Preventive Measures
5.	Noise Environment		<u>Operation Phase</u> - Noise from vehicular movement - Noise from DG sets operation	Green Belt Development shall make a barrier both for noise and air pollution.	No significant impact due to 10m. width of Greenbelt.	Use of Personal Protective Equipment (PPE) like earmuffs and earplugs during construction activities
6.	Land Environment	Soil contamination	<u>Construction Phase</u> Disposal of construction debris	Construction debris will be collected and suitably used on site.	No significant impact. Impact will be local, as waste generated will be reused for filling of low lying areas etc.	--
			<u>Operation Phase</u> Dumping of municipal solid waste on land.	It is proposed that the solid waste generated will be managed by an authorized agency. Collection, segregation, transportation and disposal will be done as per Solid Waste Management Rules, 2016 by the authorized agency Organic waste converter	Since solid waste is handled by the authorized agency, waste dumping is not going to be allowed. Not significant. Negligible impact.	--

S. No.	Environmental components	Potential Impacts	Potential Source of Impact	Controls Through EMP & Design	Impact Evaluation	Preventive Measures
				will be installed.		
7.	Biological Environment (Flora and Fauna)	Displacement of Flora and Fauna on site	<u>Construction Phase</u> Site Development during construction No tree at the site.	Additional tree will be planted as part of the green belt development.	The site has no tree.	
			<u>Operation Phase</u> Increase in green cover	Green belts will be developed as per landscaping plan in and around the site using local flora	Beneficial impact.	
8.	Socio-Economic Environment	Employment and livelihood options.	<u>Construction Phase</u> Construction activities leading to gain in direct & indirect employment	Project development as per the Building bye laws.	No negative impact. 400 employment will be generated.	
			<u>Operation Phase</u>	Project will provide employment opportunities to the local people in terms of labor during	Beneficial impact	

S. No.	Environmental components	Potential Impacts	Potential Source of Impact	Controls Through EMP & Design	Impact Evaluation	Preventive Measures
			Site operation	construction and service personnel (staff, securities, gardeners etc.) during operations • Providing quality-Integrated facility in Ghaziabad		
9.	Traffic Pattern	Increase of Vehicular traffic	<u>Operation Phase</u> Site operation	Internal Traffic management plan	Beneficial impact	
			<u>Operation Phase</u> • Traffic due to people.	• Vehicular movement will be regulated inside the project with adequate roads and parking lots in the site.	No major significant impact	

TABLE 2: EMP FOR DUST SUPPRESSION

Sources/Process	Emission Potential	Scope of Control	Effectiveness
Hydraulic excavators and loaders (e.g. Front loader, backhoe face shovel bulldozers) for the excavation, lifting and movement of material such as Soil, overburden.	High when dry or fine silty material are being handled, particularly during strong windy weather	Use of water sprays to moisten material being handled. Soils may be subject to a soil moisture content planning condition	Moderate
	Low when coarse or wet material are being handled during conditions of low wind speed	Minimize drop heights when unloading material. Protect from exposure to wind where possible.	
Tractor scrapers (Soil strippers) for cutting, lifting transporting and placing, spreading or shaping of soils	Moderate/High-when dry silty materials handled during windy weather	Use of water sprays to moisten material being handled.	Low
Vehicles for transport of material within the site.	High particularly when travelling over unsurfaced and dry site roads.	Minimize onsite transportation distances.	High
		Use of water sprays to moisten road surfaces during dry weather.	
		Use mechanical road sweepers during dry weather, to limit visible dust emissions. Restrict vehicle speeds through signage/staff training.	
		Use of covered conveyors to transport material around the site.	
Hydraulic breakers for size reduction of large rocks	Low	Water spraying of rock prior to fragmentation when high degree of control required.	Moderate
Exhausts and cooling fans on mobile plant	High if unmitigated.	Mobile plant exhausts and cooling fans will discharge	Moderate

Sources/Process	Emission Potential	Scope of Control	Effectiveness
processing quarried material.		above the horizontal to prevent dust mobilization.	
Conveyors for transporting material	Moderate if not protected from wind	Enclosure of transfer points (including roofing) of conveyors.	High
		Wind boarding.	High
	Moderate/High for dry or fine silty materials, particularly during strong wind weather	Water spraying of surfaces of material on conveyor.	High/Moderate
		Cleaning belts with scrapers and collecting scrapings in container.	Moderate
Stockpiles for storage of quarried materials and soil/overburden during extraction and site development phases.	High when dry or fine silty materials are being stored /handled particularly during strong weather.	Seed surfaces of completed mounds of overburden and top soil (restoration materials).	High
		Limit mechanical disturbance.	
		Shield from wind e.g. through the use of tree planting or screening	
		Use of water sprays to moisten surfaces during dry weather.	Moderate

ENVIRONMENTAL MONITORING

The purpose of environmental monitoring is to evaluate the effectiveness of implementation of Environmental Management Plan (EMP) by periodic monitoring. The important environmental parameters within the impact area are selected so that any adverse affects are detected and time action can be taken. The project proponent will monitor ambient air Quality, Ground Water Quality and Quantity, and Soil Quality in accordance with an approved monitoring schedule mentioned in **Table 3**.

Table 3: Environmental Monitoring Schedule for Compliance

S. No	Particulars	Monitoring Frequency	Duration of Sampling	Important Monitoring Parameters
1	Ambient Air Quality Monitoring			
	Project site	Once in 6 Months	24 hr continuously except CO (8 hourly)	PM ₁₀ , PM _{2.5} , SO ₂ , NO ₂ & CO
3	Ambient Noise Level			
	Near DG set	Once in 6 Months	8 hr continuous with 1 hr interval	Noise level in dB(A)
4	Ground/Drinking Water Quality Monitoring			
	Ground Water – (If applicable)	Once in 6 Months	Grab Sampling	Parameters specified under IS:10500, 2012
5	Soil Quality			
	At the green belt area	Twice in a year	Samples will be collected from three different depths viz., 30cm, 60cm, and 100cm below the surface	Parameter for soil quality: pH, texture, electrical conductivity, organic matter, nitrogen, phosphate, sodium, calcium, potassium and Magnesium.

Annexure-XV

Receiving of Previous Compliance Report of Dec, 2021

ASTHETIC TOWNSHIP DEVELOPERS PRIVATE LIMITED

Reg. Office- 262, DDA OFFICE COMPLEX, JHANDEWALA EXT., NEW DELHI - 110055

Ref. No. APL/P/21/040

Date: 15 Nov 2021

To,
The Director,
Northern Regional Office (MoEF&CC),
Bays No. 24 -25, Sector- 31-A,
Dakshin Marg,
Chandigarh - 160030

Subject: Submission of six-monthly Compliance Report for December 2021 of the Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana by M/s. Asthetic Township Developers Pvt. Ltd.

Reference: F.No.21-137 /2018-IA-111, Dated: 07/02/2019

Respected Sir,

This is with reference to above-mentioned subject, we are herewith submitting six monthly compliance report of **December 2021** for the period of **April 2021 – September 2021** for the Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana by M/s. Asthetic Township Developers Pvt. Ltd. along with the necessary annexure for your kind perusal.

We understand that the above is in line with requirement of Ministry of Environment & Forest and Climate Change, GOI.

Thanking You,

Yours Sincerely,



For M/s. Asthetic Township Developers Pvt. Ltd.

Mukesh Gour

(Authorized Signatory)

भारत सरकार / Govt. of India
पर्यावरण, वायु एवं जलवायु परिवर्तन मंत्रालय
Min. of Environment, Forests & Climate Change
बेय नं. 24-25, सेक्टर 31-ए
Bays No. 24-25, Sec-31 A
चण्डीगढ़/Chandigarh

29/11/2021

Enclosure: Compliance Report; Soft copy of Report in C.D

- Copy to:** 1. Member Secretary, Haryana State Pollution Control Board, C-11 Sec-6, Panchkula, Haryana
2. The Chairman, State Environmental Impact Assessment Authority, Bays No. 55 - 58, 1st Floor, Paryatan Bhawan, Sector 2, Panchkula, Haryana

CIN NO. U45201DL2006PTC147126

Email: asthetic64@gmail.com

ASTHETIC TOWNSHIP DEVELOPERS PRIVATE LIMITED

Reg. Office- 262, DDA OFFICE COMPLEX, JHANDEWALA EXT., NEW DELHI - 110055

Ref. No. APL/P/21/040

Date: 15 Nov 2021

To,
The Director,
Northern Regional Office (MoEF&CC),
Bays No. 24 -25, Sector- 31-A,
Dakshin Marg,
Chandigarh - 160030

Subject: Submission of six-monthly Compliance Report for December 2021 of the Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana by M/s. Asthetic Township Developers Pvt. Ltd.

Reference: F.No.21-137 /2018-IA-111, Dated: 07/02/2019

Respected Sir,

This is with reference to above-mentioned subject, we are herewith submitting six monthly compliance report of **December 2021** for the period of **April 2021 – September 2021** for the Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana by M/s. Asthetic Township Developers Pvt. Ltd. along with the necessary annexure for your kind perusal.

We understand that the above is in line with requirement of Ministry of Environment & Forest and Climate Change, GOI.

Thanking You,

Yours Sincerely,



For M/s. Asthetic Township Developers Pvt. Ltd.
Mukesh Gour
(Authorized Signatory)

Enclosure: Compliance Report; Soft copy of Report in C.D

Copy to; 1. Member Secretary, Haryana State Pollution Control Board, C-11 Sec-6,
Panchkula, Haryana
2. The Chairman, State Environmental Impact Assessment Authority, Bays No.
55 - 58, 1st Floor, Paryatan Bhawan, Sector 2, Panchkula, Haryana

CIN NO. U45201DL2006PTC147126
Email: asthetic64@gmail.com

29/11/21
Haryana State Pollution Control Board
C-11, Sector-6, Panchkula

ASTHETIC TOWNSHIP DEVELOPERS PRIVATE LIMITED

Reg. Office- 262, DDA OFFICE COMPLEX, JHANDEWALA EXT., NEW DELHI - 110055

Ref. No. APL/P/21/040

Date: 15 Nov 2021

29/11/2021

To,
The Director,
Northern Regional Office (MoEF&CC),
Bays No. 24 -25, Sector- 31-A,
Dakshin Marg,
Chandigarh - 160030

Subject: Submission of six-monthly Compliance Report for December 2021 of the Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana by M/s. Asthetic Township Developers Pvt. Ltd.

Reference: F.No.21-137 /2018-IA-111, Dated: 07/02/2019

Respected Sir,

This is with reference to above-mentioned subject, we are herewith submitting six monthly compliance report of **December 2021** for the period of **April 2021 – September 2021** for the Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana by M/s. Asthetic Township Developers Pvt. Ltd. along with the necessary annexure for your kind perusal.

We understand that the above is in line with requirement of Ministry of Environment & Forest and Climate Change, GOI.

Thanking You,

Yours Sincerely,



For M/s. Asthetic Township Developers Pvt. Ltd.
Mukesh Gour
(Authorized Signatory)



Enclosure: Compliance Report; Soft copy of Report in C.D

Copy to: 1. Member Secretary, Haryana State Pollution Control Board, C-11 Sec-6, Panchkula, Haryana
2. The Chairman, State Environmental Impact Assessment Authority, Bays No. 55 - 58, 1st Floor, Paryatan Bhawan, Sector 2, Panchkula, Haryana

CIN NO. U45201DL2006PTC147126

Email: asthetic64@gmail.com

ASTHETIC TOWNSHIP DEVELOPERS PRIVATE LIMITED

Reg. Office- 262, DDA OFFICE COMPLEX, JHANDEWALA EXT., NEW DELHI - 110055

Ref. No. APL/P/21/040

Date: 15 Nov 2021

To,
The Director,
Northern Regional Office (MoEF&CC),
Bays No. 24 -25, Sector- 31-A,
Dakshin Marg,
Chandigarh - 160030

Subject: Submission of six-monthly Compliance Report for December 2021 of the Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana by M/s. Asthetic Township Developers Pvt. Ltd.

Reference: F.No.21-137 /2018-IA-111, Dated: 07/02/2019

Respected Sir,

This is with reference to above-mentioned subject, we are herewith submitting six monthly compliance report of **December 2021** for the period of **April 2021 – September 2021** for the Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana by M/s. Asthetic Township Developers Pvt. Ltd. along with the necessary annexure for your kind perusal.

We understand that the above is in line with requirement of Ministry of Environment & Forest and Climate Change, GOI.

Thanking You,

Yours Sincerely,



For M/s. Asthetic Township Developers Pvt. Ltd.
Mukesh Gour
(Authorized Signatory)

Handwritten signature and date: 30/11/21

Enclosure: Compliance Report; Soft copy of Report in C.D

Copy to: 1. Member Secretary, Haryana State Pollution Control Board, C-11 Sec-6,
Panchkula, Haryana

2. The Chairman, State Environmental Impact Assessment Authority, Bays No.
55 - 58, 1st Floor, Paryatan Bhawan, Sector 2, Panchkula, Haryana

✓ 3. The Regional office, Region Gurugram (North) Vikas Sadan, 1st floor North Court
Gurgaon 124.

CIN NO. U45201DL2006PTC147126

Email: asthetic64@gmail.com

Annexure-XVI
RMC Purchase Bill

--

<



TAX INVOICE
RDC CONCRETE (INDIA) PRIVATE LIMITED
Village Behrampur, Sector 59, Sector 59, Gurgaon, Dist-Gurgaon
HR, PIN - 122011



Phone : 6239317406 Email-Id : customercare@rdcconcrete.com
GSTIN : 06AAACU0108Q1ZC PAN : AAACU0108Q CIN : U74999MH1993PTC172842 TAN : MUMR22552F

Bill To Party		Ship To Party	
Party Name :	S.S. Construction Co (Bharti Reality) RAMKRISHAN HOUSE, NEAR MLA TEJPAL TANWAR KOTHI,VILL. RAMGARII PO BADSHAPUR GURGAON,HARYANA 122101 06AEFPS1460P1Z3	Party Name :	S.S. Construction Co (Bharti Reality) Site Bharti reality C/O Asthetic Township Developers Pvt Ltd Near IFFCO Chowk Metro Station, Sec- 27 GURGAON,HARYANA122002 06AEFPS1460P1Z3
Address :		Address :	
GSTIN :		GSTIN :	
PAN :		PAN :	
Invoice Number :	1GU21ARS15298	Terms of Payment :	60 Days
Invoice Date :	31-03-2022	Transport Mode :	By Road LUT No:
State :	HARYANA	State :	HARYANA Code: 06
State Code :	06	Vehicle No :	PB65AU6245
DC No :	1GU21ARS15298	Place of Supply :	GURGAON
DC Date :	31-03-2022 13:47:59	Date of Supply :	31-03-2022
Sales Order :	100621600724	PO No:	SSC/Bharti/WO-101/03/22
		IRN :	4a3a9b2ba7b896aa6c0eca9830aaaaaab6ad36c6f29bc 40cf2ec5b35b122823 132212170899201
Whether tax is payable on reverse charge basis: No		Ackno.Number :	2022-03-31 13:49:00
		Ackno. Date :	

Sl. No	Description of Goods	HSN Code	UOM	Qty	Unit Price	Basic Amount	CGST %	CGST Amount	SGST %	SGST Amount	IGST %	IGST Amount	Gross Amount (Without TCS)
1	M10	38245010	CUM	7	3975	27825.00	9	2504.25	9	2504.25		0	32833.50

TCS % : 0.100 TCS Amount : 32.83 KFC% : KFC Amount : 0.00 Grand Total 32866.33

Net Value in Rupees : Rupees Thirty Two Thousand Eight Hundred Sixty Six and paise Thirty Three Note: 1M3=2400Kgs +/-5%

Cementitious Type	Max. Agg Size	Admixture type	Slump	Min. Cementitious Content
OPC+PFA	20mm	PCEA	Slump: 130 +/- 50 mm	

Batch No:	GU1/2021/12371	Quantity with this load (Cubic Meter)	Cumulative Quantity (Cubic Meter)
Order Quantity (Cubic Meter)	100	7	63

Pouring Location / Structure :	Time of arrival on site:
Whether this concrete is pumped by RDC concrete: Yes/No	Admixture added at site:
Time discharged completed:	Water added at site:
Time released from site:	

Remarks:
Please Note: This concrete delivery is subject to the terms and a condition of sales shown in our quotation. The time is allowed for updating this delivery is 15 minutes. We reserve the right to charge for any detention beyond this time as per our quotation. Any unauthorized addition of water and/or any other material to concrete shall absolve us from any liability whatsoever. Any deficiency in methods of placing, compacting, finishing and curing of concrete adopted at site may affect quality of concrete in the finished work, for which we shall not be held liable and responsible. Any disputes that arise on quantity and quality (except comp. strength) of concrete supplied in this load shall be reported to us in writing within 24 hours from the time of supply. In no event shall we be liable for direct, indirect, incidental or consequential damage arising out of use of this product, even if advised of possibility of such damage. In no case shall our liability exceed the purchase price of this product.
24% interest per annum will be charged from the date of invoice on the amount remaining party or wholly unpaid after due date.
*This document also constitutes as a Delivery Challan.
I hereby confirm that:
1. I/We have accepted delivery of concrete as per the details mentioned above. 2. I/We have authorized addition of any water and for admixture as mentioned above.



Certified that the particulars given above are true and correct and amount indicated represents the price charged and that there is no flow of additional consideration directly or indirectly from the buyer

[Signature]

For RDC Concrete (India) Pvt Ltd.

[Signature]

Authorised Signatory

Caution: Cement and concrete contain lime and other chemicals which can cause irritation, dermatitis and burning. To avoid harm to skin, minimize contact with wet concrete and wear suitable protective clothing. Whenever contact occur (whether directly or through saturated clothing) wash thoroughly.


Receiver Signature & Seal

ASTHETIC TOWNSHIP DEVELOPERS PVT. LTD.
Gate Entry No. 9912
Date 31.03.22
Time 14:35
Vehicle No. PB65AU6245
Received By. *[Signature]*

DUPLICATE FOR TRANSPORTER

NUVOCO VISTAS CORP. LTD.

Name of the Plant: RP-GURGAON-I, DELHI / 4336
 Address of the Plant: PLOT NO./KH.NO.-1527/916/2/2,1528/916/2/3,REVENUE
 ESTATE VILLAGE,
 GURGAON 06-HARYANA 122001
 PAN No. :AAACL4159L
 GSTIN. :06AAACL4159L1ZC
 CIN :L26940MH1999PLC118229
 IRN : 590530e1bc54c9d176385d83dec67534adfec7d18ab24b320c235b7b752685d3
 Principal P.O.B :CHIDIYA, CHARKHI DADRI, BHIWANI, 06-HARYANA - 123306.
 CIN



TAX INVOICE

Tax Invoice Number :210710059712
 Date & Time :02.03.2022 17:09:00
 Dispatch Mode :BY ROAD
 Receipt Voucher No.
 Receipt Voucher Date
 Reverse Charge

Sales Type :FOR - FREE ON ROAD
 Sales Order No. :0130240957/SO/4336
 Customer PO / DATE :02/22/89//07.02.2022
 Name of Transporter
 Reference Number :2107055740
 Ewaybill Number :391419238512

Customer Code :50000947
 Name of Customer :S.S. CONSTRUCTION CO.
 Address of Customer :SATISH SURI
 :RAMKRISHAN HOUSE, NEAR MLA TEJPAL
 TANWAR KOTHI VILL
 PO BADSHAPUR GURGAON 06-HARYANA
 122101

Job Site Code :0021845913
 Name of Job Site :BHARTI REALTY
 State Code :06
 Address of Job Site :ASTHETIC TOWNSHIP DEVELOPER
 P.LTD NR.IFFCO CHOWK
 SEC-27, GURUGRAM GURUGRAM
 06-HARYANA 122002

BCMIX No. :433691573806

State Code :06
 PAN No. :AEFPS1460P

EMAIL ID. :vishalgupta@gmail.com

GSTIN No. :06AEFPS1460P1Z3
 Contact Name :VIPIN CHAUHAN
 Telephone Number :9719919797
 Mobile Number :9719919797
 Email ID :suriconstructions@yahoo.com
 Pump Serial No. :

Name of Product :RMC HSN/SAC :38245010

Exemption Notification if any

Sales Person's Name :
 Sales Person's Contact No. :

POURING LOCATION :Walls/Columns/Slab/Foundation/Other

Sl. No	Description	Vehicle No.	Qty.	UOM	Grade	Delivery Type	Material Code	Old Mat. Code
1	M30 SP AE MO D20 M	HR56B3199	6.000	M3	M30	JustDelivery	9000030409	CCMGFE2BH30C

Elements	Rate	Amount
Basic Price/Taxable Value	5,050.00	30,300.00
SGST @ 9 %	454.50	2,727.00
CGST @ 9 %	454.50	2,727.00
Rounding		0.00
Total Gross Value of Goods - In Figures	5,959.00	35,754.00

Total Gross Value of Goods - In Words THIRTY FIVE THOUSAND SEVEN HUNDRED FIFTY FOUR RUPEES ONLY

ASTHETIC TOWNSHIP DEVELOPERS PVT. LTD.

Gate Entry No. 9396

Date 02/03/2022

Time 18:20

Vehicle No. HR 56 B 3199

Received By. [Signature]

For NUVOCO VISTAS CORP. LTD.

Authorized Signatory

SPECIFIED TARGET SLUM	W/O	MAX. AGG.	CHEM. ADM.	MIN. ADM.	MIN. CEMENT	CEMENT TYPE
JOB SITE ARRIVAL TIME	JOB POURING START TIME	JOB POURING END TIME	JOB SITE DEPARTURE TIME	PLANT ARRIVAL TIME		

Received the above items in Good condition.

Customer Name, Signature & Seal

ORIGINAL FOR RECIPIENT

E-TAX INVOICE CUM DELIVERY CHALLAN

U/S 31 of CGST Act, 2017 read with Rule 48(4)



PRISM JOHNSON LIMITED

RMC (India) Division



Concrete Concrete Solutions

IND17: 077D

CIN: L26942TG1992PLC014033

Plant Name & Address: Dhumaapur Comm. Concrete Prism Johnson Limited Dist. Gurgaon
Vill Dhumaapur, Jail Road IN 122101

Phone:

Supply State Name: Haryana

Supply State Code: 06

IRN No: 6a2d350172663c67ca60765f61025d922ca8e86dfe4670d74764efd025219ffe

Ack No.: 132212052854456

Ack Date: 2022-03-05 14:00:00

GST Invoice No: 6107473844

Dated: 05.03.2022

Our Ref: 6040224614

Due Date:

GSTIN: 06AAACP6224A121

PAN No: AAACP6224A

TAN No: MUMR08075E

Customer: S.S. CONSTRUCTION CO.

Customer GSTIN: 06AEFFS1460P123

PAN No: AEFFS1460P

Customer Code: 136184

Customer Billing Address: S.S. CONSTRUCTION CO. RAMKRISHAN HOUSE, NEAR MLA TEJPAL TANWAR, KHOTI, VILL-RAMGARH, GURUGRAM
122002 HARYANA Haryana IndiaAssignee Delivery Site Address: ASTHETIC TOWNSHIP DEVELOPER PVT LTD NEAR IFFCO CHOWK
METRO STNSEC-27, GURUGRAM 122002Document Type Code: INV
Supply Type Code: B2B

Delivery State Name: Haryana

Delivery State Code: 6

Vehicle No: HRS55AC4657

Buyer Order No: SSC/BHARTI/VO-87/02/22

Batch Serial No: 005326

Driver: LAXMAN

Sales Engineer: UMAR FAROOQ ANSARI

Time: 13:59:04

Transport Mode: BY ROAD

<u>Aggregates (MSA)</u>		<u>Cement</u>	<u>Target</u> Slump (mm)		<u>Max W/C</u> Ratio		<u>Admix/</u> Add. Inc.	<u>Special</u> Req.
SI No.	Sale of	HSN/SAC Code	Plant Code	MOE	Qty.	U.O.M	Rate	Amount
1	RMC M 30	38245010	2653	Pumping	6.000	M3	5050.00	30300.00

Total Before Tax: 30300.00

CGST @9.00%: 2727.00

SGST @9.00%: 2727.00

Rounding Off: 0.00

Amount in Words (INR): THIRTY FIVE THOUSAND SEVEN HUNDRED FIFTY FOUR Rupees

Total: 35754.00

This is to inform that Tax Collection at Source (TCS) is applicable on Sale of Goods w.e.f. 01.10.2020 under Section 206C(1H) of Income Tax Act, 1961 pursuant to Section 206C(1H) of Income Tax Act, 1961, TCS, at applicable rates, shall be levied on all collections / sale consideration received / due to be received from customers on or after 01.10.2020 including the sales made on or before 09.2020. It is to be noted that applicable Tax Collection at Source (TCS) on a customer for will be 0.10% (0.075% for FY2020-21). Customers having PAN No. mentioned in their invoices. And those of customers without PAN No. shall be charged with TCS of 1%

Please Note:

A) The time allowed for unloading this vehicle is ten minutes plus five minutes per cum or part thereof of this load. Any detention in excess of Allowable time shall be charged extra.
B) We are not responsible for slump, loss of strength or quality of the concrete when water and/or any other materials have been added on site by or at the request of the customer.
C) This concrete is sold on and subject to the conditions of sales mention on our quotation.
D) You must ensure timely wetting and proper covering of placed concrete before it dries to avoid plastic shrinkage cracks. RMC India Division will Not be responsible for any such cracks developed in in-situ concrete.
Caution: Please warn concrete users that, to avoid any risk of serious skin injury, they should minimize contact with wet cement and wet concrete (e.g. wear suitable protective clothing) and where contact occurs, should, without delay wash thoroughly.

Cheque's dishonored due to any reason attributable to customer will attract charges of Rs.1500 +GST, without prejudice of our Rights as contemplated under the provisions of Section 138 of Negotiable Instruments Act. For information on our value added products / special concrete's. Kindly visit our website as given below.

Note:
1. In case of any discrepancy in the invoice we request you to get back to Our Accounts Dept. at the phone no's given above Within 48 hours.
2. Simple interest @18tp.a. will be levied in case payments are delayed beyond the agreed terms of payment.
3. PAYMENTS TO BE MADE AS PER INVOICE ONLY THROUGH RTGS/NEFT/CHEQUE IN FAVOR OF THE COMPANY.

Time at site: _____ Return Site: _____ Time of unloading: _____

Pour location: _____ Water and/or other material added at site: _____

I confirm that, I have received and accepted quantity and grade of the concrete ordered as above. The time shown above is correct. I have authorized the addition on site of any water and/or materials specified at our own risk.

"This product was manufactured in a plant whose quality management system is certified / registered as being in conformity with RMC Production Control Criteria."

Certified that the particulars given above are true and correct and the amount indicated represents the price actually charged and that there is no flow of additional consideration directly or indirectly from the buyer.

ASTHETIC TOWNSHIP

Gate Entry No. 9474

Date: 05/03/2022

Time: 15:10:5

Vehicle No. HR 55AC 4657

Received By: Dhceegik


PRISM JOHNSON LIMITED
RMC (INDIA) DIVISION

AUTHORISED SIGNATORY

FN 2653_005326_05032022

ORIGINAL FOR RECIPIENT

NUVOCO VISTAS CORP. LTD.



Name of the Plant: RP-GURGAON-1, DELHI / 4336
 Address of the Plant: PLOT NO./KH NO.-1527/916/2/2, 1528/916/2/3, REVENUE
 ESTATE VILLAGE,
 GURGAON 06-HARYANA 122001
 PAN No. : AAACL4159L
 GSTIN : 06AAACL4159L1ZC
 CIN : L26940MH1999PLC118229
 IRN : 9ec45af88eccfd5204fb0a5ca39b1b6b447d1bad98ddd52a0751057706ef0908
 Principal P.O.B : CHIDIYA, CHARKHI DADRI, BHIWANI, 06-HARYANA - 123306.
 State Code : 06
 State Name : Haryana

TAX INVOICE

Tax Invoice Number : 210710059260
 Date & Time : 28.02.2022 18:52:00
 Dispatch Mode : BY ROAD
 Receipt Voucher No. :
 Receipt Voucher Date :
 Reverse Charge :
 Customer Code : 50000947
 Name of Customer : S.S.CONSTRUCTION CO.
 Address of Customer : SATISH SURI
 : RAMKRISHAN HOUSE, NEAR MLA TEJPAL
 TANWAR KOTHI VILL
 PO DADSHAPUR GURGAON 06-HARYANA
 122101
 Job Site Code : 0021845913
 Name of Job Site : BHARTI REALTY
 State Code : 06
 Address of Job Site : ASTHETIC TOWNSHIP DEVELOPER
 P.LTD NR IFFCO CHOWK
 SEC-27, GURUGRAM GURUGRAM
 06-HARYANA 122002
 BCMIX No. : 433691573758
 State Code : 06
 PAN No. : AEFPS1460P
 GSTIN No. : 06AEFPS1460P1Z3
 Contact Name : VIPIN CHAUHAN
 Telephone Number : 9719919797
 Mobile Number : 9719919797
 Email ID : suriconstructions@yahoo.com
 Pump Serial No. :
 EMAIL ID : vishalgupta@gmail.com
 Name of Product : RMC
 HSN/SAC : 38245010
 Exemption Notification if any :
 POURING LOCATION : Walls/Columns/Slab/Foundation/Other
 Sales Person's Name :
 Sales Person's Contact No. :

Sl. No	Description	Vehicle No.	Qty.	UOM	Grade	Delivery Type	Material Code	Old Mat. Code
1	M30 SP AE MO D20 M	HR56B1637	4.000	M3	M30	Just Delivery	9000030409	CCMGFE2BH30C
Price Elements							Rate	Amount
Price/Taxable Value							5,050.00	
GST @ 9%							454.50	20,200.00
CGST @ 9%							454.50	1,818.00
Rounding								1,818.00
Total Gross Value of Goods - In Figures							5,959.00	0.00
Total Gross Value of Goods - In Words TWENTY THREE THOUSAND EIGHT HUNDRED THIRTY SIX RUPEES ONLY								23,836.00

ASTHETIC TOWNSHIP DEVELOPL PVT. LTD.

Gate Entry No. 92419

Date 28/02/2022

Time 20:15

Vehicle No. HR56B1637


Received By. SIKHVI

For NUVOCO VISTAS CORP. LTD.

SPECIFIED TARGET SLOPE	W/O	MAX. AGG.	CHIEF ADM.	MIN. ADM.	MIN. CEMENT	CEMENT TYPE
JOB SITE ARRIVAL TIME	JOB POURING START TIME	JOB POURING END TIME	JOB SITE DEPARTURE TIME	PLANT ARRIVAL TIME		

Received the above items in Good condition.

Regd. Off. : Equinox Business Park, Tower-3, East Wing, 41th Floor, Off. Bandra- Kurla Complex, LBS Road, Kurla-West, Mumbai. 400 070.
 Tel: (91-22) 6769 2500. FAX: (91-22) 6769 2517
 Customer Name, Signature & Seal



Phone : 6239317406 Email-Id : customercare@rdconcrete.com GSTIN : 06AAACU0108Q1ZC PAN : AAACU0108Q CIN : U74999MH1993PTC172842 TAN : MUMR22552F

Bill To Party				Ship To Party			
Party Name :	S.S. Construction Co (Bharti Reality)			Party Name :	S S. Construction Co (Bharti Reality)		
Address :	RAMKRISHAN HOUSE, NEAR MLA TEJPAL TANWAR KOTHI, VILL. RAMGARI PO BADSHAPUR GURGAON, HARYANA 122101 06AEFPS1460P1Z3			Address :	Site Bharti reality C/O Asthetic Township Developers Pvt Ltd Near IFFCO Chowk Metro Station, Sec- 27 GURGAON, HARYANA 122002 06AEFPS1460P1Z3		
GSTIN :				GSTIN :			
PAN :				PAN :			
Invoice Number :	1GU21ARSI4421			Terms of Payment :	60 Days		
Invoice Date :	25-02-2022			Transport Mode :	By Road LUT No:		
State :	HARYANA			State :	HARYANA Code: 06		
State Code :	06			Vehicle No :	T1021PB6891D		
DC No :	1GU21ARSI4421			Place of Supply :	GURGAON		
DC Date :	25-02-2022 18:59:57			Date of Supply :	25-02-2022		
Sales Order :	100621600598			PO No :	SSC/Bharti/WO-86/02/22		
				IRN :	7b4cdc7d2cd93773f10d327f380ce76f72046c3739bed4 2948c5d38d7f20f786 132212010892322		
				Ackno. Number :	2022-02-25 19:01:00		
				Ackno. Date :			

Whether tax is payable on reverse charge basis: No

Sl. No	Description of Goods	HSN Code	UOM	Qty	Unit Price	Basic Amount	CGST %	CGST Amount	SGST %	SGST Amount	IGST %	IGST Amount	Gross Amount (Without TCS)
1	M30	38245010	CUM	7	5050	35350.00	9	3181.50	9	3181.50		0	41713.00
TCS % : 0.100						TCS Amount : 41.71	KFC % :	KFC Amount : 0.00	Grand Total		41754.71		

Net Value in Rupees : Rupees Forty One Thousand Seven Hundred Fifty Four and paise Seventy One

Note: 1M3=2400Kgs +/-5%

Cementitious Type	Max. Agg Size	Admixure type	Slump	Min. Cementitious Content
OPC+PFA	20mm	PCEA	Slump : 150 +/- 25 mm	
Batch No: GU1/1920/11494				
Order Quantity (Cubic Meter)	400	Quantity with this load (Cubic Meter)	7	Cumulative Quantity (Cubic Meter)
				345
Pouring Location / Structure :				
Whether this concrete is pumped by RDC concrete: Yes/No		Time of arrival on site:		
Time discharged completed:		Time released from site:	Water added at site:	Admixure added at site:

Remarks:

Please Note: This concrete delivery is subject to the terms and a condition of sales shown in our quotation. The time is allowed for updating this delivery is 15 minute. We reserve the right to charge for any detention beyond this time as per our quotation. Any un authorized addition of water and/or any other material to concrete shall above us from any liability whatsoever. Any deficiency in methods of placing, compacting, finishing and curing of concrete adopted at site may affect quality of concrete in the finished work, for which we shall not be held liable and responsible. Any disputes that arise on quantity and quality (except comp. strength) of concrete supplied in this load shall be reported to us in writing within 24 hours from the time of supply. In no event shall we be liable for direct, indirect, incidental or consequential damage arising out of use of this product, even if advised of possibility of such damage. In no case shall our liability exceed the purchase price of this product. In case of any discrepancies in the invoice please inform us within 3 working days from the date of invoice, otherwise it will be assumed that the invoice is correct and accepted. 24% interest per annum will be charged from the date of invoice on the amount remaining party or wholly unpaid after due date. *This document also constitutes as a Delivery Challen.

I hereby confirm that:

1. We have accepted delivery of concrete as per the details mentioned above. 2. I/We have authorized addition of any water and/or admixture as mentioned above.



Certified that the particulars given above are true and correct and amount indicated represents the price charged and that there is no flow of additional consideration directly or indirectly from the buyer

[Signature]

For RDC Concrete (India) Pvt Ltd.

[Signature]

Authorised Signatory

Caution: Cement and concrete contain lime and other chemicals which can cause irritation, dermatitis and bumps. To avoid harm to skin, minimize contact with wet concrete and wear suitable protective clothing. Whenever contact occur (whether directly or through a surface) wash thoroughly.

TOWNSHIP DEVELOPERS PVT. LTD.
Gate Entry No. 9228
Date 25/02/2022
Time 20:00
Vehicle No. T1021PB6891D
Received By. JARHVI PTHA

Receiver Signature & Seal

Established in 1993

RDC Concrete

RDC Concrete (India) Private Limited

TAX INVOICE**RDC CONCRETE (INDIA) PRIVATE LIMITED**Village Behrampur, Sector 59, Sector 59 Gurgaon, Dist-Gurgaon
HR, PIN - 122011

Phone : 6239317406

Email Id : customercare@rdconcrete.com

GSTIN : 06AAACU0108Q1ZC

PAN : AAACU0108Q

CIN : U74999MH1993PTC172842 TAN : MUMR22552F

Bill To Party

Party Name : S.S. Construction Co (Bharti Reality)
Address : RAMKRISHAN HOUSE, NEAR MLA TEJPAL
TANWAR KOTHI, VILL. RAMGARII PO
BADSHAPUR
GURGAON, HARYANA 122101
GSTIN : 06AEPPS1460P1Z3
PAN :
Invoice Number : 1GU21ARSI4131
Invoice Date : 16-02-2022
State : HARYANA
State Code : 06
DC No : 1GU21ARSI4131
DC Date : 16-02-2022 15:08:47
Sales Order : 100621600565

Ship To Party

Party Name : S.S. Construction Co (Bharti Reality)
Address : Site Bharti reality C/O Asthetic Township Developers
Pvt Ltd
Near IFFCO Chowk Metro Station, Sec- 27
GURGAON, HARYANA 122002
GSTIN : 06AEPPS1460P1Z3
PAN :
Terms of Payment : 60 Days
Transport Mode : By Road LUT No: 06
State : HARYANA
Vehicle No : HR68B0510
Place of Supply : GURGAON
Date of Supply : 16-02-2022
PO No : SSC/Bharti/WO-86/02/22
IRN : 964e0f8c3162b5eb53fe63b172517a9742efa62133549
35fda72812c6c524e
132211965278340
Ackno. Number : 2022-02-16 15:10:00
Ackno. Date :

Whether tax is payable on reverse charge basis: No

Sl. No	Description of Goods	HSN Code	UOM	Qty	Unit Price	Basic Amount	CGST %	CGST Amount	SGST %	SGST Amount	IGST %	IGST Amount	Gross Amount (Without TCS)
1	M30	38245010	CUM	7	5050	35350.00	9	3181.50	9	3181.50	0	0	41713.00
TCS % : 0.100		TCS Amount : 41.71		KFC % :		KFC Amount : 0.00		Grand Total		41754.71			

Net Value in Rupees : Rupees Forty One Thousand Seven Hundred Fifty Four and

Note: 1M3=2400Kgs +/-5%

Cementitious Type	Max. Agg Size	Admixture type	Slump	Min. Cementitious Content
OPC+PFA	20mm	PCEA	Slump : 130 +/- 50 mm	
Batch No: GU1/1920/11204				
Order Quantity (Cubic Meter)		Quantity with this load (Cubic Meter)		Cumulative Quantity (Cubic Meter)
300		7		150
Pouring Location / Structure :				
Whether this concrete is pumped by RDC concrete: Yes/No		Time of arrival on site:		
Time discharged completed:	Time released from site:	Water added at site:	Admixture added at site:	

Remarks:

Please Note: This concrete delivery is subject to the terms and a condition of sales shown in our quotation. The time is allowed for unloading this delivery is 15 minute. We reserve the right to charge for any detention beyond this time as per our quotation. Any unauthorized addition of water and/or any other material to concrete shall absolve us from any liability whatsoever. Any deficiency in methods of placing, compacting, finishing and curing of concrete adopted at site may affect quality of concrete in the finished work, for which we shall not be held liable and responsible. Any disputes that arise on quantity and quality (except comp. strength) of concrete supplied in this load shall be reported to us in writing within 24 hours from the time of supply. In no event shall we be liable for direct, indirect, incidental or consequential damage arising out of use of this product, even if advised of possibility of such damage. In no case shall our liability exceed the purchase price of this product. In case of any discrepancies in the invoice please inform us within 3 working days from the date of invoice, otherwise it will be assumed that the invoice is correct and accepted.

24% interest per annum will be charged from the date of invoice on the amount remaining partly or wholly unpaid after due date.

*This document also constitutes as a Delivery Challan.

I hereby confirm that:

1. I/We have accepted delivery of concrete as per the details mentioned above. 2. I/We have authorized addition of any water and for admixture as mentioned above.



Certified that the particulars given above are true and correct and amount indicated represents the price charged and that there is no flow of additional consideration directly or indirectly from the buyer

For RDC Concrete (India) Pvt Ltd.

Authorised Signatory

Caution: Cement and concrete contain lime and other chemicals which can cause irritation, dermatitis and burning. To avoid harm to skin, minimize contact with wet concrete and wear suitable protective clothing. Whenever contact occurs, (whether directly or through saturated clothing) wash thoroughly.

ASTHETIC TOWNSHIP DEVELOPERS PVT. LTD.
Gate Entry No. 9126
Date 16/02/2022
Time 16:25
Vehicle No HR68B0510
Received By S.K. MISHRA

Receiver Signature & Seal

Name of the Plant: :RP-GURGAON-I,DELHI / 4336
Address of the Plant :PLOT NO./KH.NO.-1527/916/2/2,1528/916/2/3,REVENUE
ESTATE VILLAGE,
GURGAON 06-HARYANA 122001
PAN No. :AAACL4159L
GSTIN. :06AAACL4159L1ZC State Code :06
CIN :U26940MH1999PLC118229 State Name :Haryana
IRN : 5bdb48265506ad5b7199db8c3051be058375d57fd1a3b0526a4ed4bb64b05b78
Principal P.O.B :CHIDIYA, CHARKHI DADRI, BHIWANI, 06-HARYANA - 123306.
CIN



TAX INVOICE

Tax Invoice Number	:210710053547	Sales Type	:FOR - FREE ON ROAD
Date & Time	:04.02.2022 15:09:00	Sales Order No.	:0130238110/SO/4336
Dispatch Mode	:BY ROAD	Customer PO / DATE	:84/02/22//07.01.2022
Receipt Voucher No.	:	Name of Transporter	:
Receipt Voucher Date	:	Reference Number	:2107049925
Reverse Charge	:	Ewaybill Number	:371409257183
Customer Code	:50000947	Job Site Code	:0021845913
Name of Customer	:S.S.CONSTRUCTION CO. SATISH SURI	Name of Job Site	:BHARTI REALTY
Address of Customer	:RAMKRISHAN HOUSE,NEAR MLA TEJPAL TANWAR KOTHI VILL PO BADSHAPUR GURGAON 06-HARYANA 122101	State Code	:06
		Address of Job Site	:ASTHETIC TOWNSHIP DEVELOPER P.LTD NR.JFFCO CHOWK SEC-27,GURUGRAM GURUGRAM 06-HARYANA 122002
BCMIX No.	:433691573120	GSTIN No.	:06AEFPS1460P1Z3
State Code	:06	Contact Name	:VIPIN CHAUHAN
PAN No.	:AEFPS1460P	Telephone Number	:9719919797
		Mobile Number	:9719919797
EMAIL ID.	:vishalgupta@gmail.com	Email ID	:suriconstructions@yahoo.com
		Pump Serial No.	:
Name of Product	:RMC	HSN/SAC	:38245010
		Sales Person's Name	:
		Sales Person's Contact No.	:
POURING LOCATION	:Walls/Columns/Slab/Foundation/Other		

Sl. No	Description	Vehicle No.	Qty.	UOM	Grade	Delivery Type	Material Code	Old Mat. Code
1	M60 ROBUSTE AE MO D20 M0055	HR56B5033	6.000	M3	M60	JustDelivery	9000039809	CMHMFE2BF360

Price Elements	Rate	Amount
Price/Taxable Value	7,400.00	44,400.00
9 %	666.00	3,996.00
CGST @ 9 %	666.00	3,996.00
Rounding		0.00
Total Gross Value of Goods - In Figures	8,732.00	52,392.00

Total Gross Value of Goods - In Words FIFTY TWO THOUSAND THREE HUNDRED NINETY TWO RUPEES ONLY

8936
04/02/22 16:45
HR 56 B 5033
MCSingh

For NUVOCO VISTAS CORP. LTD.

Authorized Signatory

SPECIFIED TARGET SLUM	W/O	MAX. AGG.	CHEM. ADM.	MIN. ADM.	MIN. CEMENT	CEMENT TYPE
JOBSITE ARRIVAL TIME	JOB POURING START TIME	JOB POURING END TIME	JOBSITE DEPARTURE TIME	PLANT ARRIVAL TIME		

Received the above items in Good condition.

Customer Name, Signature & Seal



Phone : 6239317406 Email-Id : customercare@rdcconcrete.com
GSTIN : 06AAACU0108Q1ZC PAN : AAACU0108Q CIN : U74999MH1993PTC172842 TAN : MUMR22552F

Bill To Party		Ship To Party	
Party Name :	S.S. Construction Co (Bharti Reality) RAMKRISHAN HOUSE, NEAR MLA TEJPAL TANWAR KOTHI, VILL. RAMGARII PO	Party Name :	S.S. Construction Co (Bharti Reality) Site Bharti reality C/O Asthetic Township Developers Pvt Ltd
Address :	BADSHAPUR GURGAON, HARYANA 122101 06AEFPS1460P1Z3	Address :	Near IFFCO Chowk Metro Station, Sec- 27 GURGAON, HARYANA 122002 06AEFPS1460P1Z3
GSTIN :	1GU21ARSI3607	GSTIN :	60 Days
PAN :	29-01-2022	PAN :	By Road LUT No:
Invoice Number :	HARYANA	Terms of Payment :	State: HARYANA Code: 06
Invoice Date :	06	Transport Mode :	Vehicle No : HR68B0510
State :	1GU21ARSI3607	State :	Place of Supply : GURGAON
State Code :	29-01-2022 22:18:37	Vehicle No :	Date of Supply : 29-01-2022
DC No :	100621600520	Place of Supply :	PO No: SSC/Bharti/WO-81/01/22 Dated 07-Jan-22
DC Date :		Date of Supply :	IRN : 81248a98ba90b622eb1449a5731e87695606d3852ddc
Sales Order :		PO No:	00d482e74cfff2a6d53a
		IRN :	Ackno Number : 132211885368255
			Ackno Date : 2022-01-29 22:20:00

Whether tax is payable on reverse charge basis: No

Sl. No	Description of Goods	HSN Code	UOM	Qty	Unit Price	Basic Amount	CGST %	CGST Amount	SGST %	SGST Amount	IGST %	IGST Amount	Gross Amount (Without TCS)
1	M60 SUPERCRETE	38245010	CUM	7	7300	51100.00	9	4599.00	9	4599.00		0	60298.00
TCS % : 0.100		TCS Amount : 60.30		KFC % :		KFC Amount : 0.00		Grand Total		60358.30			

Net Value in Rupees : Rupees Sixty Thousand Three Hundred Fifty Eight and paise

Note: 1M3=2400Kgs +/-5%

Cementitious Type	Max. Agg Size	Admixture type	Slump	Min. Cementitious Content
OPC+PFA	20mm	PCEA	Slump : 180 +/- 25 mm	
Batch No: GU1/1920/10680				
Order Quantity (Cubic Meter)		Quantity with this load (Cubic Meter)		Cumulative Quantity (Cubic Meter)
150		7		55.5
Pouring Location / Structure :				
Whether this concrete is pumped by RDC concrete: Yes/No		Time of arrival on site:		
Time discharged completed:		Time released from site:	Water added at site:	Admixture added at site:

Remarks:

Please Note: This concrete delivery is subject to the terms and a condition of sales shown in our quotation. The time is allowed for updating this delivery is 15 minutes. We reserve the right to charge for any detention beyond this time as per our quotation. Any unauthorized addition of water and/or any other material to concrete shall absolve us from any liability whatsoever. Any deficiency in methods of placing, compacting, finishing and curing of concrete adopted at site may affect quality of concrete in the finished work, for which we shall not be held liable and responsible. Any disputes that arise on quantity and quality (except comp. strength) of concrete supplied in this load shall be reported to us in writing within 24 hours from the time of supply. In no event shall we be liable for direct, indirect, incidental or consequential damage arising out of use of this product, even if advised of possibility of such damage. In no case shall our liability exceed the purchase price of this product. In case of any discrepancies in the invoice please inform us within 3 working days from the date of invoice, otherwise it will be assumed that the invoice is correct and accepted. 24% interest per annum will be charged from the date of invoice on the amount remaining partly or wholly unpaid after due date.

*This document also constitutes as a Delivery Challan.

We hereby confirm that:

1. We have accepted delivery of concrete as per the details mentioned above. 2. I/We have authorized addition of any water and for admixture as mentioned above.



Certified that the particulars given above are true and correct and amount indicated represents the price charged and that there is no flow of additional consideration directly or indirectly from the buyer

For RDC Concrete (India) Pvt Ltd.

Authorised Signatory

Caution: Cement and concrete contain lime and other chemicals which can cause irritation, dermatitis and burning. To avoid harm to skin, minimize contact with wet concrete and wear suitable protective clothing. Whenever contact occur (whether directly or through saturated clothing) wash thoroughly.

Receiver Signature & Seal

8838
29/01/2022
22:15
HR68B0510
Sunita Singh



TAX INVOICE
RDC CONCRETE (INDIA) PRIVATE LIMITED
Village Behrampur, Sector 59, Sector 59, Gurgaon, Dist- Gurgaon
HR, PIN - 122011



Phone : 6239317406

Email-Id : customercare@rdcconcrete.com

GSTIN : 06AAACU0108Q1ZC

PAN : AAACU0108Q

CIN : U74999MH1993PTC172842 TAN : MUMR22552F

Bill To Party

Party Name : S.S. Construction Co (Bharti Reality)
RAMKRISHAN HOUSE, NEAR MLA TEJPAL
TANWAR KOTHI, VILL. RAMGARII PO
BADSHAPUR
GURGAON, HARYANA 122101
Address : 06AEFFS1460P1Z3
GSTIN :
PAN :
Invoice Number : 1GU21ARSI3504
Invoice Date : 24-01-2022
State : HARYANA
State Code : 06
DC No : 1GU21ARSI3504
DC Date : 24-01-2022 10:51:31
Sales Order : 100621600506

Ship To Party

Party Name : S.S. Construction Co (Bharti Reality)
Site Bharti realty C/O Asthetic Township Developers
Pvt Ltd
Near IFFCO Chowk Metro Station, Sec- 27
GURGAON, HARYANA 122002
Address : 06AEFFS1460P1Z3
GSTIN :
PAN :
Terms of Payment : 60 Days
Transport Mode : By Road LUT No :
State : HARYANA Code : 06
Vehicle No : T1021PB6891D
Place of Supply : GURGAON
Date of Supply : 24-01-2022
PO No : SSC/Bharti/WO-81/01/22 Dated 07-Jan-22
IRN : 149e1484501792d7c92ec7aa7fb40166ba938e1e6ba72
c3f34a9ce04cbc60d9d
132211857529701
Ackno. Number :
Ackno. Date : 2022-01-24 10:53:00

Whether tax is payable on reverse charge basis: No

Sl. No	Description of Goods	HSN Code	UOM	Qty	Unit Price	Basic Amount	CGST %	CGST Amount	SGST %	SGST Amount	IGST %	IGST Amount	Gross Amount (Without TCS)
1	M30	38245010	CUM	7	5100	35700.00	9	3213.00	9	3213.00		0	42126.00

TCS % : 0.100

TCS Amount : 42.13

KFC % :

KFC Amount : 0.00

Grand Total

42168.13

Net Value in Rupees : Rupees Fourty Two Thousand One Hundred Sixty Eight and paise Thirteen

Note: 1M3=2400Kgs +/-5%

Cementitious Type	Max. Agg Size	Admixture type	Slump	Min. Cementitious Content
OPC+PFA	20mm	PCEA	Slump : 150 +/- 25 mm	

Batch No: GU1/1920/10577

Order Quantity (Cubic Meter)	Quantity with this load (Cubic Meter)	Cumulative Quantity (Cubic Meter)
300	7	141

Pouring Location / Structure :

Whether this concrete is pumped by RDC concrete: Yes/No

Time of arrival on site:

Time discharged completed:

Time released from site:

Water added at site:

Admixture added at site:

Remarks:

Please Note: This concrete delivery is subject to the terms and a condition of sales shown in our quotation. The time is allowed for unloading this delivery is 15 minutes. We reserve the right to charge for any detention beyond this time as per our quotation. Any un authorized addition of water and/or any other material to concrete shall absolve us from any liability whatsoever. Any deficiency in methods of placing, compacting, finishing and curing of concrete adopted at site may affect quality of concrete in the finished work, for which we shall not be held liable and responsible. Any disputes that arise on quantity and quality (except comp. strength) of concrete supplied in this load shall be reported to us in writing within 24 hours from the time of supply. In no event shall we be liable for direct, indirect, incidental or consequential damage arising out of use of this product, even if advised of possibility of such damage. In no case shall our liability exceed the purchase price of this product. In case of any discrepancies in the invoice please inform us within 3 working days from the date of invoice, otherwise it will be assumed that the invoice is correct and accepted. 24% interest per annum will be charged from the date of invoice on the amount remaining partly or wholly unpaid after due date.

*This document also constitutes as a Delivery Chalan.

*I hereby confirm that:

1. We have accepted delivery of concrete as per the details mentioned above. 2. We have authorized addition of any water and for admixture as mentioned above.



Certified that the particulars given above are true and correct and amount indicated represents the price charged and that there is no flow of additional consideration directly or indirectly from the buyer

[Signature]

For RDC Concrete (India) Pvt Ltd.


[Signature]

Authorised Signatory

Caution: Cement and concrete contain lime and other chemicals which can cause irritation, dermatitis and burning. To avoid harm to skin, minimize contact with wet concrete and wear suitable protective clothing. Whenever contact occur (whether directly or through saturated clothing) wash thoroughly.

Receiver Signature & Seal

Qty No. 8763
Date 24/01/2022
Time 12:00
No. T1021PB6891D
[Signature]



Phone : 6239317406

Email-Id : customercare@rdcconcrete.com

STIN : 06AAACU0108Q1ZC

PAN : AAACU0108Q

CIN : U74999MH1993PTC172842 TAN : MUMR22552F

Bill To Party

Party Name : S.S. Construction Co (Bharti Reality)
RAMKRISHAN HOUSE, NEAR MLA TEJPAL
TANWAR KOTHI, VILL. RAMGARII PO
BADSHAPUR
GURGAON, HARYANA 122011
GSTIN : 06AEFPS1460P1Z3

Address :

STIN

PAN

Invoice Number : 1GU21ARSI3312

Invoice Date : 16-01-2022

State : HARYANA

Post Code : 06

Vehicle No : 1GU21ARSI3312

PO No : 16-01-2022 01:04:00

Order : 100621600452

Ship To Party

Party Name : S.S. Construction Co (Bharti Reality)
Site Bharti reality C/O Asthetic Township Developers
Pvt Ltd
Near IFFCO Chowk Metro Station, Sec- 27
GURGAON, HARYANA 122002
GSTIN : 06AEFPS1460P1Z3

Address :

GSTIN :

PAN :

Terms of Payment : 60 Days

Transport Mode : By Road LUT No:

State : HARYANA Code: 06

Vehicle No : HR68B3807

Place of Supply : GURGAON

Date of Supply : 16-01-2022

PO No: PO No. SSC/Bharti/WO-75/12/21 Dated 22-Dec-21

IRN : c47c25842bccd2d5ab89b79deaa6a8198dd8b383d0ef9

d1283f445514aa229eb

132211823333288

Ackno. Number : 2022-01-16 00:45:00

Ackno. Date :

Sl. No	Description of Goods	HSN Code	UOM	Qty	Unit Price	Basic Amount	CGST %	CGST Amount	SGST %	SGST Amount	IGST %	IGST Amount	Gross Amount (Without TCS)
1	M60 SUPERCRETE	38245010	CUM	7	7300	51100.00	9	4599.00	9	4599.00		0	60298.00

CS % : 0.100 TCS Amount : 60.30 KFC % :

KFC Amount : 0.00

Grand Total

60358.30

Net Value in Rupees : Rupees Sixty Thousand Three Hundred Fifty Eight and paise

Note: 1M3=2400Kgs +/-5%

Cementitious Type	Max. Agg Size	Admixture type	Slump	Min. Cementitious Content
OPC+PFA	20mm	PCEA	Slump : 180 +/- 25 mm	

Batch No: GU1/1920/10385

Order Quantity (Cubic Meter)	Quantity with this load (Cubic Meter)	Cumulative Quantity (Cubic Meter)
250	7	199

Pouring Location / Structure :

Whether this concrete is pumped by RDC

concrete: Yes/No

Time of arrival on site:

Time discharged completed:

Time released from site:

Water added at site:

Admixture added at site:

Remarks:

This concrete delivery is subject to the terms and a condition of sales shown in our quotation. The time is allowed for unloading this delivery is 15 minute. We reserve the right to charge for any detention beyond this time as per our terms. Any unauthorized addition of water and/or any other material to concrete shall absolve us from any liability whatsoever. Any deficiency in methods of placing, compacting, finishing and curing of concrete adopted at site may affect quality of the finished work, for which we shall not be held liable and responsible. Any disputes that arise on quantity and quality (except comp. strength) of concrete supplied in this load shall be reported to us in writing within 24 hours from the time of supply. In no event shall we be liable for direct, indirect, incidental or consequential damage arising out of use of this product, even if advised of possibility of such damage. In no case shall our liability exceed the purchase price of this product. In case of any discrepancies in the invoice please inform us within 3 working days from the date of invoice, otherwise it will be assumed that the invoice is correct and accepted. 12% interest per annum will be charged from the date of invoice on the amount remaining partly or wholly unpaid after due date. This document also constitutes as a Delivery Chalan.

I hereby confirm that:

1. We have accepted delivery of concrete as per the details mentioned above. 2. We have authorized addition of any water and/or admixture as mentioned above.



Certified that the particulars given above are true and correct and amount indicated represents the price charged and that there is no flow of additional consideration directly or indirectly from the buyer

[Signature]

For RDC Concrete (India) Pvt Ltd.

[Signature]

Authorised Signatory

Caution: Cement and concrete contain lime and other chemicals which can cause irritation, dermatitis and burning. To avoid harm to skin, minimize contact with wet concrete and wear suitable protective clothing. Whenever contact occur (whether directly or through saturated clothing) wash thoroughly.

Receiver Signature & Seal

8633
16/01/22
01/15
HR68B 3807
P/Cs/mh



TAX INVOICE
RDC CONCRETE (INDIA) PRIVATE LIMITED
Village Behrampur, Sector 59, Sector 59, Gurgaon, Dist-Gurgaon
HR, PIN - 122011



Phone : 6239317406

Email-Id : customercare@rdcconcrete.com

GSTIN : 06AAACU0108Q1ZC

PAN : AAACU0108Q

CIN : U74999MH1993PTC172842 TAN : MUMR22552F

Bill To Party

Party Name : S.S. Construction Co (Bharti Reality)
Address : RAMKRISHAN HOUSE, NEAR MLA TEJPAL
TANWAR KOTHI, VILL. RAMGARII PO
BADSHAPUR
GURGAON, HARYANA 122101
GSTIN : 06AEFPS1460P1Z3
PAN :
Invoice Number : 1GU21ARSI3143
Invoice Date : 06-01-2022
State : HARYANA
State Code : 06
DC No : 1GU21ARSI3143
DC Date : 06-01-2022 14:24:40
Sales Order : 100621600453

Ship To Party

Party Name : S.S. Construction Co (Bharti Reality)
Address : Site Bharti reality C/O Asthetic Township Developers
Pvt Ltd
Near IFFCO Chowk Metro Station, Sec- 27
GURGAON, HARYANA 122002
GSTIN : 06AEFPS1460P1Z3
PAN :
Terms of Payment : 60 Days
Transport Mode : By Road LUT No:
State : HARYANA Code: 06
Vehicle No : T1021PB6893D
Place of Supply : GURGAON
Date of Supply : 06-01-2022
PO No : PO No. SSC/Bharti/WO-75/12/21 Dated 22-Dec-21
IRN : fd97af0c29bbd8d3c596869e75f81a2c04cf6496972bf9
a794389763ca27fa3
Ackno. Number : 132211781820431
Ackno. Date : 2022-01-06 14:26:00

Whether tax is payable on reverse charge basis: No

Sl. No	Description of Goods	HSN Code	UOM	Qty	Unit Price	Basic Amount	CGST %	CGST Amount	SGST %	SGST Amount	IGST %	IGST Amount	Gross Amount (Without TCS)
1	M30	38245010	CUM	7	5100	35700.00	9	3213.00	9	3213.00		0	42126.00

TCS % : 0.100

TCS Amount : 42.13

KFC % :

KFC Amount : 0.00

Grand Total

42168.13

Net Value in Rupees : Rupees Forty Two Thousand One Hundred Sixty Eight and paise Thirteen

Note: 1M3=2400Kgs +/-5%

Cementitious Type		Max. Agg Size	Admixture type	Slump	Min. Cementitious Content
OPC+PFA		20mm	PCEA	Slump : 150 +/- 25 mm	-
Batch No: GU1/1920/10216					
Order Quantity (Cubic Meter)		Quantity with this load (Cubic Meter)		Cumulative Quantity (Cubic Meter)	
500		7		336	
Pouring Location / Structure :			Time of arrival on site:		
Whether this concrete is pumped by RDC concrete: Yes/No					
Time discharged completed:		Time released from site:	Water added at site:	Admixture added at site:	

Remarks:

Please Note: This concrete delivery is subject to the terms and a condition of sales shown in our quotation. The time is allowed for upaling this delivery a 15 minute. We reserve the right to charge for any detention beyond this time as per our quotation. Any un authorized addition of water and or any other material to concrete shall absolve us from any liability whatsoever. Any deficiency in methods of placing, compacting, finishing and curing of concrete adopted at site may affect quality of concrete in the finished work, for which we shall not be held liable and responsible. Any disputes that arise on quantity and quality (except comp. strength) of concrete supplied in this load shall be reported to us in writing within 24 hours from the time of supply. In no event shall we be liable for direct, indirect, incidental or consequential damage arising out of use of this product, even if advised of possibility of such damage. In no case shall our liability exceed the purchase price of this product. In case of any discrepancies in the invoice please inform us within 3 working days from the date of invoice, otherwise it will be assumed that the invoice is correct and accepted. 2% interest per annum will be charged from the date of invoice on the amount remaining partly or wholly unpaid after due date.

*This document also constitutes as a Delivery Chellan.

I hereby confirm that:

1. I/We have accepted delivery of concrete as per the details mentioned above. 2. I/We have authorized addition of any water and/or admixture as mentioned above.



Certified that the particulars given above are true and correct and amount indicated represents the price charged and that there is no flow of additional consideration directly or indirectly from the buyer

For RDC Concrete (India) Pvt Ltd.

Authorized Signatory

Caution: Cement and concrete contain lime and other chemicals which can cause irritation, dermatitis and burning. To avoid harm to skin, minimize contact with wet concrete and wear suitable protective clothing. Whenever contact occur (whether directly or through saturated clothing) wash thoroughly

Receiver Signature & Seal

8546
06/01/2022
15:05
No. T1021PB6893D
Sukhvir Singh

TAX INVOICE
RDC CONCRETE (INDIA) PRIVATE LIMITED
 Village Behrampur, Sector 59, Sector 59, Gurgaon, Dist-Gurgaon
 HR, PIN - 122011



Phone : 5239317406

Email-id : customercare@rdcconcrete.com

GSTIN : 06AAACU0108Q1ZC

PAN : AAACU0108Q

CIN : U74999MH1993PTC172842 TAN : MUM/R22552F

Bill To Party

Party Name : S.S. Construction Co (Bharti Realty)
 RAMKRISHAN HOUSE, NEAR MLA TEJPAL
 TANWAR KOTHI, VILL. RAMGARII PO
 BADSHAPUR
 Address : GURGAON, HARYANA 122101
 06AEFPS1460P1Z3

GSTIN :
 PAN : 1GU21ARSI3040
 Invoice Number : 30-12-2021
 Invoice Date : HARYANA
 State : 06
 State Code : 1GU21ARSI3040
 PO No : 30-12-2021 16:00:39
 State : 100621600452
 Order :

Whether tax is payable on reverse charge basis: No

Ship To Party

Party Name : S.S. Construction Co (Bharti Realty)
 Site Bharti realty C/O Ashtic Township Developers
 Pvt Ltd
 Address : Near IFFCO Chowk Metro Station, Sec- 27
 GURGAON, HARYANA 122002
 06AEFPS1460P1Z3

GSTIN :
 PAN :
 Terms of Payment : 60 Days
 Transport Mode : By Road LUT No:
 State : HARYANA Code: 06
 Vehicle No : PB10FV6966
 Place of Supply : GURGAON
 Date of Supply : 30-12-2021
 PO No : PO No. SSC/Bharti/WO-75/12/21 Dated 22-Dec-21
 IRN : 0007154890d78eaba1006ec0772e2ecc72d349a07b7c
 534ecf378553038e344b
 132111749150519
 Ackno. Number :
 Ackno. Date : 2021-12-30 16:14:00

Sl. No	Description of Goods	HSN Code	UOM	Qty	Unit Price	Basic Amount	CGST %	CGST Amount	SGST %	SGST Amount	IGST %	IGST Amount	Gross Amount (Without TCS)
1	M30 SUPERCRETE	38245010	CUM	5	7300	36500.00	9	3285.00	9	3285.00		0	43070.00

TCS % : 0.100 TCS Amount : 43.07 KFC % : KFC Amount : 0.00 Grand Total 43113.07

Net Value in Rupees : Rupees Forty Three Thousand One Hundred Thirteen and

Note: 1M3= 2400Kgs +/- 5%

Cementitious Type	Max. Agg Size	Admixture type	Slump	Min. Cementitious Content
OPC+PFA	20mm	PCEA	Slump : 180 +/- 25 mm	

Batch No	Order Quantity (Cubic Meter)	Quantity with this load (Cubic Meter)	Cumulative Quantity (Cubic Meter)
GUT/1920/10112	250	5	52

Placing Location / Structure :
 Whether this concrete is pumped by RDC :
 concrete: Yes/No
 Time of arrival on site:

Time discharged completed: Time released from site: Water added at site: Admixture added at site:

Remarks:
 Note: This concrete delivery is subject to the terms and a condition of sales shown in our quotation. The time is allowed for unloading this delivery is 15 minute. We reserve the right to charge for any detention beyond this time as per our
 Any un authorized addition of water and/or any other material to concrete shall absolve us from any liability whatsoever. Any deficiency in methods of placing, compacting, finishing and curing of concrete adopted at site may affect quality of
 work in the finished work, for which we shall not be held liable and responsible. Any disputes that arise on quality and quantity (except comp. strength) of concrete supplied in this load shall be reported to us in writing within 24 hours from the time
 of delivery. In no event shall we be liable for direct, indirect, incidental or consequential damage arising out of use of this product, even if advised of possibility of such damage. In no case shall our liability exceed the purchase price of this product.
 In case of any discrepancies in the invoice please inform us within 3 working days from the date of invoice, otherwise it will be assumed that the invoice is correct and accepted.
 24% interest per annum will be charged from the date of invoice on the amount remaining partly or wholly unpaid after due date.
 *This document also constitutes as a Delivery Challan.
 I hereby confirm that:
 1. I/We have accepted delivery of concrete as per the details mentioned above. 2. I/We have authorized addition of any water and/or admixture as mentioned above.



Certified that the particulars given above are true and correct and amount indicated represents the price charged and that there is no flow of additional consideration directly or indirectly from the buyer

For RDC Concrete (India) Pvt Ltd.

Authorised Signatory

Caution: Cement and concrete contain lime and other chemicals which can cause irritation, dermatitis and burning. To avoid harm to skin, minimize contact with wet concrete and wear suitable protective clothing. Whenever contact occur (whether directly or through saturated clothing) wash thoroughly.

Receiver Signature & Seal

8511
 30/12/21 16:45
 PB 10FV 6966
 MC Sim



TAX INVOICE
RDC CONCRETE (INDIA) PRIVATE LIMITED
Village Behrampur, Sector 59, Sector 59, Gurgaon Dist-Gurgaon
HR, PIN - 122011



Phone : 6239317406

GSTIN : 06AAACU0108Q1ZC

Email-Id : customercare@rdconcrete.com

PAN : AAACU0108Q

CIN : U74999MH1993PTC172842 TAN : MUMR22552F

Bill To Party

Party Name : S.S. Construction Co (Bharti Reality)
RAMKRISHAN HOUSE, NEAR MLA TEJPAL
TANWAR KOTHI, VILL. RAMGARII PO
BADSHAPUR
GURGAON, HARYANA 122101
06AEFPS1460P1Z3

GSTIN :
PAN :
Invoice Number : 1GU21ARSI2941
Invoice Date : 25-12-2021
State : HARYANA
State Code : 06
DC No : 1GU21ARSI2941
DC Date : 25-12-2021 16:56:56
Sales Order : 100621600453

Whether tax is payable on reverse charge basis: No

Ship To Party

Party Name : S.S. Construction Co (Bharti Reality)
Site Bharti reality C/O Asthetic Township Developers
Pvt Ltd
Address : Near IFFCO Chowk Metro Station, Sec- 27
GURGAON, HARYANA 122002
06AEFPS1460P1Z3
GSTIN :
PAN :
Terms of Payment : 60 Days
Transport Mode : By Road LUT No:
State : HARYANA Code: 06
Vehicle No : PB10FV6966
Place of Supply : GURGAON
Date of Supply : 25-12-2021
PO No : PO No. SSC/Bharti/WO-75/12/21 Dated 22-Dec-21
2e15df61504e4bac460a567dc5aad79ca5b118855a
897d424461314ef62e3
IRN : 132111726684150
Ackno. Number : 132111726684150
Ackno. Date : 2021-12-25 16:58:00

Sl. No	Description of Goods	HSN Code	UOM	Qty	Unit Price	Basic Amount	CGST %	CGST Amount	SGST %	SGST Amount	IGST %	IGST Amount	Gross Amount (Without TCS)
1	M30	38245010	CUM	7	5100	35700.00	9	3213.00	9	3213.00		0	42126.00

TCS % : 0.100

TCS Amount : 42.13

KFC % :

KFC Amount : 0.00

Grand Total

42168.13

Net Value In Rupees : Rupees Fourty Two Thousand One Hundred Sixty Eight and
paise Thirteen

Note: 1M3=2400Kgs +/-5%

Cementitious Type	Max. Agg Size	Admixture type	Slump	Min. Cementitious Content
OPC+PFA	20mm	PCEA	Slump : 150 +/- 25 mm	

Batch No: GU1/1920/10013

Order Quantity (Cubic Meter)

500

Quantity with this load (Cubic Meter)

7

Cumulative Quantity (Cubic Meter)

112

Pouring Location / Structure :

Whether this concrete is pumped by RDC
concrete: Yes/No

Time of arrival on site:

Time discharged completed:

Time released from site:

Water added at site:

Admixture added at site:

Remarks:

Please Note: This concrete delivery is subject to the terms and a condition of sales shown in our quotation. The time is allowed for updating this delivery is 15 minute. We reserve the right to charge for any detention beyond this time as per our quotation. Any un authorized addition of water and oil any other material to concrete shall absolve us from any liability whatsoever. Any deficiency in methods of placing, compacting, finishing and curing of concrete adopted at site may affect quality of concrete in the finished work, for which we shall not be held liable and responsible. Any disputes that arise on quantity and quality (except comp. strength) of concrete supplied in this load shall be reported to us in writing within 24 hours from the time of supply. In no event shall we be liable for direct, indirect, incidental or consequential damage arising out of use of this product, even if advised of possibility of such damage. In no case shall our liability exceed the purchase price of the product. In case of any discrepancies in the invoice please inform us within 3 working days from the date of invoice, otherwise it will be assumed that the invoice is correct and accepted.

24% interest per annum will be charged from the date of invoice on the amount remaining partly or wholly unpaid after due date.

*This document also constitutes as a Delivery Challan.

hereby confirm that:

1. We have accepted delivery of concrete as per the details mentioned above. 2. We have authorized addition of any water and for admixture as mentioned above.



Certified that the particulars given above are true and correct and amount indicated represents the price charged and that there is no flow of additional consideration directly or indirectly from the buyer

For RDC Concrete (India) Pvt Ltd.

Authorised Signatory

Caution: Cement and concrete contain lime and other chemicals which can cause irritation, dermatitis and burning. To avoid harm to skin, minimize contact with wet concrete and wear suitable protective clothing. Whenever contact occur (whether directly or through saturated clothing) wash thoroughly.

Receiver Signature & Seal

8467
23/12/21 12:40
PB 10 FV 6966
P/S, msh

Established in 1993

RDC Concrete

RDC Concrete (India) Private Limited

TAX INVOICE**RDC CONCRETE (INDIA) PRIVATE LIMITED**Village Behrampur, Sector 59, Sector 59, Gurgaon, Dist-Gurgaon
HR, PIN - 122011

Phone : 6239317406

Email-id : customerscare@rdconcrete.com

GSTIN : 06AAACU0108Q1ZC

PAN : AAACU0108Q

CIN : U74999MH1993PTC172842 TAN : MUMR22552F

Bill To Party

Party Name :

Address :

GSTIN :

PAN :

Invoice Number :

Invoice Date :

State :

State Code :

DC No. :

DC Date :

Sales Order :

S.S. Construction Co (Bharti Reality)
RAMKRISHAN HOUSE, NEAR MLA TEJPAL
TANWAR KOTHI, VILL. RAMGARII PO
BADSHAPUR
GURGAON, HARYANA 122101
06AEFFS1460P1Z3**Ship To Party**

Party Name :

Address :

GSTIN :

PAN :

Terms of Payment :

Transport Mode :

State :

Vehicle No. :

Place of Supply :

Date of Supply :

PO No. :

IRN :

Ackno. Number :

Ackno. Date :

S.S. Construction Co (Bharti Reality)
Site Bharti reality C/O Asthetic Township Developers
Pvt Ltd
Near IFFCO Chowk Metro Station, Sec- 27
GURGAON, HARYANA 122002
06AEFFS1460P1Z3

LUT No: 06

PO No. SSC/Bharti/WO-74/11/21 Dated 10-Nov-21
4d4503aa08ba661dbc155964220446adf1e83eff0dfc3a
2df93e3950ec0d1807
132111706876531
2021-12-21 17:22:00

Whether tax is payable on reverse charge basis: No

Sl. No	Description of Goods	HSN Code	UOM	Qty	Unit Price	Basic Amount	CGST %	CGST Amount	SGST %	SGST Amount	IGST %	IGST Amount	Gross Amount (Without TCS)
1	M60 SUPERCRETE	38245010	CUM	6	7300	43800.00	9	3942.00	9	3942.00		0	51684.00

TCS % : TCS Amount : KFC % : KFC Amount : 0.00 Grand Total 51684.00

Net Value in Rupees : Rupees Fifty One Thousand Six Hundred Eighty Four

Note: 1M3=2400Kgs +/-5%

Cementitious Type Max. Agg Size Admixture type Slump Min. Cementitious Content

OPC+PFA 20mm PCEA Slump : 180 +/- 25 mm

Batch No: GU1/1920/9924

Order Quantity (Cubic Meter)

Quantity with this load (Cubic Meter)

Cumulative Quantity (Cubic Meter)

125 6 37

Pouring Location / Structure :

Whether this concrete is pumped by RDC

Time of arrival on site:

concrete: Yes/No

Time discharged completed:

Time released from site:

Water added at site:

Admixture added at site:

Remarks

Please Note: This concrete delivery is subject to the terms and a condition of sales shown in our quotation. The time is allowed for updating this delivery is 15 minute. We reserve the right to charge for any detention beyond this time as per our quotation. Any un-authorized addition of water and/or any other material to concrete shall absolve us from any liability whatsoever. Any deficiency in methods of placing, compacting, finishing and curing of concrete adopted at site may affect quality of concrete in the finished work, for which we shall not be held liable and responsible. Any disputes that arise on quantity and quality (except comp. strength) of concrete supplied in this load shall be reported to us in writing within 24 hours from the time of supply. In no event shall we be liable for direct, indirect, incidental or consequential damage arising out of use of this product, even if advised of possibility of such damage. In no case shall our liability exceed the purchase price of this product.

In case of any discrepancies in the invoice please inform us within 3 working days from the date of invoice, otherwise it will be assumed that the invoice is correct and accepted.

24% interest per annum will be charged from the date of invoice on the amount remaining partly or wholly unpaid after due date.

*This document also constitutes as a Delivery Challen.

Customer confirm that

We have accepted delivery of concrete as per the details mentioned above. 2. I/we have authorized addition of any water and/or admixture as mentioned above.



Certified that the particulars given above are true and correct and amount indicated represents the price charged and that there is no flow of additional consideration directly or indirectly from the buyer

For RDC Concrete (India) Pvt Ltd.

Authorised Signatory

Caution: Cement and concrete contain lime and other chemicals which can cause irritation, dermatitis and burning. To avoid harm to skin, minimize contact with wet concrete and wear suitable protective clothing. Whenever contact occur (whether directly or through saturated clothing) wash thoroughly.

Receiver Signature & Seal

8491
21/12/21 18:00
PB 10HP 3109
PDSmk


Established in 1993

RDC Concrete

RDC Concrete (India) Private Limited

TAX INVOICE

RDC CONCRETE (INDIA) PRIVATE LIMITED
Village Behrampur, Sector 59, Sector 59, Gurgaon, Dist- Gurgaon
HR, PIN -122011



Phone : 6239317406

Email-Id : customercare@rdcconcrete.com

GSTIN : 06AAACU0108Q1ZC

PAN : AAACU0108Q

CIN : U74999MH1993PTC172842 TAN : MUMR22552F

Bill To Party

Party Name : S.S. Construction Co (Bharti Reality)
RAMKRISHAN HOUSE, NEAR MLA TEJPAL
TANWAR KOTHI,VILL. RAMGARII PO
BADSHAPUR
GURGAON,HARYANA 122101
06AEFPS1460P1Z3

Address :
GSTIN :
PAN :
Invoice Number : 1GU21ARS12860
Invoice Date : 22-12-2021
State : HARYANA
State Code : 06
No : 1GU21ARS12860
Date : 22-12-2021 09:05:47
Order : 100621600420

Whether tax is payable on reverse charge basis: No

Ship To Party

Party Name : S.S. Construction Co (Bharti Reality)
Site Bharti reality C/O Asthetic Township Developers
Pvt Ltd
Address : Near IFFCO Chowk Metro Station, Sec- 27
GURGAON,HARYANA122002
06AEFPS1460P1Z3
GSTIN :
PAN :
Terms of Payment : IMMEDIATE
Transport Mode : By Road LUT No:
State : HARYANA Code : 06
Vehicle No : PB10HP3109
Place of Supply : GURGAON
Date of Supply : 22-12-2021
PO No : PO No, SSC/Bharti/WO-74/11/21 Dated 10-Nov-21
IRN : d40aad9aa770a1820988cec7da07b5795cbfbc2fca5e0
515c65fc1d5c35c630
Ackno.Number : 132111712275742
Ackno. Date : 2021-12-22 17:58:00

Sl. No	Description of Goods	HSN Code	UOM	Qty	Unit Price	Basic Amount	CGST %	CGST Amount	SGST %	SGST Amount	IGST %	IGST Amount	Gross Amount (Without TCS)
1	M60 SUPERCRETE	38245010	CUM	6	7300	43800.00	9	3942.00	9	3942.00		0	51684.00

TCS % : TCS Amount : KFC % : KFC Amount : 0.00 Grand Total 51684.00

Net Value in Rupees : Rupees Fifty One Thousand Six Hundred Eighty Four

Note: 1M3=2400Kgs +/-5%

Cementitious Type	Max. Agg Size	Admixture type	Slump	Min. Cementitious Content
OPC+PFA	20mm	PCEA	Slump : 180 +/- 25 mm	

Batch No: GU1/1920/9932

Order Quantity (Cubic Meter)	Quantity with this load (Cubic Meter)	Cumulative Quantity (Cubic Meter)
125	6	43

Pouring Location / Structure :

Whether this concrete is pumped by RDC concrete: Yes/No

Time discharged completed: Time released from site: Water added at site: Admixture added at site:

Remarks:

Please note: This concrete delivery is subject to the terms and a condition of sales shown in our quotation. The time is allowed for unloading this delivery is 15 minute. We reserve the right to charge for any detention beyond this time as per our quotation. Any un authorized addition of water and/or any other material to concrete shall absolve us from any liability whatsoever. Any deficiency in methods of placing, compacting, finishing and curing of concrete adopted at site may affect quality of concrete in the finished work, for which we shall not be held liable and responsible. Any disputes that arise on quantity and quality (except comp. strength) of concrete supplied in this load shall be reported to us in writing within 24 hours from the time of delivery. In no event shall we be liable for direct, indirect, incidental or consequential damage arising out of use of this product, even if advised of possibility of such damage. In no case shall our liability exceed the purchase price of this product. 24% interest per annum will be charged from the date of Invoice on the amount remaining partly or wholly unpaid after due date.

*This document also constitutes as a Delivery Chellan.

I hereby confirm that:

1. We have accepted delivery of concrete as per the details mentioned above. 2. We have authorized addition of any water and/or admixture as mentioned above.



Certified that the particulars given above are true and correct and amount indicated represents the price charged and that there is no flow of additional consideration directly or indirectly from the buyer

For RDC Concrete (India) Pvt Ltd.

Authorised Signatory

Caution: Cement and concrete contain lime and other chemicals which can cause irritation, dermatitis and burning. To avoid harm to skin, minimize contact with wet concrete and wear suitable protective clothing. Whenever contact occur (whether directly or through saturated clothing) wash thoroughly.

Receiver Signature & Seal

8432
22/12/21 9.40
PB 10 HP 3109
PC Smith

Established In 1993
RDC Concrete
RDC Concrete (India) Private Limited

TAX INVOICE
RDC CONCRETE (INDIA) PRIVATE LIMITED
Village Behrampur, Sector 59, Sector 59, Gurgaon, Dist-Gurgaon
HR, PIN - 122011



Phone : 6239317406

Email Id : customercare@rdcconcrete.com

GSTIN : 06AAACU0108Q1ZC

PAN : AAACU0108Q

CIN : U74999MH1993PTC172842 TAN : MUMR22552F

Bill To Party

Party Name : S.S. Construction Co (Bharti Reality)
RAMKRISHAN HOUSE, NEAR MLA TEJPAL
TANWAR KOTHI, VILL. RAMGARII PO
BADSHAPUR
GURGAON, HARYANA 122101
06AEFPS1460P1Z3

Address :
GSTIN :
PAN :
Invoice Number : 1GU21ARS12762
Invoice Date : 14-11-2021
State : HARYANA
State Code : 06
DC No : 1GU21ARS12762
DC Date : 14-11-2021 13:40:01
Sales Order : 100621600409

Ship To Party

Party Name : S.S. Construction Co (Bharti Reality)
Site Bharti reality C/O Asthetic Township Developers
Pvt Ltd
Near IFFCO Chowk Metro Station, Sec- 27
GURGAON, HARYANA 122002
06AEFPS1460P1Z3
GSTIN :
PAN :
Terms of Payment : 30 Days
Transport Mode : By Road LUT No:
State : HARYANA Code: 06
Vehicle No : HR68B1812
Place of Supply : GURGAON
Date of Supply : 14-11-2021
PO No : SSC/Bharti/MO-74/11/21 Dated 10-Nov-21
20fe79ac11fae0add37c319fce8adca80faeff621f08ca8c
9f0f211202a8bfab
132111539705370
Ackno. Number :
Ackno. Date : 2021-11-14 13:42:00

Whether tax is payable on reverse charge basis: No

Sl. No	Description of Goods	HSN Code	UOM	Qty	Unit Price	Basic Amount	CGST %	CGST Amount	SGST %	SGST Amount	IGST %	IGST Amount	Gross Amount (Without TCS)
1	M30	38245010	CUM	5	5100	25500.00	9	2295.00	9	2295.00		0	30090.00
Grand Total										30120.09			

TCS % : 0.100 TCS Amount : 30.09 KFC% : KFC Amount : 0.00

Note: 1M3=2400Kgs +/-5%

Net Value in Rupees : Rupees Thirty Thousand One Hundred Twenty and paise

Nine Cementitious Type Max. Agg Size Admixture type Slump Min. Cementitious Content
OPC+PFA 20mm PCEA Slump : 150 +/- 25 mm

Batch No: GU1/1920/9834 Cumulative Quantity (Cubic Meter)
Order Quantity (Cubic Meter) Quantity with this load (Cubic Meter)
300 5 90

Pouring Location / Structure : Time of arrival on site:
Whether this concrete is pumped by RDC
concrete: Yes/No Time released from site: Water added at site: Admixture added at site:
Time discharged completed:

Remarks:

Please Note: This concrete delivery is subject to the terms and a condition of sales shown in our quotation. The time is allowed for updating this delivery is 15 minute. We reserve the right to charge for any detention beyond this time as per our quotation. Any on authorized addition of water and/or any other material to concrete shall absolve us from any liability whatsoever. Any deficiency in methods of placing, compacting, finishing and curing of concrete adopted at site may affect quality of concrete in the finished work, for which we shall not be held liable and responsible. Any disputes that arise on quantity and quality (except comp. strength) of concrete supplied in this load shall be reported to us in writing within 24 hours from the time of supply. In no event shall we be liable for direct, indirect, incidental or consequential damage arising out of use of this product, even if advised of possibility of such damage. In no case shall our liability exceed the purchase price of this product. In case of any discrepancies in the invoice please inform us within 3 working days from the date of invoice, otherwise it will be assumed that the invoice is correct and accepted. 24% interest per annum will be charged from the date of invoice on the amount remaining party or wholly unpaid after due date. *This document also constitutes as a Delivery Challen.

We have accepted delivery of concrete as per the details mentioned above. 2. I/We have authorized addition of any water and for admixture as mentioned above hereby confirm that



Certified that the particulars given above are true and correct and amount indicated represents the price charged and that there is no flow of additional consideration directly or indirectly from the buyer

For RDC Concrete (India) Pvt Ltd.

Authorised Signatory

Caution: Cement and concrete contain lime and other chemicals which can cause irritation, dermatitis and burning. To avoid harm to skin, minimize contact with wet concrete and wear suitable protective clothing. Whenever contact occur (whether directly or through saturated clothing) wash thoroughly.

Receiver Signature & Seal

8384

14/11/21 14:40
HR 68/B. 1812
RDC Singh

Established In 1993

RDC Concrete

RDC Concrete (India) Private Limited

TAX INVOICE**RDC CONCRETE (INDIA) PRIVATE LIMITED**Village Behrampur, Sector 59, Sector 59, Gurgaon Dist-Gurgaon
HR, PIN - 122011

Phone : 6239317406

Email-Id : customercare@rdcconcrete.com

GSTIN : 06AAACU0108Q1ZC

PAN : AAACU0108Q

CIN : U74999MH1993PTC172842 TAN : MUMR22552F

Bill To Party

Party Name : S.S. Construction Co (Bharti Reality)
RAMKRISHAN HOUSE, NEAR MLA TEJPAL
TANWAR KOTHI, VILL. RAMGARH PO
BADSHAPUR
GURGAON, HARYANA 122101
06AEFPS1460P1Z3

GSTIN

PAN

Invoice Number : 1GU21ARS12705

Invoice Date : 12-11-2021

State : HARYANA

State Code : 06

DC No : 1GU21ARS12705

DC Date : 12-11-2021 16:28:40

Sales Order : 100621600410

Ship To Party

Party Name : S.S. Construction Co (Bharti Reality)
Site Bharti reality C/O Asthetic Township Developers
Pvt Ltd
Address : Near IFFCO Chowk Metro Station, Sec- 27
GURGAON, HARYANA 122002
06AEFPS1460P1Z3

GSTIN

PAN

Terms of Payment : 30 Days

Transport Mode : By Road LUT No:

State : HARYANA Code: 06

Vehicle No : HR68B3279

Place of Supply : GURGAON

Date of Supply : 12-11-2021

PO No: PO No. SSC/Bharti/WO-74/11/21 Dated 10-Nov-21

PO No: 210139d7bd2d423636d2bda32de71ab7d3412ce29cc

IRN : 58bfd21f0ba270a4273d

Ackno. Number : 132111532584495

Ackno. Date : 2021-11-12 16:30:00

Whether tax is payable on reverse charge basis: No

Sl. No	Description of Goods	HSN Code	UOM	Qty	Unit Price	Basic Amount	CGST %	CGST Amount	SGST %	SGST Amount	IGST %	IGST Amount	Gross Amount (Without TCS)
1	M80, HIGH PERFORMANCE CRETE	38245010	CUM	8	7300	43800.00	9	3942.00	9	3942.00		0	51684.00

TCS % : 0.100

TCS Amount : 51.68

KFC % :

KFC Amount : 0.00

Grand Total

51735.68

Net Value in Rupees : Rupees Fifty One Thousand Seven Hundred Thirty Five and paise Sixty Eight

Note: 1M3=2400Kgs +/-5%

Cementitious Type	Max. Agg Size	Admixure type	Slump	Min. Cementitious Content
OPC+PFA	20mm	PCEA	Flow : 650 - 800 mm	

Batch No: GU11/1920/9777

Order Quantity (Cubic Meter)	Quantity with this load (Cubic Meter)	Cumulative Quantity (Cubic Meter)
200	6	34

Pouring Location / Structure :

Whether this concrete is pumped by RDC concrete: Yes/No

Time of arrival on site:

Time discharged completed:

Time released from site:

Water added at site:

Admixure added at site:

Remarks:

Please Note: This concrete delivery is subject to the terms and a condition of sales shown in our quotation. The time is allowed for updating this delivery is 15 minutes. We reserve the right to charge for any detention beyond this time as per our quotation. Any on authorized addition of water and/or any other material to concrete shall absolve us from any liability whatsoever. Any deficiency in methods of placing, compacting, finishing and curing of concrete adopted at site may affect quality of concrete in the finished work, for which we shall not be held liable and responsible. Any disputes that arise on quantity and quality (except comp. strength) of concrete supplied in this load shall be reported to us in writing within 24 hours from the time of supply. In no event shall we be liable for direct, indirect, incidental or consequential damage arising out of use of this product, even if advised of possibility of such damage. In no case shall our liability exceed the purchase price of this product. In case of any discrepancies in the invoice please inform us within 3 working days from the date of invoice, otherwise it will be assumed that the invoice is correct and accepted.

4% interest per annum will be charged from the date of invoice on the amount remaining partly or wholly unpaid after due date.

*This document also constitutes as a Delivery Challan.

I hereby confirm that:

1. We have accepted delivery of concrete as per the details mentioned above. 2. We have authorized addition of any water and for admixture as mentioned above.



For RDC Concrete (India) Pvt Ltd.

Certified that the particulars given above are true and correct and amount indicated represents the price charged and that there is no flow of additional consideration directly or indirectly from the buyer

Authorised Signatory

Caution: Cement and concrete contain lime and other chemicals which can cause irritation, dermatitis and burning. To avoid harm to skin, minimize contact with wet concrete and wear suitable protective clothing. Whenever contact occur (whether directly or through saturated clothing) wash thoroughly.

Receiver Signature & Seal


8333

12/11/21

17:00

HR68B - 3279

Mr Singh



Name of the Plant:
Address of the Plant

RP-GURGAON-I, DELHI / 4336
PLOT NO./KH.NO.-1527/916/2/2, 1528/916/2/3, REVENUE
ESTATE VILLAGE,
GURGAON 06-HARYANA 122001
AAACL4159L

Pin No.
TIN.

06AAACL4159L1ZC
U26940MH1999PLC118229

State Code : 06
State Name : Haryana

Principal P.O.B

CHIDIYA, CHARKHI DADRI, BHIWANI, 06-HARYANA - 123306.
CIN

TAX INVOICE

Invoice Number
Date & Time
Dispatch Mode
Receipt Voucher No.
Receipt Voucher Date
Reverse Charge

:210710039066
:09.11.2021 01:26:00
:BY ROAD

Sales Type
Sales Order No.
Customer PO / DATE
Name of Transporter
Reference Number
Ewaybill Number

:FOR - FREE ON ROAD
:0130229724/SO/4336
:66/10/21//07.10.2021
:
:2107036553
:331377927767

Customer Code
Name of Customer
Address of Customer

:50000947
:S.S.CONSTRUCTION CO.
:SATISH SURI
:RAMKRISHAN HOUSE, NEAR MLA TEJPAL
:TANWAR KOTHI VILL
:PO BADSHAPUR GURGAON 06-HARYANA
:122101

Job Site Code
Name of Job Site
State Code
Address of Job Site

:0021845913
:BHARTI REALTY
:
:06
:ASTHETIC TOWNSHIP DEVELOPER
:P.LTD NR.IFFCO CHOWK
:SEC-27, GURUGRAM GURUGRAM
:06-HARYANA 122002

CMIX No.

:433691572014

State Code
PIN No.

:06
:AEFPS1460P

GSTIN No.
Contact Name
Telephone Number
Mobile Number
Email ID
Pump Serial No.

:06AEFPS1460P1Z3
:VIPIN CHAUHAN
:9719919797
:9719919797
:suriconstructions@yahoo.com
:

MAIL ID.

:vishalgupta@gmail.com

Name of Product

:RMC

HSN/SAC

:38245010

Exemption Notification if any

:Walls/Columns/Slab/Foundation/Other

Sales Person's Name
Sales Person's Contact No.

POURING LOCATION

Sl. No.	Description	Vehicle No.	Qty.	UOM	Grade	Delivery Type	Material Code	Old Mat. Code
1	M30 FLUIDE AE MO D20 M075	HR56B0968	7.000	M3	M30	JustDelivery	9000043791	CMUGFE2BI301

	Rate	Amount
Basic Price/Taxable Value	4,800.00	33,600.00
SGST @ 9 %	432.00	3,024.00
CGST @ 9 %	432.00	3,024.00
Rounding		0.00
Total Gross Value of Goods - In Figures	5,664.00	39,648.00

Total Gross Value of Goods - In Words THIRTY NINE THOUSAND SIX HUNDRED FORTY EIGHT RUPEES ONLY

8997
09/11/2021
02:40
HR56B0968

For NUVOCO VISTAS CORP. LTD.

Authorized Signatory

SPECIFIED TARGET SLUM	W/O	MAX. AGG.	CHEM. ADM.	MIN. ADM.	MIN. CEMENT	CEMENT TYPE
JOB SITE ARRIVAL TIME	JOB POURING START TIME	JOB POURING END TIME	JOB SITE DEPARTURE TIME	PLANT ARRIVAL TIME		

Received the above items in Good condition.


Dhanwinder Singh
Customer Name, Signature & Seal

Established In 1993

RDC Concrete

RDC Concrete (India) Private Limited

TAX INVOICE
RDC CONCRETE (INDIA) PRIVATE LIMITED
Village Behrampur, Sector 59, Sector 59, Gurgaon, Dist-Gurgaon
HR, PIN - 122011



Phone: 6239317406

GSTIN: 06AAACU0108Q1ZC

Email-Id: customercare@rdconcrete.com

PAN: AAACU0108Q

CIN: U74999MH1993PTC172842 TAN: MUMR22552F

Bill To Party

Party Name: S.S. Construction Co (Bharti Realty)
Address: RAMKRISHAN HOUSE, NEAR MLA TEJPAL
TANWAR KOTHI, VILL. RAMGARII PO
BADSHAPUR
GURGAON, HARYANA 122101
06AEFPS1460P1Z3

GSTIN: 06AAACU0108Q1ZC
PAN: AAACU0108Q
Invoice Number: 1GU21ARSI2575
Invoice Date: 02-11-2021
State: HARYANA
State Code: 06
DC No: 1GU21ARSI2575
DC Date: 02-11-2021 18:04:39
Sales Order: 100621600364

Ship To Party

Party Name: S.S. Construction Co (Bharti Realty)
Address: Site Bharti realty C/O Asthetic Township Developers
Pvt Ltd
Near IFFCO Chowk Metro Station, Sec- 27
GURGAON, HARYANA 122002
06AEFPS1460P1Z3

GSTIN: 06AAACU0108Q1ZC
PAN: AAACU0108Q
Terms of Payment: 30 Days
Transport Mode: By Road LUT No:
State: HARYANA Code: 06
Vehicle No: HR68B0510
Place of Supply: GURGAON
Date of Supply: 02-11-2021
PO No: PO No. SSC/Bharti/WO-68/10/21 Dated 07-Oct-21
1860707aa13b2388cac15c1431752eddbebf1f1716c0b
b1f8ccc5875f470cd5
132111497625280
2021-11-02 18:06:00
Ackno. Number: 132111497625280
Ackno. Date: 2021-11-02 18:06:00

Whether tax is payable on reverse charge basis: No

Sl. No	Description of Goods	HSN Code	UOM	Qty	Unit Price	Basic Amount	CGST %	CGST Amount	SGST %	SGST Amount	IGST %	IGST Amount	Gross Amount (Without TCS)
1	M60, HIGH PERFORMANCE CRETE	3824501 0	CUM	7	7030	49210.00	9	4428.90	9	4428.90		0	58067.80
TCS %: 0.100		TCS Amount: 58.07		KFC %:		KFC Amount: 0.00		Grand Total		58125.87			

Net Value in Rupees: Rupees Fifty Eight Thousand One Hundred Twenty Five and paise Eighty Seven

Note: 1M3=2400Kgs +/-5%

Cementitious Type	Max. Agg Size	Admixture type	Slump	Min. Cementitious Content
OPC+PFA	20mm	PCEA	Slump: 180 +/- 25 mm	
Batch No: GU1/1920/9646	Order Quantity (Cubic Meter)	Quantity with this load (Cubic Meter)	Cumulative Quantity (Cubic Meter)	
	200	7	188.5	

Pouring Location / Structure:

Whether this concrete is pumped by RDC concrete: Yes/No

Time discharged completed:

Time released from site:

Water added at site:

Admixture added at site:

Remarks:

Please Note: This concrete delivery is subject to the terms and a condition of sales shown in our quotation. The time is allowed for updating this delivery is 15 minutes. We reserve the right to charge for any detention beyond this time as per our quotation. Any unauthorized addition of water and/or any other material to concrete shall absolve us from any liability whatsoever. Any deficiency in methods of placing, compacting, finishing and curing of concrete adopted at site may affect quality of concrete in the finished work, for which we shall not be held liable and responsible. Any disputes that arise on quantity and quality (except comp. strength) of concrete supplied in the load shall be reported to us in writing within 24 hours from the time of supply. In no event shall we be liable for direct, indirect, incidental or consequential damage arising out of use of this product, even if advised of possibility of such damage. In no case shall our liability exceed the purchase price of this product. 24% interest per annum will be charged from the date of invoice on the amount remaining party or wholly unpaid after due date. This document also constitutes as a Delivery Challan.

We confirm that:

We have accepted delivery of concrete as per the details mentioned above. 2. I/We have authorized addition of any water and for admixture as mentioned above.



Certified that the particulars given above are true and correct and amount indicated represents the price charged and that there is no flow of additional consideration directly or indirectly from the buyer

Raj Kumar

For RDC Concrete (India) Pvt Ltd.

Signature

Authorised Signatory

Caution: Cement and concrete contain lime and other chemicals which can cause irritation, dermatitis and burning. To avoid harm to skin, minimize contact with wet concrete and wear suitable protective clothing. Whenever contact occur (whether directly or through saturated clothing) wash thoroughly.

Receiver Signature & Seal

8242
02/11/21
18:55
HR 6813-0510
J Singh

Name of the Plant: RP-GURGAON-I, DELHI / 4336
 Address of the Plant: PLOT NO./KH.NO.-1527/916/2/2,1528/916/2/3,REVENUE
 ESTATE VILLAGE,
 GURGAON 06-HARYANA 122001
 PAN No. : AAACL4159L
 GSTIN : 06AAACL4159L1ZC
 CIN : U26940MH1999PLC118229
 IRN : 702b404aad322773879c1799899547044d8531062cc780c5ce4f219f27337f7d
 Principal P.O.B : CHIDIYA, CHARKHI DADRI, BHIWANI, 06-HARYANA - 123306.
 CIN

TAX INVOICE

Tax Invoice Number : 210710037774
 Date & Time : 31.10.2021 04:43:00
 Dispatch Mode : BY ROAD
 Receipt Voucher No. :
 Receipt Voucher Date :
 Reverse Charge :
 Sales Type : FOR - FREE ON ROAD
 Sales Order No. : 0130228976/SO/4336
 Customer PO / DATE : 66/10/21/07.10.2021
 Name of Transporter :
 Reference Number : 2107035354
 Ewaybill Number : 361375895168
 Customer Code : 50000947
 Name of Customer : S.S.CONSTRUCTION CO.
 Address of Customer : SATISH SURI
 : RAMKRISHAN HOUSE, NEAR MLA TEJPAL
 TANWAR KOTHI VILL
 PO BADSHAPUR GURGAON 06-HARYANA
 122101
 Job Site Code : 0021845913
 Name of Job Site : BHARTI REALTY
 State Code : 06
 Address of Job Site : ASTHETIC TOWNSHIP DEVELOPER
 P.LTD NR.IFFCO CHOWK
 SEC-27,GURUGRAM GURUGRAM
 06-HARYANA 122002
 BCMIX No. : 433691571771
 State Code : 06
 PAN No. : AEFPS1460P
 EMAIL ID : vishalgupta@gmail.com
 GSTIN No. : 06AEFPS1460P1Z3
 Contact Name : VIPIN CHAUHAN
 Telephone Number : 9719919797
 Mobile Number : 9719919797
 Email ID : suriconstructions@yahoo.com
 Pump Serial No. :
 Name of Product : RMC
 HSN/SAC : 38245010
 Exemption Notification if any :
 POURING LOCATION : Walls/Columns/Slab/Foundation/Other

Sl. No	Description	Vehicle No.	Qty.	UOM	Grade	Delivery Type	Material Code	Old Mat. Code
--------	-------------	-------------	------	-----	-------	---------------	---------------	---------------

1	M60 ROBUSTE AE MO D20 M0055	HR56B9282	6.000	M3	M60	JustDelivery	9000039809	CMHMF2BF36C
---	-----------------------------	-----------	-------	----	-----	--------------	------------	-------------

Price Elements	Rate	Amount
Basic Price/Taxable Value	7,000.00	42,000.00
SGST @ 9 %	630.00	3,780.00
CGST @ 9 %	630.00	3,780.00
Rounding		0.00
Total Gross Value of Goods - In Figures	8,260.00	49,560.00

Total Gross Value of Goods - In Words FORTY NINE THOUSAND FIVE HUNDRED SIXTY RUPEES ONLY

8194
 31/10/21 06:00
 HR56B9282
 DCS/mh

For NUVOCO VISTAS CORP. LTD.

Authorized Signatory

SPECIFIED TARGET SLUM	W/O	MAX. AGG.	CHEM. ADM.	MIN. ADM.	MIN. CEMENT	CEMENT TYPE
JOBSITE ARRIVAL TIME	JOB POURING START TIME	JOB POURING END TIME	JOBSITE DEPARTURE TIME	PLANT ARRIVAL TIME		

Received the above items in Good condition.

Customer Name, Signature & Seal

Established In 1993

RDC Concrete

RDC Concrete (India) Private Limited

TAX INVOICE**RDC CONCRETE (INDIA) PRIVATE LIMITED**
Village Behrampur, Sector 59, Sector 59, Gurgaon, Dist-Gurgaon
HR, PIN - 122011

Phone : 6239317406

Email Id : customercare@rdconcrete.com

GSTIN : 06AAACU0108Q1ZC

PAN : AAACU0108Q

CIN : U74999MH1993PTC172842 TAN : MUMR22552F

Bill To Party

Party Name : S.S. Construction Co (Bharti Reality)
RAMKRISHAN HOUSE, NEAR MLA TEJPAL
TANWAR KOTHI, VILL. RAMGARII PO
BADSHAPUR
GURGAON, HARYANA 122101
06AEFPS1460P1Z3

Address :
GSTIN :
PAN :
Invoice Number : 1GU21ARS12283
Invoice Date : 22-10-2021
State : HARYANA
State Code : 06
DC No : 1GU21ARS12283
DC Date : 22-10-2021 07:23:17
Sales Order : 100621600355

Ship To Party

Party Name : S.S. Construction Co (Bharti Reality)
Site Bharti reality C/O Asthetic Township Developers
Pvt Ltd
Near IFFCO Chowk Metro Station, Sec- 27
GURGAON, HARYANA 122002
06AEFPS1460P1Z3

Address :
GSTIN :
PAN :
Terms of Payment : 30 Days
Transport Mode : By Road LUT No:
State : HARYANA Code: 06
Vehicle No : HR68B8278
Place of Supply : GURGAON
Date of Supply : 22-10-2021
PO No : PO No. SSC/Bharti/WO-68/10/21 Dated 07-Oct-21
IRN : 070369af10f6e7731a0a12f66b4350fbbbbe897b64803f
26b59ac7059f4e217
132111435954236
2021-10-22 07:24:00

Ackno. Number :
Ackno. Date :

Whether tax is payable on reverse charge basis: No

Sl. No	Description of Goods	HSN Code	UOM	Qty	Unit Price	Basic Amount	CGST %	CGST Amount	SGST %	SGST Amount	IGST %	IGST Amount	Gross Amount (Without TCS)
1	M30	38245010	CUM	2	4750	9500.00	9	855.00	9	855.00		0	11210.00
Grand Total												11221.21	

TCS % : 0.100 TCS Amount : 11.21 KFC % : KFC Amount : 0.00

Note: 1M3=2400Kgs +/-5%

Net Value in Rupees : Rupees Eleven Thousand Two Hundred Twenty One and paise Twenty One

Cementitious Type	Max. Agg Size	Admixture type	Slump	Min. Cementitious Content
OPC+PFA	20mm	PCEA	Slump : 150 +/- 25 mm	

Batch No: GU1/1920/9354 Quantity with this load (Cubic Meter) Cumulative Quantity (Cubic Meter)

Order Quantity (Cubic Meter)

2

34

Pouring Location / Structure :

Whether this concrete is pumped by RDC concrete: Yes/No

Time of arrival on site:

Time discharged completed:

Time released from site:

Water added at site:

Admixture added at site:

Remarks:

Please Note: This concrete delivery is subject to the terms and a condition of sales shown in our quotation. The time is allowed for updating this delivery is 15 minutes. We reserve the right to charge for any detention beyond this time as per our quotation. Any un authorized addition of water and/or any other material to concrete shall absolve us from any liability whatsoever. Any deficiency in methods of placing, compacting, finishing and curing of concrete adopted at site may affect quality of concrete in the finished work, for which we shall not be held liable and responsible. Any disputes that arise on quantity and quality (except comp. strength) of concrete supplied in this load shall be reported to us in writing within 24 hours from the time of supply. In no event shall we be liable for direct, indirect, incidental or consequential damage arising out of use of this product, even if advised of possibility of such damage. In no case shall our liability exceed the purchase price of this product. In case of any discrepancies in the invoice please inform us within 3 working days from the date of invoice, otherwise it will be assumed that the invoice is correct and accepted.

24% interest per annum will be charged from the date of invoice on the amount remaining party or wholly unpaid after due date.
*This document also constitutes as a Delivery Challan.

I hereby confirm that:

1. I/We have accepted delivery of concrete as per the details mentioned above. 2. I/We have authorized addition of any water and/or admixture as mentioned above.



Certified that the particulars given above are true and correct and amount indicated represents the price charged and that there is no flow of additional consideration directly or indirectly from the buyer

For RDC Concrete (India) Pvt Ltd.

Authorised Signatory

Caution: Cement and concrete contain lime and other chemicals which can cause irritation, dermatitis and burning. To avoid harm to skin, minimize contact with wet concrete and wear suitable protective clothing. Whenever contact occur (whether directly or through saturated clothing) wash thoroughly.

Receiver Signature & Seal

8064
22/10/2021
07:15
HR68B8278
Sankar Singh



DELIVERY CHALLAN

UltraTech Cement Limited

UltraTech
CONCRETE
 WE MAKE GOOD CONCRETE BETTER

Unit Address:-

158, Naurangpur
Gurgaon - 122001 Haryana

GSTIN: 06AAACL6442L1ZE

CIN No: L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No:

Recipient PO Date: 15/10/2021

Name & Address of Recipient

S.S. CONSTRUCTION CO.
RAMKRISHAN HOUSE NEAR MLA TEJAPALTANWAR,
KOTHIVILL RAMGARH PO BADSHAPUR,
GURUGRAM 122001

Name & Address of Delivery

S.S. CONSTRUCTION CO. (SEC-27)
BHARTI REALTY C/O ASTHETIC TOWNSHIP I
NR. IFFCO CHOWK METRO STATION SEC-27,
GURUGRAM 122001Place of Supply: GURGAON CITY
State Code: 06
Recipient GSTN/UIN No: 06AEFPS1460P123State Code: 06
State: HARYANADelivery Challan No: 205236546
Delivery Challan Date: 15/10/2021
Order No: 6605797
Order Qty: 30.00
Cum Qty: 15.50
HSN Code: 38245010
Plant Code: 824

Description of Goods: M60 - HIGH STRENGTH CONCRETE

TM Qty (M3):- 3.50 Date & Time of Removal of Goods: 15/10/2021 23:28:19

Transporter Details:

Transporter Name:
Vehicle No: MH12LT8732
Mode of Transport: By Road
Pump Descp:
Destination:LR No:
LR Date: 15/10/2021
Pump Qty:
Inco Term: FOR

Particulars	Quantity	UOM	Rate Per Unit (in Rs.)	Amount (in Rs.)
Basic	3.50	M3	7000.00	24500.00
CGST @ 9.00%				2205.00
SGST @ 9.00%				2205.00
Round Off				0.00
Total Invoice Value:				28910.00

Driver Name: XYZ

Driver MobNo: 9990948737

Amount in Words:- Four Thousand Four Hundred Ten Rupees and Zero Paise
Twenty-Eight Hundred Nine Hundred Ten Rupees and Zero Paise

Certified that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Unit: Gurgaon - II - Navrangpur

Checked By

Authorised Signatory

We hereby confirmed that we have received above referred material in good condition

Date:

Signature Name & Mobile No of Person/Party
Who receiving the material with rubber stampCement Type:
Min Cem Content: OPC
Max Size Aggr: 20MM
Slump at SiteChemical Admix Type: ADMHYPLAST
Mineral Admix Type: FLYASHR
Slump Specified:
Water Added at Site:Batching Time: 23:27:43
Pour Structure:
Max W/C Ratio: 0.27
Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA20MM	188.00	0.00	188.00	658.00	658.00	0.00
FACS	709.00	0.00	709.00	2481.50	2481.50	0.00
CA10MM	688.00	0.00	688.00	2408.00	2408.00	0.00
CEMOPC	450.00	0.00	450.00	1575.00	1575.00	0.00
FLYASHR	160.00	0.00	160.00	560.00	560.00	0.00
ADMHYPLAST	5.10	0.00 kg	5.10	17.85	17.85	0.00
WATERR	165.00	0.00 kg	165.00	577.50	577.50	0.00
TOTAL	2365.10		2365.10	8277.85	8277.85	0.00

M/S - 35 kg cum

Vikram

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT BE RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

DELIVERY CHALLAN

UltraTech
 CONCRETE

Unit Address:-

 158, Naurangpur
 Gurgaon - 122001 Haryana

GSTIN: 06AAAC16442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No:

Recipient PO Date: 06/10/2021

 Name & Address of Recipient
 S.S. CONSTRUCTION CO.
 RAMKRISHNAN HOUSENEAR MLA TEJPALTANWAR,
 KOTHIVILL RAMGARH PO BADSHAPUR,
 GURUGRAM 122001

 Name & Address of Delivery
 S.S. CONSTRUCTION CO. (SEC-27)
 BHARTI REALTY C/O ASTHETIC TOWNSHIP I
 NR. IFFCO CHOWK METRO STATION SEC-27,
 GURUGRAM 122001

 Place of Supply: GURGAON CITY
 State Code: 06
 Recipient GSTIN/UIN No: 06AEFPS1460P123

 State Code: 06
 State: HARYANA

 Delivery Challan No: 205235939
 Delivery Challan Date: 06/10/2021
 Order No: 6603095
 Cum Qty: 70.00
 HSN Code: 21.00
 Plant Code: 3824 50 10
 824

Description of Goods: M30 REGULAR GRADE CONCRETE

TM Qty (M3):- 7.00

Date & Time of Removal of Goods: 06/10/2021 00:50

Transporter Details:

 Transporter Name: BANSAL CORPORATION
 Vehical No: HR56B9070
 Mode of Transport: By Road
 Pump Descp: Line Pump
 Destination:

 LR No:
 LR Date: 06/10/2021
 Pump Qty:
 Inco Term: FOR

Particulars	Quantity	UOM	Rate Per Unit (in Rs.)	Amount (in Rs)
Basic	7.00	M3	3800.00	33600.00
CGST @ 9.00%				3024.00
SGST @ 9.00%				3024.00
Round Off				0.00
Total Invoice Value:				39648.00

Driver Name: ASZX

Driver Mob No: 9718991156

 Amount in Words:- Six Thousand Forty-Eight Rupees and Zero Paise
 Amount in Words:- Thirty-Nine Thousand Six Hundred Forty-Eight Rupees and Zero Paise

I hereby confirmed that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Unit: Gurgaon - II - Navrangpur

Checked By

We hereby confirmed that we have received above referred material in good condition

Date:

 Cement Type:
 Min Cem Content: OPC
 Max Size Aggr: 20MM
 Slump at Site

 Chemical Admix Type: ADMHYPLAST
 Mineral Admix Type: FLYASHR
 Slump Specifide: 120+-25
 Water Added at Site:

 Signature Name & Mobile No of Person/Party
 Who receiving the material with ruber stamp

 Batching Time: 00:47:26
 Pour Structure:
 Max W/C Ratio: 0.41
 Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA20MM	665.00	-0.50	661.66	4631.62	4617.95	-0.30
FACS	749.00	0.50	752.76	5269.32	5250.10	-0.37
CA10MM	443.00	-0.50	440.77	3085.39	3089.75	0.14
CEMOPC	300.00	0.00	300.00	2100.00	2099.80	-0.01
FLYASHR	100.00	0.00	100.00	700.00	699.00	-0.14
ADMHYPLAST	2.20	-0.60 kg	1.60	11.20	11.37	1.54
WATERR	165.00	1.80 kg	166.80	1167.60	1168.65	0.09
TOTAL	2424.20		2423.59	16965.13	16936.62	-0.17

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION. WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

Annexure-XVII

Electricity Approval for Construction

Office of the
Executive Engineer, Electrical Inspectorate, Haryana, Block C-2,
Sushant Lok-I, Huda Primary School Building,
Gurugram (e-mail: xenceiggn@gmail.com).

To

M/s S.S Construction Co.
C/o M/s Asthetic Township Developers Pvt. Ltd.
Sector-27, Near Millenium Plaza,
Gurugram

Memo No: H.T.I/ 14110

Dated: 21/08/2020

Subject: Inspection of HT installation comprising of 1x200 KVA 11/0.433KV T/F installed at S.S Construction Co., Gurugram.

The subject cited installation was inspected by this department on 21.08.2020 and the same was found generally complying with the relevant provisions of CEA (Measures Relating to Safety and Electric Supply) Regulations, 2010.

The following observations be attended under intimation to this office:

1. Earth pits be maintained and marked properly for identification.

Approval for energisation of the subject cited installations is hereby accorded subject to consistent compliance of the relevant provisions of CEA Regulations, 2010 in the installation at your end. Please note that it shall be the responsibility of the owner of electrical installations to maintain and operate the installations in a condition free from danger and as recommended by the manufacturer or by the relevant code of practice of the Bureau of Indian Standards.

Your next inspection shall fall due in the month of August every year. You are therefore requested to deposit inspection fee as per schedule under the Head of A/c "0043-Taxes and Duties on Electricity Fees payable under I.E Rules, 1956" and send the original receipted treasury challan to this office one month before the due date.


Executive Engineer,
Electrical Inspectorate, Haryana,
Gurugram.

CC: The SDO/AGM OP S/Divn., DHBVN, DLF S/Divn., Gurugram for information and necessary action.

DHBVN

DAKSHIN HARYANA BIJLI VITARAN NIGAM
Office of the SDO DLF City Sub Division
DHBVN, Sec-31, Gurugram- 122001 (Haryana)
0124-2384755 Website www.dhbvn.com Email ID: sdodlfcity@gmail.com

From

SDO,
DLF City Sub-Divn.
D.H.B.V.N, Gurugram

To

The Executive Engineer,
M&P Division,
DHBVN, Gurugram.

Memo No. 4589

Date 28/8/2020

Sub: -

Performa for release of new HT CT meter connection of SS Construction co
Ashtetic Township Developers Pvt Ltd. Sec 27 Gurugram. A/C No. G 21-620-
43 San load 150 KW NDS, category.


Enclosed please find here with the Performa for release of new connection
having San. Load 150 KW of the subject cited consumer for further action in your office please

DA/ As above:-

SDO,
DLF City Sub-Divn.
D.H.B.V.N, Gurugram

PERFORMA FOR RELEASE OF LT CT CONNECTION OF M&P DIVISION.

1. NAME OF SUB-DIVISION: DLF City S/Division Gurugram
2. NAME OF DIVISION: Sub-Urban Division Gurugram
3. NAME OF CIRCLE: "OP" Circle Gurugram
4. NAME OF CONSUMER & A/C NO.: S S Constraction Co..
Online Application no.G-21-620-43.
5. NATURE/KIND OF INDUSTRY: NDS
6. LOCATION OF PREMISES: Asthetic Township Developers Pvt Ltd, Gurugram.
7. S.J.O NO. & DATE: SCO no. G-21-620-43 Date
8. SANCTION LOAD/CONTRACT DEMAD: 150 KW
9. CONNECTED LOAD VERIFIED BY A.G.M.: 150 KW
10. PARTICULARS OF ELECTRONIC METER & CT: Meter Sr no.-X1258217, GS 1125/20, Secure,-/5 A
HT/CT's Sr. no. 3838 A,B,C .MAKE-ELTECH.HT
CT CAPICITY -10/5A.
11. SIZE OF LT/CT CABLE: 95 mm
12. CAPACITY OF TRANSFORMER INSTALLED: 200 KVA T/F
13. CAPACITY OF CAPACITOR INSTALLED: NA
14. DETAILS OF HOUSING THE METERING EQUIPMENT: Near pole
15. WHETHER THE INSTALLATION HAS BEEN INSPECTED & DECLARED FIT FOR ENERGISATION BY CEI-HARYANA:
16. SYSTEM VOLTAGE ON WHICH CONNECTION IS PROPOSED TO BE RELEASED: 400 KV


SDO,
DLF City S/Divn.
D.H.B.V.N, Gurugram

DAKSHIN HARYANA BIJLI VITRAN NIGAM LTD. **STORES CHALLAN BOOK**

Book No. 15

Date. 25-8-20

Serial No. 55

From

To

S.D.O. M&T Lab GGN

S.D.O. D.L.F city S/DIVISION

Lorry No.

Name of Driver

GEM

Through. Sh. Ashok KUMAR JE

Serial No.	Sr. No. of Meter	Block Number	Make	Capacity	Reading	Remarks
	1	2	3	4	5	6
I	3 IN. HT. CTS. make - Jai Durga	VA=5	clan 20.85	ROL		
	CTS No 2	HC 21852				520 to 79 km
		HC 21859	Jai Durga	Ratio	At No = 46683.3806	
		HC 21860	3X5/5	5/5		
			M/S DLF Ltd.	Primary	School	
	M&T	Sub N.M. 7867038	39	40		
	Accuracy checked in Lab and Found <u>WIP</u>					
				Received by		

Issuing Officer

Store Issued.

Date.

JE M&T Lab
 DHBVN Gurgaon

S.S. Construction Co.
ENGINEERS & CONTRACTORS

S.C.O. 375, IInd Floor
Sector 37-D, Chandigarh
Ph.: 0172-2691095
Fax : 0172-2691095

E-mail : suriconstructions@yahoo.co
info@ssconstructions.in
Website : www.ssconstructions.in

Ref. No. SSC/BHARTI/2020/01

Cash/ce

24/8/20

Dated 24 Aug 2020

To

SDO
DHBVN
SECTOR 31 Gurgaon.

Sub: CUBICAL METER PANNEL FEES
WITH CPT

ALNO 89717550273

Respected Sir,

Enclosed herewith please find the
DD No. 092696 dt 24/8/2020 of amount 32600
for the above mentioned fees.

You are request to do the needful.

Thanking you in anticipation.

For S.S. CONSTRUCTION CO.

Authorised Signatory

RAJINDER SINGH

for SS Construction

Mb- 85972

Book No.

001108

R.No.

L.D. Center

188

R.O.No. 4

Account No.

Received from Shri.

sum of Rs.

subject to realization

89717550273

SS Construction

MF Sec-27 Haryana

by Cash/Cheque/M.O.

32600

092696

MORE

Cashier

Dakshin Haryana Bijli Vitran Nigam

Energy & Other Charges	ED	Bank Charges	Total Amount
HT panel cost			32600
			1
			32600

Att.

DD - M

M/S S.S. Construction Co.
 Address: Aesthetic Township Development (P) Ltd.
 Description of Premises: Sector-27 Gurgaon Dom./Comm./SP. Supply
 Application No.: E-21-620-43 Date: Gurgaon A/C No.:
 Owner of premises Self
 From W. Contractor
 & Valid upto

M/S ANKUR ELECTRICALS
 'A' Class Electric Contractor
 11 KVA Licence No. H-382/A

Supervisor
 Name of Supervisor
 SHRI

No. 94 To The S.D.O.
 D.H.B.V.N. Ltd.
 Tattal-local 150. k.w. Detail
 Back side

REPORT

Please note the Electrical Installation belonging to above consumer detailed on back in now ready for the Board's test.

The installation was tested by me/us. 24/07/20 (Date) and insulation resistance was shown the reverse of the Test Report.

Signature of Contractors

For TEHSIL Gurgaon ONLY

BOARD INSTALLATION TEST ORDER

To The Junior Engineer.
 Please test the installation details on back page fill in column and report as below and (in the case of subsequent due to the first providing installation to be defective) collect Rs.in advance.

.....S.D.O. Date.....

REPORT

Above installation as tested by me (Date).....and the installation was as show on me back page

- Remark:
1. Whether first subsequent visit.....
 2. Whether contractor or his representative has been present.....
 3. Whether installation defective.....
 4. Whether charge of Rs. has been collected (if due)
 5. Signature.....

Junior Engineer.....Date.....

M/S ANKUR ELECTRICALS
A' Class Electrician Contractor
11 KVA Licence No. H-382/A

Signature Wiring Contractor

License No. H-.....

Annexure-XVIII

Current photographs of site



GPS Map Camera



Gurugram, Haryana, India

661, Sushant Lok Phase I, Sector 27, Gurugram,
Haryana 122009, India


Lat 28.465922°

Long 77.07401°

09/04/22 01:45 PM



GPS Map Camera

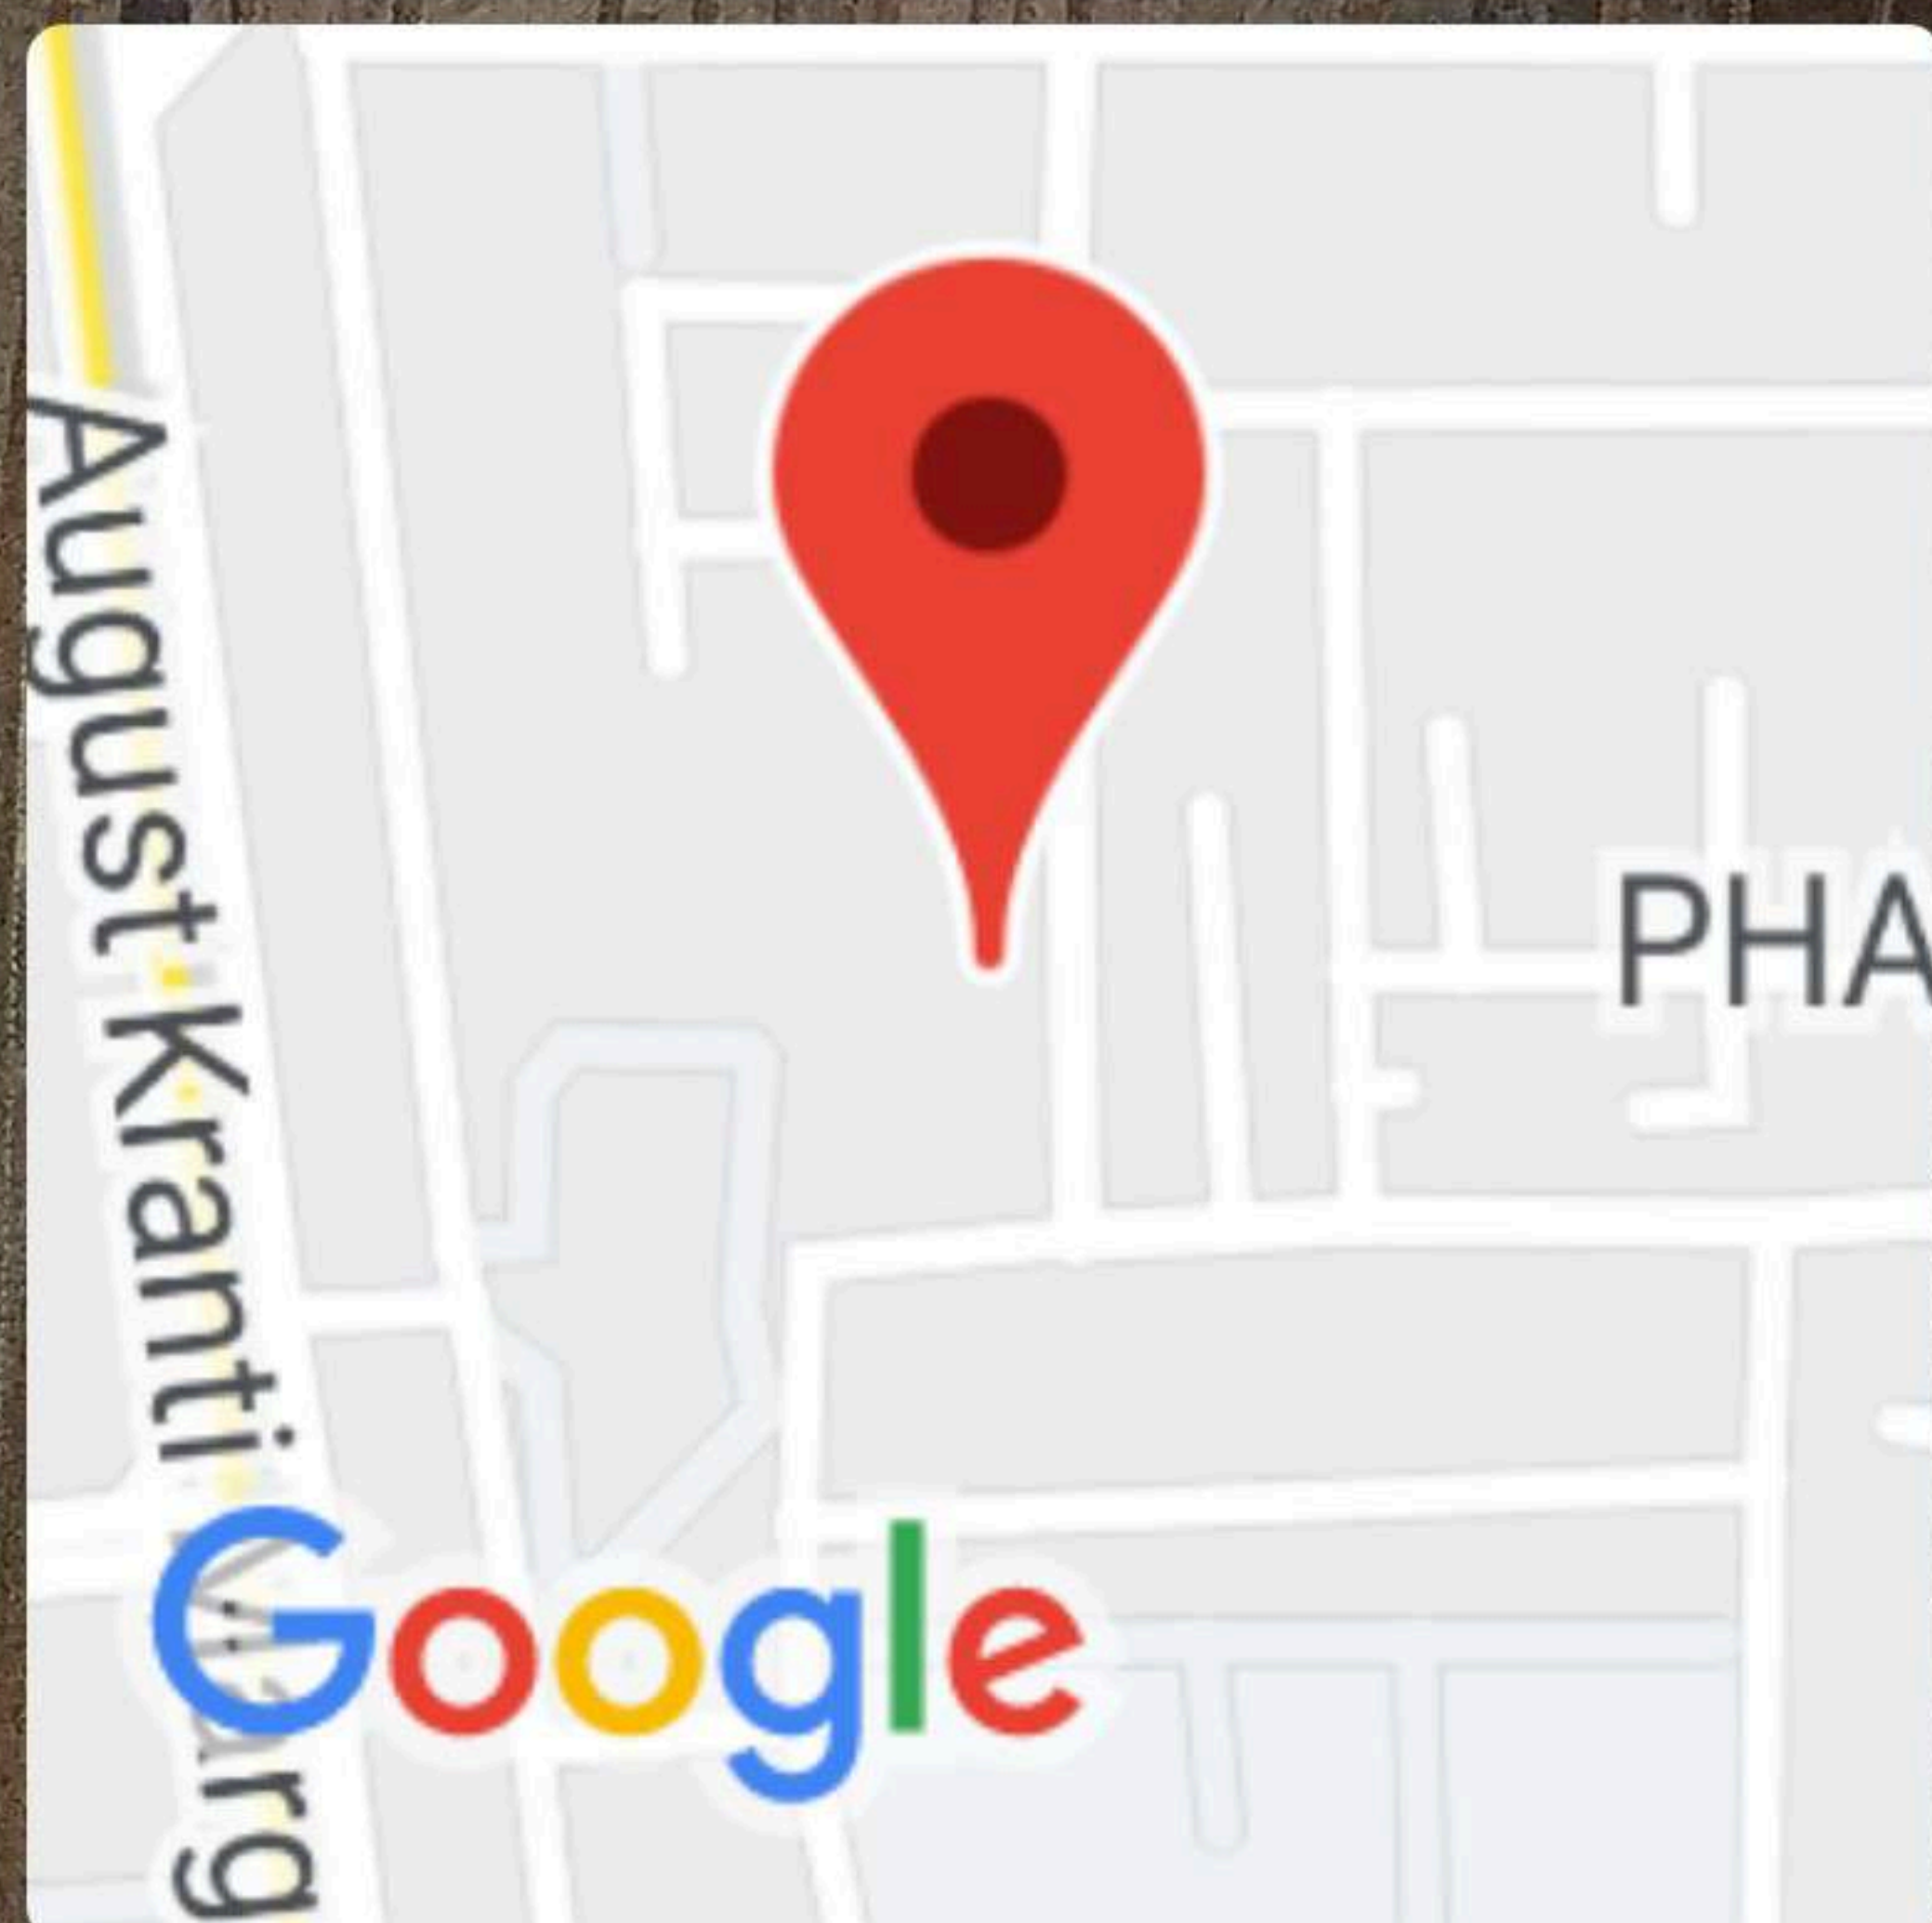

Gurugram, Haryana, India

**361A, Sushant Lok Phase I, Sector 27, Gurugram,
Haryana 122009, India**

Lat 28.465724°

Long 77.075322°

09/04/22 02:13 PM

Annexure-XIX

Photographs of Basic Infrastructure provided at Project Site

Photographs of Basic Infrastructure

1. Drinking water facility for workers



2. Toilets for workers



3. Labour Hutment



4. Safety instructions on site, First Aid, Emergency Hospitals and contact numbers display





Annexure-XX

AAI NOC



भारतीय विमानपत्तन प्राधिकरण AIRPORTS AUTHORITY OF INDIA

AAI/RH&NR/ATM/NOC/2019/117/527-530

M/s Asthetic Township Developers Pvt. Ltd.

262, DDA Office Complex, Jhandewalan
Extn, New Delhi-110055

Date: 25-03-2019

Valid Upto: 24-03-2027

No Objection Certificate for Height Clearance

1. This NOC is issued by Airports Authority of India (AAI) in pursuance of responsibility conferred by and as per the provisions of Govt. of India (Ministry of Civil Aviation) order GSR751 (E) dated 30th Sep. 2015 for Safe and Regular Aircraft Operations.

2. This office has no objection to the construction of the proposed structure as per the following details:

NOC ID :	PALM/NORTH/B/030819/377136
Applicant Name*	Satya Pal Singh
Site Address*	Proposed Commercial colony on site admeasuring 11537.57 Sq. Meter located at Sector-27, Rect No. 59, Village - Sukhrati, Gurugram, Haryana, Sukhrati, Gurgaon, Haryana
Site Coordinates*	77 04 26.27-28 27 57.54, 77 04 26.95-28 27 59.06, 77 04 26.98-28 27 55.15, 77 04 26.98-28 27 57.11, 77 04 29.45-28 27 57.08, 77 04 29.48-28 27 55.11, 77 04 30.08-28 27 57.93, 77 04 30.55-28 27 55.13, 77 04 31.77-28 27 59.03, 77 04 31.80-28 27 56.10
Site Elevation in mtrs AMSL as submitted by Applicant*	241.95 M
Permissible Top Elevation in mtrs Above Mean Sea Level(AMSL)	346.95M

*As provided by applicant

3. This NOC is subject to the terms and conditions as given below:

a. Permissible Top elevation has been issued on the basis of Site coordinates and Site Elevation submitted by Applicant. AAI neither owns the responsibility nor authenticates the correctness of the site coordinates & site elevation provided by the applicant. If at any stage it is established that the actual data is different, this NOC will stand null and void and action will be taken as per law. The office in-charge of the concerned aerodrome may initiate action under the Aircraft (Demolition of Obstruction caused by Buildings and Trees etc.) Rules, 1994"

b. The Site coordinates as provided by the applicant in the NOC application has been plotted on the street view map and satellite map as shown in ANNEXURE. Applicant/Owner to ensure that the plotted coordinates corresponds to his/her site. In case of any discrepancy, Designated Officer shall be requested for cancellation of the NOC.

c. Airport operator or his designated representative may visit the site (with prior coordination with applicants or owner) to ensure that NOC terms & conditions are complied with.

d. The Structure height (including any superstructure) shall be calculated by subtracting the Site elevation in AMSL from the Permissible Top Elevation in AMSL i.e. Maximum Structure Height - Permissible Top Elevation minus (-) Site Elevation.

e. The issue of the 'NOC' is further subject to the provisions of Section 9-A of the Indian Aircraft Act, 1934 and any notifications issued there under from time to time including the Aircraft (Demolition of Obstruction caused by Buildings and Trees etc.) Rules, 1994.

क्षेत्रीय मुख्यालय उत्तरी क्षेत्र, परिचालन कार्यालय परिसर रंगपुरी, नई दिल्ली - 110037 दूरभाष संख्या - 91-11-25653566

Regional headquarter Northern Region, Operational Offices Complex Rangpuri, New Delhi-110 037 Tel: 91-11-25653566

K. K. A. Kabir
25/03/19
के के ए कबीर / K. K. A. KABIR
महानिदेशक (वायु वातावरण प्रबन्धन-उत्तरी क्षेत्र) / General Manager (ATM), NR
भारतीय विमानपत्तन प्राधिकरण / Airports Authority of India
प्रचालन कार्यालय / Operational Offices
राजकीय वायुमार्ग रोड नई दिल्ली-37/Rangpuri, Gurugram Road, New Delhi-37

"हिंदी पत्रों का स्वागत है।"



भारतीय विमानपत्तन प्राधिकरण AIRPORTS AUTHORITY OF INDIA

f. No radio/TV Antenna, lighting arresters, staircase, Mumtec, Overhead water tank and attachments of fixtures of any kind shall project above the Permissible Top Elevation of 346.95M (AMSL), as indicated in para 2.

g. Use of oil, electric or any other fuel which does not create smoke hazard for flight operations is obligatory, within 8 KM of the Aerodrome Reference Point.

h. The certificate is valid for a period of 8 years from the date of its issue. One time revalidation without assessment may be allowed, provided construction work has commenced, subject to the condition that such request shall be made within the validity period of the NOC and the delay is due to circumstances which are beyond the control of the developer.

i. No light or a combination of lights which by reason of its intensity, configuration or colour may cause confusion with the aeronautical ground lights of the Airport shall be installed at the site at any time, during or after the construction of the building. No activity shall be allowed which may affect the safe operations of flights

j. The applicant will not complain/claim compensation against aircraft noise, vibrations, damages etc. caused by aircraft operations at or in the vicinity of the airport.

k. Day markings & night lighting with secondary power supply shall be provided as per the guidelines specified in chapter 6 and appendix 6 of Civil Aviation Requirement Series B Part I Section 4, available on DGCA India website: www.dgca.nic.in

l. The applicant is responsible to obtain all other statutory clearances from the concerned authorities including the approval of building plans. This NOC for height clearances is to ensure the safe and regular aircraft operations and shall not be used as document for any other purpose/claim whatsoever, including ownership of land etc.

m. This NOC has been issued w.r.t. the Civil Airports. Applicant needs to seek separate NOC from Defence, if the site lies within their jurisdiction. Applicants also need to seek clearance from state Govt. as applicable, for sites which lies in the jurisdiction of unlicensed aerodrome as outlined in Rule 13 of GSR751 (E)

n. In case of any discrepancy/interpretation of NOC letter, English version shall be valid.

o. In case of any dispute w.r.t site elevation and/or AGL height, top elevation in AMSL shall prevail.


Chairman NOC Committee



Region Name: NORTH

Address: General Manager Airports Authority of India, Regional Headquarter, Northern Region, Operational Offices, Gurgaon Road, New Delhi-110037

Email ID: noc_nr@aai.aero

Contact No: 011-25653551

 25/03/19
के के ए कबीर / K. K. A. KABIR सहायक (वायु यातायात प्रबन्धन-उत्तरी क्षेत्र) / General Manager (ATM), NR भारतीय विमानपत्तन प्राधिकरण / Airports Authority of India प्रबन्धन कार्यालय / Operational Offices रंगपुरी, गुग्रांम रोड, नई दिल्ली-37/Rangpuri, Gurgaon Road, New Delhi-37

Name / Designation / Sign with Date	
Prepared By :	 Narceenjam ATM (ATM)
Verified By :	 25/3/19 मधु.म.नं. (एटीएम)

क्षेत्रीय मुख्यालय उत्तरी क्षेत्र, परिचालन कार्यालय परिसर रंगपुरी, नई दिल्ली - 110037 दूरभाष संख्या - 91-11-25653566
Regional headquarter Northern Region, Operational Offices Complex Rangpuri, New Delhi-110 037 Tel: 91-11-25653566

" हिंदी पत्रों का स्वागत है "

Distance From Nearest Airport And Bearing

Airport Name	Distance (Meters) from Nearest ARP	Bearing (Degree) from Nearest ARP
I.G.I Airport	11897.44	196.42
Rohini Heliport	31696.15	175.98
Safdarjung Airport	18348.83	223.29
NOCID	PALM/NORTH/B/030819/377136	

Street view



March 8 2019

Scale: 1:3,000
 0 500 1000 1500 2000 2500 3000 3500 4000 4500 5000 5500 6000 6500 7000 7500 8000 8500 9000 9500 10000 10500 11000 11500 12000 12500 13000
 0 0.5 1 1.5 2 2.5 3 3.5 4 4.5 5 5.5 6 6.5 7 7.5 8 8.5 9 9.5 10 10.5 11 11.5 12 12.5 13
 0 0.5 1 1.5 2 2.5 3 3.5 4 4.5 5 5.5 6 6.5 7 7.5 8 8.5 9 9.5 10 10.5 11 11.5 12 12.5 13
 Google Maps data © 2019 Google, Imagery © 2019 Google, Labels © 2019 Google, Terrain © 2019 Google, Streets © 2019 Google, Satellite © 2019 Google, All rights reserved.

Satellite View



March 8 2019

Scale: 1:3,000
 0 500 1000 1500 2000 2500 3000 3500 4000 4500 5000 5500 6000 6500 7000 7500 8000 8500 9000 9500 10000 10500 11000 11500 12000 12500 13000
 0 0.5 1 1.5 2 2.5 3 3.5 4 4.5 5 5.5 6 6.5 7 7.5 8 8.5 9 9.5 10 10.5 11 11.5 12 12.5 13
 0 0.5 1 1.5 2 2.5 3 3.5 4 4.5 5 5.5 6 6.5 7 7.5 8 8.5 9 9.5 10 10.5 11 11.5 12 12.5 13
 Google Maps data © 2019 Google, Imagery © 2019 Google, Labels © 2019 Google, Terrain © 2019 Google, Streets © 2019 Google, Satellite © 2019 Google, All rights reserved.



भारतीय विमानपत्तन प्राधिकरण
AIRPORTS AUTHORITY OF INDIA

File No. AAI/RHQ/NR/ATM/NOC/2019/117/527-530.

Copy to:

1. The Distt. Town Planner, Gurgaon, HUDA, Complex, Sector-14, Gurgaon, Haryana.
2. The Chief Executive Officer, Delhi International Airport, New Uddan Bhawan, I.G.I Airport Terminal -3, New Delhi-110037.
3. Guard file.

Annexure-XXI

Copy of receipt from MCG

From G-8 Rule-IV

रसीद



नाम : S.S CONSTRUCTION COMPANY

पता : HQ- 27, SUSHNAT LOK B BLOCK, SECTOR 27, GURUGRAM

गुरुग्राम नगर निगम कार्यालय गुरुग्राम।

निम्न खाते में जमा करने के लिए ऑनलाइन 128905065135 वसूल पाया।

रसीद नं.: 1727467

करदाता का खाता नं./बिल नं./नोटिस नं. व:	अदायगी का विवरण	रकम/रुपये. पैसे
130-50	Construction Demulation Waste Income	10800.00

अदायगी की तिथि/समय: 16/10/2021 11:21 AM

Payment made by cheque is subject to realization **MCG MUNICIPAL CORPORATION GURUGRAM**

CCS:CFC3, MEMO NO: JC/HQ/MCG/2021/775 DATED: 16-10-2021 C & D WASTE TOTAL QUANTITY IN KG: 15000 KG CARD NO.5857 INVOICE NO.001984,Ref.ID2:

PermitsPro, Mob.:9599445520, AccountNo:130-50

जोड़ = 10800.00

(In words: Ten Thousand Eight Hundred)


रसीद जारी करने वाले के हस्ताक्षर
Parmod Kumar

From G-8 Rule-IV

रसीद



नाम : S.S CONSTRUCTION COMPANY

पता : HQ. 27, SUSHANT LOK, B FLOCK, SECTOR 27, GGN

गुरुग्राम नगर निगम कार्यालय गुरुग्राम

निम्न खाते में जमा करने के लिए ऑनलाइन 127109251287 वसूल पाया।

रसीद नं.: 1704349

करदाता का खाता नं./बिल नं./नोटिस नं. व.	अदायगी का विवरण	रकम/राशियाँ देते
130-50	Construction Demulation Waste Income	7200.00

अदायगी की तिथि/समय: 28/09/2021 02:59 PM

MCG

जोड़ = 7200.00

Payment made by cheque is subject to realization **MUNICIPAL CORPORATION GURUGRAM**

(In words: Seven Thousand Two Hundred)

DT:5/10/21, MEMO NO: JC/HQ/MCG/2021/689 DATED: 28-09-2021 C & D WASTE TOTAL QUANTITY IN KG: 10000 KG CARD NO.4201 INVOICE NO.001927 Ref ID2:

PermittoPro, Mob:9599445520 AccountNo:150-50

(Signature)

रसीद जारी करने वाले के हस्ताक्षर
Parmod Kumar

From G-8 Rule-IV

रसीद



रसीद नं.: 1654067

नाम : S S CONSTRUCTION COMPANY
पता : HQ-27, SUSHANT LOK B-BLOCK, SECTOR 27, GURUGRAM
गुरुग्राम नगर निगम कार्यालय गुरुग्राम।
निम्न खाते में जमा करने के लिए ऑनलाइन 120110026944 वसूल पाया।

करदाता का खाता नं./बिल नं./नोटिस नं. व:	अदायगी का विवरण	रकम/रुपये. पैसे
130-50	Construction Demulation Waste Income	7200.00

अदायगी की तिथि/समय: 20/07/2021 03:50 PM

Payment made by cheque is subject to realization

MCG
MUNICIPAL CORPORATION GURUGRAM

(In words: Seven Thousand Two Hundred)

CCS:CFC2, MEMO NO: JC/HQ/MCG/2021/439 DATED: 20-07-2021 C & D WASTE TOTAL QUANTITY IN KG: 10000 KG CARD NO.4201 INVOICE NO.000839, Ref.ID2:

PermitsPro, Mob.:9599445520, AccountNo:130-50

रसीद जारी करने वाले के हस्ताक्षर
Parmod Kumar

Annexure-XXII
Copy of Purchase AACs block


SHREE CEMENT LIMITED

UP GRINDING UNIT, 12, SIKANDRABAD INDUSTRIAL AREA, SIKANDRABAD-203205, UP

TAX INVOICE

ORIGINAL FOR BUYER

Invoice No. : SC/REG/127	PAN No. : AACCS8796G	CIN No. : L26943RJ1979PL0001935	TAN No. : 2275579000
Invoice No. : 137/21 P/9659	Date : 28-MAR-22	DI No. : 27912157	DI Date : 28-MAR-22
Invoice No. : 137/206378	Type : SC/AACBRIC K	GR/RR No. : F01/VIS/2322	GR/RR date : 28-MAR-22
Billed to : S/S CONSTRUCTION CO MEHAM KRISHAN, B/O RAM KRISHAN HOUSE, NEAR ME A TEJ PAL 5, 23/32 UP VILL, RAMGARH, RADSHAHPUR, GURGAON, Haryana		Delivery At : S/S CONSTRUCTION CO BHARTI REALTY, C/O ASTHETIC TOWNSHIP DEVELOPERS PVT LTD, NEAR (RT) CHOWK METRO SEC27, GURGAON, Haryana	
State : Haryana	State Code : 06	Place of Supply : Haryana	
GST No. : 06A1F0K146011/3	PAN : AEFPS1460P	Reverse Charge : No	
Mode : ROAD	Term : FOR		
Payment Type : Bill to Bill	Delivery is FOR, all the transit risk lies with supplier		
VISHAI: ROADLINES			
Invoice No. : 137/206378	Date : 28-MAR-22		
Invoice No. : 137/206378	Validity : 30		
Invoice No. : 137/206378	Rs. 542 PMT		
Invoice No. : 137/206378	Date : 28-MAR-2022		



Description of Goods	HSN	Qty(MT)	Qty(Cum)/Nos/Bags	Rate/CUM	Amount (Rs)
	68159910	17.52	24 768	3380.96	811.13

After Discount Total Taxable Amount

IGST 5% 4057.15

Tax Collected at Source (Sale) 1% 85.2

Total invoice amount (in Rs.) 85285.35

Amount in words : Rs Eighty Five Thousand Two Hundred Eighty Five And Paise Thirty Five only

Wagon No.	Qty. (Bags)	Qty. (MT)	Actual Wt. (MT)	Charged Wt. (MT)	Freight PMT(Rs.)	Total Freight(Rs.)

Vehicle 29/3/22

Digitally signed by PRAVEEN CHANDRA MEHROTRA
Date: 2022.03.28 20:58:28
For Shree Cement Limited

(Authorised Signatory)

Payment against this invoice should be made by A/C Payee
Please DD RTGS/NEFT ACH/UPIMPS
Only name of SHREE CEMENT LTD.
Payment made after 30 days of invoice
Payment made after 30 days of invoice

ASTHETIC TOWNSHIP DEVELOPERS PVT. LTD.
Gate Entry No. 9882
Date: 29/03/22
Time: 05:05
Vehicle No. HR-61P-7598
Received By: *[Signature]*


SHREE CEMENT LIMITED

UP GRINDING UNIT, 12, SIKANDRABAD INDUSTRIAL AREA, SIKANDRABAD-203205, UP

TAX INVOICE

ORIGINAL FOR BUYER

PAN No: AACCS8796G		CIN No: L26943RJ1979PLC001935		TAN No: JCHS1964	
Date: 24-MAR-22		DI No: 27871049		DI Date: 23-MAR-22	
Type: SC/AACBRIC K		GR/RR No: FGE/SCT/244		GR/RR date: 23-MAR-22	
Billed to: S. S. CONSTRUCTION CO. BHARTI REALTY C/O ASTHRIC TOWN SHIP DEVELOPERS PVT LTD, NEAR IFFCO CHOWK METRO SEC27, GURGAON, Haryana			Delivery At: S. S. CONSTRUCTION CO. BHARTI REALTY C/O ASTHRIC TOWN SHIP DEVELOPERS PVT LTD, NEAR IFFCO CHOWK METRO SEC27, GURGAON, Haryana		
State: Haryana		State Code: 06		Place of Supply: Haryana	
PAN: AEFPS1460P		Reverse Charge: No			
Term: FOR		Delivery is FOR, all the transit risk lies with supplier			
SHREE CHHILLAR TRANSPORT COMPANY					
Date: 24-MAR-22					
Validity: Rs. 527 PMT					
Date: 24-MAR-2022					

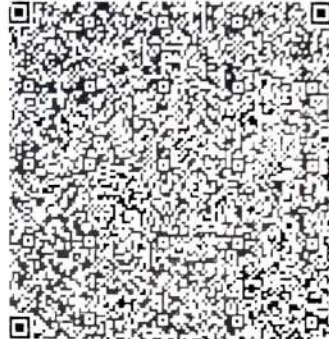

Description of Goods	HSN	Qty(MT)	Qty(Cum)/Nos/Bags	Rate/CUM	Amount (Rs)
	68159910	33.58	46	3142.86	144571.43
			1472		

15 packets damaged

After Discount Total Taxable Amount

IGST 5% 7228.57

Tax Collected at Source (Sale) 1% 151.8

Total invoice amount (in Rs.)

151951.8

Amount in words : Rs One Lakh Fifty One Thousand Nine Hundred Fifty One And Paise Eighty only

Wagon No.	Qty. (Bags)	Qty. (MT)	Actual Wt. (MT)	Charged Wt. (MT)	Freight PMT(Rs.)	Total Freight(Rs.)
Total:						

Signature

Digitally signed by PRAVEEN CHANDRA MEHROTRA Date: 2022.03.24 01:29:59

For Shree Cement Limited

(Authorised Signatory)

Note: 1. 100% Input tax credit is allowable from invoice price as per the applicable provisions of law.
 2. Payment against this invoice should be made by A/C Payee cheque/DD/RTGS/NEFT/ACH/UPI/IMPS.
 3. Only in name of "SHREE CEMENT LTD".
 4. Discount 1% will be charged if payment made after 30 days of invoice date.
 5. Jurisdiction: Pan-asthan Jurisdiction only.

ASTHRIC TOWNSHIP DEVELOPERS PVT. LTD.
 Gate Entry No. 25/103/2022
 Date: 24-03-2022
 Time: 15:19
 Received By: [Signature]
 Received Date: 24-03-2022

Head Office: 12, Sikandrabad Industrial Area, Sikandrabad-203205, UP.
 New Delhi: 110002, Phase-II, M.G. Road, Gurgaon, Haryana-122002.
 Phone: (91) 11-23731084, 23731085 Fax: (91) 11-23731084

Date-23/2/22

GRAHA date 22-FEB-20

Delivery At

Delivery At: RAJ CONSTRUCTION CO
REALTY, COASTAL TOWNSHIP DEVELOPERS PVT LTD, NEAR PCCO
STATION, MIDT STREET, GURGAON, Haryana

Reverse Charge :

State	EXPENSE	State Code	Dr
ATTN: Mr. J. J. J. J. J.		PAN	ATTN: J. J. J. J.

Freight Mode	ROAD / ROAD	Term	FOB
Freight Type	To the Buyer	Delivery is FOB, all the transport risk on with supplier	
Driver Mobile			
Transporter	VISUAL ROADLINE		


Way (H₀: No) Date 3/11/20

Lance Kirby	<i>Vice</i>	Date
		Validity

3. Luck, N. G.	101107529	Eng. 1973 DMI
----------------	-----------	---------------

Journal of Interpersonal Violence 26(10) 1987-2001
© The Author(s) 2011
Reprints and permissions: <http://www.sagepub.com/journalsPermissions.nav>

Date: 2011-11-14 20:22



6 per damage

Description of Goods	HSN	Qty(MT)	Qty(Cum)/Nos/ Bags	Rate/CUM	Amount (Rs)
WATER RESISTANT COAT	68159910	17.52	24		
			768	3142.88	75428

After Discount Total Taxable Amount

IGST 5%	3771.45
---------	---------

Total Invoice amount (In Rs.)	76200.46
-------------------------------	----------

Amount in words : Rs Seventy Nine Thousand Two Hundred And Paise Forty Five only

Wagon No.	Qty. (Bags)	Qty. (MT)	Actual Wt. (MT)	Charged Wt. (MT)	Freight PMT(Rs.)	Total Freight(Rs.)
Total						

ASTHETIC TOWNSHIP DEVELOPERS PVT LTD

Case: any No. 9243

Date 23/02/2021

Time... 05:45

NR 6127578

Digitally signed by PRAVEEN
CHANDRA MEHROTRA
Date: 2022.02.23 02:46:48

For Shree Cement Limited

This is not a declaration of a conflict of interest. It is a declaration of a conflict of interest.

Payment against this invoice should be made by A/C Payne

cheque/024TGS/NUT/ACH/PI/MP3

Only in name of "SHREE CEMENT LTD"

^(c) The charged if payment made after 30 days of invoice

TABLE 1. *Mean values of the variables measured in the 1000 m and 2000 m races*

(Authorised Signatory)

© 2003 Blackwell Publishing Ltd *British Journal of Plastic Surgery* 56: 203–209

5. A. J. A. Cook, *Journal of the Royal Microscopical Society*, **117**, 122 (1997).

16. *Blackburn, J. and G. Blackburn* 1999. *Blackburn's* 110 (90) Phone: (911) 11-21/31084, 217-1085 Fax: (911) 11-23/21094

SHREE CEMENT LIMITED

UP GRINDING UNIT, 12, SIKANDRABAD INDUSTRIAL AREA, SIKANDRABAD-203205, UP
TAX INVOICE

GST No. : 09AACCS8796G1ZP				PAN No. AACCS8796G		CIN No. L26943RJ1979PLC001935		ORIGINAL FOR BUYER					
Invoice No. FGE/21/P/8997		Date 01-MAR-22		DI No. 27655112		TAN No. JDHS01295A							
Order No. 2021005860		Type SC/AACBRIC K		GR/RR No. FGE/VIS/2124		DI Date 01-MAR-22							
Billed to : 878580 S S CONSTRUCTION CO C/O MR RAM KRISHAN, R/O RAM KRISHAN HOUSE, NEAR MLA TEJ PAL JANWAR KOTHII, VILL RAMGARH, BADSHAHPUR, GURGAON, Haryana				Delivery At : S S CONSTRUCTION CO BHARTI REALTY C/O ASTHRIC TOWN SHIP DEVELOPERS PVT LTD, NEAR IFFCO CHOWK METRO SEC27, GURGAON, Haryana									
State Haryana		State Code 06		Place of Supply : Haryana									
GST No. 06AEFPS1460P1Z3		PAN AEFPS1460P		Reverse Charge : No									
Freight Mode ROAD / ROAD		Term FOR											
Freight Type To Be Billed		Delivery is FOR, all the transit risk lies with supplier											
Driver Mobile													
Transporter VISHAL ROADLINES													
Way Bill No. 411234584992		Date 01-MAR-22											
Distance(KM) 125		Validity											
Truck No. HR61D3145		Rs. 542 PMT											
IRN No. d9dcc3b981592ca014a8bb89da8719f30a32240aae92346 1c9c19600685a8e60													
Ack No. 142211049624022		Date 02-MAR-2022											
Description of Goods		HSN		Qty(MT)		Qty(Cum)/Nos/Bags		Rate/CUM		Amount (Rs)			
AACB 625250150 100SL		68159910		10.95		15 640		3142.87		47143			
After Discount Total Taxable Amount													
IGST 5%										2357.15			
Tax Collected at Source (Sale) 1%										49.5			
Total Invoice amount (in Rs.)										49549.65			
Amount in words : Rs Forty Nine Thousand Five Hundred Forty Nine And Paise Sixty Five only													
Wagon No.		Qty. (Bags)		Qty. (MT)		Actual Wt. (MT)		Charged Wt. (MT)		Freight PMT(Rs.)		Total Freight(Rs.)	
Total													

ASTHETIC TOWNSHIP DEVELOPERS PVT. LTD.

Gate Entry No. 9372

Date 02/03/22

Time 09:00

Digitally signed by PRAVEEN
CHANDRA MEHROTRA
Date: 2022.03.02 00:01:21

For Shree Cement Limited

Note:

- 1 Post Invoice discounts / incentives / variations from invoice value as per the declared schemes.
- 2 Payment against this invoice should be made by A/C Payee cheque/DD/RTGS/NEFT/ACH/UP/IMPS
- 3 Only in name of "SHREE CEMENT LTD"
- 4 Interest @ 18% would be charged if payment made after 30 days of invoice
- 5 Subject to Haryana (Rajasthan) Jurisdiction only

(Authorised Signatory)

Marketing Office

112/124, Block B, Bhawan, 1, Bahadur Nagar Marg, New Delhi 110022 Ph. 011-23370828, 23370776, Fax 23370729

11/101, Block B1, DLF Commercial Park, DLF City, Phase-III, M.G. Road, Gurugram, Haryana-122002

15A PCM Building, 16 Badli Amba Road, Connaught Place, New Delhi 110 001 Phone: (91) 11-23731084, 23731085 Fax (91) 11-23731084

Tax Invoice

(ORIGINAL FOR RECEIPT)

Trade Solutions Delhi B-166, Matiala Road Uttam Nagar New Delhi - 110059 MOB. NO. 9625637370 GSTIN/UIN: 07AAP160241121	Invoice No 024/21/22	e-Way Bill No 2012 1200 2796	Dated 25.02.2022
	Delivery Note		Mode/Terms of Payment
Consignee M/s S.S Construction Co. Bharti realty C/O Asthetic Township Developers Pvt Ltd Near IITCO Chowk metro station, Sec - 27, Gurgaon	Supplier's Ref 024/21/22		Other Reference(s)
	Buyer's Order No PO/TSD/21-22/WO-12-01-22		Dated 12.01.2022
	Despatch Document No.		Motor Vehicle No. HR63C4466
GSTIN/UIN: 06AFEP51460P123 State Name: HARYANA, Code: 06	Despatched through		Destination
Buyer (if other than consignee) M/s S.S Construction Co. Ramkrishan House, Near MLA Tejpal Tanwar Kothi Vill, Ramgarh PO Badshapur Gurgram PAN No. AAPIT6024J	Terms of Delivery		
GSTIN/UIN: 06AFEP51460P123 State Name: HARYANA, Code: 06			

S.N.	Description of Goods	HSN/SAC Code	Quantity	Unit	Rate	per	Disc %	Amount ()
1	AAC Block of 600x 250x 200 mm Thickness	68159910	25.0	M3	3142.83	M3		78,572.25
1 Feb 2022 ASTHETIC TOWNSHIP DEVELOPERS PVT. LTD. Gate Entry No. 7200 Date. 26/02/22 Time. 16:00 Vehicle No. HR63C 4466 Received By. [Signature]								3,928.61
OUTPUT IGST								82,500.82
Total			25.00					E & O E

Amount (in words)

Indian Rupees : Eighty Two Thousand five Hundred One Only.

GSTIN
06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123

06AFEP51460P123


SHREE CEMENT LIMITED

UP GRINDING UNIT, 12, SIKANDRABAD INDUSTRIAL AREA, SIKANDRABAD-203205, UP

TAX INVOICE

DUPLICATE FOR TRANSPORTER

Invoice No. AACCS8796G		PAN No. AACCS8796G		CIN No. L26343RJ1979PI C001935		TAN No. JDI1501295A	
Invoice Date 21-FEB-22		Date 21-FEB-22		DI No. 27562100		DI Date 21-FEB-22	
Invoice Type SC/AACBRIC K		Type SC/AACBRIC K		GR/RR No. FGE/VIS/2055		GR/RR date 21-FEB-22	
Delivered to S S CONSTRUCTION CO B HARTI REALTY C/O ASTHRIC TOWNSHIP DEVELOPERS PVT LTD NEAR JFFCO CHOWK METRO SEC 27, GURGAON, Haryana				Delivery At : S S CONSTRUCTION CO B HARTI REALTY C/O ASTHRIC TOWNSHIP DEVELOPERS PVT LTD NEAR JFFCO CHOWK METRO SEC 27, GURGAON, Haryana			
State Code 06		State Code 06		Place of Supply : Haryana		Reverse Charge : No	
PAN AEFPS1460P		PAN AEFPS1460P					
ROAD ROAD		Term FOR					
In Bill Mode		Delivery is FOR, all the transit risk lies with supplier					
VISHAL ROADLINES							
191/20591589		Date 21-FEB-22					
125		Validity					
HIS 542 PMT							
/010a1b5a0b71c5dca00fb04ac63f360956d7ac6bf8ad5f743cd44214141b892e							
140211027555230		Date 21-FEB-2022					



Description of Goods	HSN	Qty(MT)	Qty(Cum)/Nos/Bags	Rate/CUM	Amount (Rs)
	68159910	17.52	24 768	3142.88	75429

After Discount Total Taxable Amount

8 Pcs Damaged

IGST 5% 3771.45

Total invoice amount (in Rs.)

79200.45

Amount in words : Rs Seventy Nine Thousand Two Hundred And Paise Forty Five only

Wagon No.	Qty. (Bags)	Qty. (MT)	Actual Wt. (MT)	Charged Wt. (MT)	Freight PMT (Rs.)	Total Freight (Rs.)
Total						

ASTHETIC TOWNSHIP DEVELOPERS PVT. LTD.

Gate Entry No. 9224
 Date 22/02/22
 Time 06:30
 Vehicle No. HR 61 D 9698
 Received By. [Signature]
 Digitally signed by PRAVEEN CHANDRA MEHROTRA
 Date: 2022.02.21 19:22:33
 For Shree Cement Limited
 (Authorised Signatory)

Payment against this invoice should be made by A/C Payee
 within 10 days of invoice date
 Payment made after 30 days of invoice
 (Bank transaction only)

HIL Limited

HIL Limited, Amritsar, Punjab, India

HIL

TOGETHER, WE BUILD.

Dhagar

4106 Haryana

Phone No. 08221004709

GSTIN Number 06AAACH2676Q1Z4

PAN Number AAACH2676Q

CIN Number L749991G1955PLC000656

E-Mail Id

PIN 1510804db90ec8417e7c4dea8e7558a4254233463ec5 172470a78f0da7c1683

TAX INVOICE



Invoice Number	2018030797	Date & Time of Preparation	12-02-2022 & 18:12:36
Invoice Date	12-02-2022	Transporter Name	BHUVI LOGISTICS
Invoice Number & Date	759931 & 12-02-2022	LR/RR Number & Date	1957
Order Ref & DI	SSC/BHARTIWO-11/01/ & 12-01-2022	Vehicle/Lorry/Wagon No	HR55V5205
Delivery OBD No	81034295	Gross Weight	30,093.000 KG (30.093 MT)
Invoice Number	30 Days Direct Credit	Net Weight	30,093.000 KG (30.093 MT)
Payment Terms	30 Days Direct Credit	E-Way Bill No	361412401604
Delivery (Inco Terms)	F O R	Insurance Policy No	5005002118P117410203
ST Range : RANGE-3	GST Division: ROHTAK	GST Commissionerate: ROHTAK	State GST FARIDABAD (WEST) WARD - 5
Bill to Party 133779 S.S. CONSTRUCTION CO C/O MR Ram krishan, R/o Ram Krishan House, Near Mr. A Tej Pal Tanwar Kulb: Vill. Bangarh, PO - Badshah Pur., Gurgaon Gurgaon 122101, Haryana CIN Number GST Number : 06AEFPS1460P1Z3 PAN Number : AEFPS1460P Phone Number : 9599445520		Place of Supply 1133779-S.S. CONSTRUCTION CO. C/O Asthetic Township Developers Pvt Ltd, near IFFCO chowk metro station, Site Bharti realty, Sector- 27., GURUGRAM GURUGRAM, 122002, Haryana TIN Number GST Number : 06AEFPS1460P1Z3 PAN Number : AEFPS1460P Phone Number : 9599445520	

Material Code	Description of Goods/Services & HSN / SAC Code	Quantity	UOM	Volume (In M3)	Wt. in KG	Unit Rate	Basic Amount	Discount (-)	Taxable Amount In INR
81034295	FLY ASH BLOCKS (AAC) GR-1 600X250X200 MM HSN - 68159990	1.42	EA	42.9900	30,093	102.15	146378.87	-11296.07	135082.80
Insurance									29.72
Gross Amount							146378.87	-11296.07	135112.52
CGST @ 2.50 %									3,377.81
SGST @ 2.50 %									3,377.81
Total Amount									141,868.14

12 Pcs damage

HSN/SAC : 68159990 ARTICLES OF STONE OR OF OTHER MINERAL SUBSTANCES"

Tax Amount in Words (SGST/CGST/IGST) : Rupees Six Thousand Seven Hundred Fifty Five And Paise Sixty Two Only

Total Amount in Words : Rupees One Lakh Forty One Thousand Eight Hundred Sixty Eight And Paise Fourteen Only

Lorry Driver's Signature :

Location Date:

Signature of Supplier / Authorised Representative
For HIL LIMITED

1. On receipt of goods, the goods are delivered to the carrier/customer as applicable.

2. The carrier/customer is responsible for the goods from the time of receipt to the time of delivery.

3. The carrier/customer is responsible for the goods from the time of receipt to the time of delivery.

4. The carrier/customer is responsible for the goods from the time of receipt to the time of delivery.

5. The carrier/customer is responsible for the goods from the time of receipt to the time of delivery.

6. The carrier/customer is responsible for the goods from the time of receipt to the time of delivery.

7. The carrier/customer is responsible for the goods from the time of receipt to the time of delivery.

8. The carrier/customer is responsible for the goods from the time of receipt to the time of delivery.

9. The carrier/customer is responsible for the goods from the time of receipt to the time of delivery.

10. The carrier/customer is responsible for the goods from the time of receipt to the time of delivery.

Authorised Signatory

& OE

Regd. Office: L7 Floor, 12/12/22, 9086 ORIGINAL FOR BUYER
No. 133, Near Botanical Gardens, Gachibowli, Hyderabad - 500 032, Telangana, India.

Vehicle No. HR 55V 5205

HIL Limited

Akeri, near Jampur, Amadashahpur, Matantwal

HIL

TOGETHER, WE BUILD.

(A CK BIRLA GROUP OF COMPANIES)

TAX INVOICE



Bhagar

1/4 V/6 Haryana

Phone No: 08221004709

GSTIN Number: 06AAACH2676Q1Z4

PAN Number: AAACH2676Q

CIN Number: L74999TG1955PLC000656

E-Mail Id

IRN: e517937bfc859f1239752baa99ce09ae14d4be3b693034a61cf79e58aa0a2140

Invoice Number	2018030690	Date & Time of Preparation	07.02.2022 & 20.10.07
Invoice Date	07.02.2022	Transporter Name	RANA TRANSPORT
SO Number & Date	757679 & 07.02.2022	LR/RR Number & Date	3894
Order Ref & Dt	SSC/BHARTI/WO-11/01/ & 12.01.2022	Vehicle/Lorry/Wagon No	RJ32GC4153
Delivery / OBD No	81030997	Gross Weight	30.093.000 KG (30.093 MT)
L/C Number		Net Weight	30.093.000 KG (30.093 MT)
Payment Terms	30 Days Direct Credit	E-Way Bill No	311410346849
Delivery (Inco Terms)	F O R	Insurance Policy No	5005002118P117410203

GST Range : RANGE-3	GST Division: ROHTAK	GST Commissionerate: ROHTAK	State GST FARIDABAD (WEST) WARD - 5
------------------------	-------------------------	--------------------------------	--

Bill to Party

3779-S.S. CONSTRUCTION CO.
C/O MR. Ram krishan, R/o Ram Krishan House, Near MLA Tej Pal Tanwar
Kothi,
Vill- Ramgarh, PO- Badshahpur,, Gurgaon
Gurgaon, 122101 Haryana
TIN Number:
GST Number: 06AEFPS1460P1Z3
PAN Number: AEFPS1460P
Phone Number: 9599445520

Place of Supply

1133779-S.S. CONSTRUCTION CO.
C/O Asthetic Township Developers Pvt Ltd, near IFFCO chowk metro
station,
Site Bharti really, Sector- 27,, GURUGRAM
GURUGRAM, 122002, Haryana
TIN Number :
GST Number : 06AEFPS1460P1Z3
PAN Number : AEFPS1460P
Phone Number : 9599445520

Material Code	Description of Goods/Services & HSN / SAC Code	Quantity	UOM	Volume (In M3)	Wt. In KG	Unit Rate	Basic Amount	Discount (-)	Taxable Amount In INR
900310220	FLY ASH BLOCKS (AAC) GR-1 600X250X200 MM HSN - 68159990	1433	EA	42.9900	30.093	102.15	146378.87	-11296.07	135082.80

Insurance

Gross Amount

29.72

146378.87

-11296.07

135112.52

CGST @ 2.50 %

3,377.81

SGST @ 2.50 %

3,377.81

Total Amount

141,868.14

HSN/SAC : 68159990 ARTICLES OF STONE OR OF OTHER MINERAL SUBSTANCES

Tax Amount in Words (SGST/CGST/IGST) : Rupees Six Thousand Seven Hundred Fifty Five And Paise Sixty Two Only
Total Amount in Words : Rupees One Lakh Forty One Thousand Eight Hundred Sixty Eight And Paise Fourteen Only

Lorry Driver's Signature :

Location Date:

Signature of Supplier / Authorised Representative

Terms & Conditions

1. Our responsibility ceases once the goods are delivered to the carrier/customer as applicable.
2. No claim should be considered for damage or shortage thereafter.
3. Make - as - or - as - dispatched will NOT be taken back.
4. Price, terms and conditions mentioned on the bill are part and parcel of this supply transaction.
5. Weight is based on standard testing conditions.
6. Certified that the particulars given above are true and correct and the amount indicated represents the price actually charged and that there is no flow of additional considerations, directly or indirectly from the buyer.

For HIL LIMITED
Signature valid

Digitally Signed By
DS HIL LIMITED On
Mon 07-Feb-2022 20:14:01
PRADEEP RATHI
Authorised Signatory

E & OE

QUADRUPPLICATE FOR CTD

Read Office: L7 Floor, SLN Terminus, SY No. 133, Near Botanical Gardens, Gachibowli, Hyderabad - 500 032, Telangana, India.

Page 1 of 1

HIL Limited

A Joint Venture of HIL & SAIL



TOGETHER, WE BUILD

Creating Value



Address

3, 47, Ashoka Park

Phone No. 06221004700

GSTIN Number: 06AAACH2676Q1Z4

PAN Number: AAACH2676Q

CIN Number: L7499BTG1955PLC000656

E-Mail Id:

TAX INVOICE

IRN: 1c976f01d109573b1eca25a8303b6f7dc21d122720c9c6f0f5242b871382e0ee

Invoice Number	2018030546	Date & Time of Preparation	31.01.2022 & 20.25.28						
Invoice Date	31.01.2022	Transporter Name	B K D Roadlines						
SO Number & Date	754769 & 31.01.2022	LR/RR Number & Date	1560						
Order Ref & Dt	SSC/BHARTI/WO-11/01/ & 12.01.2022	Vehicle/Lorry/Wagon No	HR63D8251						
Delivery / OBD No	81027012	Gross Weight	30,093.000 KG (30.093 MT)						
L/C Number		Net Weight	30,093.000 KG (30.093 MT)						
Payment Terms	30 Days Direct Credit	E-Way Bill No	311407786636						
Delivery (Inco Terms)	F O R	Insurance Policy No	5005002118P117410203						
GST Range : RANGE 3	GST Division: ROHTAK	GST Commissionerate: ROHTAK	State GST FAR/DABAD (WEST) WARD - 5						
Bill to Party 33779 S S CONSTRUCTION CO C/O MR Ram Krishan, Rio Ram Krishan House, Near MLA Tej Pal Tanwar Kothi, Vill- Ramgarh, PO - Badshah Pur, Gurgaon Gurgaon, 122101, Haryana TIN Number GST Number : 06AEFPS1460P1Z3 PAN Number : AEFPS1460P Phone Number : 9599445520		Place of Supply 1133779 S S CONSTRUCTION CO. C/O Asthetic Township Developers Pvt Ltd, near IFFCO chowk metro station, Site Bharti realty, Sector- 27, GURUGRAM GURUGRAM, 122002, Haryana TIN Number GST Number : 06AEFPS1460P1Z3 PAN Number : AEFPS1460P Phone Number : 9599445520							
Material Code	Description of Goods/Services & HSN / SAC Code	Quantity	UOM	Volume (in M3)	Wt.in KG	Unit Rate	Basic Amount	Discount (-)	Taxable Amount in INR
900310220	FLY ASH BLOCKS (AAC) GR-1 600X250X200 MM HSN - 68159990	1.433	EA	42.9900	30,093	102.15	146378.87	-11296.07	135082.80
Insurance								29.72	
Gross Amount							146378.87	-11296.07	135112.52
CGST @ 2.50 %									3,377.81
SGST @ 2.50 %									3,377.81
Total Amount									141,868.14
"HSN/SAC : 68159990 ARTICLES OF STONE OR OF OTHER MINERAL SUBSTANCES"									
Tax Amount in Words (SGST/CGST//IGST) : Rupees Six Thousand Seven Hundred Fifty Five And Paise Sixty Two Only									
Total Amount in Words : Rupees One Lakh Forty One Thousand Eight Hundred Sixty Eight And Paise Fourteen Only									

12 pcs damaged

Vishal
(Signature)58814
31/1/222085
HR63D 82518901
01/02/22
17:00
HR63D 8251
1205, ml

Lorry Driver's Signature :	Location Date :	Signature of Supplier / Authorised Representative
Terms & Conditions 1. Our respons only ceases once the goods are delivered to the carrier/customer as applicable 2. No claim will be considered for damage or shortage thereafter. 3. Material's once dispatched will NOT be taken back. 4. Other terms and conditions as mentioned in contract are part and parcel of this supply transaction 5. Payment is based on standard banking conditions. 6. Except that the parties given above are true and correct and the amount indicated represents the price actually charged and that there is no flow of additional considerations directly or indirectly from the buyer.		For HIL LIMITED Signature valid Digitally Signed By: DS HIL LIMITED on Mon 31-Jan-2022 20:40:18 IST PRADEEP RATHI Authorised Signatory

E & OE

ORIGINAL FOR BUYER

Regd. Office: L7 Floor, SLN Terminus, SY. No. 133, Near Botanical Gardens, Gachibowli, Hyderabad - 500 032, Telangana, India.

Page 1 of 1

Tax Invoice

Trade Solutions Delhi B-16/1, Matija Road, Jhama Nagar New Delhi - 110008 GSTIN: UIN: 07AAP1T60241177 Consigner:		Invoice No: 017/21/22 Date: 16.01.2022 Delivery Note:	Motor Vehicle No:
M/s S.S. Construction Co. Bharti Realty C/O Arthetha Township Developers Pvt Ltd Near PCCO Chowk metro station Sec- 27 Gurgaon GSTIN: UIN: 06AE1PS14601103 State Name: HARYANA, Code: 06 Buyer (if other than consigner): M/s S.S. Construction Co. Ram Krishna House Near M. A. Tripathi Farwar Killa Vill. Jangarh P.O. Badshahi Gurgaon PAN No: AAP1T60241 GSTIN: UIN: 06AE1PS14601103 State Name: HARYANA, Code: 06		Buyer's Order No: PO/TSD/21-22/WD-12-01-22 Date: 12.01.2022 Dispatch Document No:	Motor Vehicle No: HR63C4466
Despatched through:		Destination:	
Terms of Delivery:			

S.N.	Description of Goods	HSN/SAC Code	Quantity	Unit	Rate	per	Disc %	Amount (₹)
1	AAC Block of 600 x 250 x 150 mm Thickness	68159910	10.0	M3	3,428.90	M3		34,289.00
OUTPUT IGST								1,571.45
Total								33,000.31

Amount in words: **Indian Rupees - Thirty Three Thousand Only**
 E & O.K.

Taxable Value	Rate	Amount
31,428.90	5%	1,571.45
Total		1,571.45

Tax Amount in words: **Indian Rupees - One Thousand Five Hundred Seventy One and Thirty One paise Only**

Remarks:

- 1. This invoice is subject to Delhi jurisdiction E&O.T. For Trade Solutions Delhi
- 2. Goods once sent will not be taken back
- 3. Defective 0.25% will be charged if payment is not made within time
- 4. Invoice is final

for TRADE SOLUTIONS DELHI
Authorised Signatory

HIL Limited

HIL Limited, Gurgaon, Haryana

Gurgaon

121101, Haryana

Phone No. 08221004709

GSTIN Number: 06AAACH2601Z4

PAN Number: AAACH2676Q

CIN Number: U74999TG1955PLC000656

E-Mail Id

IRN: 33271140405750358462d2b4291f59968ab9c6bc92d5c9d79dc2124fa88df6

TOGETHER, WE BUILD.

SINCE 1983

TAX INVOICE



Invoice Number: 2018030390	Date & Time of Preparation: 23.01.2022 & 16:58:33
Invoice Date: 23.01.2022	Transporter Name: TRIP TELL
SO Number & Date: 751620 & 23.01.2022	LR/RR Number & Date: 685
Order Ref & Dt: SSC/BHARTI/WO 11/01/ & 12.01.2022	Vehicle/Lorry/Wagon No: HR63D9530
Delivery - OBD No: 81022322	Gross Weight: 30,093.000 KG (30.093 MT)
L/C Number:	Net Weight: 30,093.000 KG (30.093 MT)
Payment Terms: 30 Days Direct Credit	E-Way Bill No: 331404843055
Delivery (Inco Terms): F.O.R.	Insurance Policy No: 5005002118P117410203
GST Range: RANGE-3	GST Division: ROHTAK
GST Commissionerate: ROHTAK	State GST: FARIDABAD (WEST) WARD - 5
to Party J3779-S.S.CONSTRUCTION CO. C/O MR Ram krishan, R/o Ram Krishan House, Near MLA Tej Pal Tanwar Kothi, Vill. Ramgarh, PO - Badshahpur, Gurgaon Gurgaon, 122101, Haryana TIN Number: GST Number: 06AEFPS1460P1Z3 PAN Number: AEFPS1460P Phone Number: 9599445520	
Place of Supply 1133779-S.S.CONSTRUCTION CO C/O Asthetic Township Developers Pvt Ltd, near IFFCO chowk metro station, Site Bharti realty, Sector- 27,, GURUGRAM GURUGRAM, 122002, Haryana TIN Number: GST Number: 06AEFPS1460P1Z3 PAN Number: AEFPS1460P Phone Number: 9599445520	

Material Code	Description of Goods/Services & HSN / SAC Code	Quantity	UOM	Volume (in M3)	Wt.in KG	Unit Rate	Basic Amount	Discount (-)	Taxable Amount in INR
900310220	FLY ASH BLOCKS (AAC) GR-1 600X250X200 MM HSN - 68159990	1,433	EA	42.9900	30,093	102.15	146378.87	-11296.07	135082.80
									29.72
Gross Amount							146378.87	-11296.07	135112.52
							CGST @ 2.50 %		3,377.81
							SGST @ 2.50 %		3,377.81
Total Amount									141,868.14

"HSN/SAC : 68159990 ARTICLES OF STONE OR OF OTHER MINERAL SUBSTANCES"

Tax Amount in Words (SGST/CGST/IGST) : Rupees Six Thousand Seven Hundred Fifty Five And Paise Sixty Two Only

Total Amount in Words : Rupees One Lakh Forty One Thousand Eight Hundred Sixty Eight And Paise Fourteen Only

MATERIAL OUTWARD ON GATE

 GRT No: 58547
 DATE: 23/1/22 TIME: 17:00
 VEHICLE No: HR63D9530

Sign: [Signature]

Lorry Driver's Signature: [Signature]	Location Date: [Signature]	Signature of Supplier / Authorised Representative
Terms & Conditions: 1. Our responsibility ceases once the goods are delivered to the carrier/customer as applicable. 2. No claims would be considered for damage or shortage thereafter. 3. Materials once dispatched will NOT be taken back. 4. Penalties and charges as mentioned overleaf are part and parcel of this supply transaction. 5. Weights are based on standard testing conditions. 6. We warrant that the particulars given above are true and correct and the amount indicated represents the price actually charged and that there is no flow of additional considerations directly or indirectly from the buyer.		For HIL LIMITED Signature valid Digitally Signed By: DS HIL LIMITED 01 Sun 23-Jan-2022 17:02:18 IST PRADEEP RATIL Authorised Signatory

E & OE

ORIGINAL FOR BUYER

Page 1 of 1

Regd. Office: L7 Floor, SLN Terminus, SY. No. 133, Near Botanical Gardens, Gachibowli, Hyderabad - 500 032, Telangana, India.

SHREE CEMENT LIMITED


OF GONDIA UNIT-12, SIKANDRABAD INDUSTRIAL AREA, SIKANDRABAD-203205, UP

TAX INVOICE

ORIGINAL FOR BUYER

PAN No. AACCS979AC	CIN No. 126943IU979M C001935	TAN No. JHSC1295A	
Date: 08 JAN 22	DI No. 27195832	DI Date: 08 JAN 22	
Type: SCAM TRIG	GR/RR No. EGI/MAT/170	GR/RR date: 08 JAN 22	
Delivery At: S.S. CONSTRUCTION CO BHARTI REALTY, G/O ASTHIC TOWN SHIP DEVELOPERS PVT LTD, NEAR IIT CROWK METRO SEC27, GURGAON, Haryana			
Place of Supply: Haryana Reverse Charge: No			

M/s. S.S. CONSTRUCTION CO BHARTI REALTY, G/O ASTHIC TOWN SHIP DEVELOPERS PVT LTD, NEAR IIT CROWK METRO SEC27, GURGAON, Haryana	Term: FOB Delivery is FOB, all the transit risk lies with supplier	State Code: 06 PAN: AACS979AC
M/s. S.S. TRANSPORT COMPANY Date: 08 JAN 22 Validity: 31 DEC 22 Pla: 542 PMT		



Description of Goods	HSN	Qty(MT)	Qty(Cum)/Nos/Bags	Rate/CUM	Amount (Rs.)
	68159910	32.85	1443	3142.87	

20 blocks damaged
20 block Damaged/Rejected

After Discount Total Taxable Amount

Total invoice amount (in Rs.)					
Rs One Lakh Forty Eight Thousand Five Hundred And Paise Forty Five only					
Qty (MT)	Actual Wt. (MT)	Charged Wt. (MT)	Freight PMT (Rs.)	Total Freight	Total



8578

09/01/22 10:10

2032602226

PKS/mr.

Digitally signed by PRAVEEN
 CHANDIA METROTRA
 Date: 2022.01.09 21:46:55
 For Shree Cement Limited

(Authorised Signatory)

2 3127 517 32 OK

SHREE CEMENT LIMITED

UP GRINDING UNIT 12, SIKANDRABAD INDUSTRIAL AREA, SIKANDRABAD 203205, UP

TAX INVOICE

ORIGINAL FOR BUYER

PAN No. AAFPS1460P	CIN No. 136913L1097091G061006	TAN No. JDDK591296A
Date: 29 NOV 21	DI No. 26864563	DI Date: 28 NOV 21
Type: SODA/CEMENT	GR/RR No. 1-G1/MS/1393	GR/RR date: 28 NOV 21

Delivery At:	SS CONSTRUCTION CO BHATTI REALTY CO ASTHIC TOWN SHIP DEVELOPERS PVT LTD NEAR IFCO CHOWK MITRO SEC 27, GURGAON, Haryana
Place of Supply:	Haryana
Reverse Charge:	No

State: Haryana	State Code: 06	Place of Supply: Haryana
Post No: 604111 S1460P123	PAN: AAFPS1460P	Reverse Charge: No
Invoice No: 121215100280	Date: 29 NOV 21	
Invoice Date: 29 NOV 21	Validity: 12 PMT	
Invoice No: 121215100280	Date: 29 NOV 2021	



Description of Goods	HSN	Qty(MT)	Qty(Cum)/Nos/ Bags	Rate/CUM	Amount (Rs)
CEMENT	62159910	29.2	38.59 1235	2857.15	110257.4 114285.9

After Discount Total Taxable Amount

IGST 5%

Total invoice amount (in Rs.)

5512.87
5714.29
115770.27
120000.09

Amount in words : Rs One Lakh Twenty Thousand And Paise Nine only

Wagon No.	Qty (Bags)	Qty (MT)	Actual Wt. (MT)	Charged Wt. (MT)	Freight PMT(Rs.)	Total Freight(Rs.)
Total						

A 45 Pcs damaged



Digitally signed by PRAVEEN CHANDRANATH
Date: 2021.11.29 03:13:25
For Shree Cement Limited

Payment against this invoice should be made by A/C Payee

Payment name of "SHREE CEMENT LTD"

Payment made after 33 days of invoice

8409
29/11/21
11:00 (Authorised Signatory)

270267C 2744

For Shree Cement Limited

SHREE CEMENT LIMITED


UP GRINDING UNIT-12, SIKANDRABAD INDUSTRIAL AREA, SIKANDRABAD-203205, UP

TAX INVOICE

ORIGINAL FOR BUYER

PAN No. AACCSC1963	CIN No. 12694313197915 C001935	TAN No. JDDHS01295A
Date: 27 NOV 21	DI No. 26861130	DI Date: 27 NOV 21
Type: SC AACBHC	GR/RR No. 1 G/SC/183	GR/RR date: 27 NOV 21
Billed to: S S CONSTRUCTION CO BHARTI REALTY C/O ASTHRIC TOWN SHIP DI VETOH RS PVT LTD NEAR BFCO CHOWK METHO CHOWK STATION SECTOR 27 GURGAON Haryana		Delivery At:
State: Haryana	State Code: 06	Place of Supply: Haryana
GST No. 06A11PS1460P129	PAN: ALFPS1460P	Reverse Charge: No

Freight Mode: ROAD	Term: FOB
Freight Type: To be fixed	Deliveries is FOB, all the transit risk lies with supplier
Driver Mobile transporter: SHREE CHHIL LAH TRANSPORT COMPANY	
Way Bill No: 30171/25560	Date: 28 NOV 21
Distance (KM): 106	Validity:
Truck No: HH6301351	Rs. 542 PMT
GR No: 106130669cc57d81006Un5c307d0a0453f0c94320854	
GR No: 106130669cc57d81006Un5c307d0a0453f0c94320854	
GR No: 106130669cc57d81006Un5c307d0a0453f0c94320854	
Date: 27 NOV 21	Date: 27 NOV 21



Description of Goods	HSN	Qty(MT)	Qty(Cum)/Nos/Bags	Rate/CUM	Amount (Rs)
	68159910	32.85	1448	2857.13	12585.6

After Discount Total Taxable Amount

IGST 5%

Total invoice amount (in Rs.)

Amount in words : Rs One Lakh Thirty Four Thousand Nine Hundred Ninety Nine And Paise Fifty Five only

Wagon No.	Qty. (Bays)	Qty. (MT)	Actual Wt. (MT)	Charged Wt. (MT)	Freight PMT(Rs.)	Total Freight(Rs.)
Total						

30 lbs damage



8410
29/11/21
15/11/21

Digitally signed by PRAVEEN
CHANDHA MEHROTRA
Date: 2021.11.26 18:02:26
For Shree Cement Limited

(Authorised Signatory)

Note: The buyer's liability for damage to the goods from invoice price as per the declared schemes. Payment against this invoice should be made by A/C Payee cheque/DD/RTGS/NLE/FACH/UP/IMPS Only in the name of "SHREE CEMENT LTD". The buyer is to pay the freight charges within 30 days of invoice date. The buyer is to pay the freight charges only.

For Shree Cement Limited
UP GRINDING UNIT-12, SIKANDRABAD INDUSTRIAL AREA, SIKANDRABAD-203205, UP
Phone: 23333333 Fax: 23333333
E-mail: sales@shreecement.com
Website: www.shreecement.com


31/12

SHREE CEMENT LIMITED

UP GRINDING UNIT, 12, SIKANDRABAD INDUSTRIAL AREA, SIKANDRABAD-203205, UP
TAX INVOICE

ORIGINAL FOR BUYER

GST No. : DBAACCSB796G1ZP		PAN No. AACCSB796G	CIN No. L26943RJ1979PLC001935	TAN No. JDI501295A
Invoice No. FGE/21/P/5700	Date 07-NOV-21	DI No. 26722786	DI Date 07-NOV-21	
Order No. 2021003596	Type SC/AACBRIC K	GR/RR No. FGE/KKU/1532	GR/RR date 07-NOV-21	
Billed to : S S CONSTRUCTION CO C/O MR RAM KRISHAN, R/O RAM KRISHAN HOUSE, NEAR MLA TEJ PAL FANWAIKOTHI, VILLI RAMGARH, BADSHAHPUR, GURGAON, Haryana		Delivery At : S S CONSTRUCTION CO BHARTI REALTY C/O ASTHRIC TOWN SHIP DEVELOPERS PVT LTD, NEAR IFFCO CHOWK METRO CHOWK STATION SECTOR -27, GURGAON, Haryana		
State: Haryana	State Code 06	Place of Supply: Haryana		
GST No. 06AEFPS1460P1Z3	PAN AEFPS1460P	Reverse Charge: No		
Freight Mode: ROAD / ROAD	Term: FOR			
Freight Type: To Be Billed	Delivery is FOR, all the transit risk lies with supplier			
Driver Mobile: K K LOGISTICS				
Way Bill No. 451211092212	Date 07-NOV-21			
Distance(KM): 125	Validity: Rs. 542 PMT			
Truck No. RJ42GA2165				
IRN No. 904ep48d5f013a3f7d6036118b1a90472a51cd691ab11755 fcad830469730e5a				
Ack No. 142110775906494	Date 07-NOV-2021			



Description of Goods	HSN	Qty(MT)	Qty(Cum)/Nos/Bags	Rate/CUM	Amount (INR)
	68159910	36.5	50	1800	8282
After Discount Total Taxable Amount					8282
GST 5%					414.1
Total invoice amount (in Rs.)					8696.1

Amount in words : Rs One Lakh Fifty Seven Thousand Five Hundred only

Wagon No.	Qty. (Bags)	Qty. (MT)	Actual Wt. (MT)	Charged Wt. (MT)	Freight PMT(Rs.)	Total Freight
Total						

Note: (1) Invoice discounts / incentives are allowable from invoice price as per the declared conditions.
(2) Payment against this invoice should be made by A/C Payee cheque/DD/RTGS/NEFT/ACBUP/IMPS
(3) Only in name of "SHREE CEMENT LTD"
(4) Interest @ 18% would be charged if payment made after 30 days of invoice
(5) Subject to Beawar (Rajasthan) Jurisdiction only

Digitally signed by PRAVEEN CHANDRA MEHROTRA
Date: 2021.11.07 18:45:23
For Shree Cement Limited

(Authorised Signatory)

Marketing Offices:
New Delhi: 122/123, Hans Bhawan, 1, Bahadurshah Zafar Marg, New Delhi-110022 Ph: 011-23370828, 23370776, Fax: 23370729
Gurgaon: 105, 106, Mansalaya Building, 15, Barakhamba Road, New Delhi-110 001 Ph: (91) 11-23702794-96
Jaipur: 105, 106, Mansalaya Building, 15, Barakhamba Road, Connaught Place, New Delhi-110 001 Ph: (91) 11-23731084, 23731085 Fax: (91) 11-23731084

SHREE CEMENT LIMITED

UP GRINDING UNIT, 12, SIKANDRABAD INDUSTRIAL AREA, SIKANDRABAD-203205, UP


TAX INVOICE

ORIGINAL FOR BUYER

GST No. : 09AACCS8796G1ZP	PAN No. AACCS8796G	CIN No. L26943RJ1979PLC001935	TAN No. JDHS01295A
Invoice No. EGE/21/P/5626	Date 31-OCT-21	DI No. 26695125	DI Date 31-OCT-21
Order No. 2021003515	Type SC/AACBRIC K	GR/RR No. EGE/KKL/1503	GR/RR date 31 OCT 21

Billed to : S.S. CONSTRUCTION CO. C/O MR RAM KRISHAN, R/O RAM KRISHAN HOUSE, NEAR MLA TEJ PAI TAPWAR KOTHI, VILL RAMGARH, BADSHAHPUR, GURGAON, GURGAON Haryana	Delivery At : S.S. CONSTRUCTION CO. BHARTI REALTY C/O ASTHRIC TOWN SHIP DEVELOPERS PVT LTD, NEAR IFFCO CHOWK METRO CHOWK STATION SECTOR -27, GURGAON, Haryana
State Haryana State Code 06	Place of Supply : Haryana
GST No. 06AEFPS1460P1Z3 PAN AEFPS1460P	Reverse Charge : No

Freight Mode ROAD / ROAD	Term FOR
Freight Type To Be Billed	Delivery is FOR, all the transit risk lies with supplier
Driver Mobile transporter K K LOGISTICS	
Way Bill No. 401210288651	Date 31-OCT-21
Distance(KM) 125	Validity
Truck No. RJ52GA5973	Rs. 564 PMT
IRN No. 128c8186b3bcd41dfb92f73e850aa1198d61f90b10236e41f8a2cf9f6c3fd604	
Ack No. 142110763637458	Date 31-OCT-2021



Description of Goods	HSN	Qty(MT)	Qty(Cum)/Nos/Bags	Rate/CUM	Amount (Rs)
AACB 625250200 LOOSE	68159910	36.5	50 1600 /	2714.28	135714

After Discount Total Taxable Amount

IGST 5% 5785.7

Total invoice amount (in Rs.) 142499.7

Amount in words : Rs One Lakh Forty Two Thousand Four Hundred Ninety Nine And Paise Seventy only

Wagon No.	Qty. (Bags)	Qty. (MT)	Actual Wt. (MT)	Charged Wt. (MT)	Freight PMT(Rs.)	Total Freight(Rs.)
Total						



8210
01/11/21 6:00
RJ52GA5973

Digitally signed by PRAVEEN
BHARTI MEHROTRA
Date: 2021.10.31 23:17:28

For Shree Cement Limited

(Authorised Signatory)

- Note:
1. Post Invoice discounts / incentives are allowable from invoice price as per the declared schemes.
 2. Payment against this invoice should be made by A/C Payee cheque/DD/RTGS/NEFT/ACH/UP/IMPS Only in name of "SHREE CEMENT LTD"
 3. Interest @ 18% would be charged if payment made after 30 days of invoice
 4. Subject to Beawar (Rajasthan) Jurisdiction only


Contra Marketing Offices
Shree : 123, Hans Nihawan, 1, Bahadurshah Zafar Marg, New Delhi-110022 Ph: 011-23370828, 23370776, Fax: 23370729
Haryana : 5th Floor, Haridra Building, 15, Barakhamba Road, New Delhi-110 001 Fax: (91) 11-23702794-96
Rajasthan : 10A 13M Building, 16 Barakhamba Road, Connaught Place, New Delhi-110 001 Phone: (91) 11-23731084, 23731085 Fax: (91) 11-23731084

SHREE CEMENT LIMITED

UP GRINDING UNIT-12, SIKANDRABAD INDUSTRIAL AREA, SIKANDRABAD-203205, UP

TAX INVOICE

ORIGINAL FOR BUYER

GST No : 09AACCS8796G1ZP		PAN No: AACCS8796G		CIN No: L28943RJ1979PLC001936		TAN No: JDHS01295A	
Invoice No: FGE 21/P/5580		Date: 30-OCT-21		DI No: 26678847		DI Date: 29-OCT-21	
Order No: 2021003503		Type: SC/AACBRIC K		GR/RR No: FGE/KKL/1489		GR/RR date: 29-OCT-21	
Billed to :				Delivery At :			
878580 S.S. CONSTRUCTION CO C/O MR RAM KRISHAN, R/O RAM KRISHAN HOUSE, NEAR MLA TEJ PAL TANWAR KOTHI VILL RAMGARH, BADSHAHPUR, GURGAON, GURGAON, Haryana				S.S. CONSTRUCTION CO BHARTI REALTY C/O ASTHRIC TOWN SHIP DEVELOPERS PVT LTD, NEAR IFFCO CHOWK METRO CHOWK STATION SECTOR -27, GURGAON, Haryana			
State: Haryana		State Code: 06		Place of Supply: Haryana			
GST No: 06AEFPS1460P1Z3		PAN: AEFPS146CP		Reverse Charge: No			
Freight Mode: ROAD / ROAD		Term: FOR					
Freight Type: To Be Billed		Delivery is FOR, all the transit risk lies with supplier					
Driver Mobile transporter: K K LOGISTICS							
Way Bill No: 401209819123		Date: 30-OCT-21					
Distance(KM): 125		Validity: Rs. 567 PMT					
Truck No: RJ09GD0727		IRN No: 31610e51452b516cc3a4936203340f0fdcc30d881b8b16d9c3435f7eadfb70ae					
Ack. No: 142110758217843		Date: 30-OCT-2021					

Description of Goods	HSN	Qty(MT)	Qty(Cum)/Nos/ Bags	Rate/CUM	Amount (Rs)
AACB E25250200 LOOSE	68159910	36.5	50 1600	2714.28	135714

After Discount Total Taxable Amount

IGST 5%

6785.7

Total invoice amount (in Rs.)

142499.7

Amount in words : Rs One Lakh Forty Two Thousand Four Hundred Ninety Nine And Paise Seventy only

Wagon No.	Qty. (Bags)	Qty. (MT)	Actual Wt. (MT)	Charged Wt. (MT)	Freight PMT(Rs.)	Total Freight(Rs.)
Total						



Note:

1. Post invoice discounts / incentives are allowable from invoice price as per the declared schemes
2. Payment against this invoice should be made by A/C Payee cheque/DD/RTGS/NEFT/ACH/UP/IMPS
- Only in name of "SHREE CEMENT LTD"
3. Interest @18% would be charged if payment made after 30 days of invoice
4. Subject to Beawar (Rajasthan) Jurisdiction only

Digitally signed by PRAVEEN
CHANDRA MEHROTRA
Date: 2021.10.30 00:36:45
For Shree Cement Limited

(Authorised Signatory)

Shree Cement Ltd, Offices

Main Office: 12/123 Hans Bhawan-1, Bahadurshah Zafar Marg, New Delhi-110022 Ph: 011-23370828, 23370726 Fax: 23373729

Bangalore: 1st Floor, Hansalaya Building 15, Barakhamba Road, New Delhi-110 001 Fax: (91) 11-23702790

Gurgaon: 11A/12C Building, 16 Barakhamba Road, Connaught Place, New Delhi-110 001 Phone: (91) 11-23731084, 23731085 Fax: (91) 11-23731084


HIL Limited

Amadalshahpur, Matanhil,

HIL

TOGETHER, WE BUILD.

TAX INVOICE



IRN 213844128186578649eee327d3eeadadbce0b7c62b8ec8b0d004536815b5c6ad


Invoice Number	2018028972	Date & Time of Preparation	25.10.2021 & 19:21:01
Invoice Date	25.10.2021	Transporter Name	BKDR Transport Co
SO Number & Date	716641 & 25.10.2021	LR/RR Number & Date	2871
Order Ref & Dt	SSC/Bharti/WO-08/10/ & 22.10.2021	Vehicle/Lorry/Wagon No	HR63C0558
Delivery OBD No	80977346	Gross Weight	30,093.000 KG (30.093 MT)
L/C Number		Net Weight	30,093.000 KG (30.093 MT)
Payment Terms	30 Days Direct Credit	E-Way Bill No	361373468029
Delivery (Inco Terms)	F O R	Insurance Policy No	5005002118P117410203

GST Range:	GST Division:	GST Commissionerate:	State GST
RANGE 3	ROHTAK	ROHTAK	FARIDABAD (WEST) WARD - 5

Bill to Party	Place of Supply
1133779 S.S. CONSTRUCTION CO.	1133779 S.S. CONSTRUCTION CO.
30 MR Nam Krishan, R/o Ram Krishan House, Near MLA Tej Pal Tanwar Kothi,	C/O Asthetic Township Developers Pvt Ltd, near IFFCO chowk metro station,
Vill- Ramgarh, PO - Badshah Pur,, Gurgaon	Site Bharti realty, Sector- 27,, GURUGRAM
Gurgaon 122101, Haryana	GURUGRAM, 122002, Haryana
TIN Number	TIN Number
GST Number : 06AEFPS1460P1Z3	GST Number : 06AEFPS1460P1Z3
PAN Number : AEFPS1460P	PAN Number : AEFPS1460P
Phone Number : 9599445520	Phone Number : 9599445520

Material Code	Description of Goods/Services & HSN / SAC Code	Quantity	UOM	Volume (in M3)	Wt.in KG	Unit Rate	Basic Amount	Discount (-)	Taxable Amount in INR
9003.0020	FLY ASH BLOCKS (AAC) GR-I 600X250X200 Mm HSN - 68159990	1,433	EA	42.9900	30,093	100.05	143370.00	-26708.40	116661.60
Insurance							143370.00	-26708.40	116667.27
Gross Amount									2,917.18
CGST @ 2.50 %									2,917.18
SGST @ 2.50 %									122,521.63
Total Amount									

"HSN/SAC : 68159990 ARTICLES OF STONE OR OF OTHER MINERAL SUBSTANCES"
Tax Amount in Words (SGST/CGST/IGST) : Rupees Five Thousand Eight Hundred Thirty Four And Paise Thirty Six Only.
Total Amount in Words : Rupees One Lakh Twenty Two Thousand Five Hundred Twenty One And Paise Sixty Three Only



MATERIAL OUTWARD ON GATE
G.F. No. 55651
DATE 27/10/21 TIME 18:30
HR63C0558

26/10/2021
10:45
HR63C0558
Sumvir

Lorry Driver's Signature :

Location Date:

Signature of Supplier / Authorised Representative



Conditions & Warranties:
1. Liability ceases once the goods are delivered to the carrier/customer as applicable.
2. No claim should be considered for damage or shortage thereafter.
3. Once dispatched will NOT be taken back.
4. Goods and conditions as mentioned overleaf are part and parcel of this supply transaction.
5. Goods are delivered on standard testing conditions.
6. All particulars given above are true and correct and the amount indicated represents the price actually charged.
7. No flow of additional considerations directly or indirectly from the buyer.

ORIGINAL FOR BUYER

Regd. Office: L7 Floor, SLN Terminus, SY. No. 133, Near Botanical Gardens, Gachibowli, Hyderabad - 500 032, Telangana, India.

UP GRINDING UNIT, 12, SIKANDRABAD INDUSTRIAL AREA,,SIKANDRABAD-203205,UP

ORIGINAL FOR BUYER

After Discount Total Taxable Amount

Amount in words : Rs Sixty Five Thousand Five Hundred Fifty And Paise Forty Six only				Total invoice amount (in Rs.)	65550.46
Wagon	Qty	Qty			

al

(Bags)

✓

entry No. 7974
18/10/2021
10:50
B 7698
No. 0144119 smf

Dr. S. K. Chakrabarti, 15, Barakhamba Road, New Delhi-110 001 Phone (91) 11-23702794-96 Fax 23707729
 Dr. S. K. Chakrabarti, 16 Barakhamba Road, Connaught Place, New Delhi-110 001 Phone (91) 11-23731084, 23731085 Fax (91) 11-23731084

For Shree Cement Limited

(Authorised Signatory)

HIL Limited


At: Jangamudi, Anantapur District, Andhra Pradesh, India

HIL

TOGETHER, WE BUILD.

(CERBIA)

TAX INVOICE



HIL Logo

Invoice No: HS221004708

GSTIN Number: 06A4ACH2676Q124

GSTIN Number: AAACH2676Q

GSTIN Number: LT499991G1955PLC000656

E-Mail:

PAN: 1509160921P0T332A76C12a71032a70fd8d195301463c8cf284b513580dac

Invoice Number: 2018028629	Date & Time of Preparation: 08.10.2021 & 16.15.47
Invoice Date: 08.10.2021	Transporter Name: JATIN GOLDEN TRANSPORT
Invoice No & Date: 710203 & 08.10.2021	COMPANY
Origin Ref & Dt: SSC/BHARTI/WO-06/06/ & 05.08.2021	LR/RR Number & Date: 1440
Delivery: CBD No: 60966992	Vehicle/Lorry/Wagon No: HR46E7970
Invoice Number:	Gross Weight: 30,093.000 KG (30.093 MT)
Payment Terms: 30 Days Direct Credit	Net Weight: 30,093.000 KG (30.093 MT)
Delivery (Incoterms): F O R	E-Way Bill No: 311367007523
GST Range: RANGE 3	GST Division: ROHTAK
GST Division: ROHTAK	GST Commissionerate: ROHTAK
Bill to Party: 1133779-S.S.CONSTRUCTION CO.	State GST: FARIDABAD (WEST) WARD - 5
C/O MR Ram Krishan, R/o Ram Krishan House, Near MLA Tej Pal Tanwar Kuthi,	Place of Supply: 1133779-S.S.CONSTRUCTION CO.
Vikram Singh, PO - Badshahpur, Gurgaon	C/O Asthetic Township Developers Pvt Ltd, near IFFCO chowk metro station,
Gurgaon-122101, Haryana	Sile Bharti really, Sector- 27, GURUGRAM
TIN Number:	GURUGRAM, 122002, Haryana
GST Number: 06AEFPS1460P1Z3	TIN Number:
PAN Number: AEFPS1460P	GST Number: 06AEFPS1460P1Z3
Phone Number: 9599445520	PAN Number: AEFPS1460P
	Phone Number: 9599445520

Item Code	Description of Goods/Services & HSN / SAC Code	Quantity	UOM	Volume (in M)	Wt in KG	Unit Rate	Basic Amount	Discount (-)	Taxable Amount
1	1.75 IN BLOCKS (AAC) GR-1 1250X750X100 MM	1,433	EA	42.9900	30,093	100.05	143370.00	-34895.41	109474.59
Insurance									
Gross Amount							143370.00	-34895.41	108474.59
CGST @ 2.50 %									2712.46
SGST @ 2.50 %									2712.46
Total Amount									113923.37

53950 ARTICLES OF STONE OR OF OTHER MINERAL SUBSTANCES

Words (CGST/SGST/IGST): Rupees Five Thousand Four Hundred Twenty Four And Paise Ninety Two Only

Words: Rupees One Lakh Thirteen Thousand Nine Hundred Twenty Three And Paise Thirty Seven Only

No. 7825

10/10/21

11:00
HR46E7970
P/S

Driver's Signature:

Location Date:

Signature of Supplier / Authorised Representative

For HIL LIMITED
Signature valid

Digitally Signed By:

DS HIL LIMITED 01

Fri 08 Oct 2021 16:20:40

PHADEEP RATHI

Authorised Signatory

TRIFLITE FOR ASSESSEE

Plot No. 17, Floor, 11B, Tannus, SY. No. 133, Near Petrol Station, Gachibowli, Hyderabad - 500 032, Telangana, India

Annexure-XXIII

Photographs of Antismog gun and Logbook





Anti Smoke gun Register - 2022

Date	Start Time	Off Time	Sign. of Operator	Sign. of Site Incharge	Sign. of EHS Dept
9.02.22	9:00 a.m	9:15 a.m	Sah		
	12:10 p.m	12:25 p.m	Sah		
	2:00 p.m	2:15 p.m	Ranjit		
	5:15 p.m	5:30 p.m	Sah		
10.02.22	9:15 a.m	9:30 a.m	Sah		
	12:10 p.m	12:25 p.m	Sah		
	2:00 p.m	2:15 p.m	Sah		
	5:15 p.m	5:30 p.m	Ranjit		
11.02.22	8:45 a.m	9:00 a.m	Sah		
	12:00 p.m	12:15 p.m	Sah		
	2:15 p.m	2:30 p.m	Sah		
	5:00 p.m	5:15 p.m	Sah		
12.02.22	9:00 a.m	9:15 a.m	Sah		
	12:15 p.m	12:30 p.m	Sah		
	2:00 p.m	2:15 p.m	Ranjit		
	4:45 p.m	5:00 p.m	Sah		
13.02.22	8:45 a.m	9:00 a.m	Sah		
	12:15 p.m	12:30 p.m	Sah		
	2:00 p.m	2:15 p.m	Sah		
	5:15 p.m	5:30 p.m	Sah		
14.02.22	9:00 a.m	9:15 a.m	Sah		
	12:10 p.m	12:15 p.m	Ranjit		
	2:00 p.m	2:15 p.m	Sah		
	4:45 p.m	5:00 p.m	Sah		
15.02.22	9:15 a.m	9:30 a.m	Sah		
	12:00 p.m	12:15 p.m	Sah		
	2:15 p.m	2:30 p.m	Ranjit		
	5:00 p.m	5:15 p.m	Sah		
16.02.22	9:00 a.m	9:15 p.m	Sah		
	11:45 a.m	12:00 p.m	Sah		
	2:00 p.m	2:15 p.m	Sah		
	5:15 p.m	5:30 p.m	Sah		

Anti Smoke gun Register - 2022

Date	Start Time	Off Time	Sign. of Operator	Sign. of Site Incharge	Sign. of EHS Dept
17.02.22	8:45 a.m	9:00 a.m	Sah		
	12:10 p.m	12:25 p.m	Ranjit		
	2:00 p.m	2:15 p.m	Ranjit		
	4:45 p.m	5:00 p.m	Sah		
18.02.22	9:00 a.m	9:15 a.m	Sah		
	11:45 a.m	12:00 p.m	Sah		
	2:00 p.m	2:15 p.m	Ranjit		
	4:45 p.m	5:00 p.m	Sah		
19.02.22	8:45 a.m	9:00 a.m	Sah		
	12:00 p.m	12:15 p.m	Sah		
	2:05 p.m	2:30 p.m	Sah		
	4:45 p.m	5:00 p.m	Ranjit		
20.02.22	9:00 a.m	9:15 a.m	Sah		
	12:00 p.m	12:15 p.m	Sah		
	2:00 p.m	2:15 p.m	Sah		
	5:00 p.m	5:15 p.m	Sah		
21.02.22	9:00 a.m	9:15 p.m	Ranjit		
	11:45 a.m	12:00 p.m	Sah		
	2:15 p.m	2:30 p.m	Sah		
	5:00 p.m	5:15 p.m	Sah		
22.02.22	9:15 a.m	9:30 p.m	Ranjit		
	12:00 p.m	12:15 p.m	Ranjit		
	2:00 p.m	2:15 p.m	Sah		
	5:00 p.m	5:15 p.m	Sah		
23.02.22	8:30 a.m	8:45 a.m	Sah		
	12:00 p.m	12:15 p.m	Ranjit		
	2:00 p.m	2:15 p.m	Ranjit		
	5:15 p.m	5:30 p.m	Sah		
24.02.22	9:00 a.m	9:15 a.m	Sah		
	12:00 p.m	12:15 p.m	Sah		
	2:15 p.m	2:30 p.m	Ranjit		
	5:00 p.m	5:15 p.m	Sah		

Anti Smoke gun Register - 2022

Date	Start Time	Off Time	Sign. of Operator	Sign. of Site Incharge	Sign. of DELTA	Sign. of EHS Dept
25.01.22	8:30 a.m	8:45 a.m	Romjit			
	12:00 p.m	12:15 p.m	Sah			
	2:15 p.m	2:30 p.m	Sah			
	5:00 p.m	5:15 p.m	Sah			
26.01.22	9:00 a.m	9:15 a.m	Romjit			
	12:10 p.m	12:25 p.m	Sah			
	2:00 p.m	2:15 p.m	Sah			
	4:45 p.m	5:00 p.m	Sah			
27.01.22	8:45 a.m	9:00 a.m	Romjit			
	12:00 p.m	12:15 p.m	Sah			
	2:00 p.m	2:15 p.m	Sah			
	5:15 p.m	5:30 p.m	Sah			
28.01.22	9:00 a.m	9:15 a.m	Romjit			
	12:15 a.m	12:25 p.m	Sah			
	2:00 p.m	2:15 p.m	Sah			
	5:15 p.m	5:30 p.m	Sah			
29.01.22	8:45 a.m	9:00 a.m	Romjit			
	12:00 p.m	12:15 p.m	Sah			
	2:15 p.m	2:30 p.m	Sah			
	5:00 p.m	5:15 p.m	Sah			
30.01.22	9:00 a.m	9:15 a.m	Romjit			
	12:15 p.m	12:30 p.m	Sah			
	2:00 p.m	2:15 p.m	Sah			
	5:15 p.m	5:30 p.m	Romjit			
31.01.22	8:30 a.m	8:45 a.m	Sah			
	12:15 p.m	12:30 p.m	Sah			
	2:00 p.m	2:15 p.m	Romjit			
	5:00 p.m	5:15 p.m	Romjit			

Anti Smoke gun Register - 2022

Date	Start Time	Off Time	Sign. of Operator	Sign. of Site Incharge	Sign. of DELTA	Sign. of EHS Dept
01.02.22	9:00 a.m	9:15 a.m	Romjit			
	12:15 p.m	12:30 p.m	Sah			
	2:00 p.m	2:15 p.m	Sah			
	5:15 p.m	5:30 p.m	Sah			
02.02.22	8:45 a.m	9:00 a.m	Romjit			
	12:00 a.m	12:15 p.m	Sah			
	2:15 p.m	2:30 p.m	Sah			
	5:00 p.m	5:15 p.m	Romjit			
03.02.22	9:00 a.m	9:15 a.m	Romjit			
	11:45 a.m	12:00 p.m	Sah			
	2:00 p.m	2:15 p.m	Romjit			
	5:15 p.m	5:30 p.m	Romjit			
04.02.22	9:00 a.m	9:15 a.m	Sah			
	12:15 p.m	12:30 p.m	Sah			
	2:15 p.m	2:30 p.m	Romjit			
	5:00 p.m	5:15 p.m	Sah			
05.02.22	8:45 a.m	9:00 p.m	Sah			
	12:00 p.m	12:15 p.m	Sah			
	2:00 p.m	2:15 p.m	Romjit			
	5:15 p.m	5:30 p.m	Romjit			
06.02.22	9:00 a.m	9:15 a.m	Sah			
	12:15 p.m	12:30 p.m	Sah			
	2:00 p.m	2:15 p.m	Romjit			
	5:00 p.m	5:15 p.m	Sah			
7.02.22	8:45 a.m	9:00 a.m	Sah			
	12:00 p.m	12:15 p.m	Sah			
	2:15 p.m	2:30 p.m	Sah			
	4:45 p.m	5:00 p.m	Sah			
8.02.22	9:00 a.m	9:15 a.m	Romjit			
	11:45 a.m	12:00 p.m	Sah			
	2:00 p.m	2:15 p.m	Sah			
	5:15 p.m	5:30 p.m	Sah			

Anti Smoke gun Register - 2022

Date	Start Time	Off Time	Sign. of Operator	Sign. of Site Incharge	Sign. of BLT	Sign. of FHS Dept
9.01.22	9:15 a.m	9:30 p.m	Sah			
	12:30 p.m	12:45 p.m	Sah			
	2:00 p.m	2:15 p.m	Sah			
	5:30 p.m	5:45 p.m	Sah			
10.01.22	9:00 a.m	9:15 a.m	Sah			
	12:00 p.m	12:15 p.m	Ranjit			
	2:00 p.m	2:15 p.m	Sah			
	5:00 p.m	5:15 p.m	Sah			
11.01.22	9:15 a.m	9:30 p.m	Sah			
	12:10 p.m	12:25 p.m	Sah			
	2:00 p.m	2:15 p.m	Ranjit			
	5:00 p.m	5:15 p.m	Sah			
12.01.22	9:00 a.m	9:15 p.m	Sah			
	12:15 p.m	12:30 p.m	Ranjit			
	2:10 p.m	2:25 p.m	Sah			
	5:00 p.m	5:15 p.m	Sah			
13.01.22	8:45 a.m	9:00 p.m	Sah			
	12:00 p.m	12:15 p.m	Ranjit			
	2:30 p.m	2:45 p.m	Sah			
	5:00 p.m	5:15 p.m	Sah			
14.01.22	9:00 a.m	9:15 p.m	Sah			
	12:15 p.m	12:30 p.m	Ranjit			
	2:30 p.m	2:45 p.m	Sah			
	5:15 p.m	5:30 p.m	Sah			
15.01.22	8:45 a.m	9:00 p.m	Sah			
	12:00 p.m	12:15 p.m	Ranjit			
	2:00 p.m	2:15 p.m	Sah			
	5:00 p.m	5:15 p.m	Sah			
16.01.22	9:00 p.m	9:15 p.m	Sah			
	12:15 p.m	12:30 p.m	Sah			

Anti Smoke gun Register - 2022

Date	Start Time	Off Time	Sign. of Operator	Sign. of Site Incharge	Sign. of BLT	Sign. of FHS Dept
17.01.22	8:40 a.m	8:55 p.m	Ranjit			
	12:00 p.m	12:15 p.m	Sah			
	2:30 p.m	2:45 p.m	Sah			
	5:00 p.m	5:15 p.m	Sah			
18.01.22	9:00 a.m	9:15 a.m	Ranjit			
	12:15 p.m	12:30 p.m	Sah			
	2:10 p.m	2:25 p.m	Sah			
	5:05 p.m	5:20 p.m	Sah			
19.01.22	9:00 a.m	9:15 a.m	Sah			
	12:15 p.m	12:20 p.m	Ranjit			
	2:10 p.m	2:25 p.m	Sah			
	5:00 p.m	5:15 p.m	Sah			
20.01.22	8:45 a.m	9:00 a.m	Sah			
	12:10 p.m	12:25 p.m	Ranjit			
	2:30 p.m	2:45 p.m	Sah			
	5:00 p.m	5:15 p.m	Sah			
21.01.22	9:00 a.m	9:15 a.m	Sah			
	12:30 p.m	12:45 p.m	Ranjit			
	2:30 p.m	2:45 p.m	Sah			
	5:15 p.m	5:30 p.m	Sah			
22.01.22	8:30 a.m	8:45 a.m	Ranjit			
	12:10 p.m	12:25 p.m	Ranjit			
	2:10 p.m	2:15 p.m	Sah			
	5:00 p.m	5:15 p.m	Sah			
23.01.22	9:00 a.m	9:15 a.m	Ranjit			
	12:15 a.m	12:30 a.m	Sah			
	2:00 p.m	2:15 p.m	Sah			
	5:10 p.m	5:30 p.m	Ranjit			
24.01.22	8:45 a.m	9:00 a.m	Sah			

Anti Smoke gun Register - 2022

Date	Start Time	Off Time	Sign. of Operator	Sign. of S/O Incharge	Sign. of DELTA	Sign. of B/L	Sign. of EHS Dept
25.02.22	8:45am	9:00am	Sah				
	12:10pm	12:25pm	Ranjit				
	2:05pm	2:15pm	Sah				
	4:45pm	5:00pm	Sah				
26.02.22	9:00am	9:15am	Sah				
	12:30pm	12:45pm	Sah				
	2:15pm	2:30pm	Ranjit				
	5:00pm	5:15pm	Sah				
27.02.22	9:15am	9:30am	Sah				
	12:00pm	12:15pm	Sah				
	2:00pm	2:15pm	Ranjit				
	5:00pm	5:15pm	Sah				
28.02.22	8:45am	9:00am	Sah				
	12:15pm	12:30pm	Ranjit				
	2:10pm	2:25pm	Sah				
	5:15pm	5:30pm	Sah				

Anti Smoke gun Register - 2022

Date	Start Time	Off Time	Sign. of Operator	Sign. of S/O Incharge	Sign. of DELTA	Sign. of B/L	Sign. of EHS Dept
01.03.22	9:00am	9:15am	Sah				
	12:10pm	12:25pm	Sah				
	2:00pm	2:15pm	Ranjit				
	5:00pm	5:15pm	Sah				
02.03.22	9:15am	9:30am	Sah				
	11:45am	12:00pm	Sah				
	2:00pm	2:15pm	Ranjit				
	5:15pm	5:30pm	Sah				
03.03.22	9:00am	9:15am	Sah				
	12:00pm	12:15pm	Sah				
	2:15pm	2:30pm	Ranjit				
	4:45pm	5:00pm	Sah				
04.03.22	9:15am	9:30am	Sah				
	12:00pm	12:15pm	Sah				
	2:15pm	2:30pm	Ranjit				
	5:00pm	5:15pm	Ranjit				
05.03.22	8:45am	9:00am	Sah				
	12:00pm	12:15pm	Sah				
	2:00pm	2:15pm	Ranjit				
	5:00pm	5:15pm	Ranjit				
06.03.22	9:00am	9:15am	Sah				
	11:45am	12:00pm	Sah				
	2:15pm	2:30pm	Ranjit				
	4:45pm	5:00pm	Sah				
07.03.22	9:15am	9:30am	Sah				
	12:00pm	12:15pm	Sah				
	2:15pm	2:30pm	Ranjit				
	5:00pm	5:15pm	Ranjit				
08.03.22	9:00am	9:15am	Sah				
	12:00pm	12:15pm	Sah				
	2:00pm	2:15pm	Sah				
	5:00pm	5:15pm	Sah				
























Anti Smoke gun Register - 2022

January - 2022

Date Pg No

DELTA

Pg No

Date	Start time	Off time	Signature of Operator	Signature of Site Incharge	Signature of BCL	Signature of EHS Dept
01.01.22	9:00 a.m	9:15 a.m	Ranjit			
	12:30 p.m	12:45 p.m	Sah			
	2:30 p.m	2:45 p.m	Sah			
	5:20 p.m	5:15 p.m	Ranjit			
02.01.22	9:00 a.m	9:15 a.m	Ranjit			
	12:30 p.m	12:45 p.m	Sah			
	2:30 p.m	2:45 p.m	Ranjit			
	5:00 p.m	5:15 p.m	Sah			
03.01.22	9:00 a.m	9:15 a.m	Ranjit			
	12:30 p.m	12:45 p.m	Sah			
	2:30 p.m	2:45 p.m	Sah			
	5:00 p.m	5:15 p.m	Ranjit			
04.01.22	9:00 a.m	9:15 a.m	Ranjit			
	12:30 p.m	12:45 p.m	Sah			
	2:30 p.m	2:45 p.m	Sah			
	5:00 p.m	5:15 p.m	Ranjit			
05.01.22	9:00 a.m	9:15 a.m	Ranjit			
	12:00 p.m	12:15 p.m	Sah			
	2:30 p.m	12:45 p.m	Sah			
	5:00 p.m	5:15 p.m	Ranjit			
6.01.22	9:30 a.m	9:45 p.m	Sah			
	12:30 p.m	12:45 p.m	Ranjit			
	2:30 p.m	2:45 p.m	Sah			
	5:00 p.m	5:15 p.m	Sah			
7.01.22	9:30 a.m	9:45 a.m	Sah			
	12:30 p.m	12:45 p.m	Ranjit			
	2:30 p.m	2:45 p.m	Sah			
	5:00 p.m	5:15 p.m	Sah			
8.01.22	9:30 a.m	9:45 p.m	Sah			
	12:30 p.m	12:45 p.m	Ranjit			
	2:30 p.m	2:45 p.m	Sah			
	5:00 p.m	5:15 p.m	Sah			

Annexure-XXIV
Copy of HSD bills

100/1822110

BILL/INVOICE

PH-0124-2572744

100/1822110

MOB -9711373818

SHAHEED RAMPHAL KAJLA FILLING STATION
DEALER- INDIAN OIL CORPORATION LIMITED

NEAR- 1FFCO CHOWK METRO STATION, SECTOR-29, GURUGRAM, HARYANA
HSN CODE : MS&XP95 : 27101241 / HSD: 27101944 / BS VI

DEBIT NO.2648

DATED : 31/03/2022

100/1822110 CONSTRUCTION CO.

RAM KRISHAN HOUSE, NEAR- MLA TEJ PAL

TANWAR KOTHI, VILL- RAMGARH

100/1822110 BADSHAHPUR, GURGAON

PAN#. AEFPS1460P

BILLING PERIOD : FROM 16/03/2022 TO 31/03/2022

PAGE NO. : 1

PARTICULARS	QUANTITY	RATE	AMOUNT
100/1822110	200.000	87.92	17584.00
100/1822110	200.000	88.72	17744.00
100/1822110	200.000	89.52	17904.00
100/1822110	200.000	90.85	18170.00
100/1822110	200.000	91.20	18240.00
100/1822110	200.000	92.70	18540.00

ASTHETIC TOWNSHIP DEVELOPERS PVT LTD

Gate Entry No. 9937

Date. 01/04/2022

Time. 13:30

Vehicle No. By hand

Received By. Sheeraj K.

TOTAL AMOUNT	:	108182.00
BILL AMOUNT	:	108182.00
NET PAYABLE AMOUNT	:	108182.00

100/1822110 SLIP : 6

RS 108182.00

(TEN LAKH EIGHT THOUSAND ONE HUNDRED EIGHTY TWO ONLY)

TERMS & CONDITIONS

100/1822110 WILL BE CHARGED IF THE PAYMENT IS NOT MADE WITHIN 7 DAYS FROM THE DATE OF BILL.

100/1822110 SOLD WILL NOT BE TAKEN BACK.

100/1822110 WILL BE CHARGED IF CHEQUE WILL BE BOUNCED.

100/1822110 DETAILS:

100/1822110 100/1822110 LTD.

100/1822110 100/1822110

100/1822110 100/1822110

100/1822110 100/1822110-29, GURUGRAM

FOR SHAHEED RAMPHAL KAJLA FILLING STATION

AUTHORISED SIGN.

100/1822110 01/04/22

SHAHED RAMPHAL KAJLA FILLING STATION
DEALER - INDIAN OIL CORPORATION LIMITED

NEAR- IFFCO CHOWK METRO STATION, SECTOR-29, GURUGRAM, HARYANA
HSN CODE : MS&XP95 : 27101241 / HSD: 27101944 / BS VI

DATED : 16/03/2022

CONSTRUCTION CO.

ASHAN HOUSE, NEAR- MLA TEJ PAL

RAMGARH VILL- RAMGARH

BADSHAHPUR, GURGAON

AEFPS1460P

PERIOD : FROM 01/03/2022 TO 15/03/2022

PAGE NO. : 1

QUANTITY	RATE	AMOUNT
1400.000	87.11	121954.00

ASTHETIC TOWNSHIP DEVELOPERS PVT. LTD.

Gate Entry No. 9681

Date 16/03/22

Time 14:30

Vehicle No. By hand

Received By. [Signature]

Phan
16/3/22

TOTAL AMOUNT	:	121954.00
BILL AMOUNT	:	121954.00
NET PAYABLE AMOUNT	:	121954.00

INR 121954.00

(ONE LAKH TWENTY ONE THOUSAND NINE HUNDRED FIFTY FOUR ONLY)

TERMS & CONDITIONS

1. 1% DISCOUNT WILL BE CHARGED IF THE PAYMENT IS NOT MADE WITHIN 7 DAYS FROM THE DATE OF BILL.

2. CASH ON DELIVERY WILL NOT BE TAKEN BACK.

3. 1% DISCOUNT WILL BE CHARGED IF CHEQUE WILL BE BOUNCED.

4. BANK DETAILS

BANK NAME: HDFC BANK LTD.

BRANCH: 208730000014

IFSC: HDFC0000000

BRANCH: SECTOR-29, GURUGRAM

FOR SHAHEED RAMPHAL KAJLA FILLING STATION

AUTHORISED SIGN.

[Signature]

BILL/INVOICE

PH-0124-2572744

MOB -9711373818

SHAHEED RAMPHAL KAJLA FILLING STATION

DEALER- INDIAN OIL CORPORATION LIMITED

NEAR- IFFCO CHOWK METRO STATION, SECTOR-29, GURUGRAM, HARYANA

HSN CODE : MS&XP95 : 27101241 / HSD: 27101944 / BS VI

BILL NO.2376

DATED : 28/02/2022

S. S. CONSTRUCTION CO.

RAM KRISHAN HOUSE, NEAR- MLA TEJ PAL

TANWAR KOTHI, VILL- RAMGARH

P O BADSHAHPUR, GURGAON

PAN# : AEFPS1460P

BILLING PERIOD : FROM 16/02/2022 TO 28/02/2022

PAGE NO. : 1

PARTICULARS	QUANTITY	RATE	AMOUNT
HSD	800.000	87.11	69688.00
MS	18.680	95.90	1791.41

TOTAL AMOUNT : 71479.41

ROUND OFF AMOUNT : -0.41

BILL AMOUNT : 71479.00

NET PAYABLE AMOUNT : 71479.00

TOTAL SLIP : 5

RS. 71479.00

SEVENTY ONE THOUSAND FOUR HUNDRED SEVENTY NINE ONLY)

TERMS & CONDITIONS

1. PAYMENT 24% WILL BE CHARGED IF THE PAYMENT IS NOT MADE WITHIN 7 DAYS FROM THE DATE OF BILL.
2. GOODS ONCE SOLD WILL NOT BE TAKEN BACK.
3. PAYMENT 5% WILL BE CHARGED IF CHEQUE WILL BE BOUNCED.

BANK DETAILS

BANK NAME : HDFC BANK LTD.

ACCOUNT : 17298730000014

IFSC : HDFC0001729

BRANCH : SECTOR-29, GURUGRAM

FOR SHAHEED RAMPHAL KAJLA FILLING STATION

AUTHORISED SIGN.

ASTHETIC TOWNSHIP DEVELOPERS PVT. LTD.

Gate Entry No. 9363

Date. 01/03/2022

Time. 15:05

Vehicle No.

Received By. [Signature]

PH-0124-2572744
MOB -9711373818

BILL/INVOICE

PH-0124-2572744
MOB -9711373818

SHAAHEED RAMPHAL KAJLA FILLING STATION
DEALER INDIAN OIL CORPORATION LIMITED

DEAL: TIMEO CHOWK METRO STATION, SECTOR-29, GURUGRAM, HARYANA
HSN CODE MS&XP95 : 27101241 / HSD: 27101944 / BS VI

2081

DATED : 31/01/2022

INSTRUCTION CO

SHAN HOUSE, NEAR- MLA TEJ PAL

THI VILL RAMGARH

RAJSHAHIPUR, GURGAON

WIPFS1460P

PERIOD : FROM 16/01/2022 TO 31/01/2022

PAGE NO. : 1

QUANTITY	RATE	AMOUNT
1000 000	87.11	87110.00

8893
22/22 15.00
30.000000
A/Inka
11/2/22

TOTAL AMOUNT	87110.00
BILL AMOUNT	87110.00
NET PAYABLE AMOUNT	87110.00

SEVEN THOUSAND ONE HUNDRED TEN ONLY)

TERMS & CONDITIONS

1. THE BILL WILL BE CHARGED IF THE PAYMENT IS NOT MADE WITHIN 7 DAYS FROM THE DATE OF BILL.

2. CASH WILL NOT BE TAKEN BACK.

3. THE BILL WILL BE CHARGED IF CHEQUE WILL BE BOUNCED.

FOR SHAAHEED RAMPHAL KAJLA FILLING STATION

AUTHORIZED SIGN.

NO: 06071822110
GST: 06AFDPP3568G1ZO

BILL/INVOICE

PH-0124-2572744
MOB -9711373818

SHAHEED RAMPHAL KAJLA FILLING STATION
DEALER- INDIAN OIL CORPORATION LIMITED
NEAR- IFFCO CHOWK METRO STATION, SECTOR-29, GURUGRAM, HARYANA
HSN CODE : MS&XP95 : 27101241 / HSD: 27101944 / BS VI

DATED : 16/01/2022

NO. 2049

S. S. CONSTRUCTION CO.
RAM KRISHAN HOUSE, NEAR- MLA TEJ PAL
TANWAR KOTHI, VILL- RAMGARH
P.O- BADSHAHPUR, GURGAON
PAN#: AEFPS1460P
BILLING PERIOD : FROM 01/01/2022 TO 15/01/2022

PAGE NO. : 1

PARTICULARS	QUANTITY	RATE	AMOUNT
HSD	1200.000	87.11	104532.00



TOTAL AMOUNT	:	104532.00
BILL AMOUNT	:	104532.00
NET PAYABLE AMOUNT	:	104532.00

TOTAL SLIP : 6

RS. 104532.00
(ONE LAKH FOUR THOUSAND FIVE HUNDRED THIRTY TWO ONLY)

TERMS & CONDITIONS

1. INTEREST 24% WILL BE CHARGED IF THE PAYMENT IS NOT MADE WITHIN 7 DAYS FROM THE DATE OF BILL.

2. GOODS ONCE SOLD WILL NOT BE TAKEN BACK.

3. INTEREST 5% WILL BE CHARGED IF CHEQUE WILL BE BOUNCED.

BANK DETAILS:

BANK NAME: HDFC BANK LTD.

ACC. NO. 17208730000014

IFSC: HDFC0001720

BRANCH: SECTOR-29, GURUGRAM

FOR SHAHEED RAMPHAL KAJLA FILLING STATION

AUTHORISED SIGN.

8655
17/01/22 12:50
134 hand
1965 m

PH-113
-9711373818

BILL/INVOICE

PH-0124-2572744
MOB -9711373818

SHAHEED RAMPHAL KAJLA FILLING STATION
DEALER- INDIAN OIL CORPORATION LIMITED
NEAR- IFFCO CHOWK METRO STATION, SECTOR-29, GURUGRAM, HARYANA
HSN CODE : MS&XP95 : 27101241 / HSD: 27101944 / BS VI

1865

DATED : 31/12/2021

CONSTRUCTION CO.
KASHISHAN HOUSE, NEAR- MLA TEJ PAL
KOTHI, VILL- RAMGARH
BADSHAHPUR, GURGAON
AFFPS1460P

PERIOD : FROM 16/12/2021 TO 31/12/2021

PAGE NO. : 1

QUANTITY	RATE	AMOUNT
600.000	87.11	52266.00

TOTAL AMOUNT	: 52266.00
BILL AMOUNT	: 52266.00
NET PAYABLE AMOUNT	: 52266.00

52266.00
TWO THOUSAND TWO HUNDRED SIXTY SIX ONLY)

TERMS & CONDITIONS

7% WILL BE CHARGED IF THE PAYMENT IS NOT MADE WITHIN 7 DAYS FROM THE DATE OF BILL.
SOLD WILL NOT BE TAKEN BACK.

WILL BE CHARGED IF CHEQUE WILL BE BOUNCED.

DETAILS

STATE BANK LTD
78730000014
1726
GURUGRAM



FOR SHAHEED RAMPHAL KAJLA FILLING STATION
AUTHORISED SIGN.

8322
03/01/22
17:00
By hand
PK Singh

PH-0124-2572744
MOB - 9711373818

BILL/INVOICE

SHAHEED RAMPHAL KAJLA FILLING STATION
DEALER- INDIAN OIL CORPORATION LIMITED
NEAR- IFFCO CHOWK METRO STATION, SECTOR-29, GURUGRAM, HARYANA
HSN CODE : MS&XP95 : 27101241 / HSD: 27101944 / BS VI

1640

DATED : 30/11/2021

CONSTRUCTION CO.
SHAN HOUSE, NEAR- MLA TEJ PAL
KOTHU, VILL- RAMGARH
KADSHAMPUR, GURGAON
NEFPS1460P

PERIOD : FROM 16/11/2021 TO 30/11/2021

PAGE NO. : 1

QTY	QUANTITY	RATE	AMOUNT
	200.000	87.11	17422.00
	35.060	95.90	3362.25



TOTAL AMOUNT	:	20784.25
ROUND OFF AMOUNT	:	-0.25
BILL AMOUNT	:	20784.00
NET PAYABLE AMOUNT	:	20784.00

84.00

THOUSAND SEVEN HUNDRED EIGHTY FOUR ONLY)

TERMS & CONDITIONS

94% WILL BE CHARGED IF THE PAYMENT IS NOT MADE WITHIN 7 DAYS FROM THE DATE OF BILL.
SOLD WILL NOT BE TAKEN BACK.
WILL BE CHARGED IF CHEQUE WILL BE BOUNCED.

DEBIT BANK LTD

120000000014

1200001720

SECTOR-29, GURUGRAM



FOR SHAHEED RAMPHAL KAJLA FILLING STATION

AUTHORISED SIGN.

8413

01/12/21

15:00

By hand P/Singh

BILL/INVOICE

PH-0124-2572744
MOB -97113738186071822110
6AFDPD356BG120SHAHEED RAMPHAL KAJLA FILLING STATION
DEALER- INDIAN OIL CORPORATION LIMITED
NEAR- IFFCO CHOWK METRO STATION, SECTOR-29, GURUGRAM, HARYANA
HSN CODE : MS&XP95 : 27101241 / HSD: 27101944 / BS VI

DATED : 16/11/2021

BILL NO.1605

S. S. CONSTRUCTION CO.
RAM KRISHAN HOUSE, NEAR- MLA TEJ PAL
KOTHI, VILL- RAMGARH
RADSHAHPUR, GURGAON
PAN# AEFPS1460P
BILLING PERIOD : FROM 01/11/2021 TO 15/11/2021

PAGE NO. : 1

PARTICULARS	QUANTITY	RATE	AMOUNT
	700.000	87.11	60977.00
	20.000	107.61	2152.20

TOTAL AMOUNT	:	63129.20
ROUND OFF AMOUNT	:	-0.20
BILL AMOUNT	:	63129.00
NET PAYABLE AMOUNT	:	63129.00

FORM SLIP : 5

63129.00
THREE THOUSAND ONE HUNDRED TWENTY NINE ONLY)

TERMS & CONDITIONS

- INTEREST 24% WILL BE CHARGED IF THE PAYMENT IS NOT MADE WITHIN 7 DAYS FROM THE DATE OF BILL.
- GOODS ONCE SOLD WILL NOT BE TAKEN BACK.
- INTEREST 5% WILL BE CHARGED IF CHEQUE WILL BE BOUNCED.

BANK DETAILS:
STATE BANK LTD
BRANCH NO. 100730000014
BRANCH NO. 100730000014
BRANCH NO. 100730000014
BRANCH NO. 100730000014

FOR SHAHEED RAMPHAL KAJLA FILLING STATION

AUTHORISED SIGN.

Received
16/11/21

1822110
340003568G1Z0

BILL/INVOICE

PH-0124-2572744
MOB -9711373818

SHAHEED RAMPHAL KAJLA FILLING STATION
DEALER- INDIAN OIL CORPORATION LIMITED
NEAR- IFFCO CHOWK METRO STATION, SECTOR-29, GURUGRAM, HARYANA
HSN CODE : MS&XP95 : 27101241 / HSD: 27101944 / BS VI

NO.1462

DATED : 31/10/2021

S S CONSTRUCTION CO.
RAM KRISHAN HOUSE, NEAR- MLA TEJ PAL
TANWAR KOTHI, VILL- RAMGARH
P.O- BADSHAHPUR, GURGAON
PAN#: AEFPS1460P

DURATION PERIOD : FROM 16/10/2021 TO 31/10/2021

PAGE NO. : 1

ITEMS	QUANTITY	RATE	AMOUNT
BSVI	200.000	95.31	19062.00
HSD	200.000	96.72	19344.00
HSD	200.000	97.07	19414.00
HSD	50.000	98.12	4906.00
BSVI	200.000	98.48	19696.00

✓

TOTAL AMOUNT	:	82422.00
BILL AMOUNT	:	82422.00
NET PAYABLE AMOUNT	:	82422.00

RS. 82422.00
(EIGHTY TWO THOUSAND FOUR HUNDRED TWENTY TWO ONLY)

TERMS & CONDITIONS

1. A NET 24% WILL BE CHARGED IF THE PAYMENT IS NOT MADE WITHIN 7 DAYS FROM THE DATE OF BILL.
2. ONCE SOLD WILL NOT BE TAKEN BACK.
3. A 5% WILL BE CHARGED IF CHEQUE WILL BE BOUNCED.

BANK DETAILS:

BANK NAME: HDFC BANK LTD.
A/C NO.: 17208730000014
IFSC: HDFC0001720
BRANCH: SECTOR-29, GURUGRAM

FOR SHAHEED RAMPHAL KAJLA FILLING STATION

AUTHORISED SIGN.

8215
01/11/21 16:00
BY hand
Pcsimph



BILL/INVOICE

PH-0124-2572744
MOB -9711373818

SHAHEED RAMPHAL KAJLA FILLING STATION
DEALER- INDIAN OIL CORPORATION LIMITED
NEAR- IFFCO CHOWK METRO STATION, SECTOR-29, GURUGRAM, HARYANA
HSN CODE : MS&XP95 : 27101241 / HSD: 27101944 / BS VI

NO 1337

DATED : 16/10/2021

CONSTRUCTION CO.

RAM KRISHAN HOUSE, NEAR- MLA TEJ PAL
TANWAR KOTHI, VILL- RAMGARH
P.O- BADSHAHPUR, GURGAON
PAN#: AEFPS1460P

BILLING PERIOD : FROM 01/10/2021 TO 15/10/2021

PAGE NO. : 1

QUANTITY	RATE	AMOUNT
200.000	91.49	18298.00
200.000	92.50	18500.00
200.000	93.56	18712.00
200.000	93.91	18782.00
200.000	94.61	18922.00
24.000	101.24	2429.76

TOTAL AMOUNT : 95643.76
ROUND OFF AMOUNT : 0.24
BILL AMOUNT : 95644.00
NET PAYABLE AMOUNT : 95644.00

TOTAL SLIP : 6

RS. 95644.00

(FIFTY FIVE THOUSAND SIX HUNDRED FORTY FOUR ONLY)

TERMS & CONDITIONS

DISCOUNT 2% WILL BE CHARGED IF THE PAYMENT IS NOT MADE WITHIN 7 DAYS FROM THE DATE OF BILL.
GOODS ONCE SOLD WILL NOT BE TAKEN BACK.

DISCOUNT 2% WILL BE CHARGED IF CHEQUE WILL BE BOUNCED.

BANK DETAILS:

BANK NAME : IDFC BANK LTD.

BANK NO : 17208730000014

BANK BRANCH : GURUGRAM

BANK ADDRESS : SECTOR 29, GURUGRAM

FOR SHAHEED RAMPHAL KAJLA FILLING STATION

AUTHORISED SIGN.

1 Speed
16/10/21

4957
16/10/21
14:40
By hand
PC Singh

Annexure-XXV

Copies of Newspaper Advertisement

भर्ती

अन्य रिक्तियाँ

भर्ती-रिक्त पदों की स्थिति

एकाधिक रिक्तियाँ

अकादमिक

सामान्य

ASHA SCHOOL
RING ROAD, DELHI CANTT
Invites application for the post of
SPECIAL EDUCATOR
B Ed in Sp Ed/Sp in Sp Edn with 3 Yrs
experience (Honarium - ₹ 375/- p.m.)
OCCUPATIONAL THERAPIST
BOT preferable with experience
(Honarium - ₹ 375/- p.m.)
ACCOUNT CLERK
B.Com from Recognized University
and preferably 2 yrs. exp.
(Honarium - ₹ 425/- p.m.)
HOUSEKEEPER
C/Pass (Honarium - ₹ 14,220/- p.m.)
Interested persons may
please contact for details
8860417192
awwaashadehi@gmail.com
Last date of application
is 15 February 2022

घर से काम
(वर्क फ्रॉम होम)

Home Mart Networking Co.
को चाहिए मेल फ्रीमेल, हाउस
वाइफ SMS Email जॉब 12000 -
36000/- महिला, लैपटॉप फेसिलिटी,
50% एडवांस सैलरी # 8828170929

रिक्त पद

REQD. Computer Operator
having min 5 YR EXP. CONT-
Shah Jindal, E478, Greater
Kailash 2, 2nd Flr, New Delhi-48

बिजनेस

लोन

लेखा

बैंकिंग

REQ. For Banking
Recovery/collection Apply
Only Dra Manager Supervisor
Telecallers Tracer Salary 8000-

मैसर्स ऐस्थेटिक टाउनशिप
डेवलपर्स प्राइवेट लिमिटेड,
सुरात लोक, सेक्टर-27,
गुरुग्राम, हरियाणा
सार्वजनिक सूचना
एतद्वारा सर्वसाधारण को सूचित
किया जाता है कि मैसर्स ऐस्थेटिक
टाउनशिप डेवलपर्स प्राइवेट
लिमिटेड द्वारा सुरात लोक,
सेक्टर-27, गुरुग्राम, हरियाणा में
"कॉन्फिडेंसल कॉन्सेप्स प्रोजेक्ट
का विस्तार" की परियोजना को
सम्बन्धित पर्यावरण प्रभाव आकलन
प्राधिकरण, हरियाणा द्वारा एक सं.
21-137/2018-आईए-111
दिनांकित 07 फरवरी, 2019 को
मान्यता से पर्यावरण मंजूरी प्रदान
की जा चुकी है। पर्यावरण मंजूरी
की प्रति एआईआईए, हरियाणा के
पास उपलब्ध है तथा एआईआईए
एवं सीसी की वेबसाइट
<https://parivesh.nic.in/> पर
भी देखी जा सकती है।
मैसर्स ऐस्थेटिक टाउनशिप डेवलपर्स
प्राइवेट लिमिटेड

निविदाएं (टेंडर्स)

75
आज़ादी का
अमृत महोत्सव
यूनियन बैंक
एनालिटिक्स सेंटर ऑफ़ एक्सीलेंस,
5वीं मंजिल, केन्द्रीय कार्यालय,
239, विधान भवन मार्ग, नरीमन पॉइंट,

Lowest Gold Rate in all over Delhi

₹44400 Per 10g

Today's B.I.S. Hallmark 91.6/22CT Gold Rate

8% Making on Gold Testing Machine Available

KAPIL JEWELLERS SINCE 2010

F-24/35-36, Sec-7 **Rohini**
9999889969, 01127042254

Lowest Gold Rate in Delhi NCR

(दुकानदार भाईयों के लिए मान सम्मान रखा जाएगा)
₹44221 Per 10g

Today's B.I.S. Hallmark 91.6/22CT Gold Rate

7% Making on Gold Testing Machine Available

GIRI ZEVR MAHAL PVT. LTD. SINCE 1990

A-11, Central Mkt. Delhi **Kalyanpuri**
9971075268 GURUJI Walking Distance Sanjay Lake Metro Station

QUICK PROCESS LOAN FOR BUSINESS PEOPLE ONLY

MINIMUM ₹5 CRORES & ABOVE
SECURED / UNSECURED LOAN

☑ Manufacturing Units
☑ Hospitals
☑ Educational Institutions
☑ Jewellery
☑ Textiles
☑ Real Estate
☑ Construction
☑ Start UPS/ N

Cibil Not Required

8144260260
doculoan.kg@gmail.com

PROFITABLE AUTO COM

Chennai based Company, part of well-renowned Group, mfg precision components for reputed Tier-1 clients; specializing in Anodizing, Chromating, Machining, Brazing. Skilled workforce, sizeable orders and good growth prospects. Promoters divesting 100% stake focus on other businesses of the Group but will continue for smooth transition to the stakeholders.

Please contact

vasu@riverbridge.in

+91 9884779540

jobs

SITUATION VACANT

REQ. Asstt. Secy Govt. Aprvd Sports Org., Graduate, Sports & Indian Sign Lang/ C O D A . V i s i t : aiscd.org/applform.php

REQD. Computer Operator having min 5 YR EXP. CONT. Shah Jindal, E478, Greater Kailash 2, 2nd Flr, New Delhi-48

personal

LOST & FOUND

NOTICE is hereby given to all concerned that, I Rajiv Jain s/o Late K.K. Jain, resident of Sector D, Mandir Marg New Delhi, had lost original REGISTRY OF MY RESIDENTIAL PLOT NO. 656, BLOCK C, SECTOR 36, GREATER NOIDA - 201308. On 14/01/2022. For which FIR no. LR No:44941/2022 is registered.

real estate

FOR SALE

GURGAON

SALE commercial plot 3 side Open-2700(90x30)sq.ft @ 7 cr. & 900sq.ft @ 3 cr. near Patara Chowk Sulted for Hosptl / Lab/ Hardware/Jeweller #8968892675

tender & notices

PUBLIC NOTICE

NOTICE from Prayag Sangit Samiti, Prayagraj, Prabhakar theory exam of Prayag Sangit Samiti which is scheduled for 22nd and 23rd Jan'22 at centralized location in Delhi is postponed due to Covid till further notice. Next date will be updated on website soon.

M/s Asthetic Township Developers Pvt. Ltd., at Sushant Lok, Sector-27, Gurugram, Haryana
PUBLIC NOTICE

General public is hereby informed that Environment Clearance to the project of "Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana by M/s Asthetic Township Developers Pvt. Ltd. has been accorded with Environment Clearance vide F.No.21-137/2018-IA-111 dated 07th February 2019 by State Environment Impact Assessment Authority, Haryana. The copy of Environment Clearance is available with SEIAA, Haryana and can also be seen on website of MoEF&CC at <https://parivesh.nic.in/> M/s Asthetic Township Developers Pvt. Ltd.

TENDERS

The Energy and Resources Institute (TERI), New Delhi invites quotes for the Water Conservation through Rejuvenation of Pond with Participatory Community Engagement. Detailed documents can be viewed and downloaded from TERI website at <http://www.teriin.org/announcements>. Interested suppliers shall submit their bids manually on or before 31st January, 2022, addressed to: Manager-Materials, TERI, Darbari Seth Block, Lodhi Road, New Delhi - 110003

Union Bank of India
Analytics Centre of Excellence, 5th Floor, Central Office, 239, Vidhan Bhavan Marg, Nariman Point, Mumbai - 400 021.

E-TENDER NOTICE

Union Bank of India invites e-Tender from reputed, established and experienced vendors for following items.

Tender Ref: UBI/ACOE/2021-22/01

Item/Job Description: RFP for Selection of Consultant for Establishment and Development of Analytics Centre of Excellence.

Date and time of tender publication: 20.01.2022 11:00 hours

Last Date and Time for Bid Submission: 11.02.2022 16:00 hours

For other details and downloading of RFP document, please visit our Bank's website www.unionbankofindia.co.in or the Government tender portal www.eprocure.gov.in.

PROPERTY FOCUS

DLF MIDTOWN

ONE MIDTOWN
Book Today

Homes Starting @ 1NR3 Cr.

Buniyad Retail India Pvt. Ltd. ☎ +91-9910006110

DLF AUTHORISED CHANNEL PARTNER | RERA Registration No.: DLRERA2021A0117

To place an ad in

TIMES interad

Logon to : ads.timesgroup.com

Scan QR Code



E- Auction Form Disposal of Fire & Approx. 309.846 Jabi, Ropes Stg sold on Per Water on "As is Where Hooghly Infrastr (Hukumchand Jabi no.6, PO- Hazir Parganas, PS- Bengal-743135) Umakant Mish 09903905016 done: Upto 28th appointment Date 28/01/2022 from auction Form w Deposit (EMD) latest by 28/01/2022 the auctioneer's address is www.thesaleandregister.com obtained from below: For Inq. Adanya Goel, Aarti Gahyan, Mamta Sehraw, The Salvago Bldg, Behind Canara Town, Delhi-110

LOOK BR

Delhi based height 5771 Corporate a multi ad Call on

SCAN, SU for this att



Logon to Select Cl

Tenders/ company prospectiv Details

Land ad-n 11477 sq. & building

Movable as being constr material like bars, bricks & office equipm

Note:

1. Inspection

Annexure-XXVI

Copy of Office Memorandum (OM)

F.No.22-65/2017-IA.III
Government of India
Ministry of Environment, Forest and Climate Change
Impact Assessment Division

Indira Paryavaran Bhawan
Jor Bagh Road, Aliganj
New Delhi – 110003
e-mail: sharath.kr@gov.in

Dated: 30th September, 2020

Office Memorandum

Sub: Deliberation on the commitments made by project proponent and requirements to address the concerned raised during the public consultation and prescribe as specific condition(s) while recommending the proposal, for prior environment clearance, in physical terms in lieu of Corporate Environment Responsibility (CER) – regarding.

This is in supersession of the OM of even number dated 1st May, 2018, regarding guidelines in respect of Corporate Environment Responsibility. Ministry is in receipt of several representations regarding imposition of certain percentage of project cost or expansion cost as Corporate Environment Responsibility. Further, the said OM was also challenged before the Hon'ble High Court of Delhi in WP(C) No. 13252/2019 in the matter of CREDAI, NCR *Versus* Union of India and Ors.

The matter has since been examined in the Ministry and it is hereby decided that henceforth the Expert Appraisal Committee or State Level Expert Appraisal Committee shall deliberate on the commitments made by the project proponent to address the concerns raised during the public consultation and prescribe specific condition(s) in physical terms while recommending the proposal, for grant of prior environment clearance instead of allocation of funds under Corporate Environment Responsibility

Further, it is directed that all the activities proposed by the project proponent or prescribed by the Expert Appraisal Committee or State Level Expert Appraisal Committee, as the case may be, shall be part of the Environment Management Plan.

This issues with the approval of competent authority.


(Sharath Kumar Pallerla)
Scientist 'F'/Director (IA-Policy)

To,

1. Chairman and Member Secretary of Central Pollution Control Board

2. Chairpersons and Members of all the Expert Appraisal Committees
3. Chairpersons and Member Secretaries of all the SEIAA/SEACs
4. Chairpersons and Member Secretaries of all SPCBs/UTPCCs
5. Member Secretaries of all the Expert Appraisal Committees
6. All the officers of IA Division

Copy for information to:

1. PS to Minister for Environment, Forest and Climate Change
2. PS to MoS for Environment, Forest and Climate Change
3. PPS to Secretary (EF&CC)
4. PPS to AS(RA) / AS(RSP)
5. PPS to JS(GM) / JS(AKN)/JS(SKB)
6. Website, MoEF&CC
7. Guard File.


(Sharath Kumar Pallerla)
Scientist 'F'/Director (IA-Policy)

Annexure-XXVII
Request Letter to GMDA

ASTHETIC TOWNSHIP DEVELOPERS PRIVATE LIMITED

Reg. Office- 262, DDA OFFICE COMPLEX, JHANDEWALA EXT., NEW DELHI - 110055

Ref. No. APL/P/20/005

Date: 19.05.2020

To,
Executive Engineer
GMDA
Sector-32, Gurugram
Haryana

Subject: Assurance letter for supply of fresh water commissioning for domestic purpose for Commercial Colony at Sector 27, Gurugram, admeasuring area 2.851 acres, License No. 97 of 2011 dated 09.11.2011

Dear Sir,

We are developing a commercial colony on the land admeasuring 2.851 acres in Sector 27, Gurugram, Haryana vide License No. 97 of 2011 dated 09.11.2011 issued by DTCP, Haryana, Chandigarh ("Project").

It is requested to kindly provide assurance letter for supply of 187 KLD domestic water for the commissioning of said Project.

It is kindly requested to consider this ultimate water requirement keeping in consideration the future planning for laying infrastructure by Gurugram Metropolitan Development Authority (GMDA), Gurugram. We further undertake to comply with the guidelines issued by the authority.

Thanking You.

Authorized Signatory

For M/s Asthetic Township Developers Private Limited



Authorized Signatory

Received
A.T.
24/06/2020

CIN NO. U45201DL2006PTC147126

Email: asthetic64@gmail.com
