

ASTHETIC TOWNSHIP DEVELOPERS PRIVATE LIMITED

Reg. Office- 262, DDA OFFICE COMPLEX, JHANDEWALA EXT., NEW DELHI - 110055

Ref. No. APL/P/21/030

Date: 04 May 2021

To,
The Director,
Northern Regional Office (MoEF&CC),
Bays No. 24 -25, Sector- 31-A,
Dakshin Marg,
Chandigarh - 160030

Subject: Submission of six-monthly Compliance report of **June-2021** for the Commercial Colony admeasuring 2.851 acres, Sector-27, Gurugram, Haryana with License No 97 of 2011 dated 09.11.2011 developed by M/s. Asthetic Township Developers Pvt. Ltd.

Reference: EC Letter No. : 21-137 /2018-IA-III; Dated 07/02/2019.

Respected Sir,

This is with reference to the above-mentioned subject. We are herewith submitting six monthly compliance Report of "**June-2021**" for the period of **October 2020 to March 2021** for the Commercial Colony Project admeasuring 2.851 acres at Sector-27, Gurugram, Haryana by M/s. Asthetic Township Developers Pvt. Ltd. along with the necessary annexure for your kind perusal.

We understand that the above is in line with requirement of Ministry of Environment, Forest and Climate Change, GOI.

Thanking You,

Yours Sincerely,



For M/s. Asthetic Township Developers Pvt. Ltd.
Mukesh Gour
(Authorized Signatory)

Enclosure: Compliance Report; Soft copy of Report in C.D

Copy to: 1. Member Secretary, Haryana State Pollution Control Board, C-11, Sector-6,
Panchkula, Haryana
2. Member Secretary, SEIAA, Haryana Bays No. 55 - 58, Paryatan Bhawan, 1st
floor, Sector 2, Panchkula, Haryana 134115

CIN NO. U45201DL2006PTC147126

Email: asthetic64@gmail.com

Commercial Complex

‘Six Monthly Compliance Report’

**Expansion of Commercial Complex Project at
Sushant Lok, Sector-27, Gurugram Haryana by
M/s. Asthetic Township Developers Pvt. Ltd.**

SUBMITTED BY

**M/s Asthetic Township Developers
Pvt. Ltd.**

JUNE 2021

TABLE OF CONTENT

S.No	Description
Compliance of Specific and General Conditions	

LIST OF ANNEXURES

Annexure	Description
Annexure-I	Environment Clearance Letter
Annexure-II	HSPCB/Consent/: 329962320GUNOCTE7324277 dated 03/02/2020
Annexure-III	Aravali NOC
Annexure-IV	Renewal of Licence from Directorate of Town & Country Planning, Haryana
Annexure-V	Intekaal Letter
Annexure-VI	Water Balance
Annexure-VII	RWH Details
Annexure-VIII	Waste management plan during Construction & Operation Phase
Annexure-IX	Photographs of construction of Wind Breaking wall of 10 mtrs. height for dust control
Annexure-X	Environment Monitoring Reports i.e. AAQ, Noise, Water & soil and its interpretation
Annexure-XI	Landscape plan
Annexure-XII	Photographs showing Excavated top soil is preserved
Annexure-XIII	PUC Certificate
Annexure-XIV	Environment Management and Monitoring Plan
Annexure-XV	Receiving of Previous Compliance Report of December, 2020
Annexure-XVI	RMC Purchase Bill
Annexure-XVII	Electricity Approval for construction
Annexure-XVIII	Bill for C&D Waste Disposal
Annexure-XIX	Photographs of Basic Infrastructure provided at Project Site
Annexure-XX	AAI NOC

LIST OF TABLES

Tables	Description	Page No
Table-1	Schedule of Ambient Air Quality Monitoring	01
Table-1(a)	Monitoring Result of SO ₂	01
Table-1(b)	Monitoring Result of NO ₂	02
Table-1(c)	Monitoring Result of PM ₁₀	03
Table-1(d)	Monitoring Result of PM _{2.5}	04

Tables	Description	Page No
Table-1(e)	MonitoringResultof CO	05
Table-2	Schedule of Noise Monitoring	06
Table-2(a)	Day time Monitoring result for Ambient Noise	07
Table-2(b)	Night time Monitoring result for Ambient Noise	07
Table-3	Schedule of R.O. water Monitoring	08
Table-3(a)	Result of R.O. water monitoring	09
Table-4	Soil Monitoring results	10

LISTOFFIGURES

Tables	Description	Page No
Figure-1(a)	SO ₂ Concentration	02
Figure-1(b)	NO ₂ Concentration	03
Figure-1(c)	PM ₁₀ Concentration	04
Figure-1(d)	PM _{2.5} Concentration	05
Figure-1(e)	CO Concentration	06
Figure-2(a)	Graph showing day time noise monitoring results	07
Figure-2(b)	Graph showing night time noise monitoring results	08

COMPLIANCE REPORT

Specific and General Conditions as per the Environmental Clearance issued for Expansion vide F. No. 21-137/2018-IA.III Dated: 07/02/2019 (Annexure-I) for Construction and Operation phases of the Project.

S No	Conditions	Compliance
Part A Specific conditions		
I. Construction phase		
i.	The project proponent shall obtain all necessary clearance/ permission from all relevant agencies including town planning authority before commencement of work. All the construction shall be done in accordance with the local building byelaws.	We would obtain all the necessary clearances/ permission from all the concerned departments in due course of time. As we are in initial stage of construction phase. Following permission we have already obtained: i. Environmental Clearance, ii. Consent to Establish, iii. Aravali NOC, iv. Renewal of License from Directorate of Town & Country Planning, Haryana v. Intekaal Letter Copies of these permissions/clearances are attached as Annexure I, II, III, IV & V respectively.
ii.	“Consent for Establishment /Operate” for the project shall be obtained from the State Pollution Control Board as required under Air (Prevention and Control of Pollution) Act, 1981 and the Water (Prevention and Control of Pollution) Act, 1974.	We have received Consent to Establish for the project. The Copy of the CTE issued by HSPCB vide CTE order no. HSPCB/Consent/: 329962320GUNOC7324277 dated 03/02/2020 is attached for your reference as Annexure-II .
iii.	The approval of the Competent Authority shall be obtained for structural safety of buildings due to earthquakes, adequacy of firefighting equipment etc as per National Building Code including protection measures from lightening etc.	We will submit the Structure Stability certificate in due course of time.
Topography and natural Drainage		
iv.	The natural drain system should be maintained for ensuring unrestricted flow of water. No construction shall be allowed to obstruct the natural drainage through the site, on wetland and water bodies. Check dams, bio- swales, landscape, and other sustainable urban drainage systems	This condition will be complied. Topographical survey has already been done to maintain the natural unrestricted flow of water, when required.

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram
Haryana by M/s. Asthetic Township Developers Pvt. Ltd.**

*

S No	Conditions	Compliance
	(SUDS) are allowed for maintaining the drainage pattern and to harvest rain water. Buildings shall be designed to follow the natural topography as much as possible. Minimum cutting and filling should be done.	
Water requirement, Conservation, rain water Harvesting, and Ground Water Recharge		
v.	Fresh water requirement from HUDA supply shall not exceed 42 KLD with prior permission.	This condition will be complied.
vi.	A certificate shall be obtained from the local body supplying water, specifying the total annual water availability with the local authority, the quantity of water already committed the quantity of water allotted to the project under consideration and the balance water available. This should be specified separately for ground water and surface water sources, ensuring that there is no impact on other users.	We will obtain a certificate from the local body regarding supply of water for operation phase of the project and the same will be submitted.
vii.	The quantity of fresh water usage, water recycling and rainwater harvesting shall be measured and recorded to monitor the water balance as projected by the project proponent. The record shall be submitted to the Regional Office, MoEF&CC along with six monthly Monitoring reports.	For measurement of water consumption, we will install water meter at all the required points of water consumption and record of the same will be maintained and submitted.
viii.	At least 20% of the open spaces as required by the local building bye laws shall be pervious. Use of Grass pavers, paver blocks with at least 50% opening, landscape etc. would be considered as pervious surface.	This condition will be complied.
ix.	Installation of dual pipe plumbing for supplying fresh water for drinking, cooking and bathing etc and other for supply of recycled water for flushing, landscape irrigation, car washing, thermal cooling, conditioning etc. shall be	Dual plumbing system has already been taken into consideration. Water Balance showing use of treated water is attached as Annexure-VI for your reference.

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram
Haryana by M/s. Asthetic Township Developers Pvt. Ltd.**

S No	Conditions	Compliance
	done.	
x.	Use of water saving devices fixtures (viz. low flow flushing systems; use of low flow faucets tap aerators etc) for water conservation shall be incorporated in the building plan.	This condition will be complied during Operation Phase.
xi.	Separation of grey and black water should be done by the use of dual plumbing system. In case of single stack system separate recirculation lines for flushing by giving dual plumbing system be done.	Dual plumbing system has already been taken into consideration. Water Balance showing use of treated water is attached as Annexure-VI for your reference.
xii.	Water demand during construction should be reduced by use of pre-mixed concrete, curing agents and other best practices referred.	Ready Mix Concrete used for Construction work and Purchase bill for the period (October, 2020 to March, 2021) of RMC is attached as Annexure XVI .
xiii.	The local bye-law provisions on rain water harvesting should be followed. If local bye-law provision is not available, adequate provision for storage and recharge should be followed as per the Ministry of Urban Development Model Building Byelaws, 2016. As proposed 03 nos. of rain water harvesting recharge pits shall be provided for rain water harvesting after filtration as per CGWB guidelines.	We have proposed 03 nos. of rain water harvesting recharge pits for rain water harvesting. We have considered all the design criteria of local authority and CGWB. Detail of RWH is attached as Annexure-VII .
xiv.	No ground water shall be used during construction/ operation phase of the project.	Noted the Condition
xv.	Any ground water dewatering should be properly managed and shall conform to the approvals and the guidelines of the CGWA in the matter. Formal approval shall be taken from the CGWA for any ground water abstraction or dewatering.	This condition will be complied.
Solid Waste Management		
xvi.	The provision of the Solid waste (Management) Rules, 2016, e-waste (Management) Rules, 2016, and the Plastics waste (Management) Rules, 2016 shall be	Waste management plan for construction and operation phase of the project has been prepared and submitted during Environmental Clearance. Detailed waste management plan solid waste, e-waste, and Plastic waste is attached as Annexure-VIII .

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram
Haryana by M/s. Asthetic Township Developers Pvt. Ltd.**

S No	Conditions	Compliance
	followed.	
xvii.	Disposal of muck during construction phase shall not create any adverse effect on the neighbouring communities and be disposed taking the necessary precautions for general safety and health aspects of people, only in approved sites with the approval of competent authority.	This condition will be complied.
xviii.	Separate wet and dry bins must be provided in each unit and at the ground level for facilitating segregation of waste. Solid waste shall be segregated into wet garbage and inert materials. Wet garbage shall be composted in Organic Waste Converter. Adequate area shall be provided for solid waste management within the premises which will include area for segregation composting. The inert waste from project will be sent to dumping site.	Detailed waste management plan is prepared. Waste management plan is attached as Annexure-VIII .
xix.	Any hazardous waste generated during construction phase, shall be disposed off as per applicable rules and norms with necessary approvals of the State Pollution Control Board.	Hazardous waste generated during Construction and Operation phase of the project will be disposed off through Hazardous and Other Wastes (Management and Transboundary Movement) Rules, 2016.
xx.	A certificate from the competent authority handling municipal solid wastes, indicating the existing civic capacities of handling and their adequacy to cater to the M.S.W. generated from project shall be obtained.	We would obtain this certificate from the concerned government department and same will be submitted in due course of time.
Sewage Treatment Plant		
xxi.	Sewage shall be treated in the STP based on SBR technology with tertiary treatment i.e. Ultra Filtration. The treated effluent from STP shall be recycled/re-used for flushing and horticulture. Excess water shall be discharged to Municipal Sewer with prior permission.	This condition will be complied. We are in a stage of finalization of contractor for STP installation. We will submit the document in due course of time. This will be submitted after installation & commissioning of STP for Operational Phase.

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram
Haryana by M/s. Asthetic Township Developers Pvt. Ltd.**

S No	Conditions	Compliance
xxii.	A certificate from the competent authority for discharging treated effluent/ untreated effluents into the Public sewer/ disposal/ drainage systems along with the final disposal point shall be obtained.	We will obtain this certificate and submit in due course of time.
xxiii.	No sewage or untreated effluent water would be discharged through storm water drains.	This condition will be complied.
xxiv.	The project proponents would devise a monitoring plan to the satisfaction of the State Pollution Control Board so as to continuously monitor the treated waste water being used for flushing in terms of faecal coliforms and other pathogenic bacteria.	This Condition will be complied during operation phase and we will re-used treated waste water for flushing and other use as per the guideline of HSPCB.
xxv.	The project proponents would commission a third party study on the implementation of conditions related to quality and quantity of recycle and reuse of treated water, efficiency of treatment systems, quality of treated water being supplied for flushing (specially the bacterial counts), comparative bacteriological studies from toilet seats using recycled treated waters and fresh waters for flushing, and quality of water being supplied through spray faucets attached to toilet seats.	This condition will be complied as project is in construction phase. Detailed plan for Operational phase will be submitted in due course of time.
xxvi.	The installation of the Sewage Treatment Plant (STP) shall be certified by an independent expert and a report in this regard shall be submitted to the Ministry before the project is commissioned for operation. Periodical monitoring of water quality of treated sewage shall be conducted. Necessary measures should be made to mitigate the odour problem from STP.	We will obtain the adequacy report for designed STP and submit the same in due course of time. We will ensure that there should not be any odour problem. This will be submitted after installation & commissioning of STP for Operational Phase.

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram
Haryana by M/s. Asthetic Township Developers Pvt. Ltd.**

S No	Conditions	Compliance
xxvii.	Sludge from the onsite sewage treatment, including septic tanks, shall be collected, conveyed and disposed as per Ministry of Urban Development, Central Public Health and Environmental Engineering Organization (CPHEEO) Manual on Sewerage and Sewage Treatment Systems, 2013.	This condition will be complied and we will make agreement with the authorized vendor for disposal of sludge.
Energy		
xxviii.	Compliance with the Energy Conservation Building Code (ECBC) of Bureau of Energy Efficiency shall be ensured. Buildings in the States which have notified their own ECBC, shall comply with the State ECBC. Outdoor and common area lighting shall be LED. Concept of passive solar design that minimize energy consumption in buildings by using design elements, such as building orientation, landscaping, efficient building envelope, appropriate fenestration, increased day lighting design and thermal mass etc. shall be incorporated in the building design. Wall, window, and roof u-values shall be as per ECBC specifications.	This condition will be complied. As we are in early stage of construction of the project. We will submit the detailed ECBC plan in due course of time.
xxix.	Energy conservation measures like installation of CFLs/ LED for the lighting the area outside the building should be integral part of the project design and should be in place before project commissioning. Used CFLs, TFL and LED shall be properly collected and disposed off / sent for recycling as per the prevailing guidelines / rules of the regulatory authority to avoid mercury contamination.	This condition will be complied. As we are in early stage of construction of the project. We will submit the detailed ECBC plan in due course of time. The E-Waste (Management) Rules, 2016 will be followed for disposal of Used CFLs, TFL and LED during Construction and Operation Phase.
xxx.	Solar, wind or other Renewable Energy shall be installed to meet electricity generation equivalent to 1% of the demand load or as per	This condition will be complied. We are doing feasibility detailing for the same. Detailed plan for Energy Conservation Plan as per ECBC 2017 will be submitted during operation phase of the project.

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram
Haryana by M/s. Asthetic Township Developers Pvt. Ltd.**

S No	Conditions	Compliance
	the state level/ Local building bye-laws requirement, whichever is higher. Follow super ECBC requirement of ECBC 2017 and provide compliance report.	
xxxi.	Solar power shall be used for lighting in the apartment to reduce the power load on grid. Separate electric meter-shall be installed for solar power. Solar water heating shall be provided to meet 20% of the hot water demand of the commercial and institutional building or as per the requirement of the local building bye-laws, whichever is higher. Residential buildings are also recommended to meet its hot water demand from solar water heaters, as far as possible.	This condition will be complied and detailed will be submitted in due course of time.
xxxii.	Use of environment friendly materials in bricks, blocks and other construction materials, _shall be required for at least 20% of the construction material quantity. These include Fly Ash bricks, hollow bricks, AACs, Fly Ash Lime Gypsum blocks, Compressed earth blocks, and other environment friendly materials- Fly ash should be used as building material in the construction as per the provision of Fly Ash Notification of September, 1999 and amended as on 27 th August, 2003 and 25 th January, 2016. Ready mixed concrete must be used in building construction.	Noted & details will be submitted in due course of time.
xxxiii.	A certificate of adequacy of available power from the agency supplying power to the project along with the load allowed for the project shall be submitted.	Permission for Electricity Connection from Dakshin Haryana Bijli Vitran Nigam for Construction work has been obtained and copy of permission is attached as Annexure XVII .
Air Quality and Noise		
xxxiv.	Construction site shall be adequately barricaded before the construction begins. Dust, smoke & other air pollution prevention	Work for construction of Wind Breaking wall of 10 mtrs. height for dust control has already been completed. Photograph of the same is attached for

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram
Haryana by M/s. Asthetic Township Developers Pvt. Ltd.**

S No	Conditions	Compliance
	measures shall be provided for the building as well as the site. These measures shall include screens for the building under construction, continuous dust wind breaking walls all around the site (at least 3 meter height). Plastic/tarpaulin sheet covers shall be provided for vehicles bringing in sand, cement, murram and other construction materials prone to causing dust pollution at the site as well as taking Out debris from the site. Sand, murram, loose soil, cement stored on site shall be covered adequately so as to prevent dust pollution. Wet jet shall be provided for grinding and stone cutting. Unpaved surfaces and loose soil shall be adequately sprinkled with water to suppress dust.	your reference as Annexure-IX .
xxxv.	Notification GSR 94(E) dated 25.01.2018 of MoEF&CC regarding Mandatory implementation of Dust Mitigation Measures for Construction and Demolition Activities for projects requiring Environmental Clearance shall be complied with.	We have noted the condition. We will follow the Mandatory implementation of Dust Mitigation Measures during construction activity.
xxxvi.	All construction and demolition debris shall be stored at the site (and not dumped on the roads or open spaces outside) before they are properly disposed. All demolition and construction waste shall be managed as per the provisions of the Construction and Demolition Waste Rules, 2016. All workers working at the construction site and involved in loading, unloading, carriage of construction material and construction debris or working in any area with dust pollution shall be provided with dust mask.	C&D Waste generated at project during construction work have been given to Municipal Corporation Gurugram. Bill for lifting of Construction waste at site is attached as Annexure XVIII . Mask has been provided to all construction workers for protection from the dust.

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram
Haryana by M/s. Asthetic Township Developers Pvt. Ltd.**

S No	Conditions	Compliance
xxxvii.	The diesel generator sets to be used during construction phase shall be low sulphur diesel type and shall conform to Environmental (Protection) prescribed for air and noise emission standards.	Noted the condition.
xxviii.	The gaseous emissions from DG set shall be dispersed through adequate stack height as per CPCB standards. Acoustic enclosure shall be provided to the generator sets to mitigate the noise pollution. The location of the DG set and exhaust pipe height shall be as per the provisions of the Central Pollution Control Board (CPCB) norms.	Adequate stack height as per CPCB standards will be provided for the DG sets during Operation Phase. DG Set will be acoustically enclosed for noise control.
xxxix.	For indoor air quality the ventilation provisions as per National Building Code of India.	This condition will be complied.
xl.	Ambient noise levels shall conform to residential standard both during day and night as per Noise Pollution (Control and Regulation) Rules, 2000. Incremental pollution loads on the ambient air and noise quality shall be closely monitored during construction phase Adequate measures shall be made to reduce ambient air and noise level during construction phase, so as to conform to the stipulated standards by CPCB / SPCB.	Regular Monitoring, as per the statutory requirements of Ambient Noise and Ambient Air Quality are doing at the site. AAQ and Ambient Noise Monitoring report is attached as Annexure-XI .
Green Cover		
xli.	No tree cutting/transplantation of existing trees has been proposed in the project. A minimum of 1 tree for every 80 sqm of land should be planted and maintained. The existing trees will be counted for this purpose. The landscape planning should include plantation of native species. The species with heavy foliage, broad leaves and wide canopy cover are desirable. Water intensive and/or invasive species should not be used for landscaping As proposed 2423.82	This condition will be complied. Landscape Plan attached for your reference as Annexure-XII .

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram
Haryana by M/s. Asthetic Township Developers Pvt. Ltd.**

S No	Conditions	Compliance
	sqm area shall be provided for green area development.	
Top Soil preservation and Reuse		
xlii.	Topsoil should be stripped to a depth of 20 c m from the areas proposed for buildings, roads, paved areas, and external services. It should be stockpiled appropriately in designated areas and reapplied during plantation of the proposed vegetation on site.	Excavated top soil is preserved for use during Landscape development activities. Photograph of the same is attached as Annexure-XIII .
Transport		
xliii.	As proposed, adequate provision will be made for car/vehicle parking at the proposed project site. There shall also be adequate parking provisions for visitors so as not to disturb the traffic and allow smooth movement at the site.	This condition will be complied. Approved parking plan will be submitted in due course of time.
xliv.	A comprehensive mobility plan, as per MoUD best practices guidelines (URDPFI), shall be prepared to include motorized, non-motorized, public, and private networks. Road should be designed with due consideration for environment, and safety of users. The road system can be designed with these basic criteria. • Hierarchy of roads with proper segregation of vehicular and pedestrian traffic. • Traffic calming measures • Proper design of entry and exit points. • Parking norms as per local regulation	This condition will be complied.
xlvi.	A detailed traffic management and traffic decongestion plan shall be drawn up to ensure that the current level of service of the roads within a 05 km s radius of the project is maintained and improved upon after the implementation of the project. This plan should be based on cumulative impact of all development and increased	This condition will be complied and the same will be submitted in due course of time.

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram
Haryana by M/s. Asthetic Township Developers Pvt. Ltd.**

S No	Conditions	Compliance
	habitation being carried out or proposed to be carried out by the project or other agencies in this 05 Kms radius of the site in different scenarios of space and time and the traffic management plan shall be duly validated and certified by the State Urban Development department and the P.W.D./ competent authority for road augmentation and shall also have their consent to the implementation of components of the plan which involve the participation of these departments.	
xlvi.	Vehicles hired for bringing construction material to the site should be in good condition and should have a pollution check certificate and should conform to applicable air and noise emission standards be operated only during non-peak hours.	We are ensuring that all vehicles which are coming to the site are in good condition & monitoring record of PUC certificate of Vehicle is enclosed as Annexure-XIV .
Environment management Plan		
xlvii.	An environmental management plan (EMP) as prepared and submitted shall be implemented to ensure compliance with the environmental conditions specified above. A dedicated Environment Monitoring Cell with defined functions and responsibility shall be put in place to implement the EMP. The environmental cell shall ensure that the environment infrastructure like Sewage Treatment Plant, Landscaping, Rain Water Harvesting, Energy efficiency and conservation, water efficiency and conservation, solid waste management, renewable energy etc. are kept operational and meet the required standards. The environmental cell shall also keep the record of environment monitoring and those related to the	Environment Management and Monitoring Plan is submitted for EC. Copy the same is attached as Annexure-XIV for your reference.

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram
Haryana by M/s. Asthetic Township Developers Pvt. Ltd.**

S No	Conditions	Compliance
	environment infrastructure.	
Others		
xlvi.	Provisions shall be made for the housing of construction labour within the site with all necessary infrastructure and facilities such as fuel for cooking, mobile toilets, mobile STP, safe drinking water, medical health care, creche etc. The housing may be in the form of temporary structures to be removed after the completion of the project.	This condition will be complied . Photographs of Basic infrastructure provided at project sit are attached as Annexure XIX .
xlix.	A First Aid Room shall be provided in the project both during construction and operations of the project.	Photographs showing first Aid room at the project is attached as Annexure XIX .
i.	The company shall draw up and implement corporate social Responsibility plan as per the Company's Act of 2013.	This condition will be complied as per the amended requirements.
li.	As per the Ministry's Office Memorandum F. No. 22-6512017-1A.III dated 1 st May 2018, and proposed by the project proponent, an amount of Rs. 2.4 Crore @1.5% of project Cost shall be earmarked under Corporate Environment Responsibility (CER) for the activities such as drinking water supply, health and education. The activities proposed under CER shall be restricted to the affected area around the project. The entire activities proposed under the CER shall be treated as project and shall be monitored. The monitoring report shall be submitted to the regional office as a part of half yearly compliance report, and to the District Collector. It should be posted on the website of the project proponent	This condition will be complied.
PART B – GENERAL CONDITIONS		
i.	A copy of the environmental clearance letter shall also be displayed on the website of the concerned State Pollution Control	This condition will be complied.

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram
Haryana by M/s. Asthetic Township Developers Pvt. Ltd.**

S No	Conditions	Compliance
	Board. The EC letter shall also be displayed at the Regional Office. District industries Centre and Collector's Office/ Tehsildars office for 30 days.	
ii.	The funds earmarked for environmental protection measures shall be kept in separate account and shall not be diverted for other purpose. Year-wise expenditure shall be reported to this Ministry and its concerned Regional Office.	This condition will be complied.
iii.	Officials from the concerned Regional Office of MoEF&CC who would be monitoring the implementation of environmental safeguards should be given full cooperation, facilities and documents/data by the project proponents during their inspection. A complete set of all the documents submitted to MoEF&CC shall be forwarded to the concerned APCCF, Regional Office of MoEF&CC.	This condition will be complied. A complete set of all the documents we have submitted for Environmental Clearance will be submitted to APCCF, Regional Office of MoEF&CC in due course of time.
iv.	In the case of any change(s) in the scope of the project, the project would require a fresh appraisal by this Ministry.	Noted the Condition.
v.	The Ministry reserves the right to add additional safeguard measures subsequently if found necessary and to take action including revoking of the environment clearance under the provisions of the Environmental (Protection) Act, 1986 to ensure effective implementation of the suggested safeguard measures in a time bound and satisfactory manner.	If any additional condition will be imposed on project we will comply with all the conditions.
vi.	All other statutory clearances such as the approvals for storage of diesel from Chief Controller of Explosives, Fire Department, Civil Aviation Department, the Forest Conservation Act, 1980 and the Wildlife (Protection) Act, 1972 etc.	We are in process for getting all statutory clearance from concerned department, which will be obtained and submitted in due course of time. Currently, we obtained AAI NOC which is attached as Annexure XX .

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram
Haryana by M/s. Asthetic Township Developers Pvt. Ltd.**

S No	Conditions	Compliance
	shall be obtained, as applicable by project proponents from the respective competent authorities.	
vii.	These stipulations would be enforced among others under the provisions of the Water (Prevention and Control of Pollution) Act, 1974, the Air (Prevention and Control of Pollution) Act 1981, the Environment (Protection) Act, 1986, the Public Liability (Insurance) Act, 1991 and the EIA Notification, 2006.	Noted the condition.
viii.	The project proponent shall advertise in at least two local Newspapers widely circulated in the region, one of which shall be in the vernacular language informing that the project has been accorded Environmental Clearance and copies of clearance letters are available with the State Pollution Control Board and may also be seen on the website of the Ministry of Environment, Forest and Climate Change at http://www.envfor.nic.in . The advertisement shall be made within Seven days from the date of receipt of the Clearance letter and a copy of the same shall be forwarded to the concerned Regional Office of this Ministry.	Copies of the newspaper advertisement will be provided in due course of time.
ix.	Any appeal against this clearance shall lie with the National Green Tribunal, if preferred, within a period of 30 days as prescribed under Section 16 of the National Green Tribunal Act, 2010.	Noted the condition.
x.	A copy of the clearance letter shall be sent by the proponent to concerned Panchayat, Zilla Parisad/Municipal Corporation, Urban Local Body and the Local NGO, if any, from whom suggestions/ representations, if any,	This condition will be complied.

**Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram
Haryana by M/s. Asthetic Township Developers Pvt. Ltd.**

S No	Conditions	Compliance
	were received while processing the proposal. The clearance letter shall also be put on the website of the company by the proponent.	
xi.	The proponent shall upload the status of compliance of the stipulated EC conditions, including results of monitored data on their website and shall update the same periodically. It shall simultaneously be sent to the Regional Office of MoEF&CC, the respective Zonal Office of CPCB and the SPCB. The criteria pollutant levels namely; PM _{2.5} , PM ₁₀ , SO ₂ NO _x (ambient levels as well as stack emissions) or critical sectoral parameters indicated for the project shall be monitored and displayed at a convenient location near the main gate of the company in the public domain.	We will regularly upload the status of compliance of all the stipulated EC conditions. We will also submit Environmental Monitored data and shall update the same periodically. We will regularly submit compliance reports to the Regional Office of MoEF&CC, the respective Zonal Office of CPCB and the SPCB, which is due for submission on 1st June and 1st December of every year. We have monitored all the criteria pollutant levels namely; PM_{2.5}, PM₁₀, SO₂ NO_x (ambient levels as well as stack emissions). All Monitoring report is attached as Annexure-X.
xii.	The environmental statement for each financial year ending 31 st March in Form-V as is mandated to be submitted by the project proponent to the concerned State Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall also be put on the website of the company along with the status of compliance of EC conditions and shall also be sent to the respective Regional Offices of MoEF&CC by email.	This condition will be complied during Operation phase of the project.

Annexure-I
Environmental Clearance Letter

F.No.21-137/2018-IA-III
Government of India
Ministry of Environment, Forest and Climate Change
(IA.III Section)

Indira Paryavaran Bhawan,
Jor Bagh Road, New Delhi - 3

Date: 7th February, 2019

To,

**Shri Vijay Kumar Yadav, Managing Director,
M/s Asthetic Township Developers Pvt. Ltd.,**
Apt. no. E - 301, Uniworld City,
Sector 30, Gurgaon - 122002.

Phone: 9811929655

E-mail: atwnship@gmail.com

Subject: Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana by M/s Asthetic Township Developers Pvt. Ltd. - Environmental Clearance - reg.

Sir,

This has reference to your online proposal No. IA/HR/MIS/84906/2018 dated 15th November, 2018 submitted to this Ministry for grant of Environmental Clearance (EC) in terms of the provisions of the Environment Impact Assessment (EIA) Notification, 2006 under the Environment (Protection) Act, 1986.

2. The proposal for grant of environmental clearance to the project 'Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana by M/s Asthetic Township Developers Pvt. Ltd.', was considered by the EAC in its 36th meeting held on 26-28 November, 2018. The details of the project, as per the documents submitted by the project proponent, and also as informed during the above meeting are as under:-

- (i) The project is located at Sushant Lok, Sector-27, District Gurugram, Haryana. Latitude: 28°27.996" N and Longitude: 77°4.495" E.
- (ii) This is an Expansion project. The total plot area is 11,537.57 sqm, FSI area is 42,088.21 sqm and total construction (built-up) area of 71,057.12 sqm. Maximum height of the building is 95.95 m.
- (iii) The project was earlier granted Environment Clearance by SEIAA, Haryana vide letter no. SEIAA/HR/2013/1507 dated 24th December, 2013 for plot area 11,537.57 sqm and Built-up area 41,841.21 sqm
- (iv) The total water requirement for the construction of Expansion of Commercial Complex Project is estimated to be approx. 355 KLD. The water supply during Construction phase will be met through HUDA. During the construction phase, soak pits and septic tanks are provided for disposal of waste water. Temporary toilets will be provided for labourers.

- (v) During operational phase, total water demand of the project is estimated to be 337 KLD and the same will be met by 42 KLD fresh water from HUDA and 295 KLD treated water. Wastewater generated (131 KLD) will be treated in STP of total 160 KLD capacity. About 118 KLD of treated wastewater will be generated from which 97 KLD will be used for flushing, 3 KLD for gardening and remaining 18 KLD for DG cooling. Additional 177 KLD treated water will be sourced from HUDA supply for use for DG cooling (12 KLD) and HVAC cooling (165 KLD).
- (vi) About 1226 kg/day solid waste will be generated from the project. The biodegradable waste (490.4 kg/day) will be processed in OWC, Inert wastes (122.6 kg/day) will be sent to land fill and the non-biodegradable waste generated (613 kg/day) will be handed over to vendors.
- (vii) The total power requirement during operation phase is 4004 KW and will be met from Dakshin Haryana Bijli Vitran Nigam (DHBVN).
- (viii) Parking facility for 677 No. of four wheelers are proposed to be provided against the requirement of 672 No. (according to local norms).
- (ix) Proposed energy saving measures: Energy will be saved using energy efficient lighting fixtures, Electronic Ballast, Timer based lighting and APFC Panel.
- (x) It is not located within 10 km of any Eco Sensitive areas.
- (xi) Estimated Cost of the project is Rs. 160.3 Crores.
- (xii) Employment potential: It will generate direct and indirect employment opportunities for both skilled and unskilled labor during construction & operation phase.
- (xiii) Benefits of the project: Direct & Indirect employment opportunities and Infrastructural Development of the Area.

3. The project/activity is covered under category 'B' of item 8(a) 'Building and Construction projects' of the Schedule to the EIA Notification, 2006 and its subsequent amendments, and requires appraisal at State level. However due to absence of SEIAA/SEAC in Haryana, the proposal is appraised at Central Level.

4. Based on the information submitted by the Project Proponent and detailed discussions held on all the issues, the EAC recommended the project for grant of environmental clearance and stipulated specific conditions along with other environmental conditions. As per recommendations of the EAC, the Ministry of Environment, Forest and Climate Change hereby accords Environmental Clearance to the project Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana by M/s Asthetic Township Developers Pvt. Ltd., under the provisions of the EIA Notification, 2006 and amendments/circulars issued thereon, and subject to the specific and general conditions as under:-

PART A - SPECIFIC CONDITIONS:

- (i) The project proponent shall obtain all necessary clearance/ permission from all relevant agencies including town planning authority before commencement of work. All the construction shall be done in accordance with the local building byelaws.
- (ii) Consent to Establish/Operate for the project shall be obtained from the State Pollution Control Board as required under the Air (Prevention and Control of Pollution) Act, 1981 and the Water (Prevention and Control of Pollution) Act, 1974.
- (iii) The approval of the Competent Authority shall be obtained for structural safety of buildings due to earthquakes, adequacy of firefighting equipment etc as per National Building Code including protection measures from lightening etc.

Topography and natural Drainage

- (iv) The natural drain system should be maintained for ensuring unrestricted flow of water. No construction shall be allowed to obstruct the natural drainage through the site, on wetland and water bodies. Check dams, bio-swales, landscape, and other sustainable urban drainage systems (SUDS) are allowed for maintaining the drainage pattern and to harvest rain water. Buildings shall be designed to follow the natural topography as much as possible. Minimum cutting and filling should be done.

Water requirement, Conservation, rain water Harvesting, and Ground Water Recharge

- (v) Fresh water requirement from HUDA supply shall not exceed 42 KLD with prior permission.
- (vi) A certificate shall be obtained from the local body supplying water, specifying the total annual water availability with the local authority, the quantity of water already committed the quantity of water allotted to the project under consideration and the balance water available. This should be specified separately for ground water and surface water sources, ensuring that there is no impact on other users.
- (vii) The quantity of fresh water usage, water recycling and rainwater harvesting shall be measured and recorded to monitor the water balance as projected by the project proponent. The record shall be submitted to the Regional Office, MoEF&CC along with six monthly Monitoring reports.
- (viii) At least 20% of the open spaces as required by the local building bye-laws shall be pervious. Use of Grass pavers, paver blocks with at least 50% opening, landscape etc. would be considered as pervious surface.
- (ix) Installation of dual pipe plumbing for supplying fresh water for drinking, cooking and bathing etc and other for supply of recycled water for flushing,

landscape irrigation, car washing, thermal cooling, conditioning etc. shall be done.

- (x) Use of water saving devices/ fixtures (viz. low flow flushing systems; use of low flow faucets tap aerators etc) for water conservation shall be incorporated in the building plan.
- (xi) Separation of grey and black water should be done by the use of dual plumbing system. In case of single stack system separate recirculation lines for flushing by giving dual plumbing system be done.
- (xii) Water demand during construction should be reduced by use of pre-mixed concrete, curing agents and other best practices referred.
- (xiii) The local bye-law provisions on rain water harvesting should be followed. If local bye-law provision is not available, adequate provision for storage and recharge should be followed as per the Ministry of Urban Development Model Building Byelaws, 2016. As proposed 03 nos. of rain water harvesting recharge pits shall be provided for rain water harvesting after filtration as per CGWB guidelines.
- (xiv) No ground water shall be used during construction/ operation phase of the project.
- (xv) Any ground water dewatering should be properly managed and shall conform to the approvals and the guidelines of the CGWA in the matter. Formal approval shall be taken from the CGWA for any ground water abstraction or dewatering.

Solid Waste Management

- (xvi) The provisions of the Solid Waste (Management) Rules, 2016, e-Waste (Management) Rules, 2016, and the Plastics Waste (Management) Rules, 2016 shall be followed.
- (xvii) Disposal of muck during construction phase shall not create any adverse effect on the neighboring communities and be disposed taking the necessary precautions for general safety and health aspects of people, only in approved sites with the approval of competent authority.
- (xviii) Separate wet and dry bins must be provided in each unit and at the ground level for facilitating segregation of waste. Solid waste shall be segregated into wet garbage and inert materials. Wet garbage shall be composted in Organic Waste Converter. As proposed, 80 sqm area shall be provided for solid waste management within the premises which will include area for segregation, composting. The inert waste from project will be sent to dumping site.
- (xix) Any hazardous waste generated during construction phase, shall be disposed off as per applicable rules and norms with necessary approvals of the State Pollution Control Board.

- (xx) A certificate from the competent authority handling municipal solid wastes, indicating the existing civic capacities of handling and their adequacy to cater to the M.S.W. generated from project shall be obtained.

Sewage Treatment Plant

- (xxi) Sewage shall be treated in the STP based on SBR technology with tertiary treatment i.e. Ultra Filtration. The treated effluent from STP shall be recycled/re-used for flushing and horticulture. Excess water shall be discharged to Municipal Sewer with prior permission.
- (xxii) A certificate from the competent authority for discharging treated effluent/ untreated effluents into the Public sewer/ disposal/drainage systems along with the final disposal point shall be obtained.
- (xxiii) No sewage or untreated effluent water would be discharged through storm water drains.
- (xxiv) The project proponents would devise a monitoring plan to the satisfaction of the State Pollution Control Board so as to continuously monitor the treated waste water being used for flushing in terms of faecal coliforms and other pathogenic bacteria.
- (xxv) The project proponents would commission a third party study on the implementation of conditions related to quality and quantity of recycle and reuse of treated water, efficiency of treatment systems, quality of treated water being supplied for flushing (specially the bacterial counts), comparative bacteriological studies from toilet seats using recycled treated waters and fresh waters for flushing, and quality of water being supplied through spray faucets attached to toilet seats.
- (xxvi) The installation of the Sewage Treatment Plant (STP) shall be certified by an independent expert and a report in this regard shall be submitted to the Ministry before the project is commissioned for operation. Periodical monitoring of water quality of treated sewage shall be conducted. Necessary measures should be made to mitigate the odour problem from STP.
- (xxvii) Sludge from the onsite sewage treatment, including septic tanks, shall be collected, conveyed and disposed as per the Ministry of Urban Development, Central Public Health and Environmental Engineering Organization (CPHEEO) Manual on Sewerage and Sewage Treatment Systems, 2013.

Energy

- (xxviii) Compliance with the Energy Conservation Building Code (ECBC) of Bureau of Energy Efficiency shall be ensured. Buildings in the States which have notified their own ECBC, shall comply with the State ECBC. Outdoor and common area lighting shall be LED. Concept of passive solar design that minimize energy consumption in buildings by using design elements, such as building orientation, landscaping, efficient building envelope, appropriate fenestration,

increased day lighting design and thermal mass etc. shall be incorporated in the building design. Wall, window, and roof u-values shall be as per ECBC specifications.

- (xxix) Energy conservation measures like installation of CFLs/ LED for the lighting the area outside the building should be integral part of the project design and should be in place before project commissioning. Used CFLs, TFL and LED shall be properly collected and disposed off/sent for recycling as per the prevailing guidelines/rules of the regulatory authority to avoid mercury contamination.
- (xxx) Solar, wind or other Renewable Energy shall be installed to meet electricity generation equivalent to 1% of the demand load or as per the state level/ local building bye-laws requirement, whichever is higher. Follow super ECBC requirement of ECBC 2017 and provide compliance report.
- (xxxi) Solar power shall be used for lighting in the apartment to reduce the power load on grid. Separate electric meter shall be installed for solar power. Solar water heating shall be provided to meet 20% of the hot water demand of the commercial and institutional building or as per the requirement of the local building bye-laws, whichever is higher. Residential buildings are also recommended to meet its hot water demand from solar water heaters, as far as possible.
- (xxxii) Use of environment friendly materials in bricks, blocks and other construction materials, shall be required for at least 20% of the construction material quantity. These include Fly Ash bricks, hollow bricks, AACs, Fly Ash Lime Gypsum blocks, Compressed earth blocks, and other environment friendly materials. Fly ash should be used as building material in the construction as per the provision of Fly Ash Notification of September, 1999 and amended as on 27th August, 2003 and 25th January, 2016. Ready mixed concrete must be used in building construction.
- (xxxiii) A certificate of adequacy of available power from the agency supplying power to the project along with the load allowed for the project shall be submitted.

Air Quality and Noise

- (xxxiv) Construction site shall be adequately barricaded before the construction begins. Dust, smoke & other air pollution prevention measures shall be provided for the building as well as the site. These measures shall include screens for the building under construction, continuous dust/ wind breaking walls all around the site (at least 3 meter height). Plastic/tarpaulin sheet covers shall be provided for vehicles bringing in sand, cement, murrum and other construction materials prone to causing dust pollution at the site as well as taking out debris from the site. Sand, murrum, loose soil, cement, stored on site shall be covered adequately so as to prevent dust pollution. Wet jet shall be provided for grinding and stone cutting. Unpaved surfaces and loose soil shall be adequately sprinkled with water to suppress dust.

- (xxxv) Notification GSR 94(E) dated 25.01.2018 of MoEF&CC regarding Mandatory Implementation of Dust Mitigation Measures for Construction and Demolition Activities for projects requiring Environmental Clearance shall be complied with.
- (xxxvi) All construction and demolition debris shall be stored at the site (and not dumped on the roads or open spaces outside) before they are properly disposed. All demolition and construction waste shall be managed as per the provisions of the Construction and Demolition Waste Rules, 2016. All workers working at the construction site and involved in loading, unloading, carriage of construction material and construction debris or working in any area with dust pollution shall be provided with dust mask.
- (xxxvii) The diesel generator sets to be used during construction phase shall be low sulphur diesel type and shall conform to Environmental (Protection) prescribed for air and noise emission standards.
- (xxxviii) The gaseous emissions from DG set shall be dispersed through adequate stack height as per CPCB standards. Acoustic enclosure shall be provided to the DG sets to mitigate the noise pollution. Low sulphur diesel shall be used. The location of the DG set and exhaust pipe height shall be as per the provisions of the Central Pollution Control Board (CPCB) norms.
- (xxxix) For indoor air quality the ventilation provisions as per National Building Code of India.
- (xl) Ambient noise levels shall conform to residential standard both during day and night as per Noise Pollution (Control and Regulation) Rules, 2000. Incremental pollution loads on the ambient air and noise quality shall be closely monitored during construction phase. Adequate measures shall be made to reduce ambient air and noise level during construction phase, so as to conform to the stipulated standards by CPCB / SPCB.

Green Cover

- (xli) No tree cutting/transplantation of existing trees has been proposed in the project. A minimum of 1 tree for every 80 sqm of land should be planted and maintained. The existing trees will be counted for this purpose. The landscape planning should include plantation of native species. The species with heavy foliage, broad leaves and wide canopy cover are desirable. Water intensive and/or invasive species should not be used for landscaping. As proposed 2423.82 sqm area shall be provided for green area development.

Top Soil preservation and Reuse

- (xlii) Topsoil should be stripped to a depth of 20 cm from the areas proposed for buildings, roads, paved areas, and external services. It should be stockpiled appropriately in designated areas and reapplied during plantation of the proposed vegetation on site.

Transport

- (xlili) As proposed, adequate provision will be made for car/vehicle parking at the proposed project site. There shall also be adequate parking provisions for visitors so as not to disturb the traffic and allow smooth movement at the site.
- (xliv) A comprehensive mobility plan, as per MoUD best practices guidelines (URDPFI), shall be prepared to include motorized, non-motorized, public, and private networks. Road should be designed with due consideration for environment, and safety of users. The road system can be designed with these basic criteria.
 - Hierarchy of roads with proper segregation of vehicular and pedestrian traffic.
 - Traffic calming measures
 - Proper design of entry and exit points.
 - Parking norms as per local regulation
- (xlv) A detailed traffic management and traffic decongestion plan shall be drawn up to ensure that the current level of service of the roads within a 05 kms radius of the project is maintained and improved upon after the implementation of the project. This plan should be based on cumulative impact of all development and increased habitation being carried out or proposed to be carried out by the project or other agencies in this 05 Kms radius of the site in different scenarios of space and time and the traffic management plan shall be duly validated and certified by the State Urban Development department and the P.W.D./ competent authority for road augmentation and shall also have their consent to the implementation of components of the plan which involve the participation of these departments.
- (xlvi) Vehicles hired for bringing construction material to the site should be in good condition and should have a pollution check certificate and should conform to applicable air and noise emission standards be operated only during non-peak hours.

Environment management Plan

- (xlvii) An environmental management plan (EMP) as prepared and submitted shall be implemented to ensure compliance with the environmental conditions specified above. A dedicated Environment Monitoring Cell with defined functions and responsibility shall be put in place to implement the EMP. The environmental cell shall ensure that the environment infrastructure like Sewage Treatment Plant, Landscaping, Rain Water Harvesting, Energy efficiency and conservation, water efficiency and conservation, solid waste management, renewable energy etc. are kept operational and meet the required standards. The environmental cell shall also keep the record of environment monitoring and those related to the environment infrastructure.

Others

- (xlviii) Provisions shall be made for the housing of construction labour within the site with all necessary infrastructure and facilities such as fuel for cooking, mobile toilets, mobile STP, safe drinking water, medical health care, creche etc. The housing may be in the form of temporary structures to be removed after the completion of the project.
- (xlix) A First Aid Room shall be provided in the project both during construction and operations of the project.
- (l) The company shall draw up and implement corporate social Responsibility plan as per the Company's Act of 2013.
- (li) As per the Ministry's Office Memorandum F.No. 22-65/2017-IA.III dated 1st May 2018, and proposed by the project proponent, an amount of Rs. 2.4 Crore @1.5% of project Cost shall be earmarked under Corporate Environment Responsibility (CER) for the activities such as Education facilities in nearby communities, solar power, rain water harvesting and plantation in community areas. The activities proposed under CER shall be restricted to the affected area around the project. The entire activities proposed under the CER shall be treated as project and shall be monitored. The monitoring report shall be submitted to the regional office as a part of half yearly compliance report, and to the District Collector. It should be posted on the website of the project proponent.

PART B - GENERAL CONDITIONS

- (i) A copy of the environmental clearance letter shall also be displayed on the website of the concerned State Pollution Control Board. The EC letter shall also be displayed at the Regional Office, District Industries centre and Collector's Office/ Tehsildar's office for 30 days.
- (ii) The funds earmarked for environmental protection measures shall be kept in separate account and shall not be diverted for other purpose. Year-wise expenditure shall be reported to this Ministry and its concerned Regional Office.
- (iii) Officials from the concerned Regional Office of MoEF&CC who would be monitoring the implementation of environmental safeguards should be given full cooperation, facilities and documents/data by the project proponents during their inspection. A complete set of all the documents submitted to MoEF&CC shall be forwarded to the concerned APCCF, Regional Office of MoEF&CC.
- (iv) In the case of any change(s) in the scope of the project, the project would require a fresh appraisal by this Ministry.
- (v) The Ministry reserves the right to add additional safeguard measures subsequently, if found necessary, and to take action including revoking of the

environment clearance under the provisions of the Environmental (Protection) Act, 1986, to ensure effective implementation of the suggested safeguard measures in a time bound and satisfactory manner.

- (vi) All other statutory clearances such as the approvals for storage of diesel from Chief Controller of Explosives, Fire Department, Civil Aviation Department, the Forest Conservation Act, 1980 and the Wildlife (Protection) Act, 1972 etc. shall be obtained, as applicable by project proponents from the respective competent authorities.
- (vii) These stipulations would be enforced among others under the provisions of the Water (Prevention and Control of Pollution) Act, 1974, the Air (Prevention and Control of Pollution) Act 1981, the Environment (Protection) Act, 1986, the Public Liability (Insurance) Act, 1991 and the EIA Notification, 2006.
- (viii) The project proponent shall advertise in at least two local Newspapers widely circulated in the region, one of which shall be in the vernacular language informing that the project has been accorded Environmental Clearance and copies of clearance letters are available with the State Pollution Control Board and may also be seen on the website of the Ministry of Environment, Forest and Climate Change at <http://www.envfor.nic.in>. The advertisement shall be made within Seven days from the date of receipt of the Clearance letter and a copy of the same shall be forwarded to the concerned Regional Office of this Ministry.
- (ix) Any appeal against this clearance shall lie with the National Green Tribunal, if preferred, within a period of 30 days as prescribed under Section 16 of the National Green Tribunal Act, 2010.
- (x) A copy of the clearance letter shall be sent by the proponent to concerned Panchayat, Zilla Parisad/Municipal Corporation, Urban Local Body and the Local NGO, if any, from whom suggestions/ representations, if any, were received while processing the proposal. The clearance letter shall also be put on the website of the company by the proponent.
- (xi) The proponent shall upload the status of compliance of the stipulated EC conditions, including results of monitored data on their website and shall update the same periodically. It shall simultaneously be sent to the Regional Office of MoEF&CC, the respective Zonal Office of CPCB and the SPCB. The criteria pollutant levels namely; PM_{2.5}, PM₁₀, SO₂, NO_x (ambient levels as well as stack emissions) or critical sectoral parameters, indicated for the project shall be monitored and displayed at a convenient location near the main gate of the company in the public domain.
- (xii) The environmental statement for each financial year ending 31st March in Form-V as is mandated to be submitted by the project proponent to the concerned State Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall also be put on the website of the company along with the status of compliance of EC conditions

and shall also be sent to the respective Regional Offices of MoEF&CC by e-mail.

5. This issues with the approval of the Competent Authority.


(Kushal Vashist)
Director

Copy to:

- 1) The Secretary, Directorate of Environment, Government of Haryana, SCO 1-2-3, Sector 17 D (Second Floor), Chandigarh.
- 2) Addl. Principal Chief Conservator of Forests (Central), Ministry of Environment, Forests and Climate Change, Regional Office (NZ), Bay No.24-25, Sector 31-A, Dakshin Marg, Chandigarh -160030.
- 3) The Chairman, Central Pollution Control Board Parivesh Bhavan, CBD-cum-Office Complex, East Arjun Nagar, New Delhi - 110 032.
- 4) Member Secretary, Haryana Pollution Control Board, C-11, Sector-6, Panchkula, Haryana 134109
- 5) Monitoring Cell, MoEF&CC, Indira Paryavaran Bhavan, New Delhi.
- 6) Guard File/ Record File/ Notice Board.


(Kushal Vashist)
Director

Annexure-II

HSPCB/Consent/:

329962320GUNOCTE7324277 dated

03/02/2020



HARYANA STATE POLLUTION CONTROL BOARD

Gurgaon North Vikas Sadan, 1st Floor, Near DC Court, Gurgaon Ph.0124-2332775 Email:- hspcbrogrn@gmail.com

Website: www.hrocmms.nic.in E-Mail - hspcbho@gmail.com

Telephone No.: 0172-2577870-73



No. HSPCB/Consent/ : 329962320GUNOCTE7324277

Dated:03/02/2020

To.

M/s : Asthetic Township Developers Pvt Ltd
Commercial Complex at Sector 27 Gurugram
GURGAON
122009

Sub. : Grant of consent to Establish to M/s Asthetic Township Developers Pvt Ltd

Please refer to your application no. 7324277 received on dated 2020-01-27 in regional office Gurgaon North.

With reference to your above application for consent to establish, M/s Asthetic Township Developers Pvt Ltd is hereby granted consent as per following specification/Terms and conditions.

Consent Under	AIR/WATER
Period of consent	03/02/2020 - 06/02/2026
Industry Type	Building and construction project having waste water generation more than 100 KLD
Category	RED
Investment(In Lakh)	30544.0
Total Land Area (Sq. meter)	11537.57
Total Builtup Area (Sq. meter)	71057.12
Quantity of effluent	
1. Trade	0.0 KL/Day
2. Domestic	131.0 KL/Day
Number of outlets	1.0
Mode of discharge	
1. Domestic	Reuse/Recycle
2. Trade	0
Permissible Domestic Effluent Parameters	
1. BOD	30 mg/l
2. COD	250 mg/l
3. TSS	100 mg/l

Permissible Trade Effluent Parameters	
1. NA	mg/l
Number of stacks	4
Height of stack	
1. DG Set (1500 KVA)	8 METER
2. DG Set (1500 KVA)	8 METER
3. DG Set (1500 KVA)	8 METER
4. DG Set (1000 KVA)	6 METER
Permissible Emission parameters	
1. NA	
Capacity of boiler	
1. NA	Ton/hr
Type of Furnace	
1. NA	
Type of Fuel	
1. Diesel	1.1 KL/day

Regional Officer, Gurgaon North

HARYANA STATE

Haryana State Pollution Control Board.

Terms and conditions

1. The industry has declared that the quantity of effluent shall be 131 KL/Day i.e 0KL/Day for Trade Effluent, 0 KL/Day for Cooling, 131 KL/Day for Domestic and the same should not exceed .
2. The above 'Consent to Establish' is valid for 60 months from the date of its issue to be extended for another one year at the discretion of the Board or till the time the unit starts its trial production whichever is earlier. The unit will have to set up the plant and obtain consent during this period.
3. The officer/official of the Board shall have the right to access and inspection of the industry in connection with the various processes and the treatment facilities being provided simultaneously with the construction of building/machinery. The effluent should conform the effluent standards as applicable
4. That necessary arrangement shall be made by the industry for the control of Air Pollution before commissioning the plant. The emitted pollutants will meet the emission and other standards as laid/will be prescribed by the Board from time to time.
5. The applicant will obtain consent under section 25/26 of the Water (Prevention & Control of Pollution) Act, 1974 and under section 21/22 of the Air (Prevention & Control of Pollution) Act, 1981 as amended to-date-even before starting trial production
6. The above Consent to Establish is further subject to the conditions that the unit complies with all the laws/rules/decisions and competent directions of the Board/Government and its functionaries in all respects before commissioning of the operation and during its actual working strictly.
7. No in-process or post-process objectionable emission or the effluent will be allowed, if the scheme furnished by the unit turns out to be defective in any actual experience
8. The Electricity Department will give only temporary connection and permanent connection to the unit will be given after verifying the consent granted by the Board, both under Water Act and Air Act.

9. Unit will raise the stack height of DG Set/Boiler as per Board's norms.
10. Unit will maintain proper logbook of Water meter/sub meter before/after commissioning.
11. That in the case of an industry or any other process the activity is located in an area approved and that in case the activity is sited in an residential or institutional or commercial or agricultural area, the necessary permission for siting such industry and process in an residential or institutional or commercial or agricultural area or controlled area under Town and Country Planning laws CLU or Municipal laws has to be obtained from the competent Authority in law permitting this deviation and be submitted in original with the request for consent to operate.
12. That there is no discharge directly or indirectly from the unit or the process into any interstate river or Yamuna River or River Ghaggar.
13. That the industry or the unit concerned is not sited within any prohibited distances according to the Environmental Laws and Rules, Notification, Orders and Policies of Central Pollution control Board and Haryana State Pollution Control Board.
14. That of the unit is discharging its sewage or trade effluent into the public sewer meant to receive trade effluent from industries etc. then the permission of the Competent Authority owing and operating such public sewer giving permission letter to his unit shall be submitted at time of consent to operate.
15. That if at any time, there is adverse report from any adjoining neighbor or any other aggrieved party or Municipal Committee or Zila Parishad or any other public body against the unit's pollution; the Consent to Establish so granted shall be revoked.
16. That all the financial dues required under the rules and policies of the Board have been deposited in full by the unit for this Consent to Establish.
17. In case of change of name from previous Consent to Establish granted, fresh Consent to Establish fee shall be levied.
18. Industry should adopt water conservation measures to ensure minimum consumption of water in their Process. Ground water based proposals of new industries should get clearance from Central Ground Water Authority for scientific development of previous resource.
19. That the unit will take all other clearances from concerned agencies, whenever required.
20. That the unit will not change its process without the prior permission of the Board.
21. That the Consent to Establish so granted will be invalid, if the unit falls in Aravali Area or non conforming area.
22. That the unit will comply with the Hazardous Waste Management Rules and will also make the non-leachate pit for storage of Hazardous waste and will undertake not to dispose off the same except for pit in their own premises or with the authorized disposal authority.
23. That the unit will submit an undertaking that it will comply with all the specific and general conditions as imposed in the above Consent to Establish within 30 days failing which Consent to Establish will be revoked.
24. That unit will obtain EIA from MoEF, if required at any stage.
25. In case of unit does not comply with the above conditions within the stipulated period, Consent to Establish will be revoked.
26. That unit will obtain consent to operate from the board before the start of product activity.

Specific Conditions

Other Conditions :

1. The project proponent will obtain all necessary clearances from all concerned departments. 2. Project proponent will not change the quantity of domestic effluent/trade effluent/air emission without prior permission of the Board. Project Proponent will obtain prior CTO before starting of production and apply for CTO/ CTE Extension at least 90 days before expiry date of this CTE. 3. Project Proponent will install STP/ETP/ACPM along with the main project. 4. Project Proponent will install adequate acoustic enclosures/chambers on their DG SETS with proper stack height as per prescribed norms to meet the prescribed standards under EP Rules. 5. Project Proponent will comply with the provisions of Water Act, 1974, Air Act, 1981, Solid Waste Management Rules, 2016, Hazardous & Other Waste Management Rules, 2016, Plastic Waste Management Rules, 2016, E-Waste Management Rules, 2016, Battery Managements Rules, C&D Waste Management Rules, 2016& amendments and other applicable environmental legislation. 6. Project Proponent will use only treated effluent supplied from Sewage treatment plant during construction phase of the project 7. That this CTE will not provide any relaxation /benefit from any other Act/Rules/Regulations applicable to the project/land in question. 8. Project Proponent will not discharge any type Treated or untreated effluent outside the premises of the project. 9. Project Proponent will not use in their DG set as a fuel i.e. pet coke, furnace oil and LSHS etc. 10. Stack emission level should be stringent than the existing standards in terms of the identified critical pollutants. 11. Effective fugitive emission control measures should be imposed in the process, transportation, parking etc. 12. Encourage use of cleaner fuels (pet coke / furnace oil /LSHS may be avoided). 13. Best available technology may be used. For example usage of EAF/SAF/IF in place of Cupola Furnace, Usage of Supercritical technology in place of sub – critical technology. 14. Increase of green belt cover by 40% of the total land area beyond the permissible requirement of 33%, wherever feasible. 15. Stipulation of greenbelt outside the project premises such as avenue plantation, plantation in vacant areas, social forestry etc. 16. Assessment of carrying capacity of transportation load on the roads inside the industrial premises. If the roads required to be widened, shall be prescribed as a condition. 17. Project Proponent will not discharge any type of effluent inside & outside of the premises of the project and reuse/recycle of treated waste water be ensured. 18. Continuous monitoring of emission and effluent quality / quantity to be installed & will connect the same with server of CPCB and HSPCB. 19. A detailed water harvesting plan may be submitted by the project proponent. 20. Project Proponent will achieve zero discharge and install latest technology of STP/ETP and reuse/recycle of treated effluent. 21. In case, domestic waste water generation is more than 10 KLD, the industry may install STP. 22. Dumping of waste (fly ash, slag, red mud etc.) may be permitted only at designated locations approved by SPCBs/PCCs. 23. More stringent norms for management of hazardous waste. The waste generated should be preferably utilized in co-processing. 24. Monitoring of compliance of EC conditions may be submitted with third party audit every year. 25. Project Proponent will dispose off their waste/spent oil of DG sets only to authorize recyclers by the HSPCB. 26. The % of the CER may be least 1.5 times the slabs given in the OM dated 01.05.2018 for SPA and 2 times for CPA in case of Environmental Clearance. 27. Project proponent will comply all the directions of CPCB in this regard and will comply all the orders issued by any court in this regard. 28. Project Proponent will submit an affidavit regarding compliances of above said conditions within 30 days. 29. The above Consent to Establish is further subject to the conditions that the unit complies with all the laws/rules/decisions and competent directions of the Board/Government and its functionaries in all respects before commissioning of the operation and during its actual working strictly. 30. Unit will deploy anti –smog gun at site to comply with the above said directions & keep proper record of operation of the same and submit action taken report to this office within 03 days positively, failing which action shall be initiated as per applicable Acts/ Rules /Notifications. 31. CTE so granted is on the basis of detail submitted by the unit in online application, CTE granted will be without prejudice to any violation made by unit in past & will be deemed revoked & further action will be taken as per law if any violation is observed at any stage. 32. At any stage, if any violation observed of any above conditions at any time, this CTE stands cancelled /revoked & further action will be taken as per law if any violation is observed at any stage.

*Regional Officer, Gurgaon North
Haryana State Pollution Control Board.*

Annexure-III
Aravali NOC

प्रेषक

उपायुक्त, गुडगांव।

सेवा में

M/s Asthetic Township Developers Pvt. Ltd.

क्रमांक 3373 /एस0के02 दिनांक 17-10-13

विषय: Request for issuing Aravali Notification 1992 & PLPA 1900 from DFO and Tehsildar through Deputy Commissioner of M/s Asthetic Township Developers Pvt. Ltd. project at village Sukhrali, Sector-27, Gurgaon.

यादि

उपरोक्त विषय पर आपके प्रार्थना पत्र के सन्दर्भ में।

विषयाधीन मामले में इस कार्यालय द्वारा तहसीलदार गुडगांव व उप-वन संरक्षक गुडगांव से रिपोर्ट प्राप्त की गई जो निम्न प्रकार है :-

तहसीलदार गुडगांव :- तहसीलदार गुडगांव के कार्यालय के पत्र क्रमांक 2327/ओ0के0 दिनांक 07.10.2013 द्वारा इस कार्यालय में प्राप्त रिपोर्ट अनुसार नीजा सुखराली की अराजी किला नं० 59//6, 15, 8/1/1, 13/2, कित्ता 4 रकबा 14-16-3 सालम के मालिक मै० अस्थैटिक टाउनशिप डवलपर्स प्रा०लि० बरूवे इन्तकाल नं० 1438-1534 से मालिक है व किला नं० 59//7 रकबा 8-0 सालम के सुधीर पुत्र साहिबराम पुत्र शिवधन्व बरूवे इन्तकाल नं० 1437 से मालिक है। बिन्दुवार रिपोर्ट निम्नप्रकार है :-


1. उपरोक्त अराजी अरावली क्षेत्र से बाहर है।
2. 07.05.1992 के नोटिफिकेशन से पूर्व अराजी मूमी की किस्म कमी भी गैर मुमकिन पहाड़, गैर मु० राडा, गैर मु० बीहड़, बंजड़ बीहड़ व रून्ड नहीं रही है।
3. गिरदावरी 1992 से पूर्व किस्म चाही है जो ताहाल है।

उप-वन संरक्षक, गुडगांव के कार्यालय के पत्र क्रमांक 2259-20जी दिनांक 03.10.2013 द्वारा इस कार्यालय में प्राप्त रिपोर्ट अनुसार M/s Asthetic Township Developers Pvt. Ltd. vide letter No. Nil dated 14-08-2013 made a request in connection with land measuring 2.851 acres having Killa No 6, 7, 8/1/1, 13/2, 15/1 land located at village Sukhrali, District Gurgaon, Applicant made a proposal to use this land for Commercial Colony Purpose In Continuation of report submitted by RFO, Gurgaon vide letter no. 703-G dated 24-08-2013 it is made clear that:

- A As per record available above said land is not part of notified Reserved Forest, Protected Forest under Indian Forest Act, 1927 or any area closed under section 4 & 5 of Punjab Land Preservation Act 1900.
- B It is clarified that by the notification no. S.O.8/P.A2/1900/S.4/2013 dated 4th January 2013 all Revenue Estate of Gurgaon Tehsil is notified u/s 4 of PLPA 1900 and S.O. 81/PA.2/1900/S.3/12 dated 19th December 2012 u/s 3 of PLPA 1900. The area is however not recorded as forest in the Government record but felling of any tree is strictly prohibited without the permission of Divisional Forest Officer, Gurgaon.
- C If approach is required from Protected Forest by the user agency, the clearance/regularization under Forest Conservation Act, 1980 will be required without prior clearance from Forest Department, the user of Forest land for approach road is strictly prohibited M/s Asthetic Township Developers Pvt. Ltd. whose land is located at village Sukhrali, District Gurgaon must obtain clearance as applicable under Forest Conservation Act 1980.

- D As per records available with the forest Department Gurgaon, the area does not fall in areas where plantations were raised by the Forest Department under Aravalli project.
- E All other statutory clearance mandated under the Environment Protection Act, 1986 or any other Act/order shall be obtained as application by the project proponents from the concerned authorities.
- F The project proponents will not violate any judicial order/ Pronouncement issued by the Hon'ble Supreme Court/High Courts.
- G It is clarified that the Hon'ble supreme Court has issued various judgment dated 06.05.2002, 29.10.2002, 16.12.2002, 18.03.2004, etc. pertaining to Aravalli region in Haryana, which should be complied with.
- H It shall be the responsibility of user agency/applicant to get necessary clearances/permissions under various Acts and Rules applicable if any, from the respective authorities/Department..

रिपोर्ट सेवा में प्रेषित है।


कृते: उपायुक्त गुडगांव।

कमांक

/एस0के02 दिनांक

इसकी एक प्रति Director General, Town & Country Planning, Haryana, Chandigarh को सूचनार्थ एवं आवश्यक कार्यवाही हेतु प्रेषित है।


कृते: उपायुक्त गुडगांव।

Annexure-V

From: Dy. Conservator of Forests,
Gurgaon, Haryana.

To, **M/s Asthetic Township Developers Pvt. Ltd.**
262, DDA Office Complex,
Jhandewalan Extn., New Delhi-110055

No. 2259-20-9


Dated: 3/10/13

Sub.: Clarification regarding Applicability of forest laws on Non Forest land Applied by **M/s Asthetic Township Developers Pvt. Ltd.** land located at Village-Sukhrali, Sector-27, Sushant Lok District-Gurgaon.

Applicant **M/s Asthetic Township Developers Pvt. Ltd., 262, DDA Office Complex, Jhandewalan Extn., New Delhi-110055** vide letter no. Nil. dated 14.08.2013 made a request in connection with land measuring 2.851 Acres having Killa No. 6, 7, 8/1/1, 13/2, 16/1, land located at village Sukhrali, Sector-27, Sushant Lok District Gurgaon. Applicant made a proposal to use this land for **Commercial Colony Purpose**. In continuation of report submitted by RFO, Gurgaon vide Letter No. 703-G dated 24.08.2013 it is made clear that:

- a) As per records available above said land is not part of notified Reserved Forest, Protected Forest under Indian Forest Act, 1927 or any area closed under section 4 & 5 of Punjab Land Preservation Act, 1900.
- b) It is clarified that by the Notification No. S.O.8/P.A 2/1900/S.4/2013 dated 4th January, 2013, whole Revenue Estate of Gurgaon is notified u/s 4 of PLPA 1900 and S.O.81/PA.2/1900/S.3/2012 dated 19th December, 2012 u/s 3 of PLPA 1900. The area is however not recorded as forest in the Government record but felling of any tree is strictly prohibited without the permission of Divisional Forest Officer, Gurgaon.
- c) If approach is required from Protected Forest by the user agency, the clearance/regularization under Forest Conservation Act 1980 will be required. Without prior clearance from Forest Department, the use of Forest land for approach road is strictly prohibited. **M/s Asthetic Township Developers Pvt. Ltd.** whose land is located at village, Sukhrali, Sector-27, Sushant Lok District Gurgaon must obtain clearance as applicable under Forest Conservation Act 1980.
- d) As per the records available with the Forest Department, Gurgaon, the area does not fall in areas where plantations were raised by the Forest Department under Aravalli project.
- e) All the statutory clearances mandated under the Environment Protection Act, 1986, as per the notification of Ministry of Environment and Forests, Government of India, dated 07-05-1992 or any other Act/order shall be obtained as applicable by the project proponents from the concerned authorities.
- f) The projec proponent will not violate any Judicial Order/ direction issued by the Hon'ble Supreme Court/ High Courts.
- g) It is clarified that Hon'ble Supreme Court has issued various judgments dated 07.05.2002, 29.10.2002, 16.12.2002, 18.03.2004, 14.5.2004 etc. pertaining to Aravalli region in Haryana, which should be complied with, Since the proposed site falls within 5 Km. of Delhi boundary. The permission from the Mining Department, Haryana pollution Board, Deptt. of Town & Country Planning Haryana and other appropriate authorities must be obtained who is under obligation to follow the directions in the various Hon'ble Supreme Court Judgments while granting permission.
- h) It shall be the responsibility of user agency/applicant to get necessary clearances/permissions under various Acts and Rules applicable if any, from the respective authorities/Department.

Date:
Place: Gurgaon


Dy. Conservator of Forest,
Gurgaon.

Endst. No.

Dated:

A copy is forwarded to:-

- 1) Conservator of Forests, South Circle, Gurgaon for kind information.
- 2) D.G. T.C.P, Ayojana Bhawan, Sec-18, Madhya, Marg, Chandigarh for kind information
- 3) Dy.Commissioner, Gurgaon w.r.t. his letter no.3538 dated 17.07.2013 for kind information & necessary action.
- 4) Guard File.


Dy. Conservator of Forest,
Gurgaon.

प्रेषक

सेवा में,

उपायुक्त, गुडगांव।

तहसीलदार, गुडगांव

3413
25-7-13

तहसीलदार

गुडगांव
24/7/13

क्रमांक 3532/एम.बी

दिनांक 12-7-13

विषय:-

Request for issuing Aravali notification 1992 & PLPA from DFO and Tehsildar through Deputy Commissioner of M/s Asthetic Township Developers Pvt. Ltd. project at Village Sukhrabi Sec-27, Sushantlok, Gurgaon

उपरोक्त विषय पर अनुरोध है कि संलग्न प्रार्थना पत्र में प्रस्तावित भूमि का Report (not covered under Aravali Notification area) जारी की जानी है। अतः आपको मूल कार्यालय की प्रति संलग्न करके लिखा जाता है कि आप विस्तारपूर्वक रिपोर्ट/टिप्पणी सहित तैयार करके एक सप्ताह के अन्दर-अन्दर इस कार्यालय में निम्न बिन्दुओं पर भिजवाना सुनिश्चित करें ताकि आगामी कार्यवाही की जा सके।

1. प्रार्थना पत्र में वर्णित खसरा नं० अरावली क्षेत्र में है अथवा नहीं।
2. 1992 के नोटिफिकेशन से पूर्व व उसके पश्चात की गिरदावरी तथा किसम जमीन भी स्पष्ट रिपोर्ट करने का कष्ट करें।
3. वर्णित प्रार्थना पत्र में दर्शाया गए खसरा नं० शामिल/ग्राम पंचायत/नगरपालिका/नगर निगम की भूमि/मलकियत तो नहीं है।
4. आराजी भूमि की ता हाल मलकियत बारे।
5. आराजी भूमि बारे किसी इंतकाल की नजरसानी रिपोर्ट तो नहीं की गई है या इंतकाल मुतनाजा तो नहीं।
6. आराजी भूमि का किसी माननीय न्यायालय में केस तो नहीं चल रहा है।
7. आराजी भूमि पर किसी प्रकार का कोई भार तो है अथवा नहीं।

क्र. 1732 / जी. को. दिनांक 25-7-13.
एक प्रति/मूलरूप में गिरदावर इत्का गुडगांव को
आवश्यक कार्यवाही एवं रिपोर्ट/टिप्पणी हेतु प्रेषित है।

तहसीलदार
गुडगांव

कृते: उपायुक्त, गुडगांव।

क्रमांक 371 R.R. dt 30/13

पहिली उक्ता सुडनाली विमलापुसाद

विमल री

सीमाजी री विमलापुसाद काम करत आहे.


TV 113

अधिकारी रिपोर्ट की जाती है मैजिस्ट्रेट अस्थायीक दायन गीप
 डायनर्स प्रा. 10.10.10 राजी अग्रेसर एव 19/1 बसत धीहर नदी डिल्ली
 नम्बर 1438-1534 मन्थूर मुद्रा दुस्तीक / सीमा 8-2-7
 59/16 (7-12) 15/1 (5-11-1/2) 8/1 (6-6-4) 13/2 (1-6-3) किता 4
 रकबा 14-16-3 सालक की सालिक व कोविज है व सुन्दर पुत्र
 साहेबराय पुत्र शिवचन्द ई. 1437 मन्थूर मुद्रा दुस्तीक / सीमा 8-2-7
 59/17 (8-0) सालक की सालिक व कोविज है मौजा सुन्दराली
 तह. वा जीमा मुद्राबा उपरोक्त आराजी की अरावली क्षेत्र
 बाहर है उपरोक्त सारा नम्बरक सामन्त है / ग्राम पंचायत व
 नगरपालिका व नगरनिगम प्रशासित नहीं है उपरोक्त आराजी
 की पर कोई इतना नजरानी व सुतगजा नहीं है
 उपरोक्त आराजी की अनुसार रिकार्ड माल किसी न्यायालय
 के कोई केश नहीं चल रहा है उपरोक्त आराजी की अनुसार
 रिकार्ड माल के अनुसार कोई कार व लोड - भाउरक नहीं है
 रिपोर्ट अग्रिम कार्यवाही हेतु सेवा के पेश है

7/10/13

अनुमति 2327 / ok. दिनांक 7-10-13

12/10/13 जीमा 6-2-11 मुद्राबा उपरोक्त है अनुसार 12/10/13
 मन्थूर मौजा सुन्दराली व सीमा 8-2-7 59
 किता मुद्राबा 14-16-3 सालक व सीमा 8-2-7 59
 टाउन 12/10/13 सालक प्रा. 10.10.10 बसत धीहर नदी डिल्ली
 नम्बर 1438-1534 मन्थूर मुद्रा दुस्तीक / सीमा 8-2-7
 59/16 (7-12) 15/1 (5-11-1/2) 8/1 (6-6-4) 13/2 (1-6-3) किता 4
 रकबा 14-16-3 सालक की सालिक व कोविज है व सुन्दर पुत्र
 साहेबराय पुत्र शिवचन्द ई. 1437 मन्थूर मुद्रा दुस्तीक / सीमा 8-2-7
 59/17 (8-0) सालक की सालिक व कोविज है मौजा सुन्दराली
 तह. वा जीमा मुद्राबा उपरोक्त आराजी की अरावली क्षेत्र
 बाहर है उपरोक्त सारा नम्बरक सामन्त है / ग्राम पंचायत व
 नगरपालिका व नगरनिगम प्रशासित नहीं है उपरोक्त आराजी
 की पर कोई इतना नजरानी व सुतगजा नहीं है
 उपरोक्त आराजी की अनुसार रिकार्ड माल किसी न्यायालय
 के कोई केश नहीं चल रहा है उपरोक्त आराजी की अनुसार
 रिकार्ड माल के अनुसार कोई कार व लोड - भाउरक नहीं है
 रिपोर्ट अग्रिम कार्यवाही हेतु सेवा के पेश है

बाकि निशान की गमालाया गयी है
उपरोक्त अंशों को दो बार दोहराया जा रहा है
पुलिस को भी उपरोक्त अंशों को दो
बार दोहराया है और दो बार दोहराया गया है
उपरोक्त अंशों को दो बार दोहराया गया है
एक / दो / अर्ध दोहराया गया है। अर्ध दोहराया
गया है। उपरोक्त अंशों को दो बार दोहराया गया है।

लड़की लखार

लड़की

Annexure-IV

Renewal of Licence from Directorate of Town & Country Planning, Haryana

Directorate of Town & Country Planning, Haryana

Plot no. 3, Nagar Yojana Bhawan, Sector-18A, Madhya Marg, Chandigarh
Phone: 0172-2549349, e-mail:tcpharyana7@gmail.com
website:-http://tcpharyana.gov.in

Regd. To

Asthetic Township Developers Pvt. Ltd.
APT No. E-602, Uniworld City,
Sector 30, Gurugram.

Memo No. LC-2400-Asstt(RK)/2019/

31572

Dated: 20-12-2019

Subject: Renewal of licence No. 97 of 2011 dated 09.11.2011.

Please refer to your application dated 04.10.2019 on the matter cited as subject above.

2. Licence No. 97 of 2011 dated 09.11.2011 granted for setting up of commercial colony on the land measuring 2.851 acres in Sector 27, Gurugram Manesar Urban Complex is hereby renewed upto 08.11.2024 on the same terms & conditions laid down therein.
3. This renewal will not tantamount to certification of satisfactory performance of the applicant entitling him for further renewal of license.
4. The BG on account of IDW shall be got revalidated well before its expiry.
5. Service plan estimates of the colony shall be submitted for approval in the office of competent authority after approval of revised building plans.
6. That the licensee company shall submit the ultimate power load requirement within current validity period of license.
7. That the amendment in Rule 13 in respect of charging of renewal fees is under consideration, for which the draft notification was notified on 20.08.2019. Therefore, increased renewal fees shall be deposited by you in accordance with the final notification or as decided by the Department.



(K. Makrand Pandurang, IAS)
Director,
Town & Country Planning
Haryana, Chandigarh

Endst. No. LC-2400-Asstt(RK)/2019/

Dated:

A copy is forwarded to the following for information and necessary action:-

- i. Chief Administrator, HSVP, Panchkula.
- ii. Senior Town Planner, Gurugram.
- iii. Website Administrator with a request to update the status of renewal of license on the website of the Department.
- iv. District Town Planner, Gurugram.
- v. Chief Account Officer of this Directorate.


(Narender Kumar)
Distt. Town Planner (HQ)
For Director, Town & Country Planning
Haryana, Chandigarh

ORDERS

Whereas, License No. 97 of 2011 dated 09.11.2011 stands granted to Asthetic Township Developers Pvt. Ltd., APT No. E-602, Uniworld City, Sector 30, Gurugram for setting up of commercial colony over an area measuring 2.851 acres in Sector 27, Gurugram Manesar Urban Complex under the provisions of Haryana Development and Regulation of Urban Areas Act, 1975. As per terms and conditions of the licenses and of the agreement executed on LC-IV, the colonizer is required to comply with the provisions of the Haryana Development and Regulation of Urban Areas Act, 1975 and its Rules, 1976.

And, whereas, for delay in compliance of the provisions of Rule 24, 26(2), 27 & 28 of the Haryana Development and Regulation of Urban Areas Rules, 1976 upto 31.03.2019, the licensee has submitted a request for composition of said offence. As per the rates finalized by the Govt. the composition fee has worked out as Rs. 2,24,000/-. The company has deposited composition charges amounting Rs. 2,24,000/- through e-payment TCP3172519112750204 dated 27.11.2019.

Accordingly, in exercise of power conferred under Section-13(1) of the Haryana Development and Regulation of Urban Areas Act, 1975, I hereby order to compound the offence committed due to delay in compliance of above said Rules upto 31.03.2019.



(K. Makrand Pandurang, IAS)
Director,
Town and Country Planning,
Haryana, Chandigarh

Endst. No. LC-2400-Asstt(RK)/2019/ 31579

Dated: 20-12-2019

A copy is forwarded to the following for information and necessary action:-

1. Chief Accounts Officer, O/o Director, Town and Country Planning Haryana Chandigarh.
2. Asthetic Township Developers Pvt. Ltd., APT No. E-602, Uniworld City, Sector 30, Gurugram.


(Narender Kumar)
Distt. Town Planner (HQ)
For Director, Town and Country Planning,
Haryana, Chandigarh

Annexure-V
Intekaal Letter

रजिस्ट्रार

[illegible]

ये नरेश मे भवितुं कि अस्मिन् मे अमायन्ता के साथ हो सका।

Annexure-VI

Water Balance

Table 5: Calculations for Daily Water Demand

S. No.	Unit Type	Occupancy	Rate of demand (lpcd)	Total water requirement (KLD)
A	Domestic Water			
1	Ground Floor (Retail Shop)			
	• Staff	131	30	4
	• Visitors	1183	15	18
2	First to Nineteenth Floor (Office)			
	• Staff	3305	30	99
	• Visitors	367	15	6
3.	Sky Lounge (Terrace)			
	• Visitors	794	15	12
TOTAL DOMESTIC WATER DEMAND = 139 KLD				
B	HORTICULTURE (2423.82m ²)		1 l/sqm/day	3 KLD
C	HVAC (1650 TR)	10 hours	@10 Litre/TR	165 KLD
D.	DG Cooling (3 X 1500 KVA + 1 X 1000 KVA)	0.9 lt/kva/hr		30 KLD
GRAND TOTAL (A+B+C) = 337 KLD				

*DG Sets water demand are calculated for 6 Hours operation/day.

Table 6: Waste Water Calculations

Domestic Water Requirement	139 KLD
• Fresh water (@30% of domestic water)	42 KLD
• Flushing water (@ 70% of domestic water)	97 KLD
Waste Water Generated (@ 80% fresh water + 100% flushing water)	34 +97 = 131 KLD
STP Capacity	160 KL

The water balance diagrams for different seasons are shown below:

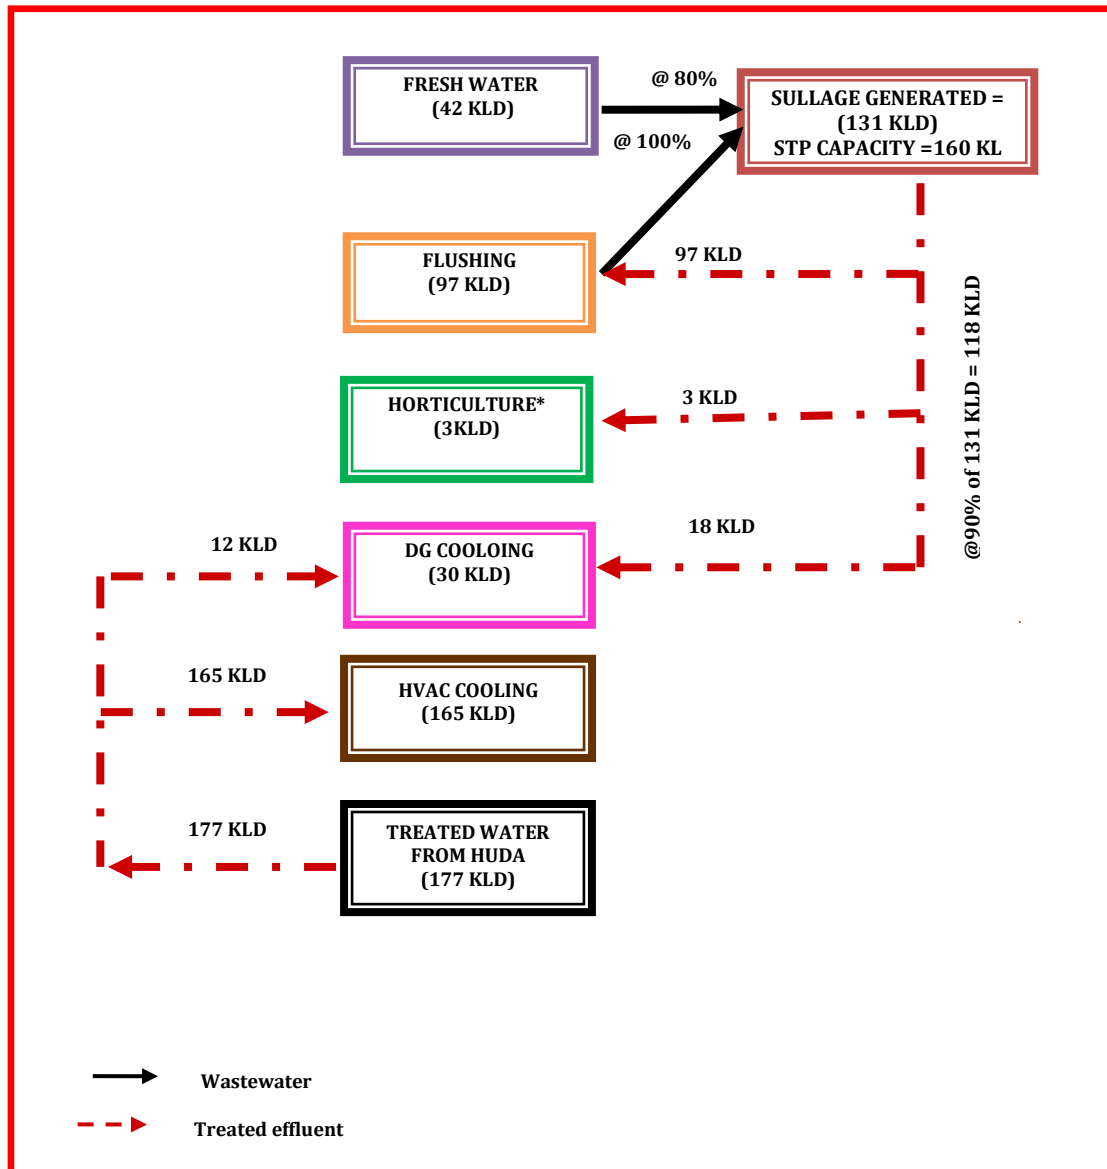


Figure 1: Water Balance Diagram (Non-Rainy Season)

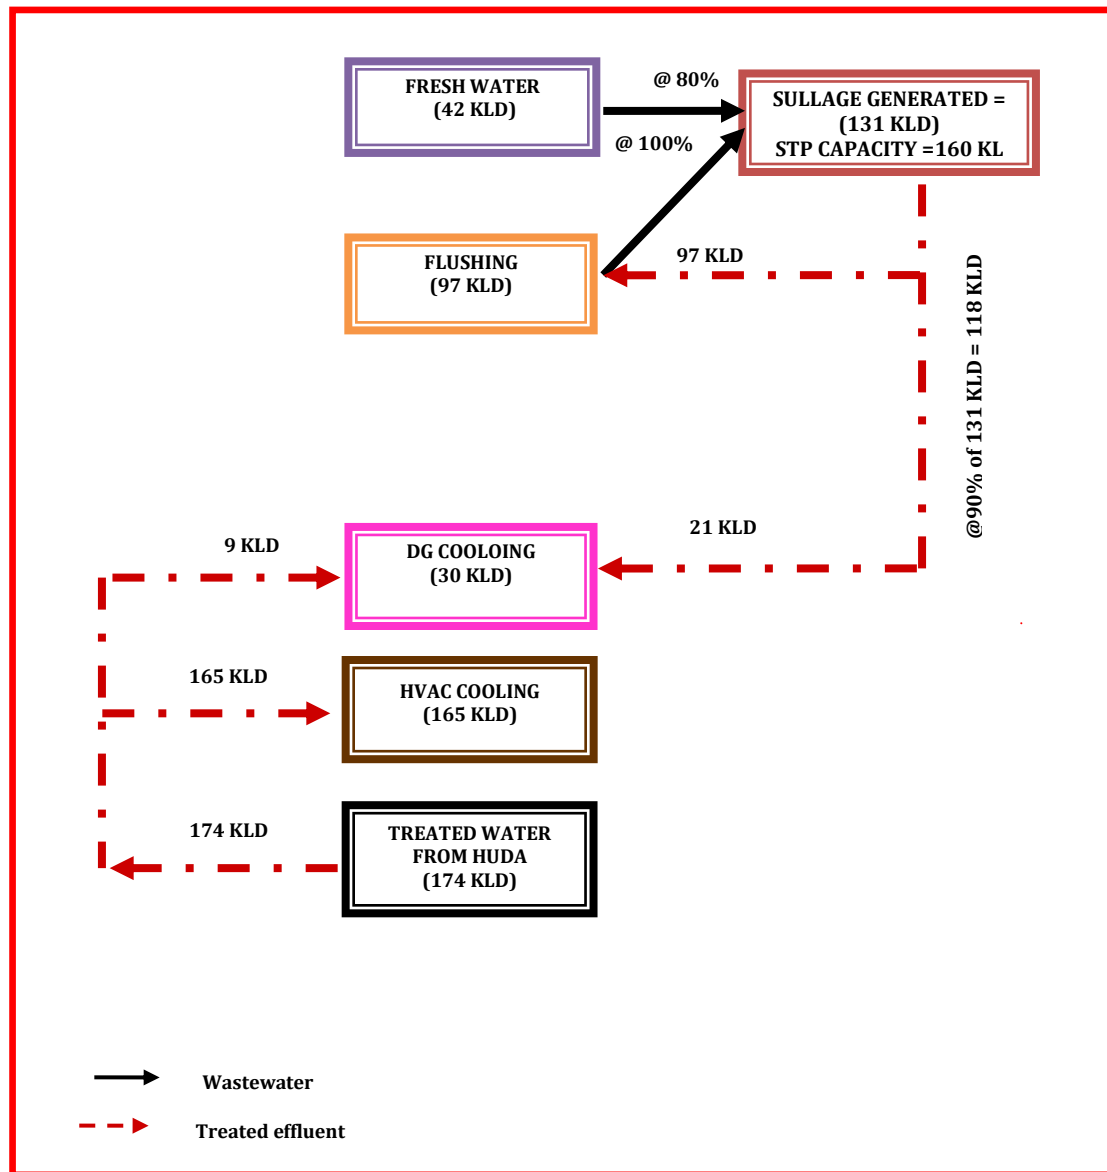


Figure 2: Water Balance Diagram (Rainy Season)

Wastewater Generation & Treatment

It is expected that the project will generate approx. 131KLD of wastewater. The wastewater will be treated in onsite STP of 160 KL capacity. The treated effluent 118 KLD will be reused for flushing, horticulture, DG Cooling & HVAC.

2.2 What is the quality of water required, in case, the supply is not from a municipal source? (Provide physical, chemical, Biological characteristics with class of water quality).

The required water will be met through the HUDA. The total water requirement is approx. 337 KLD.

SBR TECHNOLOGY

Sewerage System

An external sewage network shall collect the sewage from all units, and flow by gravity to the proposed sewage treatment plant.

Following are the benefits of providing the Sewage Treatment Plant in the present circumstances:

- Reduced net daily water requirements, source for Horticultural purposes by utilization of the treated waste water.
- Reduced dependence on the public utilities for water supply and sewerage systems.
- Sludge generated from the Sewage Treatment Plant shall be rich in organic content and an excellent fertilizer for horticultural purposes.

a. Wastewater Details

(a)	Daily load	:	131 KLD
(b)	Duration of flow to STP	:	24 hours
(c)	Temperature	:	Maximum 46°C
(d)	pH	:	6.5 to 8.5
(e)	Colour	:	Mild
(f)	T.S.S. (mg/l)	:	300-400
(g)	BOD ₅ (mg/l)	:	250-350
(h)	COD (mg/l)	:	400-600
(i)	Oil & Grease	:	10-50
(j)	Color	:	Mild

b. Final discharge characteristics

(a)	pH	:	6.5 to 7.5
(b)	Oil & Grease	:	<10 mg/l

(c)	B.O.D.	:	<20 mg/l
(d)	C.O.D.	:	<50 mg/l
(e)	Total Suspended Solids	:	<10 mg/l
(h)	Color	:	Clear

c. Treatment Technology

Sequence Batch Reactor is a most prominent technique for removing organic carbon and nutrient in a relatively short period. The fill and draw scheme constitute the basic principle of the SBR system. Raw sewage will be collected under gravity into the equalization tank after allowing to pass through the bar screen. The bar screen, by removing coarse solids from the sewage help in protecting the raw sewage pump. The raw sewage equalization tank, through temporarily holding the incoming sewage facilitates both pumping of sewage through the STP and dampening the flow variation in the received sewage. The sewage collected in equalization tank is pumped and passed through the SBR tank. Air will be introduced in this tank to prevent any potential foul smell problem & to provide the mixing of wastewater to avoid the sedimentation of solids in this tank.

The SBR is basically a single tank that serves both biological reactor and settler in a temporal sequence, whereas aeration and settling are simultaneous but in a spatial sequence.

From the reactors, The suspended solids will settle at the bottom of the tank & clear supernatant will overflow to Collection cum storage tank collected sludge at bottom shall be transferred through pumps to sludge holding tank. The clear supernatant after clarifier will be collected in to filter feed tank. This tank will act as housing tank for filter feed pumps. The clarified & dis-infected water will be then fed to filtration unit.

Filtration unit consisting of Dual Media sand filter and activated carbon filter will remove the residual impurities such as odor/color, suspended solids, BOD/COD. The treated water after the filtration unit will be collected in Irrigation cum Flushing water storage tank from where it is transferred to flushing water tank at terrace & Irrigation System.

Excess sludge from the bottom of the settling tank will be removed and transferred to sludge holding tank. Air grid shall be provided in this tank to avoid conversion into anaerobic

conditions, thickening of sludge and keep sludge in homogenous condition. The digested & thickened sludge shall be further thickened through Sludge Dewatering System and disposed off periodically through closed tanker or can be reused as manure.

Stages of Treatment: The treatment process consists of the following stages:

- Equalization
- Bio- Degradation
- Clarification & Settling
- Filtration

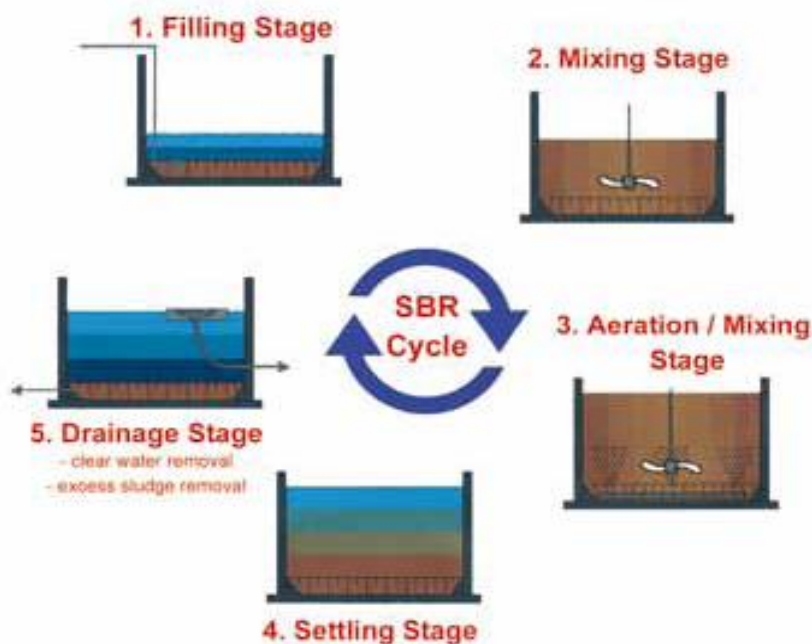


Figure 3: Flow Diagram of SBR

Sewer System

The alignment and slope of the sewer line will follow the road network, drains or natural ground surface and will be connected to the trunk sewers. The discharge point will be a treatment plant, a pumping station, a water course or an intercepting sewer. Pumping stations would be provided at places where the natural slope of the terrain is insufficient to permit gravity flow or the cost of excavation is uneconomical to do the same.

2.3 How much of water requirement can be met from the recycling of treated wastewater? (Give the details of quantities, sources and usage)

It is expected that the project will generate approx. 131 KLD of wastewater. The wastewater will be treated in onsite STP of 160 KL capacity. The treated effluent 118 KLD will be reused for flushing, horticulture, DG Cooling & HVAC.

2.4 Will there be diversion of water from other users? (Please assess the impacts of the project on other existing uses and quantities of consumption).

No. There will not be any diversion of water from other users. Rise in water demand is a local phenomenon but the project would only involve spatial shifting of water demand within a region.

2.5 What is the incremental pollution load from wastewater generated from the proposed activity? (Give details of the quantities and composition of wastewater generated from the proposed activity)

131 KLD of sullage generated which will be treated through onsite STP of 160 KL capacity.

2.6 Give details of the water requirements met from water harvesting? Furnish details of the facilities created.

The storm water collection system for the premises shall be self-sufficient to avoid any collection/stagnation and flooding of water. The amount of storm water run-off depends upon many factors such as intensity and duration of precipitation, characteristics of the tributary area and the time required for such flow to reach the drains. The drains shall be located near the carriage way along either side of the roads. Taking the advantage of road camber, the rainfall run off from roads shall flow towards the drains. Storm water from various plots/shall be connected to adjacent drain by a pipe through catch basins. Therefore, it has been calculated to provide 3 rainwater harvesting pits at selected locations, which will catch the maximum run-off from the site.

- 1) Since the existing topography is congenial to surface disposal, a network of storm water pipe drains is planned adjacent to roads. All building roof water will be brought down through rain water pipes.

Annexure-VII

RWH Details

2.3 How much of water requirement can be met from the recycling of treated wastewater? (Give the details of quantities, sources and usage)

It is expected that the project will generate approx. 131 KLD of wastewater. The wastewater will be treated in onsite STP of 160 KL capacity. The treated effluent 118 KLD will be reused for flushing, horticulture, DG Cooling & HVAC.

2.4 Will there be diversion of water from other users? (Please assess the impacts of the project on other existing uses and quantities of consumption).

No. There will not be any diversion of water from other users. Rise in water demand is a local phenomenon but the project would only involve spatial shifting of water demand within a region.

2.5 What is the incremental pollution load from wastewater generated from the proposed activity? (Give details of the quantities and composition of wastewater generated from the proposed activity)

131 KLD of sullage generated which will be treated through onsite STP of 160 KL capacity.

2.6 Give details of the water requirements met from water harvesting? Furnish details of the facilities created.

The storm water collection system for the premises shall be self-sufficient to avoid any collection/stagnation and flooding of water. The amount of storm water run-off depends upon many factors such as intensity and duration of precipitation, characteristics of the tributary area and the time required for such flow to reach the drains. The drains shall be located near the carriage way along either side of the roads. Taking the advantage of road camber, the rainfall run off from roads shall flow towards the drains. Storm water from various plots/shall be connected to adjacent drain by a pipe through catch basins. Therefore, it has been calculated to provide 3 rainwater harvesting pits at selected locations, which will catch the maximum run-off from the site.

- 1) Since the existing topography is congenial to surface disposal, a network of storm water pipe drains is planned adjacent to roads. All building roof water will be brought down through rain water pipes.

- 2) Proposed storm water system consists of pipe drain, catch basins and seepage pits at regular intervals for rain water harvesting and ground water recharging.
- 3) For basement parking, the rainwater from ramps will be collected in the basement storm water storage tank. This water will be pumped out to the nearest external storm water drain.
- 4) The peak hourly rainfall of 45 mm/hr shall be considered for designing the storm water drainage system.

Rain water harvesting has been catered to and designed as per the guideline of CGWA. Peak hourly rainfall has been considered as 45 mm/hr. The recharge pit of 4 m diameter and 3 m depth is constructed for recharging the water. Inside the recharge pit, a recharge bore is constructed having adequate diameter and depth. The bottom of the recharge structure will be kept 5m above this level. At the bottom of the recharge well, a filter media is provided to avoid choking of the recharge bore. Design specifications of the rain water harvesting plan are as follows:

- Catchments/roofs would be accessible for regular cleaning.
- The roof will have smooth, hard and dense surface which is less likely to be damaged allowing release of material into the water. Roof painting has been avoided since most paints contain toxic substances and may peel off.
- All gutter ends will be fitted with a wire mesh screen and a first flush device would be installed. Most of the debris carried by the water from the rooftop like leaves, plastic bags and paper pieces will get arrested by the mesh at the terrace outlet and to prevent contamination by ensuring that the runoff from the first 20 minutes of rainfall is flushed off.
- No sewage or wastewater would be admitted into the system.
- No wastewater from areas likely to have oil, grease, or other pollutants has been connected to the system.

Table 7: Comparative Details of Rain water Harvesting

S. No.	Particulars	EC accorded	Expansion	Total (EC accorded + Expansion)
1.	Rain water Harvesting Pits	3	---	3

Calculations for storm water load :

$$\text{Net Plot Area} = 11,537.57\text{m}^2$$

$$\text{Roof-top area} = \text{Ground Coverage} = 4,524.140 \text{ m}^2$$

$$\text{Green Area} = 2,423.82 \text{ m}^2$$

$$\begin{aligned}\text{Paved area} &= \text{Net Plot Area} - (\text{Roof-top Area} + \text{Green Area}) \\ &= 11537.57 - (4524.140 + 2423.82) \\ &= 4589.61 \text{ m}^2\end{aligned}$$

Run-off Load.

$$\begin{aligned}\text{Roof-top Area} &= 4524.140 \times 0.045 \times 0.9 \\ &= 183.227\text{m}^3/\text{hr}.\end{aligned}$$

$$\begin{aligned}\text{Green Area} &= 2423.82 \times 0.045 \times 0.2 \\ &= 21.81\text{m}^3/\text{hr}.\end{aligned}$$

$$\begin{aligned}\text{Paved Area} &= 4,589.61 \times 0.045 \times 0.7 \\ &= 144.57 \text{ m}^3/\text{hr}.\end{aligned}$$

$$\begin{aligned}\text{Total Runoff Load} &= 183.227 + 21.81 + 144.57 \text{ m}^3/\text{hr} \\ &= 349.607 \text{ m}^3/\text{hr}.\end{aligned}$$

$$\text{Taking 20 minutes retention time, volume of storm water} = 349.607 / 3 = 116.53 \text{ m}^3$$

$$\text{Capacity of Recharge pit} = \pi r^2 h = 3.14 \times 2 \times 2 \times 3 = 37.68 \text{ m}^3$$

$$\text{Hence No. of pits required} = 116.53 / 37.68 = \mathbf{3 \text{ pits}}$$

Total of 3 Rain Water Harvesting pits are proposed for artificial ground water recharge.

2.7 What would be the impact of the land use changes occurring due to the project on the runoff characteristics (quantitative as well as qualitative) of the area in the post construction phase on a long term basis? Would it aggravate the problems of flooding or water logging in any way?

Annexure-VIII

**Waste management plan during
Construction & Operation Phase**

- Provision of slit traps in storm water drains
- Good housekeeping in the above areas

10.2.4 EMP FOR LAND ENVIRONMENT

Construction Phase

The waste generated from construction activity includes construction debris, biomass from land clearing activities, waste from the temporary make shift tents for the labors and hazardous waste. Following section discuss the management of each type of waste. Besides waste generation, management of the topsoil is an important area for which management measures are required.

Construction Debris

Construction debris is bulky and heavy and re-utilization and recycling is an important strategy for management of such waste. As concrete and masonry constitute the majority of waste generated, recycling of this waste by conversion to aggregate can offer benefits of reduced landfill space and reduced extraction of raw material for new construction activity. This is particularly applicable to the project site as the construction is to be completed in a phased manner.

Mixed debris with high gypsum, plaster, shall not be used as fill, as they are highly susceptible to contamination, and will be send to designated solid waste landfill site.

Metal scrap from structural steel, piping, concrete reinforcement and sheet metal work shall be removed from the site by construction contractors. A significant portion of wood scrap will be reused on site. Recyclable wastes such as plastics, glass fiber insulation, roofing etc shall be sold to recyclers.

Hazardous waste

Construction sites are sources of many toxic substances such as paints, solvents wood preservatives, pesticides, adhesives and sealants. Hazardous waste generated during

construction phase shall be stored in sealed containers and disposed off as per The Hazardous Wastes (Management, Handling & Trans boundary Movement) Rules, 2016.

Some management practices to be developed are:

- Herbicides and pesticide will not be over applied (small-scale applications) and not applied prior to rain.
- Paintbrushes and equipment for water and oil based paints shall be cleaned within a contained area and will not be allowed to contaminate site soils, water courses or drainage systems.
- Provision of adequate hazardous waste storage facilities. Hazardous waste collection containers will be located as per safety norms and designated hazardous waste storage areas will be away from storm drains or watercourses.
- Segregation of potentially hazardous waste from non-hazardous construction site debris.
- Well labeled all hazardous waste containers with the waste being stored and the date of generation.
- Instruct employees and subcontractors in identification of hazardous and solid waste.

Even with careful management, some of these substances are released into air, soil and water and many are hazardous to workers. With these reasons, the best choice is to avoid their use as much as possible by using low-toxicity substitutes and low VOC (Volatile Organic Compound) materials.

Waste from Temporary Makes Shift Tents for Labors

Wastes generated from temporary make shift labor tents which will be managed by the contractor of the site. The wastewater generated will be channelized to the septic tank.

Top Soil Management

To minimize disruption of soil and for conservation of top soil, the contractor shall keep the top soil cover separately and stockpile it. After the construction activity is over, top soil will be utilized for landscaping activity. Other measures, which would be followed to prevent soil erosion and contamination include:

- Maximize use of organic fertilizer for landscaping and green belt development
- To prevent soil contamination by oil/grease, leak proof containers would be used for storage and transportation of oil/grease and wash off from the oil/grease handling area shall be drained through impervious drains and treated appropriately before disposal
- Removal of as little vegetation as possible during the development and re-vegetation of bare areas after the project.
- Working in a small area at a point of time (phase wise construction)
- Construction of erosion prevention troughs/berms.

Operational Phase

The philosophy of solid waste management at the proposed complex will be to encouraging the four R's of waste i.e. **Reduction, Reuse, Recycling and Recovery** (materials & energy). Regular public awareness meetings will be conducted to involve the public in the proper segregation and storage techniques. The Environmental Management Plan for the solid waste focuses on three major components during the life cycle of the waste management system i.e., collection and transportation, treatment or disposal and closure and post-closure care of treatment/disposal facility.

Collection and Transportation

- During the collection stage, the solid waste of the project will be segregated into biodegradable waste and non-biodegradable. Biodegradable waste and non biodegradable waste will be collected in

separate bins. Biodegradable waste will be treated in the project premises by Organic waste convertor. The recyclable wastes will be sent off to recyclabers. Proper guidelines for segregation, collection and storage will be prepared as per MSW Rules, 2016.

- To minimize littering and odour, waste will be stored in well-designed containers/ bins that will be located at strategic locations to minimize disturbance in traffic flow
- Care would be taken such that the collection vehicles are well maintained and generate minimum noise and emissions. During transportation of the waste, it will be covered to avoid littering.

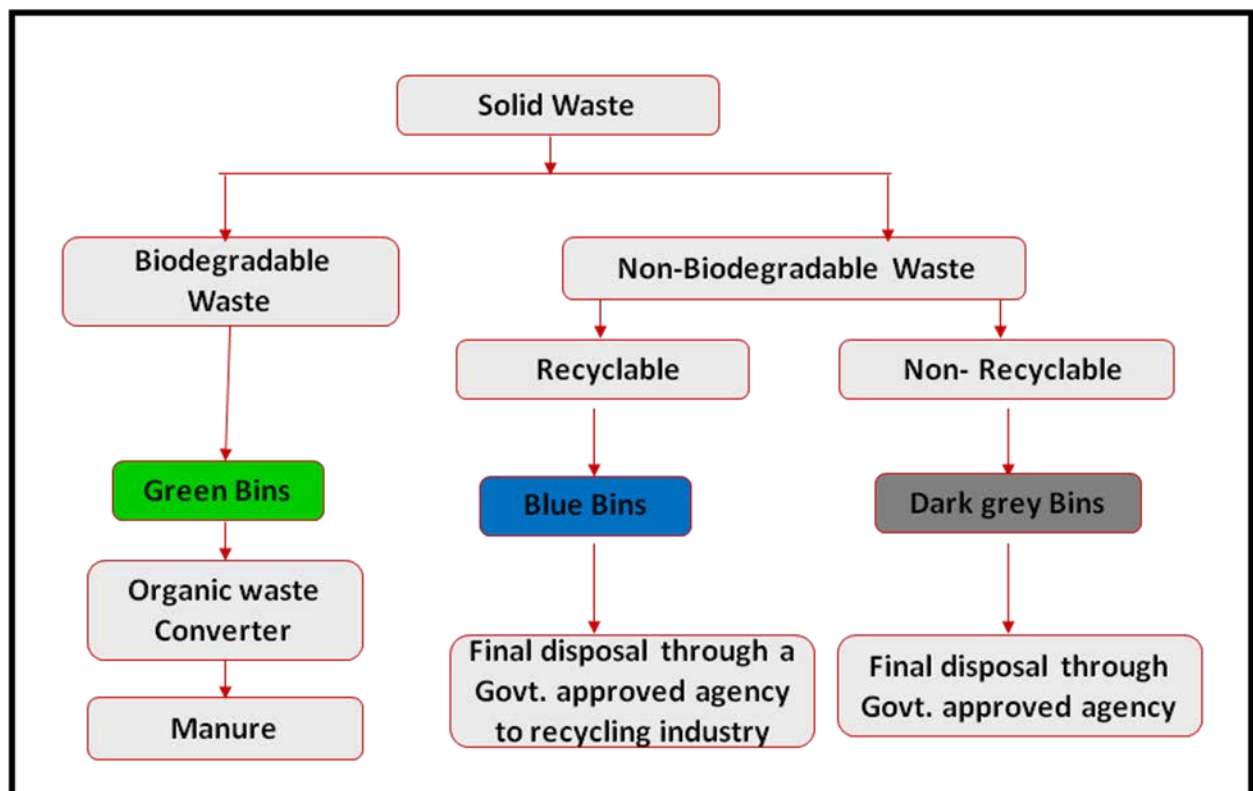


Figure 6: Waste Management Flow Diagram

Organic Waste Converter

A waste converter is a machine used for the treatment and recycling of solid and liquid refuse material. A converter is a self-contained system capable of performing the following functions: pasteurization of organic waste; sterilization of pathogenic or biohazard waste; grinding and pulverization of refuse into unrecognizable output; trash compaction; dehydration.

Benefits of organic waste converter:

1. Large quantity of solid waste is converted to manure in a very short period
2. Manure can be used as compost for gardening
3. Machine requires less space and the efficiency is high
4. Manpower and maintenance is very less
5. This is one of the latest techniques of managing biodegradable solid waste.

Operation cost of OWC:

Organic Waste Converter - 300 (Dim. 3m × 4m) is proposed to be used for composting waste 120kg/batch or 3000 kg/day & it requires electricity of about 13.5 HP.

No. of batches /day = $3000/120 = 25$ batches/day.

No. of batches to convert 490 kg/day = $490/120 = 4.08$ say 4 batches.

Operation Cost-monthly per capita:

The operating cost of OWC - 300 = 1, 80,000 INR/month

Cost/day = $1, 80,000/30$
= 6000/-

1 batch/day cost = $6000/25$
= 240 INR

Cost for 4 batch/day = $4 \times 240/-$
= 960/-

Monthly operating cost = 30×960
= Rs. 28,800/- per month

Disposal

With regards to the disposal/treatment of waste, the management will take the services of the authorized agency for waste management and disposal of the same on the project site during its operational phase.

10.2.5 EMP FOR ECOLOGICAL ENVIRONMENT

Construction activity changes the natural environment. The project requires the implementation of following choices exclusively or in combination.

Construction Stage

- Restriction of construction activities to defined project areas, which are ecologically sensitive
- Restrictions on location of temporary labor tents and offices for project staff near the project area to avoid human induced secondary additional impacts on the flora and fauna species
- Cutting, uprooting, coppicing of trees or small trees if present in and around the project site for cooking, burning or heating purposes by the labors will be prohibited and suitable alternatives for this purpose will be made
- Along with the construction work, the peripheral green belt would be developed with suggested native plant species, as they will grow to a full-fledged covered at the time of completion.

Operation Stage

Improvement of the current ecology of the project site will entail the following measures:

- Plantation and Landscaping
- Green Belt Development
- Park and Avenue Plantation

Annexure-IX

**Photographs of construction of Wind
Breaking wall of 10 mtrs. height for
dust control**

WIND BREAKING WALL



Front - Inside Barricading



Front side Barricading



Inside - Rear Road Barricading

Annexure-X

Environment Monitoring Reports i.e.
AAQ, Noise, Water & soil and its
interpretation

TEST REPORT

Issued to

M/s Asthetic Township Developers Pvt. Ltd.
Apt. No. E-301, Unworld City, Sec-30
Gurgaon- 122002


Doc No. : ELPL/IV/QF/20
Amend. No. & Amend. Date : 02 & 17.02.2018
Lab Reference No. : 210320001 A
Issue Date : 25/03/2021
Your Reference : Email
(Page1of 1)

Sample Particulars: Ambient Air Quality Monitoring was done at Commercial Complex project at Sushant Lok, Sec- 27, Gurugram Haryana, from 18/03/2021 to 19/03/2021.

Type of sample	: Ambient Air	Sample Registration Date	: 19/03/2021
Sampling Date	: 18/03/2021-19/03/2021	Analysis Starting Date	: 19/03/2021
Sampling Done by	: Lab representative	Analysis Completion Date	: 24/03/2021
Quantity received	: 24 Hourly Sample	Tests Required	: Mentioned below
Sample's Location	: Near DG Area	Sampling Method	: ELPL/III/SOP/21

S.No.	Test Parameters	Units	Results	NAAQS	Test Method
1	Particulate Matter as PM ₁₀	µg/m ³	242.5	100 (24 Hourly)	IS 5182 (Pt-23)
2	Particulate Matter as PM _{2.5}	µg/m ³	172.2	060 (24 Hourly)	ELPL/III/SOP/23
3	Sulphur Dioxide as SO ₂	µg/m ³	14.8	080 (24 Hourly)	IS 5182 (Pt-02)
4	Oxides of Nitrogen as NO _x	µg/m ³	39.5	080 (24 Hourly)	IS 5182 (Pt-06)
5	Carbon Monoxide as CO	mg/m ³	0.52	002 (08 Hourly)	IS 5182 (Pt-10)

*****END OF REPORT*****


Analyzed By
(Vikash Kumar)


Checked By
(Dr. Ramesh C. Tripathi)


Authorized Signatory
(Purushottam Kumar Sharma)



TEST REPORT

Issued to

M/s Asthetic Township Developers Pvt. Ltd.
Apt. No. E-301, Unworld City, Sec-30
Gurgaon- 122002

Doc No. : ELPL/IV/QF/20
Amend. No. & Amend. Date : 02 & 17.02.2018
Lab Reference No. : 210320002 N
Issue Date : 25/03/2021
Your Reference : Email
(Page1of 1)

Sample Particulars: Ambient Noise Level Monitoring was done at Commercial Complex project at Sushant Lok, Sec- 27, Gurugram Haryana, from 18/03/2021 to 19/03/2021.

Type of sample	: Ambient Noise	Sample Registration Date	: 19/03/2021
Sampling Date	: 18/03/2021-19/03/2021	Analysis Starting Date	: 18/03/2021
Sampling Done by	: Lab representative	Analysis Completion Date	: 19/03/2021
Quantity received	: 24 Hourly Sample	Tests Required	: Mentioned below
Sample's Location	: Near DG Area	Sampling Method	: ELPL/III/SOP/37

Time	Unit	Leq	Method
Day Time(06:00 am to 10:00 pm)	dB (A)	63.9	ELPL/III/SOP/37
Night Time(10:00 pm to 06:00 am)	dB (A)	52.5	ELPL/III/SOP/37

Standards for Ambient Noise As per Noise Pollution (Regulation & Control Rule-2000)			
Area Code	Category of Area/Zone	Limits in dB (A) Leq*	
		Day time	Night time
(A)	Industrial area	75	70
(B)	Commercial area	65	55
(C)	Residential area	55	45
(D)	Silence Zone	50	40

*****END OF REPORT*****

*Leq : It is energy mean of the noise level over a specified period.


Analyzed By
(Vikash Kumar)


Checked By
(Dr. Ramesh C. Tripathi)


Authorized Signatory
(Purushottam Kumar Sharma)



TEST REPORT

Issued to

M/s Asthetic Township Developers Pvt. Ltd.
Apt. No. E-301, Unworld City, Sec-30
Gurgaon- 122002

Doc No. : ELPL/IV/QF/20
Amend. No. & Amend. Date : 02 & 17.02.2018
Lab Reference No. : 210319008 W
Issue Date : 25/03/2021
Your Reference : Email

Sample Particulars: Water sample was collected from Tab at Commercial Complex project at
Sushant Lok, Sec- 27, Gurugram Haryana on 18/03/2021.

Type of sample	: Drinking water	Sample Registration Date	: 19/03/2021
Sampling Date	: 18/03/2021	Analysis Starting Date	: 19/03/2021
Sampling Done by	: Lab representative	Analysis Completion Date	: 24/03/2021
Quantity received	: 2 Ltr approx.	Tests Required	: Mentioned below
Sample's Location	: Pantry Room	Sampling Method	: ELPL/III/SOP/20

Page 1 of 2

S.No	Test Parameters	Units	Results	IS 10500 : 2012		Test Method
				Acceptable Limit, max.	Permissible Limit in the Absence of Alternate source, max.	
1	Color	Hazen	BDL (DL-5.0)	5	15	IS 3025 (Pt-04)
2	Odour	-	Agreeable	Agreeable	Agreeable	IS 3025 (Pt-05)
3	pH	-	7.29	6.5-8.5	No relaxation	IS 3025 (Pt-11)
4	Taste	-	Agreeable	Agreeable	Agreeable	IS 3025 (Pt-08)
5	Turbidity	NTU	BDL(DL-1.0)	1	5	IS 3025 (Pt-10)
6	Total Dissolved Solids	mg/l	118	500	2000	IS 3025 (Pt-16)
7	Ammonia (as total ammonia-N)	mg/l	BDL (DL 0.1)	0.5	No relaxation	IS 3025 (Pt-34)
8	Anionic Detergents (as MBAS)	mg/l	BDL (DL 0.1)	0.2	1.0	Annex K of IS 13428
9	Calcium as Ca	mg/l	15.7	75	200	IS 3025 (Pt-40)
10	Chloramines (as Cl ₂)	mg/l	BDL (DL0.1)	4.0	No relaxation	IS 3025 (Pt-26)
11	Chloride as Cl	mg/l	24.5	250	1000	IS 3025 (Pt-32)
12	Fluoride as F	mg/l	BDL (DL0.01)	1.0	1.5	APHA 23 rd Ed 4500F
13	Free Residual Chlorine	mg/l	BDL (DL0.05)	0.2*	1*	IS 3025 (Pt-26)
14	Nitrate as NO ₃	mg/l	BDL (DL0.1)	45	No relaxation	IS 3025 (Pt-34)
15	Phenolic Compounds (as C ₆ H ₅ OH)	mg/l	BDL (DL 0.001)	0.001	0.002	IS 3025 (Pt-43)
16	Sulphate as SO ₄	mg/l	16.8	200	400	IS 3025 (Pt-24)
17	Sulphide (as H ₂ S)	mg/l	BDL(DL 0.02)	0.05	No relaxation	IS 3025 (Pt-29)
18	Total Alkalinity as CaCO ₃	mg/l	65	200	600	IS 3025 (Pt-23)
19	Total Hardness as CaCO ₃	mg/l	78.4	200	600	IS 3025 (Pt-21)
20	Cyanide (as CN)	mg/l	BDL(DL 0.02)	0.05	No relaxation	IS 3025 (Pt-27)
21	Aluminum (as Al)	mg/l	BDL(DL 0.01)	0.03	0.2	APHA23 rd Ed.3120B
22	Barium (as Ba)	mg/l	BDL (DL 0.1)	0.7	No relaxation	APHA23 rd Ed.3120B

Analyzed By
(Shalu Srivastava)

Checked By
(Dr. Ramesh C. Tripathi)

Authorized Signatory
(Purushottam Kumar Sharma)

TEST REPORT

Issued to

M/s Asthetic Township Developers Pvt. Ltd.
Apt. No. E-301, Unworld City, Sec-30
Gurgaon- 122002

Doc No. : ELPL/IV/QF/20
Amend. No. & Amend. Date : 02 & 17.02.2018
Lab Reference No. : 210319008 W
Issue Date : 25/03/2021
Your Reference : Email

Sample Particulars: Water sample was collected from Tab at Commercial Complex project at Sushant Lok, Sec- 27, Gurugram Haryana on 18/03/2021.

Type of sample	: Drinking water	Sample Registration Date	: 19/03/2021
Sampling Date	: 18/03/2021	Analysis Starting Date	: 19/03/2021
Sampling Done by	: Lab representative	Analysis Completion Date	: 24/03/2021
Quantity received	: 2 Ltr approx.	Tests Required	: Mentioned below
Sample's Location	: Pantry Room	Sampling Method	: ELPL/III/SOP/20

Page 2 of 2

S.No	Test Parameters	Units	Results	IS 10500 : 2012		Test Method
				Acceptable Limit, max.	Permissible Limit in the Absence of Alternate source, max.	
23	Boron (as B)	mg/l	BDL (DL 0.1)	0.5	1.0	APHA 23 rd Ed.3120B
24	Copper (as Cu)	mg/l	BDL (DL 0.02)	0.05	1.5	APHA 23 rd Ed. 3120B
25	Iron as Fe	mg/l	BDL (DL 0.05)	1.0	No relaxation	IS 3025 (Pt-02)
26	Magnesium as Mg	mg/l	9.5	30	100	APHA 23 rd Ed.3500B
27	Manganese as Mn	mg/l	BDL (DL 0.05)	0.1	0.3	APHA 23 rd Ed.3120B
28	Selenium (as Se)	mg/l	BDL (DL 0.01)	0.01	No relaxation	APHA 23 rd Ed.3120B
29	Silver (as Ag)	mg/l	BDL (DL 0.05)	0.1	No relaxation	APHA 23 rd Ed.3120B
30	Zinc (as Zn)	mg/l	BDL (DL 0.05)	5	15	APHA 23 rd Ed.3120B
31	Cadmium (as Cd)	mg/l	BDL(DL 0.001)	0.003	No relaxation	APHA 23 rd Ed.3120B
32	Lead (as Pb)	mg/l	BDL(DL 0.005)	0.01	No relaxation	APHA 23 rd Ed.3120B
33	Mercury (as Hg)	mg/l	BDL (DL0.001)	0.001	No relaxation	APHA 23 rd Ed.3120B
34	Molybdenum (as MO)	mg/l	BDL (DL 0.01)	0.07	No relaxation	APHA 23 rd Ed.3120B
35	Nickel (as Ni)	mg/l	BDL (DL 0.01)	0.02	No relaxation	APHA 23 rd Ed.3120B
36	Total Arsenic (as As)	mg/l	BDL (DL 0.01)	0.01	No relaxation	APHA 23 rd Ed.3120B
37	Total Chromium (as Cr)	mg/l	BDL (DL 0.03)	0.05	No relaxation	APHA 23 rd Ed.3120B

*****END OF REPORT*****

Analyzed By
(Shalu Srivastava)

Checked By
(Dr. Ramesh C. Tripathi)

Authorized Signatory
(Purushottam Kumar Sharma)



TEST REPORT

Issued to

M/s Asthetic Township Developers Pvt. Ltd.
Apt. No. E-301, Unworld City, Sec-30
Gurgaon- 122002

Doc No. : ELPL/IV/QF/20
Amend. No. & Amend. Date : 02 & 17.02.2018
Lab Reference No. : 210319009 S
Issue Date : 25/03/2021
Your Reference : Email
(Page1of 1)

Sample Particulars: Soil sample was collected from ground at Commercial Complex project at Sushant Lok, Sec- 27, Gurugram Haryana on 18/03/2021.

Type of sample	: Soil	Sample Registration Date	: 19/03/2021
Sampling Date	: 18/03/2021	Analysis Starting Date	: 19/03/2021
Sampling Done by	: Lab representative	Analysis Completion Date	: 24/03/2021
Quantity received	: 1 Kg approx.	Tests Required	: Mentioned below
Sample's Location	: Main Tower Area	Sampling Method	: Grab Method

S.No.	Test Parameters	Unit	Result	Test Method
1	pH (1:5)	-	8.18	IS 2720(P-26)
2	Conductivity (1:5)	µmhos/cm	210	USDA Method
3	Color	-	Grey	USDA Method
4.	Texture		Sandy Clay	
	Silt	%	10	
	Clay	%	38	USDA Method
	Sand	%	52	
5	Sodium Absorption Ratio	-	0.32	USDA Method
6	Cation Exchange Capacity	Meq/100gm	44.7	IS 2720(P-24)
7	Porosity	%	29.8	USDA Method
8	Water Holding Capacity	%	28.4	USDA Method
9	Bulk Density	gm/cc	1.31	USDA Method
10	Chloride as Cl	mg/kg	98	USDA Method
11	Calcium as Ca	mg/kg	7635	USDA Method
12	Sodium as Na	mg/kg	108	USDA Method
13	Potassium as K	mg/kg	215	USDA Method
14	Magnesium as Mg	mg/kg	684	USDA Method
15	Organic matter	%	0.59	IS 2720(P-22)
16	Available Nitrogen	mg/kg	116.3	USDA Method
17	Phosphorous	mg/kg	54.3	USDA Method

*****END OF REPORT*****


Analyzed By
(Shalu Srivastava)


Checked By
(Dr. Ramesh C. Tripathi)


Authorized Signatory
(Purushottam Kumar Sharma)



Environmental Monitoring Report

1. Ambient Air Quality Monitoring

Ambient air quality monitoring has been done at one location for one day at Project site. The detail of monitoring schedule is given in **Table-1**.

Table 1: Schedule of Ambient Air Quality Monitoring

Day of sampling	Duration of sampling (hours)	Date		Sample collected on	Location
		From	To		
Day 1	24	18/03/2021	19/03/2021	19/03/2021	Project site.

Sulphur Dioxide (SO₂)

Monitoring results of SO₂ are given in **Table-1 (a)** and graphical representation is given in **Figure-1 (a)**

Table- 1(a): Monitoring results for SO₂

Parameter	Location	Days	Results (µg/m ³)	NAAQS	Time Weighted Average
				Concentration in Ambient Air(µg/m ³)	
				Industrial, Residential, Rural and other Areas	
Sulphur Dioxide(SO ₂)	Project site.	Day 1	14.8	80	24 hours

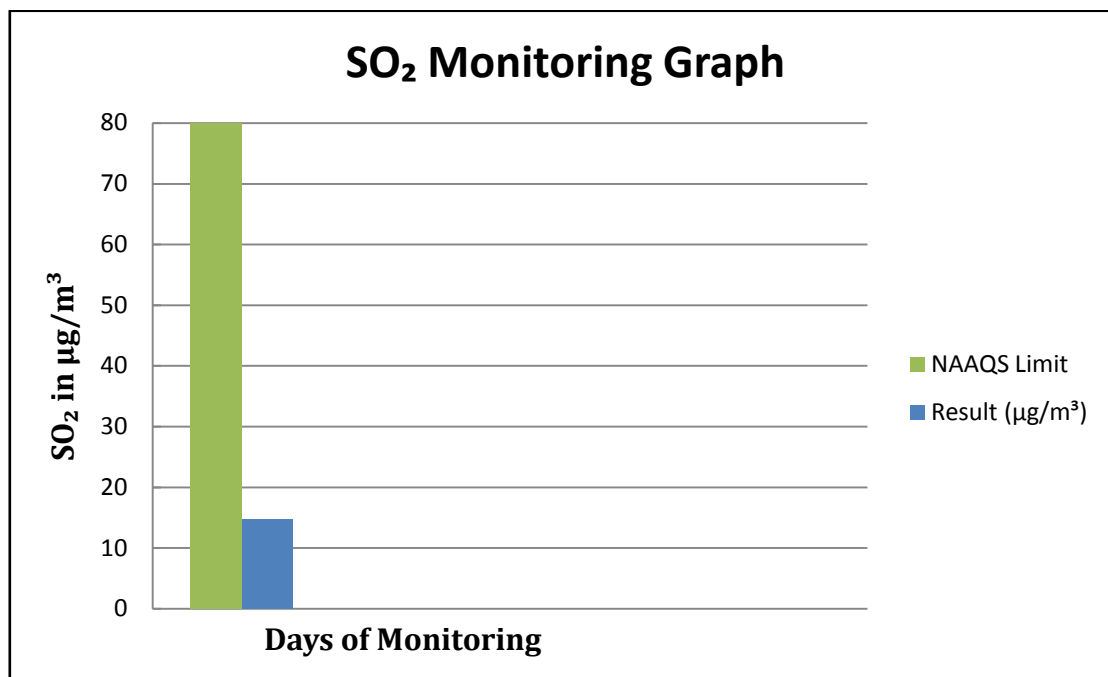


Figure-1(a): SO₂ concentrations at Project site.

The concentration of SO₂ was observed below permissible Limit as per NAAQS.


Nitrogen Dioxide (NO₂)

Monitoring results of NO₂ is given in **Table-1 (b)** and graphical representation is given in **Figure-1 (b)**

Table-1 (b) Monitoring results for NO₂

Parameter	Location	Days	Results (µg/m ³)	NAAQS	Time Weighted Average
				Concentration in Ambient Air(µg/m ³)	
				Industrial, Residential, Rural and other Areas	
Nitrogen Dioxide(NO ₂)	Project site.	Day 1	39.5	80	24 hours

Figure 1 (b): NO₂ concentrations at Project site.

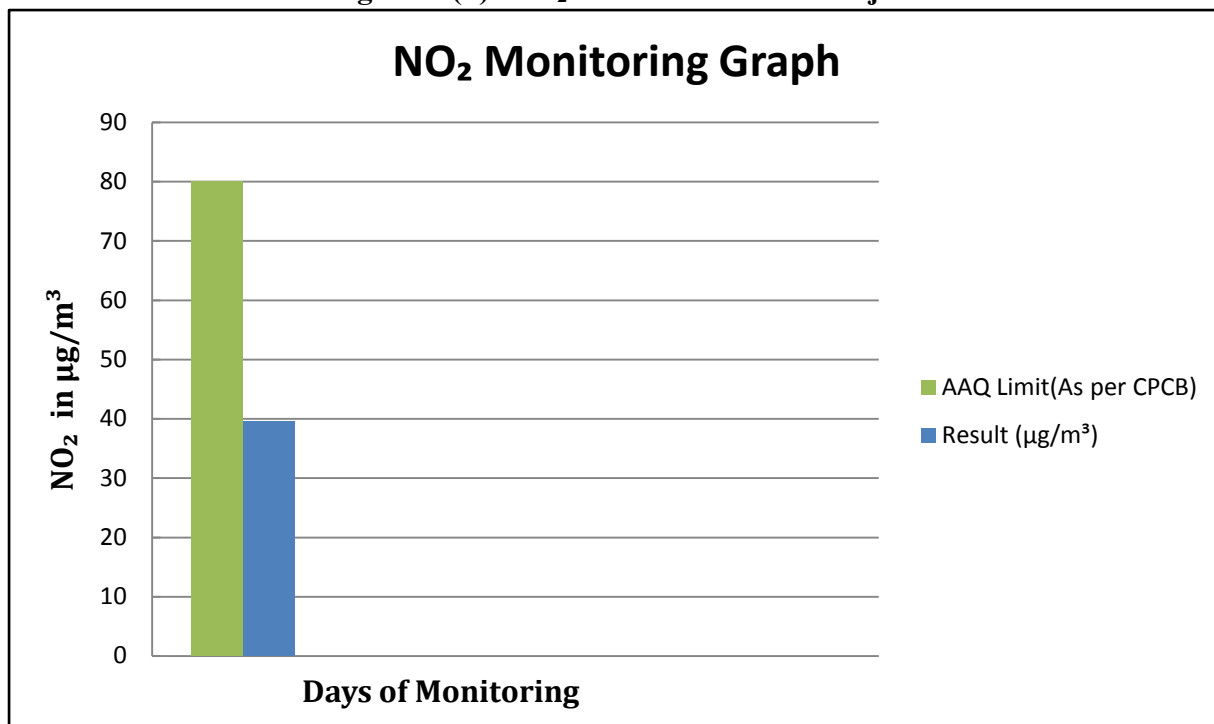

The concentration of NO₂ was below the limits as permissible limit as per NAAQS.

Particulate Matter

PM₁₀:

Monitoring results of PM₁₀ is given in **Table- 1(c)** and graphical representation is given in **Figure- 1(c)**.

Table-1 (c) : Monitoring results for PM₁₀

Parameter	Location	Days	Results (µg/m ³)	NAAQS	Time Weighted Average
				Concentration in Ambient Air(µg/m ³)	
				Industrial, Residential, Rural and other Areas	
Particular MatterSize Less than 10µm(PM ₁₀)	Project site.	Day 1	242.5	100	24 hours

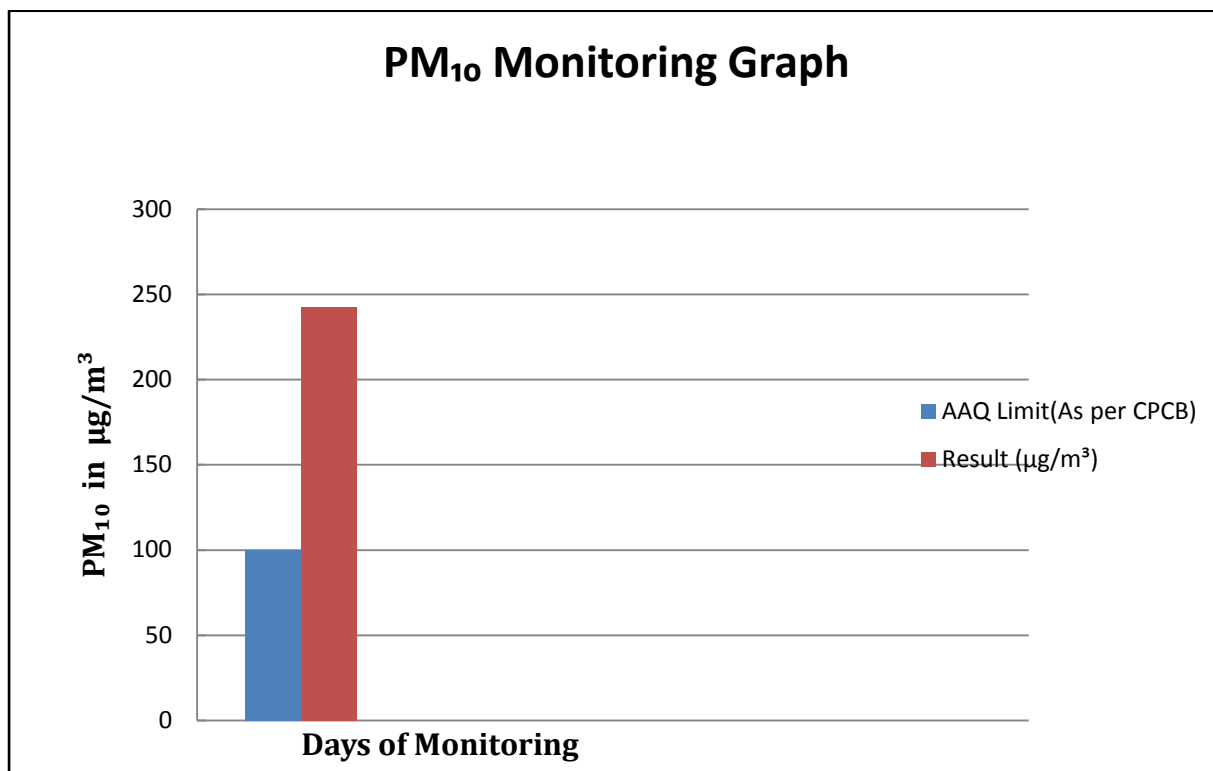


Figure 1 (c): PM₁₀ concentrations at Project site.

The concentration of PM₁₀ was found higher than permissible limit by NAAQS as there is some construction activity going on in surrounding area.

PM_{2.5}:

Monitoring results of PM_{2.5} is given in **Table-1 (d)** and graphical representation is given in **Figure- 1 (d)**

Table 1 (d): Monitoring results for PM_{2.5}

Parameter	Location	Days	Results (µg/m³)	NAAQS	Time Weighted Average
				Concentration in Ambient Air(µg/m³)	
				Industrial, Residential, Rural and other Areas	
Particular Matter Size Less than 2.5µm (PM _{2.5})	Project site.	Day 1	172.2	60	24 hours

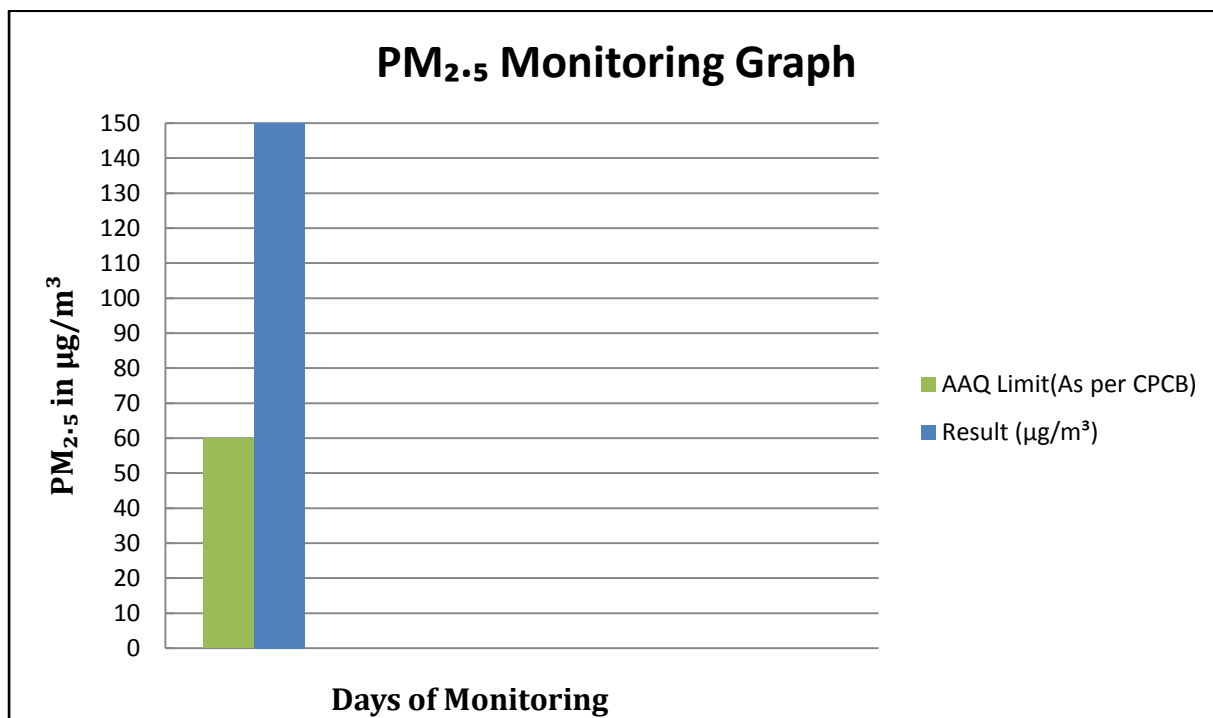


Figure 1 (d): PM_{2.5} concentrations at Project Site

The concentration of PM_{2.5} was found to be higher than permissible limit by NAAQS as some construction activity is going on in surrounding area.

Carbon Monoxide (CO)

Monitoring results of CO is given in **Table-1(e)** and graphical representation is given in **Figure-1(e)**.

Table -1 (e): Monitoring results for CO

Parameter	Location	Days	Results (mg/m ³)	NAAQS	Time Weighted Average
				Concentration in Ambient Air(mg/m ³)	
				Industrial, Residential, Rural and other Areas	
Carbon monoxide(CO)	Project site.	Day 1	0.52	2	8 hours

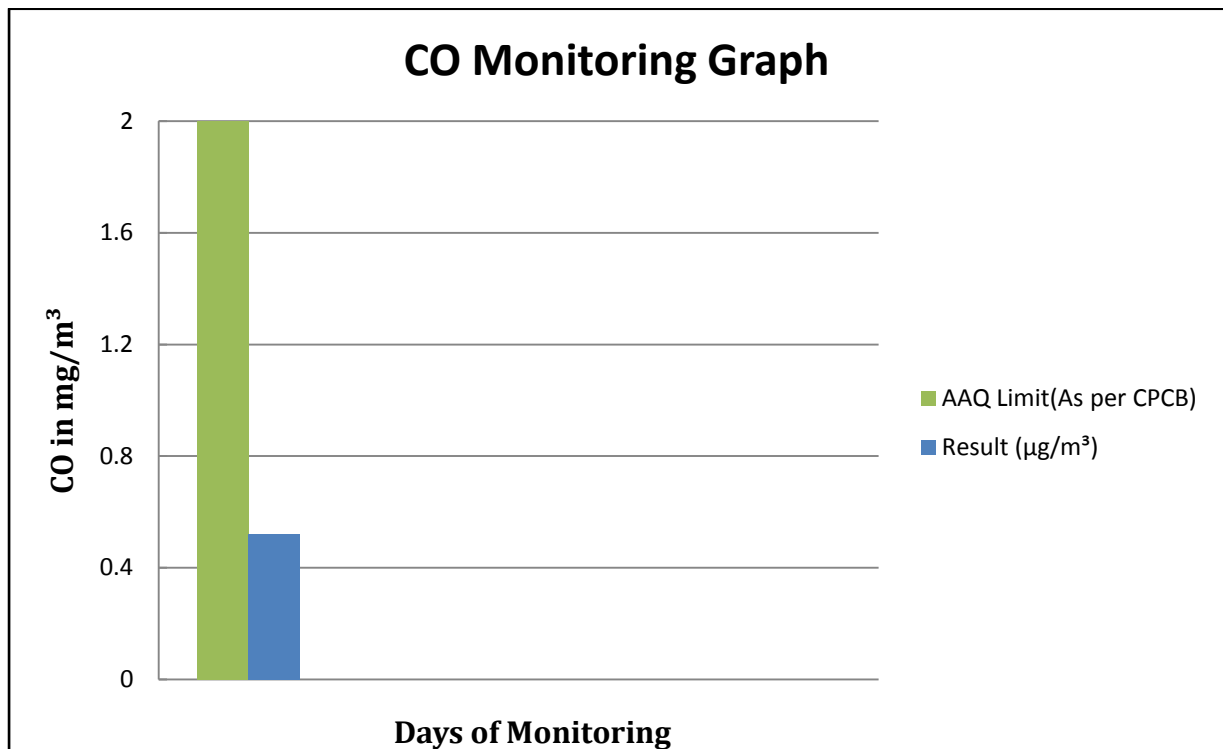


Figure 1(e): CO concentrations at Project site.

The concentration of CO was within the limit as prescribed by NAAQS.

2. Noise Monitoring

Noise monitoring was done at one location for one day at Project site. The details of monitoring are given in **Table-(2)**

Table (2): Schedule of Noise Monitoring

Day of sampling	Duration of sampling (hours)	Date		Sample collected on	Location
		From	To		
Day 1	24	18/03/2021	19/03/2021	19/03/2021	Project site

Monitoring has been done for 24 hours. The results for day time & night time observations are given below:

Day Time

Monitoring results of day time is given in **Table- 2(a)** and graphical representation is given in **Figure- 2(a)**

Table 2(a):Day Time monitoring results

Day	Result dB(A)	Permissible Limit dB(A) (as per CPCB)
	Day time (6:00 to 10:00 PM)	
Day 1	63.9	65

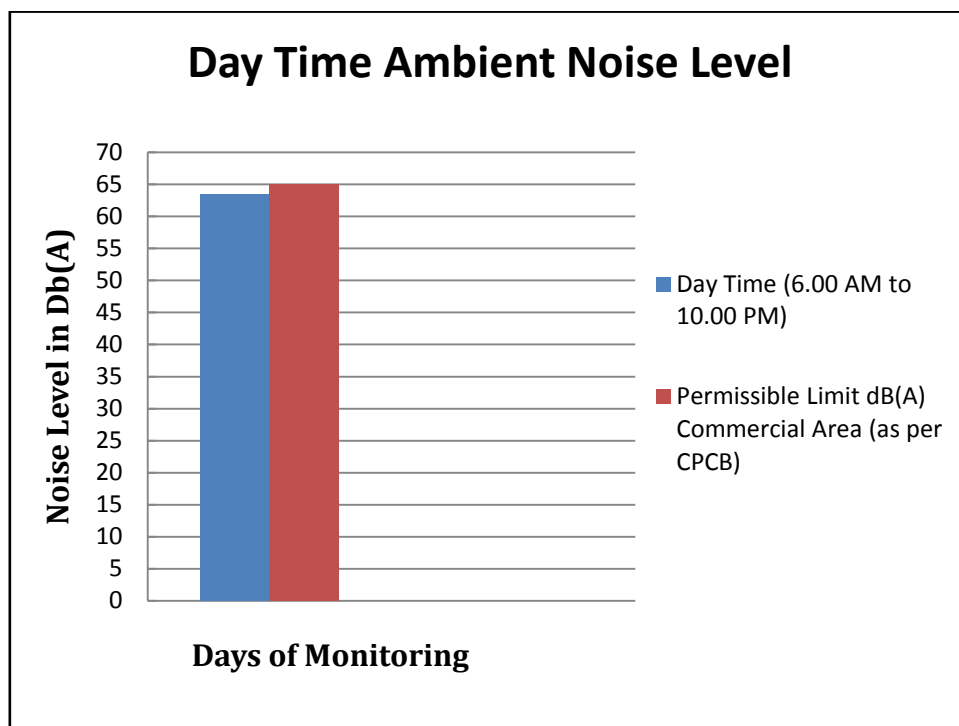


Figure 2(a): Graph showing day time noise monitoring results

The day noise result was found to be within the limit as prescribed by NAAQS.

Night Time

Monitoring results of night time is given in **Table- 2(b)** and graphical representation is given in **Figure-2(b)**

Table – 2(b): Night Time monitoring results

Night	Result dB(A)	Permissible Limit dB(A) for commercial Area
	Night Time (10:00 PM to 6:00 AM)	
Night 1	52.5	55

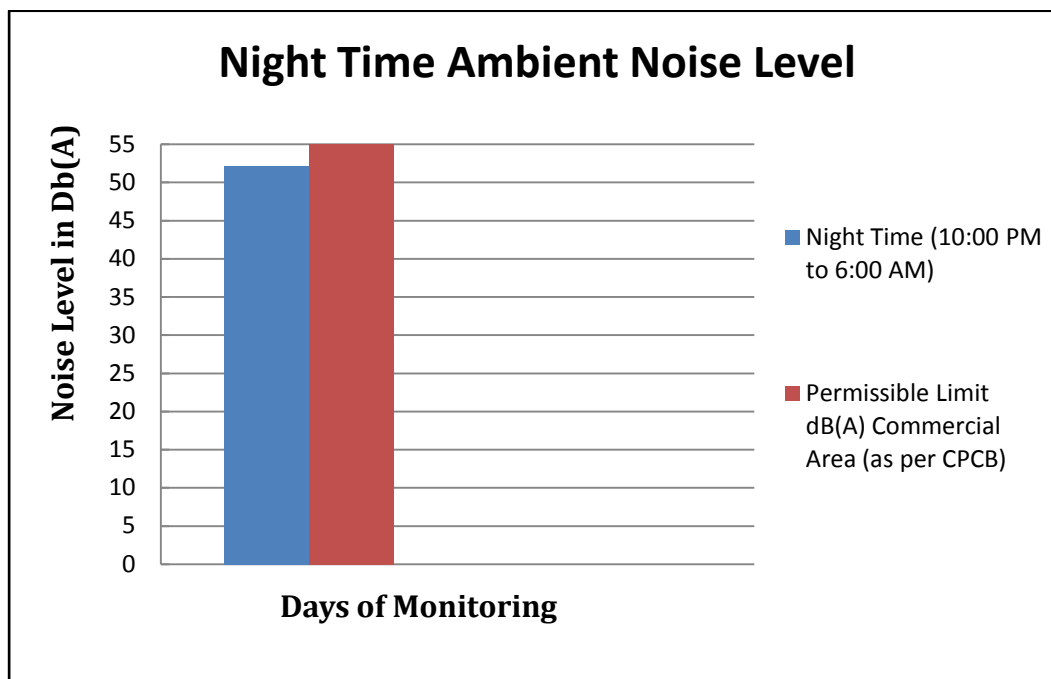


Figure 2(b): Graph showing night time noise monitoring results

The night noise result was found to be within the limit as prescribed by NAAQS.

3. RO Water Monitoring

Schedule for Drinking water monitoring is given in **Table 3**.

Table 3: Schedule for RO water sample collection

Day of sampling	Sample collected on	Location
Day 1	18/03/2021	Project site

Drinking water monitoring result is given in **Table 3(a)**.

Table 3(a): -RO water monitoring results.

S.	Test Parameters	Units	Result	IS 10500: 2012	Test Method
----	-----------------	-------	--------	----------------	-------------

**Commercial Complex project at Sushant Lok, Sec- 27, Gurugram Haryana by M/S
Asthetic Township Developers Pvt. Ltd.**

No.				Acceptable Limit, max.	Permissible Limit in the Absence of Alternate source, max.	
1	Color	Hazen	BDL (DL-5.0)	5	15	IS 3025 (Pt-04)
2	Odour	—	Agreeable	Agreeable	Agreeable	IS 3025 (Pt-05)
3	pH	—	7.29	6.5-8.5	No relaxation	IS 3025 (Pt-11)
4	Taste	—	Agreeable	Agreeable	Agreeable	IS 3025 (Pt-08)
5	Turbidity	NTU	BDL(DL-1.0)	1	5	IS 3025 (Pt-10)
6	Total Dissolved Solids	mg/l	118	500	2000	IS 3025 (Pt-16)
7	Ammonia (as N)	mg/l	BDL (DL0.1)	0.5	No relaxation	IS 3025 (Pt-34)
8	Anionic Detergents (as MBAS)	mg/l	BDL (DL0.1)	0.2	1.0	Annex K of IS 13428
9	Calcium as Ca	mg/l	15.7	75	200	IS 3025 (Pt-40)
10	Chloramines as Cl ₂	mg/l	BDL (DL0.1)	4.0	No relaxation	IS 3025 (Pt-26)
11	Chloride as Cl	mg/l	24.5	250	1000	IS 3025 (Pt-32)
12	Fluoride as F	mg/l	BDL (DL0.01)	1.0	1.5	APHA 22ND Ed 4500F
13	Free Residual Chlorine	mg/l	BDL (DL0.05)	0.2*	1*	IS 3025 (Pt-26)
14	Nitrate as NO ₃	mg/l	BDL (DL01.0)	45	No relaxation	IS 3025 (Pt-34)
15	Phenolic Compounds	mg/l	BDL (DL 0.001)	0.001	0.002	IS 3025 (Pt-43)
16	Sulphate as SO ₄	mg/l	16.8	200	400	IS 3025 (Pt-24)
17	Sulphide as H ₂ S	mg/l	BDL(DL 0.02)	0.05	No relaxation	IS 3025 (Pt-29)
18	Total Alkalinity as CaCO ₃	mg/l	65	200	600	IS 3025 (Pt-23)
19	Total Hardness as CaCO ₃	mg/l	78.4	200	600	IS 3025 (Pt-21)
20	Cyanide as CN	mg/l	BDL(DL 0.02)	0.05	No relaxation	IS 3025 (Pt-27)
21	Aluminium (as Al)	mg/l	BDL(DL 0.01)	0.03	0.2	APHA 23ND Ed.3120B
22	Barium as Ba	mg/l	BDL(DL 0.1)	0.7	No relaxation	APHA 23ND Ed.3120B
23	Boron as B	mg/l	BDL (DL 0.1)	0.5	1.0	APHA 23ND Ed.3120B
24	Copper (as Cu)	mg/l	BDL(DL 0.02)	0.05	1.5	APHA 23ND Ed.3120B
25	Iron as Fe	mg/l	BDL (DL 0.05)	1.0	No relaxation	IS 3025 (Pt-53)

**Commercial Complex project at Sushant Lok, Sec- 27, Gurugram Haryana by M/S
Asthetic Township Developers Pvt. Ltd.**

26	Magnesium as Mg	mg/l	9.5	30	100	APHA 23ND Ed.3500 mg B
27	Manganese as Mn	mg/l	BDL (DL 0.05)	0.1	0.3	APHA 23ND Ed.3120B
28	Selenium (as Se)	mg/l	BDL (DL 0.01)	0.01	No relaxation	APHA 23ND Ed.3120B
29	Silver (as Ag)	mg/l	BDL (DL 0.05)	0.1	No relaxation	APHA 23ND Ed.3120B
30	Zinc as Zn	mg/l	BDL (DL 0.05)	5	15	APHA 23ND Ed.3120B
31	Cadmium (as Cd)	mg/l	BDL (DL 0.001)	0.003	No relaxation	APHA 23ND Ed.3120B
32	Lead (as Pb)	mg/l	BDL (DL 0.05)	0.01	No relaxation	APHA 23ND Ed.3120B
33	Mercury as Hg	mg/l	BDL(DL0.001)	0.001	No relaxation	APHA 23ND Ed.3120B
34	Molybdenum as Mo	mg/l	BDL (DL 0.01)	0.07	No relaxation	APHA 23ND Ed.3120B
35	Nickel as Ni	mg/l	BDL(DL0.01)	0.02	No relaxation	APHA 23ND Ed.3120B
36	Total Arsenic as As	mg/l	BDL(DL 0.01)	0.01	No relaxation	APHA 23ND Ed.3120B
37	Total Chromium as Cr	mg/l	BDL(DL 0.03)	0.05	No relaxation	APHA 23ND Ed.3120B

4. Soil Monitoring

Soil sample was collected on 18/03/2021 from Near Project Site. Monitoring results are given in **Table 4.**


Table 4: Soil Monitoring Results

S. No.	Test Parameters	Unit	Results	Test Method
1	pH(1:5)	-	8.18	IS 2720 (P-26)
2	Conductivity(1:5)	µmhos/cm	210	USDA Method
3	Color	-	Grey	USDA Method
4	Texture		Sand Loam Silt	USDA Method
5	Silt	%	10	
6	Clay	%	38	
7	sand	%	52	
8	Sodium absorption ratio	-	0.32	USDA Method
9	Cation exchange capacity	Meq/100gm	44.7	IS 2720 (P-24)
10	Porosity	%	29.8	USDA Method

**Commercial Complex project at Sushant Lok, Sec- 27, Gurugram Haryana by M/S
Asthetic Township Developers Pvt. Ltd.**


11	Water Holding Capacity	%	28.4	USDA Method
12	Bulk Density	gm/cc	1.31	USDA Method
13	Chloride as Cl	mg/kg	98	USDA Method
14	Calcium as Ca	mg/kg	7635	USDA Method
15	Sodium as Na	mg/kg	108	USDA Method
16	Potassium as K	mg/kg	215	USDA Method
17	Magnesium as Mg	mg/kg	684	USDA Method
18	Organic matter	%	0.59	IS 2720 (P-22)
19	Available Nitrogen	mg/kg	116.3	USDA Method
20	Phosphorous	mg/kg	54.3	USDA Method

Annexure-XI
Landscape plan

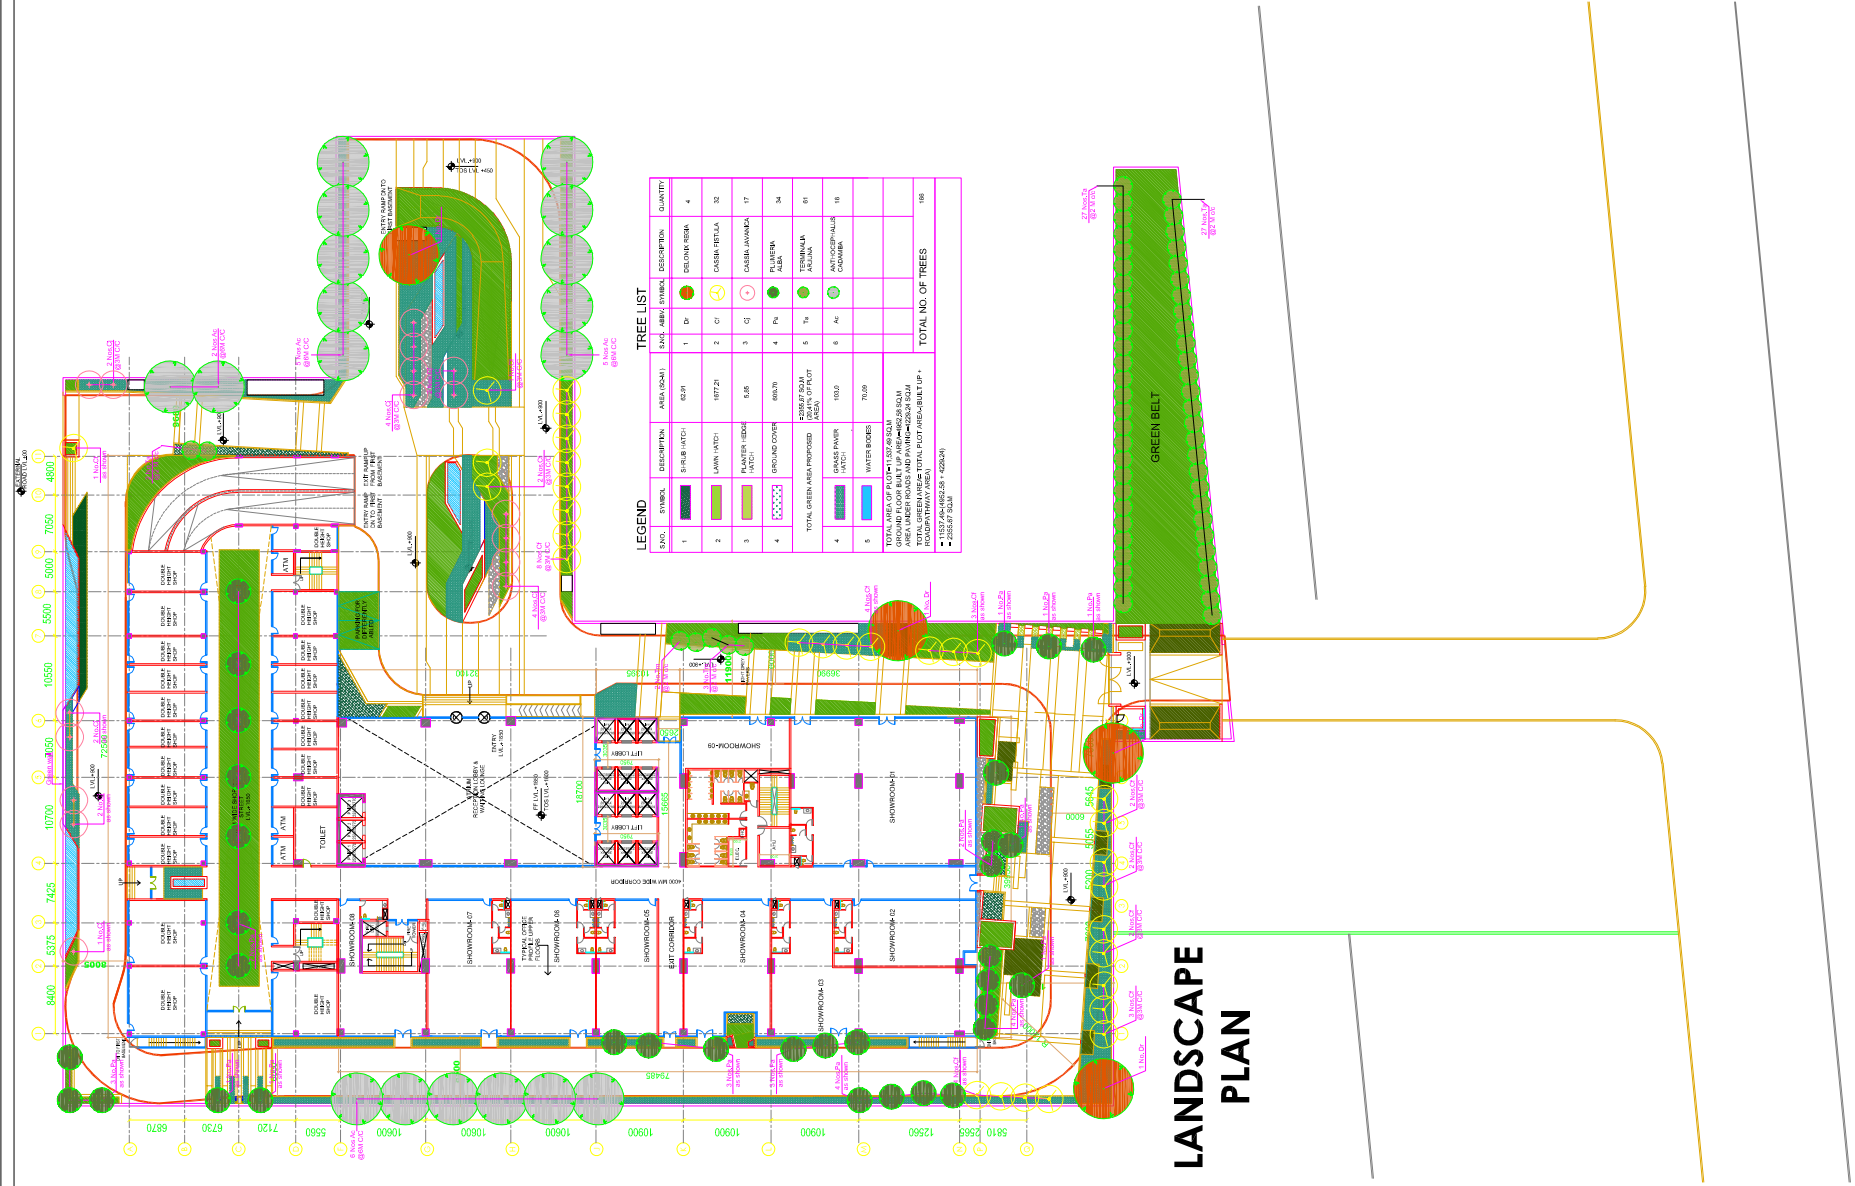

LANDSCAPE PLAN

COMMERCIAL TOWER
ASTHETIC DEVELOPERS
GURUGRAM



ARCHITECTS

ACPL

ISO 9001:2008

Architecture
Management
Planning

ACPL Design Ltd

E-24 South Extension-1
New Delhi-110048 India

www.acpltd.com

T: +91 11 24622195
+91 11 24646709

F: +91 11 24634089

Annexure-XII

**Photographs showing Excavated top
soil is preserved**

Photographs showing Excavated Top Soil



Annexure-XIII
PUC Certificate

ON UNDER CONTROL CERTIFICATE

Authorised By: RTA, GURGAON
Transport Department, Haryana



TEST RESULT : PASS
VALID TILL: 18/Nov/2021

DIESEL DRIVEN VEHICLES
Certified that the vehicle conforms to the standards prescribed under rule 115(2) of CMV Rules 1989




FUEL	Light Absorption Coefficient (Permissible Limit)	Measured Value
DIESEL	1.62	0.81

Certificate No.: HR05500490000546
Registration No.: HR55AC6918
Chassis No.: MAT448802HAF05337
Engine No.: 71E84389728
Class of Vehicle: Goods Carrier
Make: TATA MOTORS LTD
Model: 50079238300RBP24
Vehicle Category: HEAVY GOODS
Vehicle Category: VEHICLE
Date of Registration: 06/Dec/2017
Emission Norms: BHARAT STAGE IV
Fuel: DIESEL
Date of Testing: 19/Nov/2020

Signature of Jai Parkash Joon Filling Station
Pollution Checking Centre
In case of any complaint, please write to Transport
Commissioner Haryana

Auto Emission Testing Centre Code: HR0550049
Testing Centre Name: A.K. POLLUTION
CHECKING CENTRE
Centre Address: C/O. JAI PRAKASH
JOON FILLING STATION, SEC-29,
GURUGRAM, 122022
Test Conducted By: ANKUR TOMAR



TEST RESULT FOR DIESEL VEHICLE

	IDLE RPM	MAX RPM	K VALUE	OIL TEMP
TEST 1	802.0	1708.0	0.58	55.0
TEST 2	768.0	4271.0	0.97	55.0
TEST 3	591.0	4477.0	0.88	55.0
AVG	720.33334	3485.33334	0.81	55.0

This is a computer generated certificate and does not require signature

Annexure-XIV

**Environment Management and
Monitoring Plan**

ENVIRONMENT MANAGEMENT PLAN AND ENVIRONMENT MONITORING PLAN

ENVIRONMENT MANAGEMENT PLAN

The Environment Management Plan (EMP) would consist of all mitigation measures for each component of the environment due to the activities increased during the construction, operation and the entire life cycle to minimize adverse environmental impacts resulting from the activities of the project. It would also delineate the environmental monitoring plan for compliance of various environmental regulations. It will state the steps to be taken in case of emergency such as accidents at the sites including fire. The detailed EMP for the complex is given below.

Environmental Management Plan

The Environment Management Plan (EMP) is a site specific plan developed to ensure that the project is implemented in an environmental sustainable manner where all contractors and subcontractors, including consultants, understand the potential environmental risks arising from the project and take appropriate actions to properly manage that risk. EMP also ensures that the project implementation is carried out in accordance with the design by taking appropriate mitigation actions to reduce adverse environmental impacts during its life cycle. The plan outlines existing and potential problems that may adversely impact the environment and recommends corrective measures where required. Also, the plan outlines roles and responsibility of the key personnel and contractors who will be in-charge of the responsibilities to manage the project site.

The EMP is generally

- Prepared in accordance with rules and requirements of the MoEF and CPCB/ SPCB
- To ensure that the component of facility are operated in accordance with the design
- A process that confirms proper operation through supervision and monitoring
- A system that addresses public complaints during construction and operation of the facilities and
- A plan that ensures remedial measures is implemented immediately.

The key benefits of the EMP are that it offers means of managing its environmental performance thereby allowing it to contribute to improved environmental quality. The other benefits include cost control and improved relations with the stakeholders.

EMP includes four major elements :

- **Commitment & Policy:** The management will strive to provide and implement the Environmental Management Plan that incorporates all issues related to air, water, land and noise.
- **Planning:** This includes identification of environmental impacts, legal requirements and setting environmental objectives.
- **Implementation:** This comprises of resources available to the developers, accountability of contractors, training of operational staff associated with environmental control facilities and documentation of measures to be taken.
- **Measurement & Evaluation:** This includes monitoring, counteractive actions and record keeping.

It is suggested that as part of the EMP, a monitoring committee would be formed by M/s Aesthetic Township Developers Pvt. Ltd., comprising of the site in-charge/coordinator, environmental group representative and project implementation team representative. The committee's role would be to ensure proper operation and management of the EMP including the regulatory compliance.

The components of the environmental management plan, potential impacts arising, out of the project and remediation measures are summarized below in **Table 1** and EMP for dust suppression is mentioned in **Table 2**.

TABLE 1: SUMMARY OF POTENTIAL IMPACTS AND REMEDIAL MEASURES

S. No.	Environmental components	Potential Impacts	Potential Source of Impact	Controls Through EMP & Design	Impact Evaluation	Preventive Measures
1.	Ground Water Quality	Ground Water Contamination	<u>Construction Phase</u> Sewage generated from temporary labor tents.	Mobile STP and treated sewage will be used for construction purposes.	No significant impact as majority of labors would be locally deployed	--
			<u>Operation Phase</u> Sewage Discharge from the project	Proponent will provide the STP to treat the sewage of Project.	No negative impact on ground water quality envisaged. Not significant.	In an unlikely event of soil and ground water contamination. Remediation measures will be implemented.
2.	Ground Water Quantity	Ground Water Depletion	<u>Construction Phase</u> Ground water will be not be used during construction.	Not Applicable	No significant impact on ground water quantity envisaged.	
			<u>Operation Phase</u> Groundwater will not during operation phase. The required water will be met through the municipal supply	- Rain water harvesting scheme. - Black and Grey water treatment and reuse. - Storm water collection for water harvesting. - Percolation well to be introduced in landscape plan. - Awareness Campaign to	No significant impact on surface/ground water quantity envisaged.	In an unlikely event of non-availability of water supply, water will be brought using tankers.

S. No.	Environmental components	Potential Impacts	Potential Source of Impact	Controls Through EMP & Design	Impact Evaluation	Preventive Measures
				reduce the water consumption		
3.	Surface Water Quality	Surface water contamination	<u>Construction Phase</u> • Surface runoff from site during construction activity.	• Silt traps and other measures such as additional onsite diversion ditches will be constructed to control surface run-off during site development	No off-site impact envisaged as no surface water receiving body is present in the core zone.	--
			<u>Operation Phase</u> • Discharge of domestic wastewater to STP.	• Domestic water will be treated in STP	No off-site impact envisaged	Excess of water will be discharged as per CPCB standards.
4.	Air Quality	Dust Emissions	<u>Construction Phase</u> • All heavy construction activities	• Suitable control measures will be adopted for subsiding the PM level in the air as per air pollution control plan.	Not significant because dust generation will be temporary and will settle fast due to dust suppression techniques (wet scrubbers) used.	During construction phase the contractors are advised to facilitate masks for the labors. Water sprinklers will be used for suppression of dust during construction phase.
		Emissions of SPM, SO ₂ , NO ₂ and CO	<u>Construction Phase</u> • Operation of construction	• On-site construction and improved maintenance of equipment	Not significant.	Regular monitoring of emissions and control measures will be taken

S. No.	Environmental components	Potential Impacts	Potential Source of Impact	Controls Through EMP & Design	Impact Evaluation	Preventive Measures
			equipment and vehicles during site development. • Running D.G. sets (back up)			to reduce the emission levels.
			<u>Operation Phase</u> • Power generation by DG Sets during power failure • Emission from vehicular traffic in use <u>Construction Phase</u> • Operation of construction equipment and vehicle movements during site development. • Running DG sets (for power back up)	• Use of Low Sulphur diesel if available • Use of clean fuel if available • Green belt will be developed with specific species to help to reduce PM level • Use of equipment fitted with silencers • Proper maintenance of equipment • Provision of noise shields near the heavy construction operations and acoustic enclosures for DG sets Construction activity will be limited to day time hours only	Not significant	Regular monitoring of emissions and control measures will be taken to reduce the emission levels.

S. No.	Environmental components	Potential Impacts	Potential Source of Impact	Controls Through EMP & Design	Impact Evaluation	Preventive Measures
5.	Noise Environment		<u>Operation Phase</u> - Noise from vehicular movement - Noise from DG sets operation	Green Belt Development shall make a barrier both for noise and air pollution.	No significant impact due to 10m. width of Greenbelt.	Use of Personal Protective Equipment (PPE) like earmuffs and earplugs during construction activities
6.	Land Environment	Soil contamination	<u>Construction Phase</u> Disposal of construction debris	Construction debris will be collected and suitably used on site.	No significant impact. Impact will be local, as waste generated will be reused for filling of low lying areas etc.	--
			<u>Operation Phase</u> Dumping of municipal solid waste on land.	It is proposed that the solid waste generated will be managed by an authorized agency. Collection, segregation, transportation and disposal will be done as per Solid Waste Management Rules, 2016 by the authorized agency Organic waste converter	Since solid waste is handled by the authorized agency, waste dumping is not going to be allowed. Not significant. Negligible impact.	--

S. No.	Environmental components	Potential Impacts	Potential Source of Impact	Controls Through EMP & Design	Impact Evaluation	Preventive Measures
				will be installed.		
7.	Biological Environment (Flora and Fauna)	Displacement of Flora and Fauna on site	<u>Construction Phase</u> Site Development during construction No tree at the site.	Additional tree will be planted as part of the green belt development.	The site has no tree.	
			<u>Operation Phase</u> Increase in green cover	Green belts will be developed as per landscaping plan in and around the site using local flora	Beneficial impact.	
8.	Socio-Economic Environment	Employment and livelihood options.	<u>Construction Phase</u> Construction activities leading to gain in direct & indirect employment	Project development as per the Building bye laws.	No negative impact. 400 employment will be generated.	
			<u>Operation Phase</u>	Project will provide employment opportunities to the local people in terms of labor during	Beneficial impact	

S. No.	Environmental components	Potential Impacts	Potential Source of Impact	Controls Through EMP & Design	Impact Evaluation	Preventive Measures
			Site operation	construction and service personnel (staff, securities, gardeners etc.) during operations Providing quality-Integrated facility in Ghaziabad		
9.	Traffic Pattern	Increase of Vehicular traffic	<u>Operation Phase</u> Site operation	Internal Traffic management plan	Beneficial impact	
			<u>Operation Phase</u> Traffic due to people.	Vehicular movement will be regulated inside the project with adequate roads and parking lots in the site.	No major significant impact	

TABLE 2: EMP FOR DUST SUPPRESSION

Sources/Process	Emission Potential	Scope of Control	Effectiveness
Hydraulic excavators and loaders (e.g. Front loader, backhoe face shovel bulldozers) for the excavation, lifting and movement of material such as Soil, overburden.	High when dry or fine silty material are being handled, particularly during strong windy weather	Use of water sprays to moisten material being handled. Soils may be subject to a soil moisture content planning condition	Moderate
	Low when coarse or wet material are being handled during conditions of low wind speed	Minimize drop heights when unloading material. Protect from exposure to wind where possible.	
Tractor scrapers (Soil strippers) for cutting, lifting transporting and placing, spreading or shaping of soils	Moderate/High-when dry silty materials handled during windy weather	Use of water sprays to moisten material being handled.	Low
Vehicles for transport of material within the site.	High particularly when travelling over unsurfaced and dry site roads.	Minimize onsite transportation distances.	High
		Use of water sprays to moisten road surfaces during dry weather.	
		Use mechanical road sweepers during dry weather, to limit visible dust emissions. Restrict vehicle speeds through signage/staff training.	
		Use of covered conveyors to transport material around the site.	
Hydraulic breakers for size reduction of large rocks	Low	Water spraying of rock prior to fragmentation when high degree of control required.	Moderate
Exhausts and cooling fans on mobile plant	High if unmitigated.	Mobile plant exhausts and cooling fans will discharge	Moderate

Sources/Process	Emission Potential	Scope of Control	Effectiveness
processing quarried material.		above the horizontal to prevent dust mobilization.	
Conveyors for transporting material	Moderate if not protected from wind	Enclosure of transfer points (including roofing) of conveyors.	High
		Wind boarding.	High
	Moderate/High for dry or fine silty materials, particularly during strong wind weather	Water spraying of surfaces of material on conveyor.	High/Moderate
		Cleaning belts with scrapers and collecting scrapings in container.	Moderate
Stockpiles for storage of quarried materials and soil/overburden during extraction and site development phases.	High when dry or fine silty materials are being stored /handled particularly during strong weather.	Seed surfaces of completed mounds of overburden and top soil (restoration materials).	High
		Limit mechanical disturbance.	
		Shield from wind e.g. through the use of tree planting or screening	
		Use of water sprays to moisten surfaces during dry weather.	Moderate

ENVIRONMENTAL MONITORING

The purpose of environmental monitoring is to evaluate the effectiveness of implementation of Environmental Management Plan (EMP) by periodic monitoring. The important environmental parameters within the impact area are selected so that any adverse affects are detected and time action can be taken. The project proponent will monitor ambient air Quality, Ground Water Quality and Quantity, and Soil Quality in accordance with an approved monitoring schedule mentioned in **Table 3**.

Table 3: Environmental Monitoring Schedule for Compliance

S. No	Particulars	Monitoring Frequency	Duration of Sampling	Important Monitoring Parameters
1	Ambient Air Quality Monitoring			
	Project site	Once in 6 Months	24 hr continuously except CO (8 hourly)	PM ₁₀ , PM _{2.5} , SO ₂ , NO ₂ & CO
3	Ambient Noise Level			
	Near DG set	Once in 6 Months	8 hr continuous with 1 hr interval	Noise level in dB(A)
4	Ground/Drinking Water Quality Monitoring			
	Ground Water – (If applicable)	Once in 6 Months	Grab Sampling	Parameters specified under IS:10500, 2012
5	Soil Quality			
	At the green belt area	Twice in a year	Samples will be collected from three different depths viz., 30cm, 60cm, and 100cm below the surface	Parameter for soil quality: pH, texture, electrical conductivity, organic matter, nitrogen, phosphate, sodium, calcium, potassium and Magnesium.

Annexure-XV

Receiving of Previous Compliance Report of December, 2020



Ascenso Enviro <eia.ascenso@amcgroup.co.in>

Submission of six-monthly Compliance Report for December 2020 of the Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana by M/s. Asthetic Township Developers Pvt. Ltd.

Ascenso Enviro <eia.ascenso@amcgroup.co.in>

Wed, Dec 2, 2020 at 5:37 PM

To: ronz.chd-mef@nic.in

Cc: seiaa.hry@gmail.com, hspcb@hry.nic.in, hspcbho@gmail.com, ascensobackup@gmail.com

Reference: F.No.21-137 /2018-IA-111, dated : 07/02/2019

Respected Sir,

This is with reference to above-mentioned subject, we are herewith submitting six monthly compliance report of **December 2020** for the period of **April 2020 – September 2020** for the Expansion of Commercial Complex Project at Sushant Lok, Sector-27, Gurugram Haryana by M/s. Asthetic Township Developers Pvt. Ltd. along with the necessary annexure for your kind perusal.

We understand that the above is in line with requirement of Ministry of Environment & Forest and Climate Change, GOI.

Thanking you,

Yours Sincerely,

For M/s Asthetic Township Developers Pvt. Ltd.


(Authorized Signatory)



December 2020 EC Compliance Report of Aesthetic township developers (Bharti).pdf

19581K

Annexure-XVI
RMC Purchase Bill

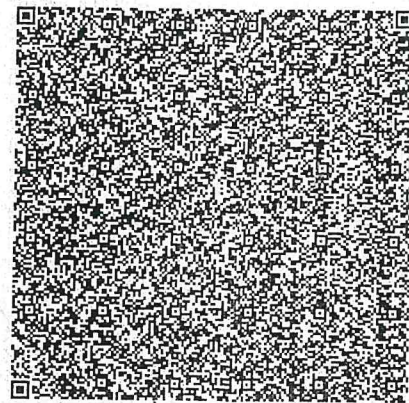

Name of the Plant: :RP-GURGAON-I, DELHI / 4336
 Address of the Plant :PLOT NO./KH.NO.-1527/916/2/2, 1528/916/2/3, REVENUE
 ESTATE VILLAGE,
 GURGAON 06-HARYANA 122001
 PAN No. :AAAACL4159L
 GSTIN. :06AAACL4159L1ZC
 CIN :U26940MH1999PLC118229
 Principal P.O.B :CHIDIYA, CHARKHI DADRI, BHIWANI, 06-HARYANA - 123306.
 CIN

TAX INVOICE

Tax Invoice Number :200710021972
 Date & Time :30.10.2020 15:13:00
 Dispatch Mode :BY ROAD
 Receipt Voucher No. :
 Receipt Voucher Date :
 Reverse Charge :
 Customer Code :50000947
 Name of Customer :S.S.CONSTRUCTION CO.
 Address of Customer :RAMKRISHAN HOUSE, NEAR MLA TEJPAL
 TANWAR KOTHI VILL
 PO BADSHAPUR GURGAON 06-HARYANA
 122101
 Sales Type :FOR - FREE ON ROAD
 Sales Order No. :0130193669/SO/4336
 Customer PO / DATE :WO-19/10-20/07.10.2020
 Name of Transporter :
 Reference Number :2007019596
 Ewaybill Number :381250925317
 Job Site Code :0021845913
 Name of Job Site :BHARTI REALTY
 State Code :06
 Address of Job Site :ASTHETIC TOWNSHIP DEVELOPE
 P.LTD NR.IFFCO CHOWK
 SEC-27,GURUGRAM GURUGRAM
 06-HARYANA 122002
 BCMIX No. :433691564170
 State Code :06
 PAN No. :AEFPS1460P
 EMAIL ID. :vishalgupta@gmail.com
 GSTIN No. :06AEFPS1460P1Z3
 Contact Name :VIPIN CHAUHAN
 Telephone Number :9719919797
 Mobile Number :9719919797
 Email ID :suriconstructions@yahoo.com
 Pump Serial No. :

Name of Product :RMC HSN/SAC :38245010

Exemption Notification if any :
 POURING LOCATION :Walls/Columns/Slab/Foundation/Other
 Sales Person's Name :
 Sales Person's Contact No. :

Sl. No	Description	Vehicle No.	Qty.	UOM	Grade	Delivery Type	Material Code	Old Mat. Co
1	M30 CUST AE MO D20 M	HR56B1105	7.000	M3	M30	HiredPump	9000034429	CCMGFE2BH30

Price Elements	Rate	Amount
Basic Price/Taxable Value	4,375.00	30,625.00
SGST @ 9 %	393.75	2,756.25
IGST @ 9 %	393.75	2,756.25
206C(1H) Goods @ 0.08 %	3.87	27.10
Rounding		0.40
Total Gross Value of Goods - In Figures	5,166.37	36,165.00

Total Gross Value of Goods - In Words THIRTY SIX THOUSAND ONE HUNDRED SIXTY FIVE RUPEES ONLY

ASTHETIC TOWNSHIP DEVELOPERS PVT. LTD.

2172
 30/10/20
 16:20
 Vehicle NO. HR56B1105
 Received by SMM

For NUVOCO VISTAS CORP. LTD.

Authorized Signatory

SPECIFIED TARGET SLUM	W/O	MAX. AGG.	CHEM. ADM.	MIN. ADM.	MIN. CEMENT	CEMENT TYPE
JOBSITE ARRIVAL TIME	JOB POURING START TIME	JOB POURING END TIME	JOBSITE DEPARTURE TIME	PLANT ARRIVAL TIME		

Received the above items in Good condition.

Customer Name, Signature & Seal

IRN : 187124e92937b58b81911d639d21bf3df1f7912402444c95e3df04a4c119658d

ACC Limited

ACC Limited RMX-Gurgaon 2

Tehsil Badshahpur

Village Badshahpur,

Dist. Gurugram, Haryana 122001

Supplying State Code : 06 Supplying State : Haryana

GSTIN : 06AAACT1507C1Z1

Order No. : acccl



Invoice Serial No: NS2P062001002498

Invoice Date : 29.10.2020

Delivery No. & Date: 1210275645 29.10.2020

Sale Order No.: 1001075447

Ticket No:- 2013805374

Whether the tax is payable on reverse charge basis No

Place of Supply(Incase of interstate

Phone No:

Fax No:

SAP Ref No: NS2P / / 2020 / CO / ZN3R / 1701931096


Sold To Party: 9110157501 Mob: 9719919797

Ship to Party: 9112126637 Mob: 9719919797

S S Construction Co
Ramkrishan House, Near MLA Tejpal Tanwar Kothi GURGAON
Vill Ramgarh PO Badshapur - 122001
State:Haryana State Code 06
GSTIN / UID: 06AEFPS1460P1Z3

S S Construction Co
Bharti Realty C/o Asthetic Township Developers Pvt Ltd.
Near IFFCO Chowk metro Station - 122001
Destination:
State:Haryana State Code:06
GSTIN / UID:

Designation of Goods	HSN Code	Qty	UOM	Rate	Particulars	Amount(Rs)
M30	38245010	6.000	M3	4,575.00	Basic	27,450.00



Taxable Value of Supply of Goods		27,450.00
SGST @	9.00 %	2,470.50
CGST @	9.00 %	2,470.50
Invoice Value		32,391.00
TCS @	0.075 %	24.29
Total Invoice value		32,415.29

Invoice value in words: Thirty Two Thousand Four Hundred Fifteen Rupees Twenty Nine Paise Only

Mob. Transport: Road	LR/RR No.:	Eway Bill No:
Transporter Code: 916003132	LR/RR Date:	Eway Bill Date & Time:
Transporter Name:PARAS ENTERPRISES		
Vehicle Reg.No: PB03BD2820		

Remarks: Any complaints relating to this delivery need to be logged within 24 hours at customercare.rm@acclimited.com. HEALTH AND SAFETY CAUTION: Wet concrete can cause serious burns to your skin. Avoid direct contact with your skin. Wash the affected skin thoroughly with water immediately in case of contact.

Terms & Condition:

- Our responsibility ceases the moment consignment is delivered to you/your carrier.
- Payment should be made by "A/C Payee only" - bank draft/cheque in favour of ACC Ltd.
- Payments received beyond agreed credit period will attract an interest @ 24% per annum.
- Goods once sold will not be taken back & all disputes are subject to Mumbai jurisdiction.
- ACC reserves the right to effect changes in concrete mix design with or without prior intimation to customer due to change in incoming raw material properties and weather conditions.
- All payments towards supplies are payable at Mumbai.
- In order to further improve upon our impeccable Corporate Governance record, ACC Board has instituted a Fraud Risk Management Policy. In case you come across any unethical behaviour of our employees, kindly contact us at: E-mail: acc@ethicalview.com or National toll free No.: 1800 209 2008 or Fax No.: +91 (22) 6645 9575 Post Box No.137, Pun 411 001. Information so received will be kept strictly confidential.

Material received in Good Condition & in Quantity	(Receiver's Signature with seal)	(Prepared by)	For ACC Limited	(Authorised Signatory)
---	----------------------------------	---------------	-----------------	------------------------

Sales unit: ACC Limited Harayana Sales Unit RMX-FARIDABAD, 20.4 kms, Sarai Khwaja Chowk, Faridabad 121001 Tel:

Reg. Office Address - ACC Limited, "CEMENT HOUSE", 121, M. K. ROAD, MUMBAI-400020. www.acclimited.com

ADITYA BIRLA



DELIVERY CHALLAN

Unit Address:-

 Unit: UltraTech Cement
 GURGAON-122001 HARYANA

UltraTech
CONCRETE
 WE MAKE GOOD CONCRETE BET

GSTIN: 06AAACL6442L1ZE

CIN No: L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No:

Recipient PO Date: 25/11/2020

 Name & Address of Recipient
 S.S. CONSTRUCTION CO.
 RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR,
 KOTHIVILL RAMGARH PO BADSHAPUR,
 GURUGRAM 122001

 Name & Address of Delivery
 S.S. CONSTRUCTION CO. (SEC-27)
 BHARTI REALTY C/O ASTHETIC TOWNSHIP I
 NR. IFFCO CHOWK METRO STATION SEC-27,
 GURUGRAM 122001

 Delivery Challan No: 201046849
 Delivery Challan Date: 25/11/2020
 Order No: 6532360
 Order Qty: 12.00
 Cum Qty: 3.50
 HSN Code: 3824 50 10
 Plant Code: 847

 Place of Supply: GURGAON CITY
 State Code: 06
 Recipient GSTN/UIN No: 06AEFPS1460P1Z3

 State Code: 06
 State: HARYANA

Description of Goods: M7.5 CUSTOMER SPECIFIED CONCRETE

Date & Time of Removal of Goods: 25/11/2020 17:53:51

Transporter Details:

 Transporter Name:
 Vehical No: HR55AE7491
 Mode of Transport: By Road
 Pump Descp:
 Destination:

 LR No:
 LR Date: 25/11/2020
 Pump Qty:
 Inco Term: FOR

DriverMobNo9728912459

Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (In Rs.)
Basic	3.50	M3	3575.00	12512.5
CGST @ 9.00%				1126.1
SGST @ 9.00%				1126.1
Round Off				0.2
Total Invoice Value:				14765.0

 Tax Amount in Words:- Two Thousand Two Hundred Fifty-Two Rupees and Twenty-Four Paise
 Invoice Amount in Word:- Fourteen Thousand Seven Hundred Sixty-Five Rupees and Zero Paise

I/We hereby declare that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

Checked By

We hereby confirm that we have received above referred material in good condition

Date:

 Signature Name & Mobile No of Person/Party
 Who receiving the material with ruber stamp

 Cement Type:
 Min Cem Content: OPC
 Max Size Aggr: 20MM
 Slump at Site

 Chemical Admix Type: ADMSPLAST
 Mineral Admix Type: FLYASHR
 Slump Specified:
 Water Added at Site:

 Batching Time: 17:53:08
 Pour Structure:
 Max W/C Ratio: 0.58
 Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017.

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA10MM	465.00	-0.50	462.68	1619.38	1626.00	0.41
CA20MM	697.00	-0.50	693.52	2427.32	2398.00	-1.21
FACS	744.00	0.00	744.00	2604.00	2565.00	-1.50
CEMOPC	105.00	0.00	105.00	367.50	364.00	-0.95
FLYASHR	195.00	0.00	195.00	682.50	679.00	-0.51
ADMSPLAST	1.50	0.00 kg	1.50	5.25	5.24	-0.19
WATERR	175.00	5.81 kg	180.81	632.84	632.00	-0.13
TOTAL	2382.50		2382.51	8338.79	8269.24	-0.83

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT BE RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

ASTHETIC TOWNSHIP DEVELOPERS PVT. LTD.

Gate Entry No. 2439

Date 25/11/2020

Time 19:10

Vehicle No. HR55AE 7491

Received by [Signature]



DELIVERY CHALLAN

Unit Address:-

UltraTech Cement
38 Milestone, Behrampur Road, Khandsa
Gurgaon - 122001 Haryana

GSTIN : 06AAACL6442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No:

Recipient PO Date: 25/11/2020

Name & Address of Recipient
S.S. CONSTRUCTION CO.
RAMKRISHNA HOUSE NEAR MLA TEJPALTANWAR,
KOTHIVILLI RAMGARH PO BADSHAPUR,
GURUGRAM 122001

Place of Supply: GURGAON CITY
State Code: 06
Recipient GSTIN/IN No: 06AEFPS1460P1Z3

Name & Address of Delivery
S.S. CONSTRUCTION CO.(SEC-27)
BHARTI REALTY C/O ASTHETIC TOWNSHIP C
NR. IFFCO CHOWK METRO STATION SEC-27,
GURUGRAM 122001

State Code: 06
State: HARYANA

Delivery Challan No: 205272047
Delivery Challan Date: 25/11/2020
Order No: 6532192
Order Qty: 28.00
Cum Qty: 14.00
HSN Code: 38245010
Plant Code: 825

Description of Goods: M30 ULTRATECH PLUS CONCRETE

Date & Time of Removal of Goods: 25/11/2020 02:18:05

Transporter Details:

Transporter Name: HR55AF4722
Vehicle No: HR55AF4722
Mode of Transport: By Road
Pump Descp: Line Pump
Destination: Inco Term: FOR
Driver Name: Pawan
Mob No: 7061950817

LR No:
LR Date: 25/11/2020
Pump Qty:
Inco Term: FOR

Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (in Rs.)
Basic	7.00	M3	4750.00	33250.00
CGST @ 9.00%				2992.50
SGST @ 9.00%				2992.50
Round Off				0.00
Total Invoice Value:				39235.00

Amount in Words:- Five Thousand Nine Hundred Eighty-Five Rupees and Zero Paise
The Amount in Word:- Thirty-Nine Thousand Two Hundred Thirty-Five Rupees and Zero Paise

Certified that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

ULTRATECH CEMENT LIMITED

Gurgaon - IV - Khandsa

Checked By

Authorised Signatory

We hereby confirmed that we have received above referred material in good condition

Date:

Signature Name & Mobile No of Person/Party
Who receiving the material with ruber stamp

Cement Type: OPC
Min Cem Content: 20MM
Max Size Aggr: 20MM
Slump at Site

Chemical Admix Type: ADMHYPLAST
Mineral Admix Type: FLYASHR
Slump Specified: 120+-25
Water Added at Site:

Batching Time: 02:14:08
Pour Structure:
Max W/C Ratio: 0.41
Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA20MM	650.00	-0.50	646.73	4527.11	4533.30	0.14
FACS	775.00	0.00	775.00	5425.00	5413.00	-0.22
CA10MM	440.00	-0.50	437.79	3064.53	3099.15	1.13
CEMOPC	300.00	0.00	300.00	2100.00	2101.35	0.06
FLYASHR	100.00	0.00	100.00	700.00	699.45	-0.08
ADMHYPLAST	2.40	-0.40 kg	2.00	14.00	14.18	1.29
WATERR	165.00	5.48 kg	170.48	1193.36	1193.90	0.05
TOTAL	2432.40		2432.00	17024.00	17054.33	0.18

1.CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2.WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3.If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4.Once Goods are loaded in vehicle the Goods will not be taken back.

2047

25/11/20

2187



DELIVERY CHALLAN

Unit Address:- UltraTech Cement
38 Milestone, Behrampur Road, Khandas
Gurgaon - 122001 Haryana



GSTIN : 06AAACL6442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No:

Recipient PO Date: 25/11/2020

Name & Address of Recipient
S.S. CONSTRUCTION CO.
RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR,
KOTHIVILL RAMGARH PO BADSHAPUR,
GURUGRAM 122001

Name & Address of Delivery
S.S. CONSTRUCTION CO. (SEC-27)
BHARTI REALTY C/O ASTHETIC TOWNSHIP E
NR. IFFCO CHOWK METRO STATION SEC-27,
GURUGRAM 122001

Delivery Challan No: 205272044
Delivery Challan Date: 25/11/2020
Order No: 6532192
Order Qty: 28.00
Cum Qty: 7.00
HSN Code: 38245010
Plant Code: 825

Place of Supply: GURGAON CITY
State Code: 06
Recipient GSTIN/UIN No: 06AEFPS1460P123

State Code: 06
State: HARYANA

Description of Goods: M30 ULTRATECH PLUS CONCRETE

Date & Time of Removal of Goods: 25/11/2020 01:18:12

Transporter Details:

Transporter Name: PALUCK TECHNOLOGIES PVT LTD
Vehical No: HR55AF0597
Mode of Transport: By Road
Pump Descp: Line Pump
Destination: GURUGRAM
Driver Mob No: 9267912764

Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (In Rs.)
Basic	7.00	M3	4750.00	33250.00
CGST @ 9.00%				2992.50
SGST @ 9.00%				2992.50
Round Off				0.00
Total Invoice Value:				39235.00

Tax Amount in Words:- Five Thousand Nine Hundred Eighty-Five Rupees and Zero Paise
Net Amount in Words:- Thirty-Nine Thousand Two Hundred Thirty-Five Rupees and Zero Paise

Certified that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

FOR ULTRATECH CEMENT LIMITED

Gurgaon - V - Khandas

Checked By

Authorised Signatory

We hereby confirmed that we have received above referred material in good condition

Date:

Signature Name & Mobile No of Person/Party
Who receiving the material with rubber stamp

Cement Type: OPC
Min Cem Content: 20MM
Max Size Aggr: 20MM
Slump at Site

Chemical Admix Type: ADMHYPLAST
Mineral Admix Type: FLYASHR
Slump Specifide: 120+-25
Water Added at Site:

Batching Time: 01:16:41
Pour Structure:
Max W/C Ratio: 0.41
Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA20MM	650.00	-0.50	646.73	4527.11	4530.50	0.08
FACS	775.00	-0.36	772.22	5405.55	5402.30	-0.06
CA10MM	440.00	-0.50	437.79	3064.53	3093.75	0.95
CEMOPC	300.00	0.00	300.00	2100.00	2107.10	0.34
FLYASHR	100.00	0.00	100.00	700.00	708.05	1.15
ADMHYPLAST	2.40	-0.40 kg	2.00	14.00	14.22	1.60
WATERR	165.00	8.26 kg	173.26	1212.81	1212.85	0.00
TOTAL	2432.40		2432.00	-17024.00	17068.77	0.26

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

25/11/20

2044

25/11/20

02102


 EWB No.341254945814
 EWB Exp.11/11/2020 16:24:00

DELIVERY CHALLAN

UltraTech
CONCRETE
 WE MAKE GOOD CONCRETE BETTER

Unit Address:-

 UltraTech Cement
 38 Milestone, Behrampur Road, Khandasa
 Gurgaon - 122001 Haryana

GSTIN : 06AAACL6442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No:

Recipient PO Date: 10/11/2020

Name & Address of Recipient

Name & Address of Delivery

 S.S. CONSTRUCTION CO.
 RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR,
 KOTHIVILL RAMGARH PO BADSHAPUR,
 GURUGRAM 122001

 S.S. CONSTRUCTION CO. (SEC-27)
 BHARTI REALTY C/O ASTHETIC TOWNSHIP C
 NR. IFFCO CHOWK METRO STATION SEC-27,
 GURUGRAM 122001

 Delivery Challan No: 205271540
 Delivery Challan Date: 10/11/2020
 Order No: 6529648
 Order Qty: 21.00
 Cum Qty: 14.00
 HSN Code: 38245010
 Plant Code: 825

Place of Supply: GURGAON CITY

State Code: 06

Recipient GSTN/UIN No: 06AEFPS1460P1Z3

State Code: 06

State: HARYANA

Description of Goods: M60-HIGH STRENGTH CONCRETE

Date & Time of Removal of Goods: 10/11/2020 16:22:06

Transporter Details:

 Transporter Name: PALUCK TECHNOLOGIES PVT LTD
 Vehical No: HR55AB1823
 Mode of Transport: By Road
 Pump Descp: Line Pump
 Destination:

 LR No:
 LR Date: 10/11/2020
 Pump Qty:
 Inco Term: FOR

Driver Name: MABECH Mob No: 9555715970

Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (in Rs.)
Basic	7.00	M3	6800.00	47600.00
CGST @ 9.00%				4284.00
SGST @ 9.00%				4284.00
Round Off				0.00
Total Invoice Value:				56168.00

 Tax Amount In Words:- Eight Thousand Five Hundred Sixty-Eight Rupees and Zero Paise
 Invoice Amount In Word:- Fifty-Six Thousand One Hundred Sixty-Eight Rupees and Zero Paise

I declare that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For: ULTRATECH CEMENT LIMITED

Gurgaon - IV - Khandasa

Checked By:

Authorized Signatory

We hereby confirmed that we have received above referred material in good condition

Date:

Signature Name & Mobile No of Person/Party Who receiving the material with rubber stamp

 Cement Type:
 Min Cem Content: OPC
 Max Size Aggr: 20MM
 Slump at Site

 Chemical Admix Type: ADMHYPLAST
 Mineral Admix Type: FLYASHR
 Slump Specified: 600+/-50
 Water Added at Site:

 Batching Time: 16:20:48
 Pour Structure:
 Max W/C Ratio: 0.26
 Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017

Raw Material	Design Qty(Kg)	%Mois/%Abs/CoRR(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA20MM	188.00	-0.50	187.05	1309.36	1341.15	2.43
FACS	709.00	-1.50	698.21	4887.44	4894.70	0.15
CA10MM	688.00	-0.50	684.54	4791.76	4783.60	-0.17
CEMOPC	450.00	0.00	450.00	3150.00	3154.00	0.13
MSILICA	35.00	0.00	34.99	244.96	245.00	0.02
FLYASHR	160.00	0.00	160.00	1120.00	1123.25	0.29
ADMHYPLAST	5.10	0.00 kg	5.10	35.70	35.74	0.10
WATERR	165.00	15.19 kg	180.19	1261.36	1261.25	-0.01
TOTAL	2400.10		2400.08	16800.58	16838.69	0.23

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT BE RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

 SNO. 1640
 16/11/20


 EWB No.341254860559
 EWB Exp.11/11/2020 14:01:00

DELIVERY CHALLAN

Unit Address:-

 UltraTech Cement
 38 Milestone, Behrampur Road, Khandasa
 Gurgaon - 122001 Haryana


GSTIN : 06AAACL6442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No:

Recipient PO Date: 10/11/2020

Name & Address of Recipient

Name & Address of Delivery

 S.S. CONSTRUCTION CO.
 RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR,
 KOTHIVILL RAMGARH PO BADSHAPUR,
 GURUGRAM 122001

 S.S. CONSTRUCTION CO. (SEC-27)
 BHARTI REALTY C/O ASTHETIC TOWNSHIP I
 NR. IFFCO CHOWK METRO STATION SEC-27,
 GURUGRAM 122001

 Delivery Challan No: 205271534
 Delivery Challan Date: 10/11/2020
 Order No: 6529648
 Order Qty: 21.00
 Cum Qty: 7.00
 HSN Code: 38245010
 Plant Code: 825

 Place of Supply: GURGAON CITY
 State Code: 06
 Recipient GSTN/UIN No: 06AEFPS1460P123

 State Code: 06
 State: HARYANA

Description of Goods: M60 -HIGH STRENGTH CONCRETE

Date & Time of Removal of Goods: 10/11/2020 13:55:38

Transporter Details:

 Transporter Name:
 Vehical No: HR55AF4722
 Mode of Transport: By Road
 Pump Descp: Line Pump
 Destination:
 Driver Name: MURESH Mob No: 7317066385

 LR No:
 LR Date: 10/11/2020
 Pump Qty:
 Inco Term: FOR

Particulars	Quantity	UOM	Rate Per Unit (Im Rs.)	Amount (in Rs.)
Basic	7.00	M3	6800.00	47600.00
CGST @ 9.00%				4284.00
SGST @ 9.00%				4284.00
Round Off				0.00
Total Invoice Value:				56168.00

 Tax Amount In Words:- Eight Thousand Five Hundred Sixty-Eight Rupees and Zero Paise
 Invoice Amount in Word:- Fifty-Six Thousand One Hundred Sixty-Eight Rupees and Zero Paise

I certify that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Gurgaon - IV - Khandasa

Checked By

Authorised Signatory

We hereby confirmed that we have received above referred material in good condition

Date:

 Cement Type:
 Min Cem Content: OPC
 Max Size Aggr: 20MM
 Slump at Site

 Chemical Admix Type: ADMHYPLAST
 Mineral Admix Type: FLYASHR
 Slump Specified: 600+/-50
 Water Added at Site:

 Signature Name & Mobile No of Person/Party
 Who receiving the material with ruber stamp

 Batching Time: 13:53:39
 Pour Structure:
 Max W/C Ratio: 0.26
 Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA20MM	188.00	-0.50	187.05	1309.36	1317.10	0.59
FACS	709.00	-1.00	701.84	4912.88	4905.05	-0.16
CA10MM	688.00	-0.50	684.54	4791.76	4788.70	-0.06
CEMOPC	450.00	0.00	450.00	3150.00	3149.75	-0.01
MSILICA	35.00	0.00	34.99	244.96	245.25	0.12
FLYASHR	160.00	0.00	160.00	1120.00	1125.15	0.46
ADMHYPLAST	5.10	0.13 kg	5.23	36.58	36.61	0.07
WATERR	165.00	11.56 kg	176.56	1235.92	1235.55	-0.03
TOTAL	2400.10		2400.21	16801.46	16803.16	0.01

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

(A Joint Declaration)

 1534 10/11/20
 1417

ADITYA BIRLA



DELIVERY CHALLAN

Unit Address:-

 UltraTech Cement
 Unit: UltraTech Concrete, 38 Milestone Behrampur Road, Khandsa Ch
 GURGAON-122001 HARYANA


GSTIN : 06AAACL6442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No:

Recipient PO Date: 07/11/2020

Name & Address of Recipient

 S.S. CONSTRUCTION CO.
 RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR,
 KOTHIVILL RAMGARH PO BADSHAPUR,
 GURUGRAM 122001

Name & Address of Delivery

 S.S. CONSTRUCTION CO. (SEC-27)
 BHARTI REALTY C/O ASTHETIC TOWNSHIP I
 NR. IFFCO CHOWK METRO STATION SEC-27,
 GURUGRAM 122001

 Place of Supply: GURGAON CITY
 State Code: 06
 Recipient GSTN/UIN No: 06AEFPS1460P1Z3

 State Code: 06
 State: HARYANA

 Delivery Challan No: 201046459
 Delivery Challan Date: 07/11/2020
 Order No: 6529021
 Order Qty: 21.00
 Cum Qty: 7.00
 HSN Code: 3824 50 10
 Plant Code: 847

Description of Goods: M7.5 CUSTOMER SPECIFIED CONCRETE

Date & Time of Removal of Goods: 07/11/2020 15:12:02

Transporter Details:

 Transporter Name:
 Vehical No: HR56B9546
 Mode of Transport: By Road
 Pump Descp: Line Pump
 Destination:
 Driver Mob No: 9599632095

 LR No:
 LR Date: 07/11/2020
 Pump Qty:
 Inco Term: FOR

Particulars	Quantity	UOM	Rate Per Unit (in Rs.)	Amount (in Rs.)
Basic	7.00	M3	3575.00	25025.00
CGST @ 9.00%				2252.25
SGST @ 9.00%				2252.25
Round Off				0.50
Total Invoice Value:				29530.00

 Four Thousand Five Hundred Four Rupees and Fifty Paise
 Twenty-Nine Thousand Five Hundred Thirty Rupees and Zero Paise

I hereby certify that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Unit: Khandsa

Checked By

Gate Entry No. 2315

Date: 7/11/2020

We hereby confirmed that we have received above referred material in good condition

Vehicle No. HR56B9546

Received by

Date:

 Signature Name & Mobile No of Person/Party
 Who receiving the material with ruber stamp

 Cement Type:
 Min Cem Content: OPC
 Max Size Aggr: 20MM
 Slump at Site

 Chemical Admix Type: ADMSPLAST
 Mineral Admix Type: FLYASHR
 Slump Specified: 120+25
 Water Added at Site:

 Batching Time: 15:10:41
 Pour Structure:
 Max W/C Ratio: 0.58
 Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 201

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA10MM	465.00	-0.50	462.68	3238.76	3249.00	0.32
CA20MM	697.00	-0.50	693.52	4854.64	4833.00	-0.45
FACS	744.00	-1.50	732.84	5129.88	5115.00	-0.29
CEMOPC	105.00	0.00	105.00	735.00	735.00	0.00
FLYASHR	195.00	0.00	195.00	1365.00	1362.00	-0.22
ADMSPLAST	1.50	0.30 kg	1.80	12.60	12.45	-1.19
WATERR	175.00	16.97 kg	191.97	1343.79	1343.00	-0.06
TOTAL	2382.50		2382.81	16679.67	16649.45	-0.18

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

ADITYA BIRLA



DELIVERY CHALLAN

Unit Address:-

UltraTech Cement
38 Milestone, Behrampur Road, Khandas
Gurgaon - 122001 Haryana

GSTIN: 06AAACL6442L1ZE

CIN No: L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No:

Recipient PO Date: 07/11/2020

Name & Address of Recipient

S.S. CONSTRUCTION CO.
RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR,
KOTHIVILL RAMGARH PO BADSHAPUR,
GURUGRAM 122001

Name & Address of Delivery

S.S. CONSTRUCTION CO. (SEC-27)
BHARTI REALTY C/O ASTHETIC TOWNSHIP C
NR. IFFCO CHOWK METRO STATION SEC-27,
GURUGRAM 122001

Delivery Challan No: 205271394

Delivery Challan Date: 07/11/2020

Order No: 6529012

Order Qty: 28.00

Cum Qty: 7.00

HSN Code: 3824 50 10

Plant Code: 825

Place of Supply: GURGAON CITY

State Code: 06

Recipient GSTN/UIN No: 06AEFPS1460P123

State Code: 06

State: HARYANA

Description of Goods: M7.5 CUSTOMER SPECIFIED CONCRETE

Date & Time of Removal of Goods: 07/11/2020 14:12:50

Transporter Details:

Transporter Name: PALUCK TECHNOLOGIES PVT LTD

Vehical No: HR55AF6801

Mode of Transport: By Road

Pump Descp: Line Pump

Destination: Mob No 8447021610

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Driver Name: JITENDER

Particulars	Quantity	UOM	Rate Per Unit (Im Rs.)	Amount (in Rs.)
Basic	7.00	M3	3575.00	25025.00
CGST @ 9.00%				2252.25
SGST @ 9.00%				2252.25
Round Off				0.50
Total Invoice Value:				29530.00

Amount in Words:- Four Thousand Five Hundred Four Rupees and Fifty Paise
 Amount in Word:- Twenty-Nine Thousand Five Hundred Thirty Rupees and Zero Paise

Certified that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Unit: Gurgaon - IV - Khandas

Checked By

Gate Entry No. 2311

Date 7/11/20

Time 15:12:00

Authorized Signatory

We hereby confirmed that we have received above referred material in good condition.

Received by

Date:

Signature Name & Mobile No of Person/Party
Who receiving the material with rubber stamp

Cement Type: OPC
 Min Cem Content: 20MM
 Max Size Aggr: 20MM
 Slump at Site

Chemical Admix Type: ADMSPLAST
 Mineral Admix Type: FLYASHR
 Slump Specifide: 120+25
 Water Added at Site:

Batching Time: 14:09:42
 Pour Structure:
 Max W/C Ratio: 0.58
 Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA20MM	697.00	-0.50	693.50	4854.50	4866.60	0.25
FACS	744.00	-1.50	732.67	5128.69	5127.10	-0.03
CA10MM	465.00	-0.50	462.66	3238.62	3261.50	0.71
CEMOPC	105.00	0.00	105.00	735.00	735.75	0.10
FLYASHR	195.00	0.00	195.00	1365.00	1370.75	0.42
ADMSPLAST	1.50	0.40 kg	1.90	13.30	13.30	-0.02
WATERR	175.00	17.17 kg	192.17	1345.19	1343.35	-0.14
TOTAL	2382.50		2382.90	16680.30	16718.35	0.23

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT BE RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

UltraTech Cement Ltd.
 (A Unit of UltraTech Concrete.)

SNO 394 7/11/20

14304

ADITYA BIRLA



DELIVERY CHALLAN

Unit Address:-

 UltraTech Cement
 38 Milestone, Behrampur Road, Khandas
 Gurgaon - 122001 Haryana


GSTIN : 06AAACL6442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No:

Recipient PO Date: 21/11/2020

 Name & Address of Recipient
 S.S. CONSTRUCTION CO.
 RAMKRISHAN HOUSE NEAR MLA TEJALTANWAR,
 KOTHIVILL RAMGARH PO BADSHAPUR,
 GURUGRAM 122001

 Name & Address of Delivery
 S.S. CONSTRUCTION CO. (SEC-27)
 BHARTI REALTY C/O ASTHETIC TOWNSHIP I
 NR. IFFCO CHOWK METRO STATION SEC-27,
 GURUGRAM 122001

 Delivery Challan No: 205271861
 Delivery Challan Date: 21/11/2020
 Order No: 6531348
 Order Qty: 48.00
 Cum. Qty: 28.00
 HSN Code: 3824 50 10
 Plant Code: 825

 Place of Supply: GURGAON CITY
 State Code: 06
 Recipient GSTN/UIN No: 06AEFPS1460P123

 State Code: 06
 State: HARYANA

Description of Goods: M 40 ULTRATECH PLUS

Date & Time of Removal of Goods: 21/11/2020 14:46:24

Transporter Details:

 Transporter Name:
 Vehical No: HR55AF4722
 Mode of Transport: By Road
 Pump Descp: Line Pump
 Destination:

 LR No:
 LR Date: 21/11/2020
 Pump Qty:
 Inco Term: FOR

Driver Name: JITENDER Mob No: 7317066385

Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (In Rs.)
Basic	7.00	M3	5100.00	35700.00
CGST @ 9.00%				3213.00
SGST @ 9.00%				3213.00
Round Off				0.00
Total Invoice Value:				42126.00

 Tax Amount In Words:- Six Thousand Four Hundred Twenty-Six Rupees and Zero Paise
 Tax Amount In Words:- Forty-Two Thousand One Hundred Twenty-Six Rupees and Zero Paise

Certified that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Gurgaon - IV - Khandas

Checked By

Authorised Signatory

We hereby confirmed that we have received above referred material in good condition

Date:

 Signature Name & Mobile No of Person/Party
 Who receiving the material with rubber stamp

 Cement Type:
 Min Cem Content: OPC
 Max Size Aggr: 20MM
 Slump at Site

 Chemical Admix Type: ADMHYPLAST
 Mineral Admix Type: FLYASHR
 Slump Specified:
 Water Added at Site:

 Batching Time: 14:44:55
 Pour Structure:
 Max W/C Ratio: 0.35
 Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017.

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA20MM	669.00	-0.50	665.64	4659.48	4659.15	-0.01
FACS	746.00	-1.00	738.46	5169.22	5158.40	-0.21
CA10MM	446.00	-0.50	443.76	3106.32	3119.35	0.42
CEMOPC	380.00	0.00	380.00	2660.00	2657.25	-0.10
FLYASHR	80.00	0.00	80.00	560.00	558.45	-0.28
ADMHYPLAST	2.30	0.00 kg	2.30	16.10	16.15	0.28
WATER	160.00	13.14 kg	173.14	1211.98	1211.25	-0.06
TOTAL	2483.30		2483.30	17383.10	17380.00	-0.02

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT BE RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

SNO: 1861

21/11/20

15205



DELIVERY CHALLAN

Unit Address:-

UltraTech Cement
38 Milestone, Behrampur Road, Khandsa
Gurgaon - 122001 Haryana

GSTIN: 06AAACL6442L1ZE

CIN No: L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No:

Recipient PO Date: 12/11/2020

Name & Address of Recipient
S.S. CONSTRUCTION CO.
RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR,
KOTHIVILL RAMGARH PO BADSHAPUR,
GURUGRAM 122001Name & Address of Delivery
S.S. CONSTRUCTION CO. (SEC-27)
BHARTI REALTY C/O ASTHETIC TOWNSHIP C
NR. IFFCO CHOWK METRO STATION SEC-27,
GURUGRAM 122001Delivery Challan No: 205271596
Delivery Challan Date: 12/11/2020
Order No: 6530074
Order Qty: 42.00
Cum Qty: 21.00
HSN Code: 3824 50 10
Plant Code: 825Place of Supply: GURGAON CITY
State Code: 06
Recipient GSTN/UIN No: 06AEFPS1460P123State Code: 06
State: HARYANA

Description of Goods: M 40 ULTRATECH PLUS

Date & Time of Removal of Goods: 12/11/2020 11:58:45

Transporter Details:

Transporter Name: DIAMOND RMC CARRIER
Vehical No: HR55AF0597
Mode of Transport: By Road
Pump Descp: Line Pump
Destination:LR No:
LR Date: 12/11/2020
Pump Qty:
Inco Term: FOR

Driver Name: BIPIN Driver Mob No: 8076386579

Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (In Rs.)
Basic	7.00	M3	5100.00	35700.00
CGST @ 9.00%				3213.00
SGST @ 9.00%				3213.00
Round Off				0.00
Total Invoice Value:				42126.00

Tax Amount In Words:- Six Thousand Four Hundred Twenty-Six Rupees and Zero Paise

Invoice Amount In Word:- Forty-Two Thousand One Hundred Twenty-Six Rupees and Zero Paise

I Certify that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Gurgaon - IV - Khandsa

Checked by:

Authorized Signatory:

We hereby confirmed that we have received above referred material in good condition

Date:

Signature Name & Mobile No of Person/Party
Who receiving the material with rubber stampCement Type: OPC
Min Cem Content: 20MM
Max Size Aggr: 20MM
Slump at SiteChemical Admix Type: ADMHYPLAST
Mineral Admix Type: FLYASHR
Slump Specifide: 120+-25
Water Added at Site:Batching Time: 11:53:40
Pour Structure:
Max W/C Ratio: 0.35
Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA20MM	669.00	-0.50	665.64	4659.48	4658.10	-0.03
FACS	746.00	-1.50	734.64	5142.48	5129.70	-0.25
CA10MM	446.00	-0.50	443.76	3106.32	3101.65	-0.15
CEMOPC	380.00	0.00	380.00	2660.00	2662.30	0.09
FLYASHR	80.00	0.00	80.00	560.00	560.25	0.05
ADMHYPLAST	2.30	-0.36 kg	1.94	13.60	13.63	0.21
WATERR	160.00	14.82 kg	174.82	1223.72	1222.00	-0.14
TOTAL	2483.30		2480.80	17365.60	17347.63	-0.10

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT BE RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

SNO. 1596

12/11/20

12/11/20



DELIVERY CHALLAN

Unit Address:- UltraTech Cement
38 Milestone, Behrampur Road, Khandsa
Gurgaon - 122001 Haryana



GSTIN : 06AAACL6442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No:

Recipient PO Date: 30/12/2020

Name & Address of Recipient
S.S. CONSTRUCTION CO.
RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR,
KOTHIVILL RAMGARH PO BADSHAPUR,
GURUGRAM 122001

Place of Supply: GURGAON CITY
State Code: 06
Recipient GSTN/UIN No: 06AEFPS1460P1Z3

Name & Address of Delivery
S.S. CONSTRUCTION CO. (SEC-27)
BHARTI REALTY C/O ASTHETIC TOWNSHIP I
NR. IFFCO CHOWK METRO STATION SEC-27,
GURUGRAM 122001

State Code: 06
State: HARYANA

Delivery Challan No: 205273779
Delivery Challan Date: 30/12/2020
Order No: 6540110
Order Qty: 35.00
Cum Qty: 6.00
HSN Code: 38245010
Plant Code: 825

Description of Goods: M60 - HIGH STRENGTH CONCRETE

Date & Time of Removal of Goods: 30/12/2020 06:53:24

Transporter Details:

Transporter Name: DIAMOND RMC CARRIER
Vehical No: HR55AB1823
Mode of Transport: By Road
Pump Descp: Line Pump
Destination:

LR No:
LR Date: 30/12/2020
Pump Qty:
Inco Term: FOR

Driver Name: GADGE RANJAN No 9899364982

Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (in Rs.)
Basic	6.00	M3	6800.00	40800.00
CGST @ 9.00%				3672.00
SGST @ 9.00%				3672.00
Round Off				0.00
Total Invoice Value:				48144.00

Amount In Words:- Seven Thousand Three Hundred Forty-Four Rupees and Zero Paise
Price Amount in Word:- Forty-Eight Thousand One Hundred Forty-Four Rupees and Zero Paise

Certified that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Unit: Gurgaon - IV - Khandsa

Checked By

Authorised Signatory

We hereby confirmed that we have received above referred material in good condition.

Date:

Cement Type:
Min Cem Content: OPC
Max Size Aggr: 20MM
Slump at Site

Chemical Admix Type: ADMHYPLAST
Mineral Admix Type: FLYASHR
Slump Specified: 600+/-50
Water Added at Site:

Signature Name & Mobile No of Person/Party
Who receiving the material with rubber stamp

Batching Time: 06:47:56
Pour Structure:
Max W/C Ratio: 0.26
Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA20MM	188.00	-0.50	187.05	1122.31	1122.65	0.03
FACS	709.00	-0.93	702.36	4214.14	4205.00	-0.22
CA10MM	688.00	-0.50	684.54	4107.25	4098.80	-0.21
CEMOPC	450.00	0.00	450.00	2699.97	2703.70	0.14
MSILICA	35.00	0.00	35.00	210.00	210.00	0.00
FLYASHR	160.00	0.00	160.00	959.98	967.55	0.79
ADMHYPLAST	5.10	-0.40 kg	4.70	28.19	28.19	-0.02
WATERR	165.00	11.05 kg	176.05	1056.30	1056.10	-0.02
TOTAL	2400.10		2399.70	14398.14	14391.99	-0.04

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT BE RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

UltraTech Cement Ltd

(A Unit UltraTech Concrete)

SNO: 779 Date: 30/12/20

Out Time: 2:15



DELIVERY CHALLAN



Unit Address:-

UltraTech Cement
158, Naurangpur
Gurgaon - 122001 Haryana

GSTIN: 06AAACL6442L1ZE

CIN No: L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No:

Recipient PO Date: 23/12/2020

Name & Address of Recipient
S.S. CONSTRUCTION CO.
RAMKRISHAN HOUSE NEAR MLA TEJ PALTANWAR,
KOTHIVILL RAMGARH PO BADSHAPUR,
GURUGRAM 122001Name & Address of Delivery
S.S. CONSTRUCTION CO. (SEC-27)
BHARTI REALTY C/O ASTHETIC TOWNSHIP C
NR. IFFCO CHOWK METRO STATION SEC-27,
GURUGRAM 122001Delivery Challan No: 205224937
Delivery Challan Date: 23/12/2020
Order No: 6538578
Order Qty: 24.00
Cum Qty: 12.00
HSN Code: 38245010
Plant Code: 824Place of Supply: GURGAON CITY
State Code: 06
Recipient GSTN/UIN No: 06AEFPS1460P1Z3State Code: 06
State: HARYANA

Description of Goods: M60 - HIGH STRENGTH CONCRETE

Date & Time of Removal of Goods: 23/12/2020 09:33:47

Transporter Details:

Particulars	Quantity	UOM	Rate Per Unit (Im Rs.)	Amount (in Rs.)
Basic	6.00	M3	6800.00	40800.00
CGST @ 9.00%				3672.00
SGST @ 9.00%				3672.00
Round Off				0.00
Total Invoice Value:				48144.00

Transporter Name: HR56B0187
Vehical No: By Road
Mode of Transport: Line Pump
Destination: Inco Term: FOR

Driver Name: HG Driver Mob No: 9718991227

Amount in Words:- Seven Thousand Three Hundred Forty-Four Rupees and Zero Paise
Voice Amount in Word:- Forty-Eight Thousand One Hundred Forty-Four Rupees and Zero Paise

Certified that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Unit: Gurgaon - II - Navrang

Checked By

Gate Entry No. 2812

Authorised Signatory

We hereby confirmed that we have received above referred material in good condition

Vehicle No. HR 56 B 0187

Received by NAVEEN

Date:

Signature Name & Mobile No of Person/Party Who receiving the material with ruber stamp

Cement Type: OPC
Min Cem Content: 20MM
Max Size Aggr: 20MM
Slump at SiteChemical Admix Type: ADMHYPLAST
Mineral Admix Type: FLYASHR
Slump Specifide: 600+/-50
Water Added at Site:Batching Time: 09:24:27
Pour Structure:
Max W/C Ratio: 0.27
Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 201

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA20MM	188.00	-0.50	187.05	1122.31	1119.40	-0.26
FACS	709.00	-1.50	698.20	4189.22	4198.55	0.22
CA10MM	688.00	-0.50	684.54	4107.25	4090.90	-0.40
CEMOPC	450.00	0.00	450.00	2699.97	2700.95	0.04
FLYASHR	160.00	0.00	160.00	959.98	959.15	-0.09
ADMHYPLAST	5.10	-0.60 kg	4.50	27.00	26.99	-0.04
WATERR	165.00	15.20 kg	180.20	1081.22	1080.80	-0.04
TOTAL	2365.10		2364.49	14186.95	14176.74	-0.07

m. Silica = 3518/m³

Suresh

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THROUGHL WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products indetifie are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warrenty or merchantability or fitness for perticular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibillites of such damages, in no case shall UltraTech Cement Limiteds liability exceed the purchas price of this product.

3. If necessary, additional dose of admixture may be added at project site to regian the workability of concrete with the mutual agreement between the consignor a the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

ADITYA BIRLA



DELIVERY CHALLAN

UltraTech Cement Limited

Unit Address:- 158, Naurangpur Gurgaon - 122001 Haryana



GSTIN : 06AAACL6442L1ZE		CIN No : L26940MH2000PLC128420																															
Recipient Code: 40083007	Recipient PO No:	Recipient PO Date: 06/12/2020																															
Name & Address of Recipient S.S. CONSTRUCTION CO. RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR, KOTHIVILL RAMGARH PO BADSHAPUR, GURUGRAM 122001 Place of Supply: GURGAON CITY State Code: 06 Recipient GSTN/UIN No: 06AEFPS1460P1Z3		Name & Address of Delivery S.S. CONSTRUCTION CO.(SEC-27) BHARTI REALTY C/O ASTHETIC TOWNSHIP I NR. IFFCO CHOWK METRO STATION SEC-27, GURUGRAM 122001 State Code: 06 State: HARYANA																															
Description of Goods: M30 ULTRATECH PLUS CONCRETE		Date & Time of Removal of Goods: 06/12/2020 23:49:06																															
Transporter Details: Transporter Name: BANSAL CORPORATION Vehicle No: HR55AC4208 Mode of Transport: By Road Pump Descp: Line Pump Destination: Driver Name: SHAMBHAJI Driver Mob No: 9718592503		<table border="1"> <thead> <tr> <th>Particulars</th> <th>Quantity</th> <th>UOM</th> <th>Rate Per Unit (In Rs.)</th> <th>Amount (In Rs.)</th> </tr> </thead> <tbody> <tr> <td>Basic</td> <td>7.00</td> <td>M3</td> <td>4750.00</td> <td>33250.00</td> </tr> <tr> <td>CGST @ 9.00%</td> <td></td> <td></td> <td></td> <td>2992.50</td> </tr> <tr> <td>SGST @ 9.00%</td> <td></td> <td></td> <td></td> <td>2992.50</td> </tr> <tr> <td>Round Off</td> <td></td> <td></td> <td></td> <td>0.00</td> </tr> <tr> <td>Total Invoice Value:</td> <td></td> <td></td> <td></td> <td>39235.00</td> </tr> </tbody> </table>		Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (In Rs.)	Basic	7.00	M3	4750.00	33250.00	CGST @ 9.00%				2992.50	SGST @ 9.00%				2992.50	Round Off				0.00	Total Invoice Value:				39235.00
Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (In Rs.)																													
Basic	7.00	M3	4750.00	33250.00																													
CGST @ 9.00%				2992.50																													
SGST @ 9.00%				2992.50																													
Round Off				0.00																													
Total Invoice Value:				39235.00																													

Tax Amount in Words:- Five Thousand Nine Hundred Eighty-Five Rupees and Zero Paise
 Invoice Amount in Word:- Thirty-Nine Thousand Two Hundred Thirty-Five Rupees and Zero Paise

Certified that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

Checked By

We hereby confirmed that we have received above referred material in good condition

Date:

Signature Name & Mobile No of Person/Party Who receiving the material with rubber stamp

Cement Type: OPC
 Min Cem Content: 20MM
 Max Size Aggr: 20MM
 Slump at Site

Chemical Admix Type: ADMHYPLAST
 Mineral Admix Type: FLYASHR
 Slump Specified: 120+25
 Water Added at Site:

Batching Time: 23:46:54
 Pour Structure:
 Max W/C Ratio: 0.41
 Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 20:

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA20MM	675.00	-0.50	671.61	4701.27	4709.05	0.17
FACS	752.00	-1.50	740.55	5183.85	5167.40	-0.32
CA10MM	440.00	-0.50	437.79	3064.53	3083.90	0.63
CEMOPC	300.00	0.00	300.00	2100.00	2099.85	-0.01
FLYASHR	100.00	0.00	100.00	700.00	698.55	-0.21
ADMHYPLAST	2.40	-0.20 kg	2.20	15.40	15.40	-0.01
WATERR	165.00	17.06 kg	182.06	1274.42	1276.85	0.19
TOTAL	2434.40		2434.21	17039.47	17051.00	0.07

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT BE RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.



DELIVERY CHALLAN

Unit Address:-

 UltraTech Cement
 38 Milestone, Behrampur Road, Khandsa
 Gurgaon - 122001 Haryana


GSTIN : 06AAACL6442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No:

Recipient PO Date: 07/12/2020

 Name & Address of Recipient
 S.S. CONSTRUCTION CO.
 RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR,
 KOTHIVILL RAMGARH PO BADSHAPUR,
 GURUGRAM 122001

 Name & Address of Delivery
 S.S. CONSTRUCTION CO. (SEC-27)
 BHARTI REALTY C/O ASTHETIC TOWNSHIP C
 NR. IFFCO CHOWK METRO STATION SEC-27,
 GURUGRAM 122001

 Place of Supply: GURGAON CITY
 State Code: 06
 Recipient GSTN/UIN No: 06AEFPS1460P1Z3

 State Code: 06
 State: HARYANA

 Delivery Challan No: 205272720
 Delivery Challan Date: 07/12/2020
 Order No: 6534918
 Order Qty: 12.00
 Cum Qty: 4.00
 HSN Code: 3824 50 10
 Plant Code: 825

Description of Goods: M30 ULTRATECH PLUS CONCRETE

Date & Time of Removal of Goods: 07/12/2020 06:26:41

Transporter Details:

Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (In Rs.)
Basic	4.00	M3	4750.00	19000.00

 Transporter Name: PALUCK TECHNOLOGIES PVT LTD
 Vehical No: HR55AJ4012
 Mode of Transport: By Road
 Pump Descp:
 Destination:
 LR No:
 LR Date: 07/12/2020
 Pump Qty:
 Inco Term: FOR

 CGST @ 9.00% 1710.00
 SGST @ 9.00% 1710.00
 Round Off 0.00
 Total Invoice Value: 22420.00

Driver Name: NARAYAN Mob No: 8076386579

 Tax Amount in Words:- Three Thousand Four Hundred Twenty Rupees and Zero Paise
 Invoice Amount in Words:- Twenty-Two Thousand Four Hundred Twenty Rupees and Zero Paise

Certified that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Unit: Gurgaon - IV - Khand

ASTHETIC TOWNSHIP DEVELOPERS PVT. LTD.

Gate Entry No. 2573

Date: 07/12/2020

Authorised Signatory

We hereby confirmed that we have received above referred material in good condition

Time: 07:30

Vehicle No. HR 55 AJ 4012

Received by: [Signature]

Date: [Signature] Signature Name & Mobile No of Person/Party Who receiving the material with rubber stamp

 Cement Type:
 Min Cem Content: OPC
 Max Size Aggr: 20MM
 Slump at Site

 Chemical Admix Type: ADMHYPLAST
 Mineral Admix Type: FLYASHR
 Slump Specified:
 Water Added at Site:

 Batching Time: 06:24:24
 Pour Structure:
 Max W/C Ratio: 0.41
 Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 20

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA20MM	650.00	-0.50	646.73	2586.92	2579.75	-0.28
FACS	775.00	0.00	775.00	3100.00	3105.10	0.17
CA10MM	440.00	-0.50	437.79	1751.16	1784.30	1.89
CEMOPC	300.00	0.00	300.00	1200.00	1199.40	-0.05
FLYASHR	100.00	0.00	100.00	400.00	398.65	-0.34
ADMHYPLAST	2.40	-0.80 kg	1.60	6.40	6.46	0.97
WATERR	165.00	5.48 kg	170.48	681.92	682.45	0.08
TOTAL	2432.40		2431.60	9726.40	9756.11	0.31

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT BE RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

 SNO: 2720
 Date: 7/12/20
 648

ADITYA BIRLA



DELIVERY CHALLAN

Unit Address:-

Unit: UltraTech Cement
GURGAON-122001 HARYANA

GSTIN: 06AAAC16442L1ZE

Recipient Code: 40083007

CIN No: L26940MH2000PLC128420

Name & Address of Recipient
S.S. CONSTRUCTION CO.
RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR,
KOTHIVILL RAMGARH PO BADSHAPUR,
GURUGRAM 122001Name & Address of Delivery
S.S. CONSTRUCTION CO. (SEC-27)
BHARTI REALTY C/O ASTHETIC TOWNSHIP I
NR. IFFCO CHOWK METRO STATION SEC-27,
GURUGRAM 122001

Recipient PO Date: 02/12/2020

Place of Supply: GURGAON CITY
State Code: 06
Recipient GSTN/UIN No: 06AEFPS1460P1Z3State Code: 06
State: HARYANADelivery Challan No: 201047002
Delivery Challan Date: 02/12/2020
Order No: 6533958
Order Qty: 12.00
Cum Qty: 6.00
HSN Code: 3824 50 10
Plant Code: 847

Description of Goods: M7.5 CUSTOMER SPECIFIED CONCRETE

Date & Time of Removal of Goods: 02/12/2020 14:43:49

Transporter Details:

Transporter Name:
Vehical No: HR55AE4075
Mode of Transport: By Road
Pump Descp:
Destination:LR No:
LR Date: 02/12/2020
Pump Qty:
Inco Term: FOR

Driver Mob No 7409279686

Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (In Rs.)
Basic	6.00	M3	3575.00	21450.00

CGST @ 9.00%				1930.50
SGST @ 9.00%				1930.50
Round Off				0.00
Total Invoice Value:				25311.00

Amount In Words:- Three Thousand Eight Hundred Sixty-One Rupees and Zero Paise
ice Amount In Words:- Twenty-Five Thousand Three Hundred Eleven Rupees and Zero Paise

Certified that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient

For ULTRATECH CEMENT LIMITED

Unit: Khandas

Checked By

Authorised Signatory

We hereby confirmed that we have received above referred material in good condition

Date:

Signature Name & Mobile No of Person/Party
Who receiving the material with ruber stampCement Type:
Min Cem Content: OPC
Max Size Aggr: 20MM
Slump at SiteChemical Admix Type: ADMSPLAST
Mineral Admix Type: FLYASHR
Slump Specifide:
Water Added at Site:Batching Time: 14:43:09
Pour Structure:
Max W/C Ratio: 0.58
Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA10MM	465.00	-0.50	462.68	2776.08	2790.00	0.50
CA20MM	697.00	-0.50	693.52	4161.12	4128.00	-0.80
FACS	744.00	-1.50	732.84	4397.04	4367.00	-0.68
CEMOPC	105.00	0.00	105.00	630.00	630.00	0.00
FLYASHR	195.00	0.00	195.00	1170.00	1170.00	0.00
ADMSPLAST	1.50	0.20 kg	1.70	10.20	10.20	0.00
WATERR	175.00	16.97 kg	191.97	1151.82	1153.00	0.10
TOTAL	2382.50		2382.71	14296.26	14248.20	-0.34

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT BE RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application, UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.


Gate Entry No. 2523

Date 02/12/2020

Time 15:50

Vehicle No. HR55AE4075

Received by Ak Singh



Name of the Plant: :RP-GURGAON-I, DELHI / 4336
 Address of the Plant: :PLOT NO./KH.NO.-1527/916/2/2,1528/916/2/3,REVENUE
 ESTATE VILLAGE,
 GURGAON 06-HARYANA 122001
 AN No. :AAACL4159L
 STIN. :06AAACL4159L1ZC
 IN :U26940MH1999PLC118229
 Principal P.O.B :CHIDIYA, CHARKHI DADRI, BHIWANI, 06-HARYANA - 123306.
 CIN

TAX INVOICE

Tax Invoice Number :200710032940
 Date & Time :09.01.2021 15:20:00
 Dispatch Mode :BY ROAD
 Receipt Voucher No. :
 Receipt Voucher Date :
 Reverse Charge :
 Sales Type :FOR - FREE ON ROAD
 Sales Order No. :0130199332/SO/4336
 Customer PO / DATE :01/21/07.01.2021
 Name of Transporter :
 Reference Number :2007030079
 Ewaybill Number :361274433548
 Customer Code :50000947
 Name of Customer :S.S.CONSTRUCTION CO.
 Address of Customer :RAMKRISHAN HOUSE, NEAR MLA TEJPAL
 TANWAR KOTHI VILL
 PO BADSHAPUR GURGAON 06-HARYANA
 122101
 Job Site Code :0021845913
 Name of Job Site :BHARTI REALTY
 State Code :06
 Address of Job Site :ASTHETIC TOWNSHIP DEVELOPER
 P.LTD NR.IFFCO CHOWK
 SEC-27,GURUGRAM GURUGRAM
 06-HARYANA 122002
 CMIX No. :433691565020
 State Code :06
 AN No. :AEFPS1460P
 GSTIN No. :06AEFPS1460P1Z3
 Contact Name :VIPIN CHAUHAN
 Telephone Number :9719919797
 Mobile Number :9719919797
 Email ID :suriconstructions@yahoo.com
 Pump Serial No. :
 MAIL ID. :vishalgupta@gmail.com
 Name of Product :RMC
 HSN/SAC :38245010
 Exemption Notification if any :
 Sales Person's Name :
 Sales Person's Contact No. :
 :Walls/Columns/Slab/Foundation/Other

POURING LOCATION

S. No.	Description	Vehicle No.	Qty.	UOM	Grade	Delivery Type	Material Code	Old Mat. Code
1	M35 SP AE MO D20 M0070	HR55AG309	6.000	M3	M35	HiredPump	9000039314	CSPHFF2BI300

Price Elements	Rate	Amount
Basic Price/Taxable Value	5,000.00	30,000.00
GST @ 9 %	450.00	2,700.00
GST @ 9 %	450.00	2,700.00
206C(1H) Goods @ 0.08 %	4.43	26.55
Rounding		0.45
Total Gross Value of Goods - In Figures	5,904.43	35,427.00

Total Gross Value of Goods - In Words THIRTY FIVE THOUSAND FOUR HUNDRED TWENTY SEVEN RUPEES ONLY

ASTHETIC TOWNSHIP DEVELOPERS PVT. LTD.
 Gate Entry No. 3033
 Date 09.01.2021
 Time 16:10
 Vehicle No. HR55AG309
 Received by 3097

For NUVOCO VISTAS CORP. LTD.

Authorized Signatory

SPECIFIED TARGET SLUM	W/O	MAX. AGG.	CHEM. ADM.	MIN. ADM.	MIN. CEMENT	CEMENT TYPE
JOBSITE ARRIVAL TIME	JOB POURING START TIME	JOB POURING END TIME	JOBSITE DEPARTURE TIME	PLANT ARRIVAL TIME		

Received the above items in Good condition.

Customer Name, Signature & Seal

ADITYA BIRLA



DELIVERY CHALLAN

Unit Address:-

 UltraTech Cement
 38 Milestone, Behrampur Road, Khandasa
 Gurgaon - 122001 Haryana

UltraTech
CONCRETE
 WE MAKE GOOD CONCRETE BETTER.

GSTIN : 06AAACL6442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No:

Recipient PO Date: 16/01/2021

Name & Address of Recipient

 S.S. CONSTRUCTION CO.
 RAMKRISHAN HOUSE NEAR MLA TEJ PALTANWAR,
 KOTHIVILL RAMGARH PO BADSHAPUR,
 GURUGRAM 122001

Place of Supply: GURGAON CITY

State Code: 06

Recipient GSTN/UIN No: 06AEFSP1460P123

Name & Address of Delivery

 S.S. CONSTRUCTION CO. (SEC-27)
 BHARTI REALTY C/O ASTHETIC TOWNSHIP E
 NR. IFFCO CHOWK METRO STATION SEC-27,
 GURUGRAM 122001

State Code: 06

State: HARYANA

 Delivery Challan No: 205274462
 Delivery Challan Date: 16/01/2021
 Order No: 6544180
 Order Qty: 70.00
 Cum Qty: 14.00
 HSN Code: 3824 50 10
 Plant Code: 825

Description of Goods: M35 CUSTOMER SPECIFIED CONCRETE

Date & Time of Removal of Goods: 16/01/2021 16:40:20

Transporter Details:

Transporter Name:

Vehical No: HR55AJ4012

Mode of Transport: By Road

Pump Descp: Line Pump

Destination:

LR No:

LR Date:

Pump Qty:

Inco Term:

16/01/2021

FOR

Driver Name: NARAYAN Mob No: 9582766151

Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (in Rs.)
Basic	7.00	M3	5000.00	35000.00
CGST @ 9.00%				3150.00
SGST @ 9.00%				3150.00
Round Off				0.00
Total Invoice Value:				41300.00

Tax Amount In Words:- Six Thousand Three Hundred Rupees and Zero Paise

Price Amount In Word:- Forty-One Thousand Three Hundred Rupees and Zero Paise

I certify that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Unit: Gurgaon - IV - Khandasa R

Checked By

Authorised Signatory

We hereby confirmed that we have received above referred material in good condition

Date:

 Signature Name & Mobile No of Person/Party
 Who receiving the material with ruber stamp

Cement Type:

Min Cem Content: OPC

Max Size Aggr: 20MM

Slump at Site

Chemical Admix Type:

Mineral Admix Type:

Slump Specified:

Water Added at Site:

ADMHYPLAST

FLYASHR

120+-25

Batching Time: 16:37:32

Pour Structure:

Max W/C Ratio: 0.37

Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA20MM	685.00	-0.50	681.56	4770.92	4773.75	0.06
FACS	680.00	-1.50	669.64	4687.48	4675.55	-0.26
CA10MM	435.00	-0.50	432.81	3029.67	3033.05	0.11
CEMOPC	350.00	0.00	350.00	2450.00	2449.35	-0.03
FLYASHR	110.00	0.00	110.00	770.00	771.80	0.23
ADMHYPLAST	2.50	0.00 kg	2.50	17.50	17.73	1.29
WATERR	170.00	15.98 kg	185.98	1301.86	1301.90	0.00
TOTAL	2432.50		2432.49	17027.43	17023.13	-0.03

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

 UltraTech Cement Ltd.
 (A Unit UltraTech Concrete)

S. No. 4462 Date: 16/01/21

Cut Time: 16:56 In Time:



DELIVERY CHALLAN

UltraTech Cement Limited

Unit Address:-158, Naurangpur Gurgaon - 122001 Haryana



GSTIN : 06AAACL6442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No:

Recipient PO Date: 10/01/2021

Name & Address of Recipient

S.S. CONSTRUCTION CO.
RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR,
KOTHIVILL RAMGARH PO BADSHAPUR,
GURUGRAM 122001

Place of Supply: GURGAON CITY

State Code: 06

Recipient GSTN/UIN No: 06AEFPS1460P1Z3

Name & Address of Delivery

S.S. CONSTRUCTION CO. (SEC-27)
BHARTI REALTY C/O ASTHETIC TOWNSHIP I
NR. IFFCO CHOWK METRO STATION SEC-27,
GURUGRAM 122001

State Code: 06

State: HARYANA

Delivery Challan No: 205225660
Delivery Challan Date: 10/01/2021
Order No: 6542692
Order Qty: 18.00
Cum Qty: 6.00
HSN Code: 38245010
Plant Code: 824

Description of Goods: M60 -HIGH STRENGTH CONCRETE

Date & Time of Removal of Goods: 10/01/2021 12:32:52

Transporter Details:

Transporter Name: BANSAL CORPORATION

Vehical No: MH04JK3820

Mode of Transport: By Road

Pump Descp: Line Pump

Destination:

Driver Name: MNNJH Driver Mob No: 9718991227

LR No:

LR Date: 10/01/2021

Pump Qty:

Inco Term: FOR

Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (in Rs.)
Basic	6.00	M3	6800.00	40800.00
CGST @ 9.00%				3672.00
SGST @ 9.00%				3672.00
Round Off				0.00
Total Invoice Value				48144.00

Tax Amount In Words:- Seven Thousand Three Hundred Forty-Four Rupees and Zero Paise

Invoice Amount In Words:- Forty-Eight Thousand One Hundred Forty-Four Rupees and Zero Paise

Confirmed that the particulars given above are true & correct & the amount indicated represents the
actually charged and there is no flow of any additional consideration directly or indirectly from
the recipient.

For ULTRATECH CEMENT LIMITED

Unit: Gurgaon - II - Navrangpur

Checked By

Authorised Signatory

We hereby confirmed that we have received above referred material in good condition

Date:

Signature Name & Mobile No of Person/Party
Who receiving the material with ruber stamp

Cement Type:

Min Cem Content: OPC

Max Size Aggr: 20MM

Slump at Site

Chemical Admix Type:

Mineral Admix Type:

Slump Specified:

Water Added at Site:

ADMHYPLAST

FLYASHR

600+/-50

Batching Time: 12:30:35

Pour Structure:

Max W/C Ratio: 0.27

Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA20MM	188.00	-0.50	187.05	1122.31	1128.35	0.54
FACS	709.00	-0.50	705.44	4232.62	4219.45	-0.31
CA10MM	688.00	-0.50	684.54	4107.25	4116.30	0.22
CEMOPC	450.00	0.00	450.00	2699.97	2698.35	-0.06
FLYASHR	160.00	0.00	160.00	959.98	959.15	-0.09
ADMHYPLAST	5.10	0.41 kg	5.51	33.05	33.01	-0.13
WATERR	165.00	7.97 kg	172.97	1037.82	1037.75	-0.01
TOTAL	2365.10		2365.51	14193.00	14192.36	0.00

m. Silica = 35 kg/m3




1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT BE RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

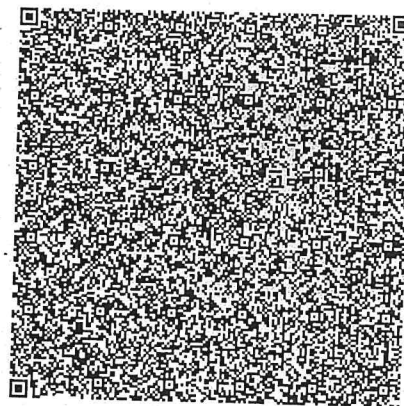

Name of the Plant: :RP-GURGAON-I, DELHI / 4336
 Address of the Plant :PLOT NO./KH.NO.-1527/916/2/2,1528/916/2/3,REVENUE
 ESTATE VILLAGE,
 GURGAON 06-HARYANA 122001
 PAN No. :AAACL4159L
 GSTIN. :06AAACL4159L1ZC
 CIN :U26940MH1999PLC118229
 Principal P.O.B :CHIDIYA, CHARKHI DADRI, BHIWANI, 06-HARYANA - 123306.
 CIN :06
 State Name :Haryana

TAX INVOICE

Tax Invoice Number :200710035153
 Date & Time :21.01.2021 10:31:00
 Dispatch Mode :BY ROAD
 Receipt Voucher No. :
 Receipt Voucher Date :
 Reverse Charge :

Sales Type :FOR - FREE ON ROAD
 Sales Order No. :0130200126/SO/4336
 Customer PO / DATE :01/21/07.01.2021
 Name of Transporter :
 Reference Number :2007032268
 Ewaybill Number :301278414103

Customer Code :50000947
 Name of Customer :S.S.CONSTRUCTION CO.
 SATISH SURI
 Address of Customer :RAMKRISHAN HOUSE, NEAR MLA TEJPAL
 TANWAR KOTHI VILL
 PO BADSHAPUR GURGAON 06-HARYANA
 122101

Job Site Code :0021845913
 Name of Job Site :BHARTI REALTY
 State Code :06
 Address of Job Site :ASTHETIC TOWNSHIP DEVELOPER
 P.LTD NR.IFFCO CHOWK
 SEC-27,GURUGRAM GURUGRAM
 06-HARYANA 122002

CMIX No. :433691565303
 State Code :06
 PAN No. :AEFPS1460P
 MAIL ID. :vishalgupta@gmail.com

GSTIN No. :06AEFPS1460P1Z3
 Contact Name :VIPIN CHAUHAN
 Telephone Number :9719919797
 Mobile Number :9719919797
 Email ID :suriconstructions@yahoo.com
 Pump Serial No. :

Name of Product :RMC
 HSN/SAC :38245010

Exemption Notification if any :
 DURING LOCATION :Walls/Columns/Slab/Foundation/Other
 Sales Person's Name :
 Sales Person's Contact No. :

Description	Vehicle No.	Qty.	UOM	Grade	Delivery Type	Material Code	Old Mat. Code
M60 ROBUSTE AE MO D20 M0055	HR56B0968	6.000	M3	M60	JustDelivery	9000039809	CMHMF2BF360

Price Elements	Rate	Amount
Basic Price/Taxable Value	6,700.00	40,200.00
ST @ 9 %	603.00	3,618.00
ST @ 9 %	603.00	3,618.00
2 (1H) Goods @ 0.08 %	5.93	35.58
undling		0.42
Total Gross Value of Goods - In Figures	7,911.93	47,472.00
Total Gross Value of Goods - In Words	FORTY SEVEN THOUSAND FOUR HUNDRED SEVENTY TWO RUPEES ONLY	

ASTHETIC TOWNSHIP DEVELOPERS PVT. LTD.

Gate Entry No. :H099

Date :21.01.21

Time :11:55

Vehicle No. :HR56B0968

Received by :SUKHVI'S SINGH

For NUVOCO VISTAS CORP. LTD.

Authorized Signatory

SPECIFIED TARGET SLUM	W/O	MAX. AGG.	CHEM. ADM.	MIN. ADM.	MIN. CEMENT	CEMENT TYPE
JOBSITE ARRIVAL TIME	JOB POURING START TIME	JOB POURING END TIME	JOBSITE DEPARTURE TIME	PLANT ARRIVAL TIME		

Received the above items in Good condition.

Customer Name, Signature & Seal



DELIVERY CHALLAN

Unit Address:- UltraTech Cement Limited
Ultratech cement Ltd, unit Ultratech concrete 38th milesto
Gurugram-122001 Haryana



GSTIN : 06AAACL6442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No:

Recipient PO Date: 09/01/2021

Name & Address of Recipient
S.S. CONSTRUCTION CO.
RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR,
KOTHIVILL RAMGARH PO BADSHAPUR,
GURUGRAM-122001

Name & Address of Delivery
S.S. CONSTRUCTION CO.(SEC-27)
BHARTI REALTY C/O ASTHETIC TOWNSHIP I
NR. IFFCO CHOWK METRO STATION SEC-27,
GURUGRAM-122001

Delivery Challan No: 205059538
Delivery Challan Date: 09/01/2021
Order No: 6542339
Order Qty: 12.00
Cum Qty: 8.00
HSN Code: 38245010
Plant Code: 852

Place of Supply: GURGAON CITY
State Code: 06
Recipient GSTN/UIN No: 06AEFPS1460P1Z3

State Code: 06
State: HARYANA

Description of Goods: M30 ULTRATECH PLUS CONCRETE

Date & Time of Removal of Goods: 09/01/2021 03:46:19

Transporter Details:

Transporter Name:
Vehical No: HR55AG6467
Mode of Transport: By Road
Pump Descp:
Destination:
Driver Name: SANDIP SINGH
Mob No: 9458619344

LR No:
LR Date: 09/01/2021
Pump Qty:
Inco Term: FOR

Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (In Rs.)
Basic	4.00	M3	4850.00	19400.00
CGST @ 9.00%				1746.00
SGST @ 9.00%				1746.00
Round Off				0.00
Total Invoice Value:				22892.00

Amount In Words:- Three Thousand Four Hundred Ninety-Two Rupees and Zero Paise

Invoice Amount in Word:- Twenty-Two Thousand Eight Hundred Ninety-Two Rupees and Zero Paise

Certified that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Unit: SOHNA ROAD

Checked By

M. Singh
Authorised Signatory

We hereby confirmed that we have received above referred material in good condition

Date:

Signature Name & Mobile No of
Person/Party Who receiving the material
with ruber stamp

Cement Type:
Min Cem Content: OPC
Max Size Aggr: 20MM
Slump at Site

Chemical Admix Type: ADMHYPLAST
Mineral Admix Type: FLYASHR
Slump Specifide:
Water Added at Site:

Batching Time: 03:40:24
Pour Structure:
Max W/C Ratio: 0.41
Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017

ASTHETIC TOWNSHIP DEVELOPERS FVT. LTD.

Gate Entry No. 3030

Date 09/01/21

Time 05:40

Vehicle No. HR55AG6467

Received by *M. Singh*

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

DELIVERY CHALLAN

UltraTech Cement
38 Milestone, Behrampur Road, Khandas
Gurgaon - 122001 Haryana

UltraTech
CONCRETE
WE MAKE GOOD CONCRETE BETTER



Unit Address:-

ESTIN : 06AAACL6442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No:

Recipient PO Date: 24/01/2021

Name & Address of Recipient
S.S. CONSTRUCTION CO.
RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR,
KOTHIVILL RAMGARH PO BADSHAPUR,
GURUGRAM 122001

Name & Address of Delivery
S.S. CONSTRUCTION CO. (SEC-27)
BHARTI REALTY C/O ASTHETIC TOWNSHIP C
NR. IFFCO CHOWK METRO STATION SEC-27,
GURUGRAM 122001

Delivery Challan No: 205274807
Delivery Challan Date: 24/01/2021
Order No: 6546242
Order Qty: 12.00
Cum Qty: 4.50
HSN Code: 3824 50 10
Plant Code: 825

Place of Supply: GURGAON CITY
State Code: 06
Recipient GSTN/UIN No: 06AEFPS1460P1Z3

State Code: 06
State: HARYANA

Description of Goods: M30 ULTRATECH PLUS CONCRETE

Date & Time of Removal of Goods: 24/01/2021 18:19:57

Transporter Details:

Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (In Rs.)
Basic	4.50	M3	4850.00	21825.00

Transporter Name: DIAMOND RMC CARRIER
Vehicle No: HR56B2260
Mode of Transport: By Road
Pump Descp:
Destination:

LR No:
LR Date: 24/01/2021
Pump Qty:
Inco Term: FOR

CGST @ 9.00% 1964.25
SGST @ 9.00% 1964.25

Driver Name: SHIVAN Mob No: 8269777390

Round Off 0.50
Total Invoice Value: 25754.00

Three Thousand Nine Hundred Twenty-Eight Rupees and Fifty Paise
Twenty-Five Thousand Seven Hundred Fifty-Four Rupees and Zero Paise

Certified that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Unit: Gurgaon - IV - Khandas

ASTHETIC TOWNSHIP DEVELOPERS PVT. LTD.

Gate Entry No. 1162

Date 24/01/21

Authorised Signatory

We hereby confirmed that we have received above referred material in good condition

Vehicle No. 1913 HR56B-2260

Received by Pk Singh

Date:

Signature Name & Mobile No of Person/Party
Who receiving the material with ruber stamp

Cement Type:
Min Cem Content: OPC
Max Size Aggr: 20MM
Slump at Site

Chemical Admix Type: ADMHYPLAST
Mineral Admix Type: FLYASHR
Slump Specifide:
Water Added at Site:

Batching Time: 18:19:01
Pour Structure:
Max W/C Ratio: 0.41
Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA20MM	650.00	-0.50	646.73	2910.30	2901.60	-0.30
FACS	775.00	-2.00	759.19	3416.35	3411.25	-0.15
CA10MM	440.00	-0.50	437.79	1970.05	1968.90	-0.06
CEMOPC	300.00	0.00	300.00	1350.00	1350.35	0.03
FLYASHR	100.00	0.00	100.00	450.00	452.00	0.44
ADMHYPLAST	2.40	-0.80 kg	1.60	7.20	7.29	1.29
WATERR	165.00	21.29 kg	186.29	838.30	838.25	-0.01
TOTAL	2432.40		2431.60	10942.20	10929.64	-0.11

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.


3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

UltraTech Cement Limited
(A Unit of UltraTech Concrete)
Khandas

S No 4807 Date 24/01/21

Out Time 18:35



Name of the Plant: :RP-GURGAON-I, DELHI / 4336
 Address of the Plant :PLOT NO./KH.NO.-1527/916/2/2,1528/916/2/3,REVENUE
 ESTATE VILLAGE,
 GURGAON 06-HARYANA 122001
 PAN No. :AAACL4159L
 GSTIN. :06AAACL4159L1ZC State Code :06
 CIN :U26940MH1999PLC118229 State Name :Haryana
 RN : 567b04f6fe57160afeadb8d3334730c5bd6df928a350ac3015075c5225afe2f0
 Principal P.O.B :CHIDIYA, CHARKHI DADRI, BHIWANI, 06-HARYANA - 123306.
 CIN

TAX INVOICE

Tax Invoice Number	:200710041767	Sales Type	:FOR - FREE ON ROAD
Date & Time	:22.02.2021 16:45:00	Sales Order No.	:0130202275/SO/4336
Dispatch Mode	:BY ROAD	Customer PO / DATE	:37/02/21/08.02.2021
Receipt Voucher No.	:	Name of Transporter	:
Receipt Voucher Date	:	Reference Number	:2007038557
Reverse Charge	:	Ewaybill Number	:361290176052
Customer Code	:50000947	Job Site Code	:0021845913
Name of Customer	:S.S.CONSTRUCTION CO. SATISH SURI	Name of Job Site	:BHARTI REALTY
Address of Customer	:RAMKRISHAN HOUSE, NEAR MLA TEJPAL TANWAR KOTHI VILL PO BADSHAPUR GURGAON 06-HARYANA 122101	State Code	:06
		Address of Job Site	:ASTHETIC TOWNSHIP DEVELOPER P.LTD NR.IFFCO CHOWK SEC-27,GURUGRAM GURUGRAM 06-HARYANA 122002
CMIX No.	:433691566159	GSTIN No.	:06AEFPS1460P1Z3
State Code	:06	Contact Name	:VIPIN CHAUHAN
PAN No.	:AEFPS1460P	Telephone Number	:9719919797
MAIL ID.	:vishalgupta@gmail.com	Mobile Number	:9719919797
		Email ID	:suriconstructions@yahoo.com
		Ump Serial No.	:

Name of Product :RMC HSN/SAC :38245010

Exemption Notification if any :Walls/Columns/Slab/Foundation/Other
 Sales Person's Name :
 Sales Person's Contact No. :

DESCRIPTION	Vehicle No.	Qty.	UOM	Grade	Delivery Type	Material Code	Old Mat. Code
M35 SP AE MO D20 M0070	HR56B3148	7.000	M3	M35	HiredPump	9000039314	CSPHFF2BI300

Price Elements	Rate	Amount
Basic Price/Taxable Value	4,850.00	33,950.00
GST @ 9 %	436.50	3,055.50
20 (IH) Goods @ 0.08 %	436.50	3,055.50
Freight	4.29	30.05
Total Gross Value of Goods - In Figures	5,727.29	40,091.00

Total Gross Value of Goods - In Words FORTY THOUSAND NINETY ONE RUPEES ONLY

Entry No. : 4646
 Date : 22/02/21
 Time : 18:00
 No. : HR56B3148
 Issued by : P. S. Singh

For NUVOCO VISTAS CORP. LTD.

Authorized Signatory

SPECIFIED TARGET SLUM	W/O	MAX. AGG.	CHEM. ADM.	MIN. ADM.	MIN. CEMENT	CEMENT TYPE
JOBSITE ARRIVAL TIME	JOB POURING START TIME	JOB POURING END TIME	JOBSITE DEPARTURE TIME	PLANT ARRIVAL TIME		

Received the above items in Good condition.

Customer Name, Signature & Seal

DELIVERY CHALLAN

UltraTech Cement

Unit Address:-

158, Naurangpur
Gurgaon - 122001 Haryana

UltraTech
CONCRETE
 WE MAKE GOOD CONCRETE BETTER.

GSTIN : 06AAAC16442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No:

Recipient PO Date: 27/02/2021

Name & Address of Recipient

S.S. CONSTRUCTION CO.
RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR,
KOTHIVILL RAMGARH PO BADSHAPUR,
GURUGRAM 122001

Place of Supply: GURGAON CITY

State Code: 06

Recipient GSTN/UIN No: 06AEFPS1460P123

Name & Address of Delivery

S.S. CONSTRUCTION CO.(SEC-27)
BHARTI REALTY C/O ASTHETIC TOWNSHIP I
NR. IFFCO CHOWK METRO STATION SEC-27,
GURUGRAM 122001

State Code: 06

State: HARYANA

 Delivery Challan No: 205227798
 Delivery Challan Date: 27/02/2021
 Order No: 6555403
 Order Qty: 42.00
 Cum Qty: 28.00
 HSN Code: 3824 50 10
 Plant Code: 824

Description of Goods: M35 CUSTOMER SPECIFIED CONCRETE

Date & Time of Removal of Goods:

27/02/2021 15:10:00

Transporter Details:

Transporter Name: BANSAL CORPORATION

Vehical No: HR56B0187

Mode of Transport: By Road

Pump Descp: Line Pump

Destination:

LR No:

LR Date:

Pump Qty:

Inco Term: FOR

27/02/2021

DriverName DILIP

DriverMob No 8565451252

Particulars	Quantity	UOM	Rate Per Unit (Im Rs.)	Amount (in Rs.)
Basic	7.00	M3	4850.00	33950.00
CGST @ 9.00%				3055.50
SGST @ 9.00%				3055.50
Round Off				0.00
Total Invoice Value:				40061.00

 Tax Amount In Words:- Six Thousand One Hundred Eleven Rupees and Zero Paise
 Invoice Amount in Word:- Forty Thousand Sixty-One Rupees and Zero Paise

Certified that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Unit:

Gurgaon - II - Navrangpur

Checked By

Date Entry No. 4740

Authorised Signatory

We hereby confirmed that we have received above referred material in good condition.

Date:

Time

Vehicle No.

Received by

Signature Name & Mobile No of Person/Party
Who receiving the material with ruber stamp

Cement Type:

Min Cem Content: OPC

Max Size Aggr: 20MM

Slump at Site

Chemical Admix Type:

Mineral Admix Type:

Slump Specifide:

Water Added at Site:

ADMHYPLAST

FLYASHR

120+-25

Batching Time: 15:07:18

Pour Structure:

Max W/C Ratio: 0.37

Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA20MM	685.00	-0.50	681.56	4770.92	4754.25	-0.35
FACS	685.00	0.00	685.00	4795.00	4777.45	-0.37
CA10MM	435.00	-0.50	432.81	3029.67	3055.40	0.85
CEMOPC	350.00	0.00	350.00	2450.00	2452.50	0.10
FLYASHR	110.00	0.00	110.00	770.00	767.55	-0.32
ADMHYPLAST	3.68	-1.94 kg	1.74	12.18	12.28	0.85
WATERR	170.00	5.62 kg	175.62	1229.34	1229.60	0.02
TOTAL	2438.68		2436.73	17057.11	17049.03	-0.05

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.


2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

ORIGINAL - FOR BUYER

NUVOCO VISTAS CORP. LTD.



Name of the Plant: :RP-GURGAON-I, DELHI / 4336
 Address of the Plant :PLOT NO./KH.NO.-1527/916/2/2,1528/916/2/3,REVE. IUE
 ESTATE VILLAGE,
 GURGAON 06-HARYANA 122001
 PAN No. :AAACL4159L
 GSTIN. :06AAACL4159L1ZC State Code :06
 CIN :U26940MH1999PLC118229 State Name :Haryana
 IRN : 0aa2282e91f5df7a1938c32801a3859b3a2ad7bc92829d8201b589106664c600
 Principal P.O.B :CHIDIYA, CHARKHI DADRI, BHIWANI, 06-HARYANA - 123306.
 CIN

TAX INVOICE

Tax Invoice Number	:200710041749	Sales Type	:FOR - FREE ON ROAD
Date & Time	:22.02.2021 15:15:00	Sales Order No.	:0130203477/SO/4336
Dispatch Mode	:BY ROAD	Customer PO / DATE	:37/02/21//08.02.2021
Receipt Voucher No.	:	Name of Transporter	:
Receipt Voucher Date	:	Reference Number	:2007038541
Reverse Charge	:	Ewaybill Number	:331290116877

Customer Code	:50000947	Job Site Code	:0021845913
Name of Customer	:S.S.CONSTRUCTION CO. SATISH SURI	Name of Job Site	:BHARTI REALTY
Address of Customer	:RAMKRISHAN HOUSE, NEAR MLA TEJPAL TANWAR KOTHI VILL PO BADSHAPUR GURGAON 06-HARYANA 122101	State Code	:06
		Address of Job Site	:ASTHETIC TOWNSHIP DEVELO P.LTD NR.IFFCO CHOWK SEC-27,GURUGRAM GURUGRA 06-HARYANA 122002

BCMIX No.	:433691566158	GSTIN No.	:06AEFPS1460P1Z3
State Code	:06	Contact Name	:VIPIN CHAUHAN
PAN No.	:AEFPS1460P	Telephone Number	:9719919797
		Mobile Number	:9719919797
		Email ID	:suriconstructions@yahoo.com
EMAIL ID.	:vishalgupta@gmail.com	Pump Serial No.	:

Name of Product :RMC HSN/SAC :38245010

Exemption Notification if any : Sales Person's Name :
 Sales Person's Contact No. :

POURING LOCATION : Walls/Columns/Slab/Foundation/Other

Sl. No.	Description	Vehicle No.	Qty.	UOM	Rate	Delivery Type	Material Code	Old Mat. C
1	M60 ROBUSTE AE MO D20 M0055	HR56B7505	6.000	M3	M60	JustDelivery	9000039810	CMHMF2BF

Price Elements	Rate	Amount
Basic Price/Taxable Value	6,650.00	39,900.00
SGST @ 9 %	598.50	3,591.00
CGST @ 9 %	598.50	3,591.00
206C(1H) Goods @ 0.08 %	5.89	35.31
Rounding		0.31
Total Gross Value of Goods - In Figures	7,852.89	47,117.00

Total Gross Value of Goods - In Words FORTY SEVEN THOUSAND ONE HUNDRED SEVENTEEN RUPEES ONLY

THE TOWNSHIP DEVELOPERS PVT. LTD.

Gate Entry No. 46413

22/02/21


Time 16:40

Vehicle No. HK 5613 - 9505

Received by Mesing

For NUVOCO VISTAS CORP.

Authorized Signatory


SPECIFIED TARGET SLUM	W/O	MAX. AGG.	CHEM. ADM.	MIN. ADM.	MIN. CEMENT	CEMENT
JOBSITE ARRIVAL TIME	JOB POURING START TIME	JOB POURING END TIME	JOBSITE DEPARTURE TIME	PLANT ARRIVAL TIME		
			Received the above items in Good condition.			
			Customer Name, Signature & Seal			

Regd. Off. : Equinox Business Park, Tower-3, East Wing, 4Th Floor, Off. Band. a- Kurla Complex, LBS Road, Kurla-West, Mumbai - 400 070.

ORIGINAL - FOR BUYER

NUVOCO VISTAS (ORP. LTD.

Name of the Plant: :RP-GURGAON-I, DELHI / 4336
 Address of the Plant :PLOT NO./KH.NO.-1527/916/2/2,1528/916/2/3,REVENUE
 ESTATE VILLAGE,
 GURGAON 06-HARYANA 122001
 PAN No. :AAACL4159L
 GSTIN. :06AAACL4159L1ZC State Code :06
 CIN :U26940MH1999PLC118229 State Name :Haryana
 IRN : f807c8c55d588a64e2bc020f746c2b005f105161a4031ebe6bf7559817ee1954
 Principal P.O.B :CHIDIYA, CHARKHI DADRI, BHIWANI, 06-HARYANA - 123306.
 CIN



TAX INVOICE

Tax Invoice Number	:200710041737	Sales Type	:FOR - FREE ON ROAD
Date & Time	:22.02.2021 14:06:00	Sales Order No.	:0130203477/SO/4336
Dispatch Mode	:BY ROAD	Customer PO / DATE	:37/02/21//08.02.2021
Receipt Voucher No.	:	Name of Transporter	:
Receipt Voucher Date	:	Reference Number	:2007038530
Reverse Charge	:	Ewaybill Number	:361290076749

Customer Code	:50000947	Job Site Code	:0021845913
Name of Customer	:S.S.CONSTRUCTION CO. SATISH SURI	Name of Job Site	:BHARTI REALTY
Address of Customer	:RAMKRISHAN HOUSE, NEAR MLA TEJPAL TANWAR KOTHI VILL PO BADSHAPUR GURGAON 06-HARYANA 122101	State Code	:06
		Address of Job Site	:ASTHETIC TOWNSHIP DEVELOP P.LTD NR.IFFCO CHOWK SEC-27,GURUGRAM GURUGRAM 06-HARYANA 122002

BCMIX No.	:433691566156	GSTIN No.	:06AEFPS1460P1Z3
State Code	:06	Contact Name	:VIPIN CHAUHAN
PAN No.	:AEFPS1460P	Telephone Number	:9719919797
		Mobile Number	:9719919797
EMAIL ID.	:vishalgupta@gmail.com	Email ID	:suriconstructions@yahoo.com
		Pump Serial No.	:

Name of Product :RMC HSN SAC :38245010

Exemption Notification if any

Sales Person's Name :
 Sales Person's Contact No. :

:Walls/Columns/Slab/Foundation/Other

Sl. No.	Description	Vehicle No.	Qty.	UOM	Grade	Delivery Type	Material Code	Old Mat. Co
I	M60 ROBUSTE AE MO D20 M0055	HR56B5033	6.000	M3	M60	JustDelivery	9000039810	CMHMF2BF3

Price Elements

	Rate	Amount
Basic Price/Taxable Value	6,650.00	39,900.00
GST @ 9 %	598.50	3,591.00
GST @ 9 %	598.50	3,591.00
206C(1H) Goods @ 0.08 %	5.89	35.31
Rounding		0.31-
Total Gross Value of Goods - In Figures	7,852.89	47,117.00

Total Gross Value of Goods - In Words FORTY SEVEN THOUSAND ONE HUNDRED SEVENTEEN RUPEES ONLY

ASTHETIC TOWNSHIP DEVELOPERS PVT. LTD.

Gate Entry No. : 1644

Date : 22/02/21

Time : 15:20

Vehicle No. : HR 56B - 5033

Received by : A. Singh

For NUVOCO VISTAS (ORP. LTD.

Authorized Signatory

SPECIFIED TARGET SLUM	W/O	MAX. AGG.	CHEM. ADM.	MIN. ADM.	MIN. CEMENT	CEMENT TYPE
JOBSITE ARRIVAL TIME	JOB POURING START TIME	JOB POURING END	ME	JOBSITE DEPARTURE TIME	PLANT ARRIVAL TIME	

Received the above items in Good condition.

Customer Name, Signature & Seal

ADITYA BIRLA



DELIVERY CHALLAN

Unit Address:-

 UltraTech Cement
 38 Milestone, Behrampur Road, Khandasa
 Gurgaon - 122001 Haryana


GSTIN : 06AAACL6442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No:

Recipient PO Date: 08/02/2021

 Name & Address of Recipient
 S.S. CONSTRUCTION CO.
 RAMKRISHAN HOUSE NEAR MLA TEJ PALTANWAR,
 KOTHIVILL RAMGARH PO BADSHAPUR,
 GURUGRAM 122001

 Name & Address of Delivery
 S.S. CONSTRUCTION CO. (SEC-27)
 BHARTI REALTY C/O ASTHETIC TOWNSHIP I
 NR. IFFCO CHOWK METRO STATION SEC-27,
 GURUGRAM 122001

 Delivery Challan No: 205275412
 Delivery Challan Date: 08/02/2021
 Order No: 6550476
 Order Qty: 21.00
 Cum Qty: 7.00
 HSN Code: 3824 50 10
 Plant Code: 825

 Place of Supply: GURGAON CITY
 State Code: 06
 Recipient GSTN/UIN No: 06AEFPS1460P1Z3

 State Code: 06
 State: HARYANA

Description of Goods: M30 ULTRATECH PLUS CONCRETE

Date & Time of Removal of Goods: 08/02/2021 15:27:19

Transporter Details:

Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (in Rs.)
Basic	7.00	M3	4650.00	32550.00

 Transporter Name: PALUCK TECHNOLOGIES PVT LTD
 Vehical No: HR55AG5999 LR No:
 Mode of Transport: By Road LR Date: 08/02/2021
 Pump Descp: Pump Qty:
 Destination: Inco Term: FOR

 CGST @ 9.00% 2929.50
 SGST @ 9.00% 2929.50

Round Off 0.00

Total Invoice Value: 38409.00

 x Amount In Words:- Five Thousand Eight Hundred Fifty-Nine Rupees and Zero Paise
 -ice Amount in Word:- Thirty-Eight Thousand Four Hundred Nine Rupees and Zero Paise

Certified that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Unit:

Gurgaon - IV - Khandasa Rc

ASTHETIC TOWNSHIP DEVELOPERS PVT. LTD.

Gate Entry No. 4402

Date 08/02/21

Authorised Signatory

Checked By

We hereby confirmed that we have received above referred material in good condition

Time 16:30

Vehicle No. HR 55AG 5999

Received by P. Singh

Date:

Signature Name & Mobile No of Person/Party Who receiving the material with ruber stamp

 Cement Type:
 Min Cem Content: OPC
 Max Size Aggr: 20MM
 Slump at Site

 Chemical Admix Type: ADMHYPLAST
 Mineral Admix Type: FLYASHR
 Slump Specified:
 Water Added at Site:

 Batching Time: 15:26:08
 Pour Structure:
 Max W/C Ratio: 0.41
 Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA20MM	650.00	-0.50	646.73	4527.11	4554.15	0.60
FACS	775.00	-1.00	767.17	5370.19	5379.50	0.17
CA10MM	440.00	-0.50	437.79	3064.53	3057.95	-0.22
CEMOPC	300.00	0.00	300.00	2100.00	2102.90	0.14
FLYASHR	100.00	0.00	100.00	700.00	709.80	1.40
ADMHYPLAST	2.40	-0.64 kg	1.76	12.30	12.52	1.76
WATERR	165.00	14.02 kg	179.02	1253.17	1252.85	-0.03
TOTAL	2432.40		2432.47	17027.30	17069.67	0.25

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.


2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

 Ultra Tech Cement Ltd.
 (A Unit UltraTech Concrete)
 14/2 8/21/21

 S. No. In Time
 Out Time 16:50

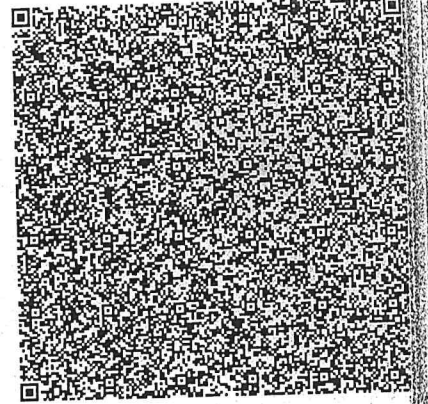

Name of the Plant: :RP-GURGAON-I, DELHI / 4336
 Address of the Plant: :PLOT NO./KH.NO.-1527/916/2/2, 1528/916/2/3, REVE UE
 ESTATE VILLAGE,
 GURGAON 06-HARYANA 122001
 PAN No. :AAACL4159L
 GSTIN. :06AAACL4159L1ZC
 CIN :U26940MH1999PLC118229
 State Code :36
 State Name :Haryana
 IRN : 86c6a1d0d69b989a4ed91dce4fed2df9885a88b3ddad34581787c6e1ecbf3ef7
 Principal P.O.B :CHIDIYA, CHARKHI DADRI, BHIWANI, 06-HARYANA - 123306.
 CIN

TAX INVOICE

Tax Invoice Number :200710041018
 Date & Time :18.02.2021 15:01:00
 Dispatch Mode :BY ROAD
 Receipt Voucher No. :
 Receipt Voucher Date :
 Reverse Charge :
 Sales Type :FOR - FREE ON ROAD
 Sales Order No. :0130202883/SO/4336
 Customer PO / DATE :02/21/08.02.2020
 Name of Transporter :
 Reference Number :2007037846
 Ewaybill Number :331288697649
 Customer Code :50000947
 Name of Customer :S.S.CONSTRUCTION CO.
 SATISH SURI
 Address of Customer :RAMKRISHAN HOUSE, NEAR MLA TEJPAL
 TANWAR KOTHI VILL
 PO BADSHAPUR GURGAON 06-HARYANA
 122101
 Job Site Code :0021845913
 Name of Job Site :BHARTI REALTY
 State Code :06
 Address of Job Site :ASTHETIC TOWNSHIP DEVELOPE
 P.LTD NR.IFFCO CHOWK
 SEC-27,GURUGRAM GURUGRAM
 06-HARYANA 122002
 BCMIX No. :433691566053
 State Code :06
 PAN No. :AEFPS1460P
 EMAIL ID. :vishalgupta@gmail.com
 GSTIN No. :06AEFPS1460P1Z3
 Contact Name :VIPIN CHAUHAN
 Telephone Number :9719919797
 Mobile Number :9719919797
 Email ID :suriconstructions@yahoo.com
 Pump Serial No. :
 Name of Product :RMC
 HSN/SAC :38245010
 Exemption Notification if any :Walls/Columns/Slab/Foundation/Other
 Sales Person's Name :
 Sales Person's Contact No. :

Sl. No.	Description	Vehicle No.	Qty.	UOM	Grade	Delivery Type	Material Code	Old Mat. Co
1	M30 SP AE MO D20 M	HR56B5033	5.000	M3	130	Just Delivery	9000030409	CCMGFE2BH3

Price Elements	Rate	Amount
Basic Price/Taxable Value	4,650.00	23,250.00
SGST @ 9 %	418.50	2,092.50
CGST @ 9 %	418.50	2,092.50
IT 16C(1H) Goods @ 0.08 %	4.12	20.58
Rounding		0.42
Total Gross Value of Goods - In Figures	5,491.12	27,456.00

Total Gross Value of Goods - In Words TWENTY SEVEN THOUSAND FOUR HUNDRED FIFTY SIX RUPEES ONLY

ASTHETIC TOWNSHIP DEVELOPERS PVT. LTD.

Gate Entry No. : 4608
 Date : 18/02/21
 Time : 16:10
 Vehicle No. : HR-56B-5033
 Received by : [Signature]

For NUVOCO VISTAS CORP.

Authorized Signatory

SPECIFIED TARGET SLUM	W/O	MAX. AGG.	CHEM. ADM.	MIN. ADM.	MIN. CEMENT	CEMENT T
JOB SITE ARRIVAL TIME	JOB POURING START TIME	JOB POURING END TIME	JOB SITE DEPARTURE TIME	PLANT ARRIVAL TIME		

Received the above items in Good condition.

Customer Name, Signature & Seal

**DELIVERY CHALLAN**

UltraTech Cement Limited

Unit Address:- 158, Naurangpur
Gurgaon - 122001 Haryana**UltraTech**
CONCRETE
WE MAKE GOOD CONCRETE BETTER

GSTIN : 06AAACL6442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No: 23/03/2021

BUREAU VERITAS
CertificationName & Address of Recipient
S.S. CONSTRUCTION CO.
RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR,
KOTHIVILL RAMGARH PO BADSHAPUR,
GURUGRAM122001Place of Supply: GURGAON CITY
State Code: 06
Recipient GSTN/UIN No: 06AEFPS1460P1Z3Name & Address of Delivery
S.S. CONSTRUCTION CO.(SEC-27)
BHARTI REALTY C/O ASTHETIC TOWNSHIP E
NR. IFFCO CHOWK METRO STATION SEC-27,
GURUGRAM122001State Code: 06
State: HARYANA

Delivery Challan No: 205228749

Delivery Challan Date: 23/03/2021
Order No: 6562031
Order Qty: 18.00
Cum Qty: 4.50
HSN Code: 38245010
Plant Code: 824

Description of Goods: M60 - HIGH STRENGTH CONCRETE

Date & Time of Removal of Goods: 23/03/2021 16:40:59

Transporter Details:

Transporter Name: BANSAL CORPORATION

Vehical No: MH04JK3809

Mode of Transport: By Road

Pump Descp:

Destination:

LR No:

LR Date: 23/03/2021

Pump Qty:

Inco Term: FOR

DriverNameABC

DriverMobNo9718991227

Particulars	Quantity	UOM	Rate Per Unit (Im Rs.)	Amount (in Rs.)
Basic	4.50	M3	7000.00	31500.00
CGST @ 9.00%				2835.00
SGST @ 9.00%				2835.00
Round Off				0.00
Total Invoice Value				37170.00

Tax Amount In Words:- Five Thousand Six Hundred Seventy Rupees and Zero Paise

Invoice Amount In Word:- Thirty-Seven Thousand One Hundred Seventy Rupees and Zero Paise

Certified that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Unit: Gurgaon - II - Navrangpur

Checked By

Authorised Signatory

We hereby confirmed that we have received above referred material in good condition

Date:

Signature Name & Mobile No of Person/Party
Who receiving the material with ruber stampCement Type: OPC
Min Cem Content: 20MM
Max Size Aggr: 20MM
Slump at SiteChemical Admix Type: ADMHYPLAST
Mineral Admix Type: FLYASHR
Slump Specifide:
Water Added at Site:Batching Time: 16:39:56
Pour Structure:
Max W/C Ratio: 0.27
Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA20MM	188.00	-0.50	187.06	841.75	855.10	1.59
FACS	709.00	-0.20	707.57	3184.05	3195.20	0.35
CA10MM	688.00	-0.50	684.54	3080.45	3066.50	-0.45
CEMOPC	450.00	0.00	450.00	2025.00	2026.35	0.07
FLYASHR	160.00	0.00	160.00	720.00	715.85	-0.58
ADMHYPLAST	5.10	0.13 kg	5.23	23.55	23.64	0.40
WATERR	165.00	5.84 kg	170.83	768.75	769.55	0.10
TOTAL	2365.10		2365.23	10643.55	10652.19	0.08



M/S - 35 kg / m3

Dm

1.CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2.WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3.If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4.Once Goods are loaded in vehicle the Goods will not be taken back.

ADITYA BIRLA



DELIVERY CHALLAN

UltraTech Cement Limited

Unit Address:- 158, Naurangpur
Gurgaon - 122001 Haryana
UltraTech
CONCRETE
 WE MAKE GOOD CONCRETE BETTER

GSTIN : 06AAAC6442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No: 28/03/2021

Name & Address of Recipient
 S.S. CONSTRUCTION CO.
 RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR,
 KOTHIVILL RAMGARH PO BADSHAPUR,
 GURUGRAM 122001

 Place of Supply: GURGAON CITY
 State Code: 06
 Recipient GSTN/UIN No: 06AEFPS1460P1Z3

Name & Address of Delivery
 S.S. CONSTRUCTION CO.(SEC-27)
 BHARTI REALTY C/O ASTHETIC TOWNSHIP I
 NR. IFFCO CHOWK METRO STATION SEC-27,
 GURUGRAM 122001

 State Code: 06
 State: HARYANA

Delivery Challan No: 205228986

 Delivery Challan Date: 28/03/2021
 Order No: 6563260
 Order Qty: 4.00
 Cum Qty: 4.00
 HSN Code: 38245010
 Plant Code: 824

 RMC Plant Capacity
 Certification
 BUREAU VERITAS
 Certification


Description of Goods: M60 - HIGH STRENGTH CONCRETE

Date & Time of Removal of Goods: 28/03/2021 05:08:03

Transporter Details:

Transporter Name: BANSAL CORPORATION

 Vehical No: HR55AC9568
 Mode of Transport: By Road
 Pump Descp:
 Destination:

 LR No:
 LR Date: 28/03/2021
 Pump Qty:
 Inco Term: FOR

DriverName: BAHADUR

DriverMobNo: 9718592507

Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (in Rs.)
Basic	4.00	M3	7000.00	28000.00
CGST @ 9.00%				2520.00
SGST @ 9.00%				2520.00
Round Off				0.00
Total Invoice Value:				33040.00

 Amount in Words:- Five Thousand Forty Rupees and Zero Paise
 Amount in Word:- Thirty-Three Thousand Forty Rupees and Zero Paise

Certified that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Unit: Gurgaon - II - Navrangpur

Checked By

 Entry No. 5295
 Date 28/03/21
 Amount 33040.00
 Signature HR55AC9568

Authorized Signatory

We hereby confirm that we have received above referred material in good condition

Date:

 Cement Type: OPC
 Min Cem Content: 20MM
 Slump at Site

 Chemical Admix Type: ADMHYPLAST
 Mineral Admix Type: FLYASHR
 Slump Specified:
 Water Added at Site:

 Batch Time: 04:58:47
 Pour Structure:
 Max W/C Ratio: 0.27
 Admix added at Site

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA20MM	188.00	-0.50	187.05	748.20	753.00	0.64
FACS	709.00	-0.50	705.44	2821.75	2836.10	0.51
CA10MM	688.00	-0.50	684.54	2738.15	2741.30	0.12
CEMOPC	450.00	0.00	450.00	1800.00	1799.25	-0.04
FLYASHR	160.00	0.00	160.00	640.00	636.90	-0.48
ADMHYPLAST	5.10	-0.15 kg	4.95	19.80	19.90	0.49
WATERR	165.00	7.96 kg	172.96	691.85	692.00	0.02
TOTAL	2365.10		2364.94	9459.75	9478.45	0.20

 M/S - 35 kg / m³

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.



DELIVERY CHALLAN



Unit Address:-

Unit: UltraTech Cement
GURGAON-122001 HARYANA

GSTIN : 06AAACL6442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

PO No & Date:

Recipient PO Date: 28/03/2021

Name & Address of Recipient
S.S. CONSTRUCTION CO.
RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR,
KOTHIVILL RAMGARH PO BADSHAPUR,
GURUGRAM 122001Name & Address of Delivery
S.S. CONSTRUCTION CO. (SEC-27)
BHARTI REALTY C/O ASTHETIC TOWNSHIP I
NR. IFFCO CHOWK METRO STATION SEC-27,
GURUGRAM 122001Delivery Challan No: 201049752
Delivery Challan Date: 28/03/2021
Order No: 6563242
Order Qty: 35.00
Cum Qty: 14.00
HSN Code: 3824 50 10
Plant Code: 847Place of Supply: GURGAON CITY
State Code: 06
Recipient GSTN/UIN No: 06AEFPS1460P123State Code: 06
State: HARYANA

Description of Goods: M35 CUSTOMER SPECIFIED CONCRETE

Date & Time of Removal of Goods: 28/03/2021 02:11:34

Transporter Details:

Transporter Name:
Vehical No: HR55AE4075
Mode of Transport: By Road
Pump Descp: Line Pump
Destination:LR No:
LR Date: 28/03/2021
Pump Qty:
Inco Term: FOR

Driver Mob No: 9958476952

Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (in Rs.)
Basic	7.00	M3	5050.00	35350.00
CGST @ 9.00%				3181.50
SGST @ 9.00%				3181.50
Round Off				0.00
Total Invoice Value:				41713.00

Tax Amount In Words:- Six Thousand Three Hundred Sixty-Three Rupees and Zero Paise
Invoice Amount in Word:- Forty-One Thousand Seven Hundred Thirteen Rupees and Zero Paise

We certify that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Unit: Khandsa

Checked By

Entry No. 5289
28/03/21

Authorised Signatory

We hereby confirm that we have received above referred material in good condition

Vehicle No. 0310
Delivered by HR55AE4075

Date:

Signature Name & Mobile No of Person/Party
Who receiving the material with rubber stampCement Type:
Min Cem Content: OPC
Max Size Aggr: 20MM
Slump at SiteChemical Admix Type: ADMHYPLAST
Mineral Admix Type: FLYASHR
Slump Specified: 120+25
Water Added at Site:Batching Time: 02:11:01
Pour Structure:
Max W/C Ratio: 0.37
Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017

Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
CA10MM	435.00	0.50	437.18	3060.26	3059.00	-0.04
CA20MM	685.00	0.50	688.43	4819.01	4810.00	-0.19
FACS	680.00	1.00	686.80	4807.60	4822.00	0.30
CEMOPC	350.00	0.00	350.00	2450.00	2450.00	0.00
FLYASHR	110.00	0.00	110.00	770.00	770.00	0.00
ADMHYPLAST	1.84	0.00 kg	1.84	12.88	12.76	-0.93
WATERR	170.00	-4.40 kg	165.60	1159.20	1162.00	0.24
TOTAL	2431.84		2439.85	17078.95	17085.76	0.04

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT BE RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

TAX INVOICE

ORIGINAL FOR RECIPIENT

IRN : 4ba76b0bb6bdfd192f2c01dbd5e21a36d37ec6972f0556291b55ea85d54afa8

..nited

Limited RMX-Gurgaon 2

ehsil Badshahpur


Village Badshahpur,

Dist. Gurugram, Haryana 122001

Supplying State: Haryana (06)

GSTIN : 06AAACT1507C1Z1

Order No. : acccl



Invoice Serial No: NS2P062001006314

Invoice Date : 27.03.2021

Delivery No. & Date: 1210530348 27.03.2021

Sale Order No.: 1001126731

Ticket No:- 2113802155

Whether the tax is payable on reverse charge basis No

Place of Supply(Incase of interstate)

Phone No: Fax No:

SAP Ref No: NS2P / / 2020 / CO / ZN3R / 1702189755

Sold To Party: 9110157501 Mob: 9719919797

S S Construction Co
Ramkrishan House, Near MLA Tejpal Tanwar Kothi GURGAON
Vill Ramgarh PO Badshapur - 122001
State:Haryana (06)
GSTIN / UID: 06AEFPS1460P1Z3

Ship to Party: 9112126637 Mob: 9719919797

S S Construction Co
Bharti Realty C/o Asthetic Township Developers Pvt Ltd
Near IFFCO Chowk metro Station - 122001
Destination:
State:Haryana (06)
GSTIN / UID:

Description of Goods	HSN Code	Qty	UOM	Rate	Particulars	
M35	38245010	6.000	M3	5,050.00	Basic	30,300.00
Entry No. 5227 27/03/21 01:25 Veh. No. UP14GT2532 2882 ACC LIMITED Dharmasput, Badshapur, Gurgaon OUTGOING MATERIAL 27 MAR 2021 Time 00:40 Security Sign						
Taxable Value of Supply of Goods						30,300.00
SGST @ 9.00 %						2,727.00
CGST @ 9.00 %						2,727.00
Invoice Value						35,754.00
TCS @ 0.075 %						26.82
Total Invoice value						35,780.82

Invoice value in words: Thirty Five Thousand Seven Hundred Eighty Rupees Eighty Two Paise Only

Mode of Transport: Road	LR/RR No.:	Eway Bill No:
Transporter Code: 916003473	LR/RR Date:	Eway Bill Date & Time:
Transporter Name:ADYCON		
Vehicle Reg.No: UP14GT2532		

Remarks: Any complaints relating to this delivery need to be logged within 24 hours at customercare.rmx@acclimited.com. HEALTH AND SAFETY CAUTION: Wet concrete can cause serious burns to your skin. Avoid direct contact with your skin. Wash the affected skin thoroughly immediately in case of contact.

Terms & Condition:

- Our responsibility ceases the moment consignment is delivered to you/your carrier.
- Payment should be made by "A/C Payee only" - bank draft/cheque in favour of ACC Ltd.
- Payments received beyond agreed credit period will attract an interest @ 24% per annum.
- Goods once sold will not be taken back & all disputes are subject to Mumbai jurisdiction.
- ACC reserves the right to effect changes in concrete mix design with or without prior intimation to customer due to change in incoming raw material properties and weather conditions.
- All payments towards supplies are payable at Mumbai.
- In order to further improve upon our impeccable Corporate Governance record, ACC Board has instituted a Fraud Risk Management Policy. In case you come across any unethical behaviour of our employees, kindly contact us at: E-mail: acc@ethicalview.com or National toll free No.: 1800 209 2008 or Fax No.: +91 (22) 6645 9575 Post Box No. 137, Pun 411 001. Information so received will be kept confidential.

Material received in Good Condition & in Quantity

For ACC Limited

(Receiver's Signature with seal)

(Prepared by)

(Authorised Signatory)

Sales unit: ACC Limited Haryana Sales Unit RMX-FARIDABAD, 20.4 kms, Sarai Khwaja Chowk, Faridabad 121001 Tel:
Reg. Office Address - ACC Limited, "CEMENT HOUSE", 121, M. K. ROAD, MUMBAI-400020. www.acclimited.com



DELIVERY CHALLAN

Unit Address:- UltraTech Cement Limited
UltraTech cement Ltd, unit UltraTech concrete 38th milesto
Gurugram-122001 Haryana



GSTIN : 06AAACL6442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

PO No & Date:

Recipient PO Date: 13/03/2021

Name & Address of Recipient
S.S. CONSTRUCTION CO.
RAMKRISHAN HOUSE NEAR MLA TEJ PALTANWAR,
KOTHIVILL RAMGARH PO BADSHAPUR,
GURUGRAM 122001

Name & Address of Delivery
S.S. CONSTRUCTION CO. (SEC-27)
BHARTI REALTY C/O ASTHETIC TOWNSHIP I
NR. IFFCO CHOWK METRO STATION SEC-27,
GURUGRAM 122001

Delivery Challan No: 205060969
Delivery Challan Date: 13/03/2021
Order No: 6559299
Order Qty: 21.00
Cum Qty: 7.00
HSN Code: 38245010
Plant Code: 852

Place of Supply: GURGAON CITY
State Code: 06
Recipient GSTN/UIN No: 06AEFPS1460P1Z3

State Code: 06
State: HARYANA

Description of Goods: M30 ULTRATECH PLUS CONCRETE

Date & Time of Removal of Goods: 13/03/2021 05:02:57

Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (In Rs.)
Basic	7.00	M3	4850.00	33950.00
CGST @ 9.00%				3055.50
SGST @ 9.00%				3055.50
Round Off				0.00
Total Invoice Value:				40061.00

Transporter Details:

Transporter Name: HR55AG6467
Vehical No: HR55AG6467
Mode of Transport: By Road
Pump Descp: Line Pump
Destination: LR No: 13/03/2021
LR Date: 13/03/2021
Pump Qty: 21.00
Inco Term: FOR

Driver Name: PABU Mob No: 8448929960

Tax Amount In Words:- Six Thousand One Hundred Eleven Rupees and Zero Paise

Invoice Amount in Word:- Forty Thousand Sixty-One Rupees and Zero Paise

Certified that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Unit: SOHNA ROAD

Mame
Authorized Signatory

Checked By

We hereby confirm that we have received above referred material in good condition

Date:

Cement Type:
Min Cem Content: OPC
Max Size Aggr: 20MM
Slump at Site

Chemical Admix Type: ADMHYPLAST
Mineral Admix Type: FLYASHR
Slump Specifide: 120+-25
Water Added at Site:

Signature Name & Mobile No of
Person/Party Who receiving the material
with ruber stamp

Batching Time: 05:02:18
Pour Structure:
Max W/C Ratio: 0.41
Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2

ASTHETIC TOWNSHIP DEVELOPERS PVT. LTD.

Gate Entry No. 4984

Date 13/03/21

Time 5:55

Vehicle No. HR 55 AG 6467

Received by P.K. Singh




Beary

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT BE RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

ADITYA BIRLA UltraTech		DELIVERY CHALLAN UltraTech Cement Limited		UltraTech CONCRETE WE MAKE GOOD CONCRETE BETTER.																																																																
Unit Address:- 38 Milestone, Behrampur Road, Khandasa Gurgaon - 122001 Haryana		GSTIN : 06AAAC6442L1ZE		CIN No : L26940MH2000PLC128420																																																																
Recipient Code: 40083007		Recipient PO No: 27/03/2021		  																																																																
Name & Address of Recipient S.S. CONSTRUCTION CO. RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR, KOTHIVILL RAMGARH PO BADSHAPUR, GURUGRAM 122001 Place of Supply: GURGAON CITY State Code: 06 Recipient GSTN/UIN No: 06AEFPS1460P123		Name & Address of Delivery S.S. CONSTRUCTION CO. (SEC-27) BHARTI REALTY C/O ASTHETIC TOWNSHIP C NR. IFFCO CHOWK METRO STATION SEC-27, GURUGRAM 122001 State Code: 06 State: HARYANA		Delivery Challan No: 205277721 Delivery Challan Date: 27/03/2021 Order No: 6563000 Order Qty: 140.00 Cum Qty: 35.00 HSN Code: 3824 50 10 Plant Code: 825																																																																
Description of Goods: M30 ULTRATECH PLUS CONCRETE		Date & Time of Removal of Goods: 27/03/2021 13:30:00																																																																		
Transporter Details:		<table border="1"> <thead> <tr> <th>Particulars</th> <th>Quantity</th> <th>UOM</th> <th>Rate Per Unit (Im Rs.)</th> <th>Amount (in Rs.)</th> </tr> </thead> <tbody> <tr> <td>Basic</td> <td>7.00</td> <td>M3</td> <td>4850.00</td> <td>33950.00</td> </tr> <tr> <td>CGST @ 9.00%</td> <td></td> <td></td> <td></td> <td>3055.50</td> </tr> <tr> <td>SGST @ 9.00%</td> <td></td> <td></td> <td></td> <td>3055.50</td> </tr> <tr> <td>Round Off</td> <td></td> <td></td> <td></td> <td>0.00</td> </tr> <tr> <td>Total Invoice Value:</td> <td></td> <td></td> <td></td> <td>40061.00</td> </tr> </tbody> </table>				Particulars	Quantity	UOM	Rate Per Unit (Im Rs.)	Amount (in Rs.)	Basic	7.00	M3	4850.00	33950.00	CGST @ 9.00%				3055.50	SGST @ 9.00%				3055.50	Round Off				0.00	Total Invoice Value:				40061.00																																	
Particulars	Quantity	UOM	Rate Per Unit (Im Rs.)	Amount (in Rs.)																																																																
Basic	7.00	M3	4850.00	33950.00																																																																
CGST @ 9.00%				3055.50																																																																
SGST @ 9.00%				3055.50																																																																
Round Off				0.00																																																																
Total Invoice Value:				40061.00																																																																
Transporter Name: Vehicle No: HR55AG5999 Mode of Transport: By Road Pump Descp: Line Pump Destination: Driver Mob No: 7827888212		LR No: LR Date: 27/03/2021 Pump Qty: Inco Term: FOR																																																																		
Amount In Words:- Six Thousand One Hundred Eleven Rupees and Zero Paise Amount in Word:- Forty Thousand Sixty-One Rupees and Zero Paise		Checked By: We hereby confirmed that we have received above referred material in good condition																																																																		
Certified that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.		For ULTRATECH CEMENT LIMITED Unit: Gurgaon - IV - Khandasa Rd Signature Name & Mobile No of Person/Party Who receiving the material with ruber stamp Signature:  Authorized Signatory																																																																		
Date: Cement Type: OPC Min Cem Content: Max Size Aggr: 20MM Slump at Site		Chemical Admix Type: ADMHYPLAST Mineral Admix Type: FLYASHR Slump Specifide: 120+-25 Water Added at Site:		Batching Time: 13:28:38 Pour Structure: Max W/C Ratio: 0.41 Admix added at Site																																																																
The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017																																																																				
<table border="1"> <thead> <tr> <th>Raw Material</th> <th>Design Qty(Kg)</th> <th>%Mois/%Abs/Corr(Kg)</th> <th>Corrected(Kg)</th> <th>Required(Kg)</th> <th>Batched(Kg)</th> <th>% Variation</th> </tr> </thead> <tbody> <tr> <td>CA20MM</td> <td>650.00</td> <td>0.30</td> <td>651.96</td> <td>4563.72</td> <td>4571.65</td> <td>0.17</td> </tr> <tr> <td>FACS</td> <td>775.00</td> <td>0.50</td> <td>778.89</td> <td>5452.23</td> <td>5452.70</td> <td>0.01</td> </tr> <tr> <td>CA10MM</td> <td>440.00</td> <td>0.30</td> <td>441.32</td> <td>3089.24</td> <td>3095.90</td> <td>0.22</td> </tr> <tr> <td>CEMOPC</td> <td>300.00</td> <td>0.00</td> <td>300.00</td> <td>2100.00</td> <td>2102.10</td> <td>0.10</td> </tr> <tr> <td>FLYASHR</td> <td>100.00</td> <td>0.00</td> <td>100.00</td> <td>700.00</td> <td>700.35</td> <td>0.05</td> </tr> <tr> <td>ADMHYPLAST</td> <td>2.40</td> <td>-0.67 kg</td> <td>1.73</td> <td>12.10</td> <td>12.11</td> <td>0.07</td> </tr> <tr> <td>WATERR</td> <td>165.00</td> <td>-7.17 kg</td> <td>157.83</td> <td>1104.81</td> <td>1104.75</td> <td>-0.01</td> </tr> <tr> <td>TOTAL</td> <td>2432.40</td> <td></td> <td>2431.73</td> <td>17022.10</td> <td>17039.56</td> <td>0.10</td> </tr> </tbody> </table>						Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation	CA20MM	650.00	0.30	651.96	4563.72	4571.65	0.17	FACS	775.00	0.50	778.89	5452.23	5452.70	0.01	CA10MM	440.00	0.30	441.32	3089.24	3095.90	0.22	CEMOPC	300.00	0.00	300.00	2100.00	2102.10	0.10	FLYASHR	100.00	0.00	100.00	700.00	700.35	0.05	ADMHYPLAST	2.40	-0.67 kg	1.73	12.10	12.11	0.07	WATERR	165.00	-7.17 kg	157.83	1104.81	1104.75	-0.01	TOTAL	2432.40		2431.73	17022.10	17039.56	0.10
Raw Material	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation																																																														
CA20MM	650.00	0.30	651.96	4563.72	4571.65	0.17																																																														
FACS	775.00	0.50	778.89	5452.23	5452.70	0.01																																																														
CA10MM	440.00	0.30	441.32	3089.24	3095.90	0.22																																																														
CEMOPC	300.00	0.00	300.00	2100.00	2102.10	0.10																																																														
FLYASHR	100.00	0.00	100.00	700.00	700.35	0.05																																																														
ADMHYPLAST	2.40	-0.67 kg	1.73	12.10	12.11	0.07																																																														
WATERR	165.00	-7.17 kg	157.83	1104.81	1104.75	-0.01																																																														
TOTAL	2432.40		2431.73	17022.10	17039.56	0.10																																																														
1.CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.																																																																				
2.WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.																																																																				
3.If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.																																																																				
4.Once Goods are loaded in vehicle the Goods will not be taken back.																																																																				
Signature:  Signature Name & Mobile No of Person/Party Who receiving the material with ruber stamp Signature:  Authorized Signatory																																																																				
S No: 721 Out Time: 13:40																																																																				

ADITYA BIRLA



DELIVERY CHALLAN

Unit Address:-
UltraTech Cement Limited
Ultratech cement Ltd, unit Ultratech concrete 38th milesto
Gurugram-122001 Haryana



GSTIN : 06AAACL6442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

PO No & Date:

Recipient PO Date: 23/03/2021

Name & Address of Recipient
S.S. CONSTRUCTION CO.
RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR,
KOTHIVILL RAMGARH PO BADSHAPUR,
GURUGRAM 122001

Name & Address of Delivery
S.S. CONSTRUCTION CO. (SEC-27)
BHARTI REALTY C/O ASTHETIC TOWNSHIP I
NR. IFFCO CHOWK METRO STATION SEC-27,
GURUGRAM 122001

Delivery Challan No: 205061223
Delivery Challan Date: 23/03/2021
Order No: 6561903
Order Qty: 14.00
Cum Qty: 7.00
HSN Code: 3824 50 10
Plant Code: 852

Place of Supply: GURGAON CITY
State Code: 06
Recipient GSTN/UIN No: 06AEFPS1460P123

State Code: 06
State: HARYANA

Description of Goods: M7.5 CUSTOMER SPECIFIED CONCRETE

Date & Time of Removal of Goods: 23/03/2021 04:53:10

Transporter Details:

Transporter Name:
Vehical No: HR55AG6442
Mode of Transport: By Road
Pump Descp:
Destination:
LR No:
LR Date: 23/03/2021
Pump Qty:
Inco Term: FOR

Driver Name: SACHIN Mob No: 9798463431

Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (In Rs.)
Basic	7.00	M3	3650.00	25550.00
CGST @ 9.00%				2299.50
SGST @ 9.00%				2299.50
Round Off				0.00
Total Invoice Value:				30149.00

Amount In Words:- Four Thousand Five Hundred Ninety-Nine Rupees and Zero Paise

Invoice Amount in Word:- Thirty Thousand One Hundred Forty-Nine Rupees and Zero Paise

Certified that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Unit: SOHNA ROAD

Checked By:

Manoj
Authorised Signatory

We hereby confirmed that we have received above referred material in good condition

Date:

Signature Name & Mobile No of
Person/Party Who receiving the material
with ruber stamp

Cement Type:
Min Cem Content: OPC
Max Size Aggr: 20MM
Slump at Site

Chemical Admix Type: ADMSPLAST
Mineral Admix Type: FLYASHR
Slump Specifide:
Water Added at Site:

Batching Time: 04:51:49
Pour Structure:
Max W/C Ratio: 0.58
Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017

ASTHETIC TOWNSHIP DEVELOPERS PVT. LTD.

Gate Entry No. 5719

Date 23/03/2021

Time 04:51:50

Vehicle No. H.P.55AD.6442

Received by: SACHIN

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT BE RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.



DELIVERY CHALLAN

UltraTech Cement Limited

Unit Address:- 38 Milestone, Behrampur Road, Khandsa
Gurgaon - 122001 Haryana

GSTIN : 06AAACL6442L1ZE

CIN No : L26940MH2000PLC128420

Recipient Code: 40083007

Recipient PO No: 21/03/2021

BUREAU VERITAS
Certification

Name & Address of Recipient
S.S. CONSTRUCTION CO.
RAMKRISHAN HOUSE NEAR MLA TEJPALTANWAR,
KOTHIVILL RAMGARH PO BADSHAPUR,
GURUGRAM 122001
Place of Supply: GURGAON CITY
State Code: 06
Recipient GSTN/UIN No: 06AEFPS1460P1Z3

Name & Address of Delivery
S.S. CONSTRUCTION CO. (SEC-27)
BHARTI REALTY C/O ASTHETIC TOWNSHIP E
NR. IFFCO CHOWK METRO STATION SEC-27,
GURUGRAM 122001
State Code: 06
State: HARYANA

Delivery Challan No: 205277474
Delivery Challan Date: 21/03/2021
Order No: 6561570
Order Qty: 12.00
Cum Qty: 11.00
HSN Code: 3824 50 10
Plant Code: 825

Description of Goods: M7.5 CUSTOMER SPECIFIED CONCRETE

Date & Time of Removal of Goods: 21/03/2021 20:06:18

Transporter Details:

Transporter Name:

Vehical No: HR56B1026
Mode of Transport: By Road
Pump Descp:
Destination:

LR No:
LR Date: 21/03/2021
Pump Qty:
Inco Term: FOR

Driver Mob No 7024969683

Particulars	Quantity	UOM	Rate Per Unit (In Rs.)	Amount (In Rs.)
Basic	6.00	M3	3650.00	21900.00
CGST @ 9.00%				1971.00
SGST @ 9.00%				1971.00
Round Off				0.00
Total Invoice Value:				25842.00

Amount In Words:- Three Thousand Nine Hundred Forty-Two Rupees and Zero Paise
Invoice Amount in Word:- Twenty-Five Thousand Eight Hundred Forty-Two Rupees and Zero Paise

Certified that the particulars given above are true & correct & the amount indicated represents the price actually charged and there is no flow of any additional consideration directly or indirectly from the recipient.

For ULTRATECH CEMENT LIMITED

Unit: Gurgaon - IV - Khandsa Ro

Checked By

Entry No. 5101

Authorised Signatory

We hereby confirmed that we have received above referred material in good condition

Date:

Cement Type: OPC
Min Cem Content: 20MM
Max Size Aggr: 20MM
Slump at Site

Chemical Admix Type: ADMSPLAST
Mineral Admix Type: FLYASHR
Slump Specified:
Water Added at Site:

Batching Time: 20:04:48
Pour Structure:
Max W/C Ratio: 0.58
Admix added at Site

The delivery challan is being used for delivery of Continuous Material and Tax Invoice will be issued on consolidated basis under Rule 46 of CGST Rules 2017

	Design Qty(Kg)	%Mois/%Abs/Corr(Kg)	Corrected(Kg)	Required(Kg)	Batched(Kg)	% Variation
Raw Material						
CA20MM	697.00	0.00	697.00	4182.00	4211.25	0.70
FACS	744.00	0.00	744.00	4464.00	4490.45	0.59
CA10MM	465.00	0.00	465.00	2790.00	2776.65	-0.48
CEMOPC	105.00	0.00	105.00	630.00	629.30	-0.11
FLYASHR	195.00	0.00	195.00	1170.00	1168.25	-0.15
ADMSPLAST	1.50	-0.57 kg	0.93	5.60	5.64	0.66
WATERR	175.00	0.00 kg	175.00	1050.00	1050.05	0.01
TOTAL	2382.50		2381.93	14291.60	14331.59	0.28

1. CAUTION: WET CEMENT AND CONCRETE ARE CAUSTIC MATERIAL WHICH CAN CAUSE SERIOUS SKIN INJURY. TO AVOID RISK OF SUCH INJURY, PROTECTIVE CLOTHING (GLOVES, BOOTS ETC.) SHOULD BE WORN AT ALL TIMES DURING HANDLING OPERATION, WHERE DIRECT SKIN CONTACT OCCURS, IT SHOULD BE WASHED THOROUGHLY WITH CLEAN WATER, PROLONGED SKIN CONTACT SHOULD BE AVOIDED. COMPANY SHALL NOT BE RESPONSIBLE FOR THE SLUMP, STRENGTH OR QUALITY OF THE CONCRETE WHEN WATER HAS BEEN ADDED ON SITE AT THE REQUEST OF THE CUSTOMER.

2. WARRANTY DISCLAIMER:- UltraTech Cement Limited warrants that the products identified are in accordance with the appropriate BIS Specifications. No one is authorized to make any modifications or additions to this warranty. UltraTech Cement Limited makes no warranty or representation, either expressed or implied with respect to this product and disclaims any implied warranty or merchantability or fitness for particular purpose. As UltraTech Cement Limited has no control over the other ingredients mixed with the products or the final application. UltraTech Cement Limited does not and cannot warrant the finished work. In no event shall UltraTech Cement Limited be liable for Direct, Indirect, special, incidental or consequential damage including without limitation loss of profit or earnings arising out of the use of the product, even if you are notified or advised of the possibilities of such damages, in no case shall UltraTech Cement Limited's liability exceed the purchase price of this product.

3. If necessary, additional dose of admixture may be added at project site to regain the workability of concrete with the mutual agreement between the consignor and the consignee.

4. Once Goods are loaded in vehicle the Goods will not be taken back.

Ultra Tech Cement Ltd.
(A Unit UltraTech Concrete)
424/213121

S. No. 922 In Time

Annexure-XVII

Electricity Approval for Construction

Office of the
Executive Engineer, Electrical Inspectorate, Haryana, Block C-2,
Sushant Lok-I, Huda Primary School Building,
Gurugram (e-mail: xenceiggn@gmail.com).

To

M/s S.S Construction Co.
C/o M/s Asthetic Township Developers Pvt. Ltd.
Sector-27, Near Millenium Plaza,
Gurugram

Memo No: H.T.I/ 14110

Dated: 21/08/2020

Subject: Inspection of HT installation comprising of 1x200 KVA 11/0.433KV T/F installed at S.S Construction Co., Gurugram.

The subject cited installation was inspected by this department on 21.08.2020 and the same was found generally complying with the relevant provisions of CEA (Measures Relating to Safety and Electric Supply) Regulations, 2010.

The following observations be attended under intimation to this office:

1. Earth pits be maintained and marked properly for identification.

Approval for energisation of the subject cited installations is hereby accorded subject to consistent compliance of the relevant provisions of CEA Regulations, 2010 in the installation at your end. Please note that it shall be the responsibility of the owner of electrical installations to maintain and operate the installations in a condition free from danger and as recommended by the manufacturer or by the relevant code of practice of the Bureau of Indian Standards.

Your next inspection shall fall due in the month of August every year. You are therefore requested to deposit inspection fee as per schedule under the Head of A/c "0043-Taxes and Duties on Electricity Fees payable under I.E Rules, 1956" and send the original receipted treasury challan to this office one month before the due date.


Executive Engineer,
Electrical Inspectorate, Haryana,
Gurugram.

CC: The SDO/AGM OP S/Divn., DHBVN, DLF S/Divn., Gurugram for information and necessary action.

DHBVN

DAKSHIN HARYANA BIJLI VITARAN NIGAM
Office of the SDO DLF City Sub Division
DHBVN, Sec-31, Gurugram- 122001 (Haryana)
0124-2384755 Website www.dhbvn.com Email ID: sdodlfcity@gmail.com

From

SDO,
DLF City Sub-Divn.
D.H.B.V.N, Gurugram

To

The Executive Engineer,
M&P Division,
DHBVN, Gurugram.

Memo No. 4589

Date 28/8/2020

Sub: - Performa for release of new HT CT meter connection of SS Construction co
Ashtetic Township Developers Pvt Ltd. Sec 27 Gurugram. A/C No. G 21-620-
43 San load 150 KW NDS, category.

Enclosed please find here with the Performa for release of new connection
having San. Load 150 KW of the subject cited consumer for further action in your office please

DA/ As above:-

SDO,
DLF City Sub-Divn.
D.H.B.V.N, Gurugram

PERFORMA FOR RELEASE OF LT CT CONNECTION OF M&P DIVISION.

1. NAME OF SUB-DIVISION: DLF City S/Division Gurugram
2. NAME OF DIVISION: Sub-Urban Division Gurugram
3. NAME OF CIRCLE: "OP" Circle Gurugram
4. NAME OF CONSUMER & A/C NO.: S S Constraction Co..
Online Application no.G-21-620-43.
5. NATURE/KIND OF INDUSTRY: NDS
6. LOCATION OF PREMISES: Asthetic Township Developers Pvt Ltd, Gurugram.
7. S.J.O NO. & DATE: SCO no. G-21-620-43 Date
8. SANCTION LOAD/CONTRACT DEMAD: 150 KW
9. CONNECTED LOAD VERIFIED BY A.G.M.: 150 KW
10. PARTICULARS OF ELECTRONIC METER & CT: Meter Sr no.-X1258217, GS 1125/20, Secure,-/5 A
HT/CT's Sr. no. 3838 A,B,C .MAKE-ELTECH.HT
CT CAPICITY -10/5A.
11. SIZE OF LT/CT CABLE: 95 mm
12. CAPACITY OF TRANSFORMER INSTALLED: 200 KVA T/F
13. CAPACITY OF CAPACITOR INSTALLED: NA
14. DETAILS OF HOUSING THE METERING EQUIPMENT: Near pole
15. WHETHER THE INSTALLATION HAS BEEN INSPECTED & DECLARED FIT FOR ENERGISATION BY CEI-HARYANA:
16. SYSTEM VOLTAGE ON WHICH CONNECTION IS PROPOSED TO BE RELEASED: 400 KV


SDO,
DLF City S/Divn.
D.H.B.V.N, Gurugram

DAKSHIN HARYANA BIJLI VITRAN NIGAM LTD. **STORES CHALLAN BOOK**

Book No. 15

Date 25-8-20

Serial No. 55

From

To

S.D.O. M&T Lab GGN

S.D.O. D.L.F city S/DIVISION

Lorry No.

Name of Driver

GEM

Through Sh. Ashok KUMAR JE

Serial No.	Sr. No. of Meter	Block Number	Make	Capacity	Reading	Remarks
	1	2	3	4	5	6
I	3 No. H.T. CTS. make - Jai Durga	VA=5	clan 20.85	ROL		
	CTS No 2	HC 21852				520 to 79 kmw
		HC 21859	Jai Durga	Ratio	At No = 46683.3806	
		HC 21860	3X5/5	5/5		
			M/S DLF Ltd.	Primary School		
	M&T	Sub N.M. 7867038	39	40		
	Accuracy checked in Lab and Found <u>WIR</u>					
				Received by		

Issuing Officer

Store Issued

Date

JE M&T Lab
DHBVN Gurgaon

S.S. Construction Co.
ENGINEERS & CONTRACTORS

S.C.O. 375, 11nd Floor
Sector 37-D, Chandigarh
Ph.: 0172-2691095
Fax : 0172-2691095

E-mail : suriconstructions@yahoo.co
info@ssconstructions.in
Website : www.ssconstructions.in

Ref. No. SSC/BHARTI/Ext/01

Cash/ce

24/8/20

Dated 24 Aug 2020

To

SDO
DHBVN
SECTOR 31 Gurgaon.

Sub: CUBICAL METER PANNEL FEES
WITH CPT

ALNO 89717550273

Respected Sir,

Enclosed herewith please find the
DD No. 092696 dt 24/8/2020 of amount 32600
for the above mentioned fees.

You are request to do the needful.

Thanking you in anticipation.

For S.S. CONSTRUCTION CO.

Authorised Signatory
RAJINDER SINGH

for SS Construction

Mb- 85922

Book No.

001108

R.No.

L.D. Center

188

R.O.No. 4

Account No.

Received from Shri.

sum of Rs.

32600

by Cash/Cheque/M.O.

subject to realization

Dakshin Haryana Bijli Vitran Nigam

Energy & Other Charges	ED	Bank Charges	Total Amount
HT panel cost			32600
			1
			32600

Cashier

CONTRACTOR TEST REPORT & BOARD INSTALLATION TEST ORDER

M/S S.S. Construction Co.
 Address: Aesthetic Township Development (P) Ltd.
 Description of Premises: Sector-27 Gurgaon Dom./Comm./SP. Supply
 Application No.: E-21-620-43 Date: Gurgaon A/C No.:

Owner of premises Self
 From W. Contractor
 & Valid upto

M/S ANKUR ELECTRICALS
 'A' Class Electric Contractor
 11 KVA Licence No. H-382/A

Supervisor
 Name of Supervisor: SHRI CPH-12

No. 94
 To The S.D.O.
 D.H.B.V.N. Ltd.

Tactical load: 150. K.W. Detail
 Back side

REPORT

Please note the Electrical Installation belonging to above consumer detailed on back in now ready for the Board's test.

The installation was tested by me/us. 24/07/20 (Date) and insulation resistance was shown the reverse of the Test Report.

Signature of Contractors: [Signature]

For TEHSIL Gurgaon ONLY

BOARD INSTALLATION TEST ORDER

To The Junior Engineer.....
 Please test the installation details on back page fill in column and report as below and (in the case of subsequent due to the first providing installation to be defective) collect Rs.....in advance.

.....S.D.O. Date.....

REPORT

Above installation as tested by me (Date).....and the installation was as show on me back page

- Remark:
- Whether first subsequent visit.....
 - Whether contractor or his representative has been present.....
 - Whether installation defective.....
 - Whether charge of Rs. has been collected (if due)
 - Signature.....

Junior Engineer.....Date.....

M/S ANKUR ELECTRICALS
A' Class Electrician Contractor
11 KVA Licence No. H-382/A

Signature Wiring Contractor

License No. H-.....

Annexure-XVIII
Bill for C&D Waste Disposal

Pick Up the Manba from door to door

Tentative
Municipal Corporation Gurugram
Assessment Notice of C&D Waste (Zone-3)



Name of Owner: S.S. Construction Company

Address: Sushant Lok B block, S-27, Sec-27

Description	Rate	Amount
Area/ Plot (Sq. Mtr.)		
No of Floor		
Total Built up Area (Sq. Mtr.)		
C&D Waste Quantity	New Construction	@ 50 Kg/ Sqm. n/a
	Repair	@ 45 Kg/ Sqm.
	Demolition	@ 400 Kg/ Sqm.
Total Quantity		
C&D Waste (in Kg)	5000 kg	
C&D Waste Generate (in Tonne)	5 MT	
Rate for Lifting C&D Waste	Segregated	@ 360/ M.T.
	Unsegregated	@ 720/ M.T. 3600/-
Assessment Amount	Penalty (+)	
Penalty 100% of Assessment Amount		
Total Amount (in Rs.)		3600/-

Three thousand Six hundred Rupees only

Note:-

This is approximate demand estimation of C&D waste to be generated/generated at your property. Final demand notice of Construction and Demolition Waste will be generated on actual basis, which you will have to submit to Municipal Corporation Gurugram immediately.

Confirmed by Property Owner
Rajat Kumar for SS-Construction Co.

Authorized Signatory of MCG
09/10/2020

7836867630

Payable in C&D waste subhead at MCG office Tower C-1 Building, 1st Floor
Info City Sector-34, Gurugram, Old Committee office in front of Civil Hospital, CFC
Branch and Community Centre Sector- 42, MCG office Zone- III.

Contact:- 7005674475

र.मं

From G-8 Rule-IV

रसीद



नाम : S.S CONSTRUCTION COMPANY
पता : SUSHANT LOK B BLOCK, HQ-27, SECTOR 27, GURUGRAM
गुरुग्राम नगर निगम कार्यालय गुरुग्राम
निम्न खाते में जमा करने के लिए नगद वसूल पाया।

रसीद नं.: 1553075

करदाता का खाता नं./बिल नं./नोटिस नं. व:	अदायगी का विवरण	रकम/रुपये. पैसे
130-50	Construction Demulation Waste Income	3600.00

अदायगी की तिथि/समय: 03/11/2020 02:22 PM

MCG

जोड़ = 3600.00

Payment made by cheque is subject to realization MUNICIPAL CORPORATION GURUGRAM (In words: Three Thousand Six Hundred)

CCS-CFC1, MEMO NO.: IC/HQ/MCG/2020/1217 ON DATED: 03-11-2020 C & D WASTE TOTAL QUANTITY IN KG: 5000 KG, Ref.ID2: PermitsPro, Mob.: 8527209087,

AccountNo:130-50

 जारी करने वाले के हस्ताक्षर
Parmod Kumar

Annexure-XIX

Photographs of Basic Infrastructure provided at Project Site

Photographs of Basic Infrastructure

1. Drinking water facility for workers



2. Toilets for workers




3. Labour Hutment



4. Safety instructions on site, First Aid, Emergency Hospitals and contact numbers display

Sl. No.	NAME OF THE STAFF	DESIGNATION	MOBILE NO
1.	Mr. Yadwinder Singh	GM Project	8288804417
2.	Mr. Gurpreet Singh	PM Project	8527809200
3.	Mr. Rajinder Singh	HR Manger	8527209087
4.	Mr. Sanjay	Sr. Eng.	9815674331
5.	Mr. Punit	Sr. Eng.	9899440081
6.	Vijay Kumar	HSE Manager	9911944566
7.	Rishi Raju	HSE Eng.	8848634536
SITE EMERGENCY CONTACT NUMBERS			
8.	Tayleen	First Aider	8398968786
9.	Site Ambulance		9671414823
EMERGENCY AGENCIES			
	Police station	100	
	Fire department	101	
	Nearest Hospital		9582688440



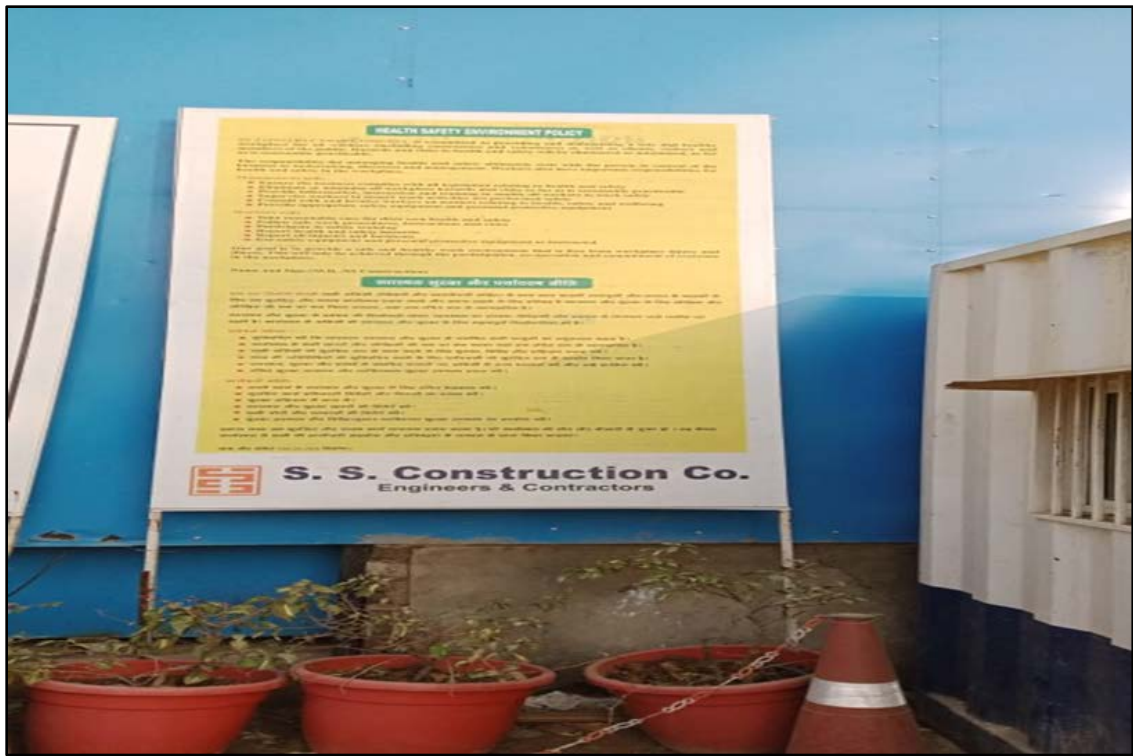

Annexure-XX

AAI NOC



भारतीय विमानपत्तन प्राधिकरण AIRPORTS AUTHORITY OF INDIA

AAI/RH&NR/ATM/NOC/2019/117/527-530
M/s Asthetic Township Developers Pvt. Ltd.

262, DDA Office Complex, Jhandewalan
Extn, New Delhi-110055

Date: 25-03-2019

Valid Upto: 24-03-2027

No Objection Certificate for Height Clearance

1. This NOC is issued by Airports Authority of India (AAI) in pursuance of responsibility conferred by and as per the provisions of Govt. of India (Ministry of Civil Aviation) order GSR751 (E) dated 30th Sep. 2015 for Safe and Regular Aircraft Operations.

2. This office has no objection to the construction of the proposed structure as per the following details:

NOC ID :	PALM/NORTH/B/030819/377136
Applicant Name*	Satya Pal Singh
Site Address*	Proposed Commercial colony on site admeasuring 11537.57 Sq. Meter located at Sector-27, Rect No. 59, Village - Sukhrali, Gurugram, Haryana, Sukhrali, Gurgaon, Haryana
Site Coordinates*	77 04 26.27-28 27 57.54, 77 04 26.95-28 27 59.06, 77 04 26.98-28 27 55.15, 77 04 26.98-28 27 57.11, 77 04 29.45-28 27 57.08, 77 04 29.48-28 27 55.11, 77 04 30.08-28 27 57.93, 77 04 30.55-28 27 55.13, 77 04 31.77-28 27 59.03, 77 04 31.80-28 27 56.10
Site Elevation in mtrs AMSL as submitted by Applicant*	241.95 M
Permissible Top Elevation in mtrs Above Mean Sea Level(AMSL)	346.95M

*As provided by applicant

3. This NOC is subject to the terms and conditions as given below:

a. Permissible Top elevation has been issued on the basis of Site coordinates and Site Elevation submitted by Applicant. AAI neither owns the responsibility nor authenticates the correctness of the site coordinates & site elevation provided by the applicant. If at any stage it is established that the actual data is different, this NOC will stand null and void and action will be taken as per law. The office in-charge of the concerned aerodrome may initiate action under the Aircraft (Demolition of Obstruction caused by Buildings and Trees etc.) Rules, 1994"

b. The Site coordinates as provided by the applicant in the NOC application has been plotted on the street view map and satellite map as shown in ANNEXURE. Applicant/Owner to ensure that the plotted coordinates corresponds to his her site. In case of any discrepancy, Designated Officer shall be requested for cancellation of the NOC.

c. Airport operator or his designated representative may visit the site (with prior coordination with applicant or owner) to ensure that NOC terms & conditions are complied with.

d. The Structure height (including any superstructure) shall be calculated by subtracting the Site elevation in AMSL from the Permissible Top Elevation in AMSL i.e. Maximum Structure Height - Permissible Top Elevation minus (-) Site Elevation.

e. The issue of the 'NOC' is further subject to the provisions of Section 9-A of the Indian Aircraft Act, 1934 and any notifications issued there under from time to time including the Aircraft (Demolition of Obstruction caused by Buildings and Trees etc.) Rules, 1994.

क्षेत्रीय मुख्यालय उत्तरी क्षेत्र, परिचालन कार्यालय परिसर रंगपुरी, नई दिल्ली - 110037 दूरभाष संख्या - 91-11-25653566
Regional headquarter Northern Region, Operational Offices Complex Rangpuri, New Delhi-110 037 Tel: 91-11-25653566

K. K. A. Kabir
25/03/19
के के ए कबीर / K. K. A. KABIR
महसबंधक (वायु यातायात प्रबन्धन-उत्तरी क्षेत्र) / General Manager (ATM), NR
भारतीय विमानपत्तन प्राधिकरण / Airports Authority of India
प्रचालन कार्यालय / Operational Offices
नई दिल्ली-37/Rangpuri, Gurugram Road, New Delhi-37

" हिंदी पत्रों का स्वागत है "



भारतीय विमानपत्तन प्राधिकरण AIRPORTS AUTHORITY OF INDIA

- f. No radio/TV Antenna, lighting arresters, staircase, Mumtee, Overhead water tank and attachments of fixtures of any kind shall project above the Permissible Top Elevation of 346.95M (AMSL), as indicated in para 2.
- g. Use of oil, electric or any other fuel which does not create smoke hazard for flight operations is obligatory, within 8 KM of the Aerodrome Reference Point.
- h. The certificate is valid for a period of 8 years from the date of its issue. One time revalidation without assessment may be allowed, provided construction work has commenced, subject to the condition that such request shall be made within the validity period of the NOC and the delay is due to circumstances which are beyond the control of the developer.
- i. No light or a combination of lights which by reason of its intensity, configuration or colour may cause confusion with the aeronautical ground lights of the Airport shall be installed at the site at any time, during or after the construction of the building. No activity shall be allowed which may affect the safe operations of flights
- j. The applicant will not complain/claim compensation against aircraft noise, vibrations, damages etc. caused by aircraft operations at or in the vicinity of the airport.
- k. Day markings & night lighting with secondary power supply shall be provided as per the guidelines specified in chapter 6 and appendix 6 of Civil Aviation Requirement Series B Part I Section 4, available on DGCA India website: www.dgca.nic.in
- l. The applicant is responsible to obtain all other statutory clearances from the concerned authorities including the approval of building plans. This NOC for height clearances is to ensure the safe and regular aircraft operations and shall not be used as document for any other purpose/claim whatsoever, including ownership of land etc.
- m. This NOC has been issued w.r.t. the Civil Airports. Applicant needs to seek separate NOC from Defence, if the site lies within their jurisdiction. Applicants also need to seek clearance from state Govt. as applicable, for sites which lies in the jurisdiction of unlicensed aerodrome as outlined in Rule 13 of GSR751 (E)
- n. In case of any discrepancy/interpretation of NOC letter, English version shall be valid.
- o. In case of any dispute w.r.t site elevation and/or AGL height, top elevation in AMSL shall prevail.


Chairman NOC Committee



Region Name: NORTH

Address: General Manager Airports Authority of India, Regional Headquarter, Northern Region, Operational Offices, Gurgaon Road, New Delhi-110037

Email ID: noc_nr@aai.aero

Contact No: 011-25653551


25/03/19
के के ए कबीर / K. K. A. KABIR
महानिबंधक (वायु यातायात प्रबंधन-उत्तरी क्षेत्र) / General Manager (ATM), NR
भारतीय विमानपत्तन प्राधिकरण / Airports Authority of India
प्रचालन कार्यालय / Operational Offices
रंगपुरी, गुग्गम रोड, नई दिल्ली-37/Rangpuri, Gungram Road, New Delhi-37

Name / Designation / Sign with Date	
Prepared By :	 Narceenjam ATM (ATM)
Verified By :	 25/3/19

क्षेत्रीय मुख्यालय उत्तरी क्षेत्र, परिचालन कार्यालय परिसर रंगपुरी, नई दिल्ली - 110037 दूरभाष संख्या - 91-11-25653566
Regional headquarter Northern Region, Operational Offices Complex Rangpuri, New Delhi-110 037 Tel: 91-11-25653566

" हिंदी पत्रों का स्वागत है । "

Distance From Nearest Airport And Bearing

Airport Name	Distance (Meters) from Nearest ARP	Bearing (Degree) from Nearest ARP
I.G.I Airport	11897.44	196.42
Rohini Heliport	31696.15	175.98
Safdarjung Airport	18348.83	223.29
NOCID	PALM/NORTH/B/030819/377136	

Street view



March 8, 2019

Satellite View



March 8, 2019



भारतीय विमानपत्तन प्राधिकरण
AIRPORTS AUTHORITY OF INDIA

File No. AAI/RHQ/NR/ATM/NOC/2019/117/527-530,

Copy to:

1. The Distt. Town Planner, Gurgaon, HUDA, Complex, Sector-14, Gurgaon, Haryana.
2. The Chief Executive Officer, Delhi International Airport, New Uddan Bhawan, I.G.I Airport Terminal -3, New Delhi-110037.
3. Guard file.
